



ग्राम विकास विभाग

स्वातंत्र्याचा अमृत महोत्सव अंतर्गत

महाआवास अभियान २.०: आढावा बैठक

दिनांक ०९.१२.२०२१



राज्य व्यवस्थापन कक्ष-ग्रामीण गृहनिर्माण  
महाराष्ट्र राज्य

# प्रधानमंत्री आवास योजना ग्रामीण : Sanction (PWL)

Sr. No.	District	Target (PWL)	Sanctions	Remaining
1	AMRAVATI	88907	69221	19686
2	NAGPUR	38235	29849	8386
3	SOLAPUR	43919	36502	7417
4	AHMEDNAGAR	47674	41926	5748
5	AKOLA	44287	38622	5665
6	JALGAON	61304	55965	5339
7	BULDHANA	27750	23916	3834
8	PUNE	18752	15298	3454
9	WARDHA	16163	13131	3032
10	BHANDARA	54790	51959	2831
11	NANDURBAR	102644	99930	2714
12	CHANDRAPUR	31360	28936	2424
13	YAVATMAL	39530	37130	2400
14	SANGLI	18338	16007	2331
15	NANDED	47304	45118	2186
16	SATARA	13071	11077	1994
17	JALNA	13296	11676	1620

Sr. No.	District	Target (PWL)	Sanctions	Remaining
18	LATUR	10851	9254	1597
19	NASHIK	70003	68568	1435
20	KOLHAPUR	14328	12990	1338
21	WASHIM	10319	9082	1237
22	RAIGAD	8524	7750	774
23	OSMANABAD	6036	5328	708
24	HINGOLI	10076	9514	562
25	BEED	18957	18445	512
26	GADCHIROLI	22283	21840	443
27	SINDHUDURG	3909	3694	215
28	PARBHANI	6973	6763	210
29	RATNAGIRI	5988	5963	25
30	THANE	6732	6708	24
31	PALGHAR	25670	25650	20
32	AURANGABAD	22084	22067	17
33	DHULE	46471	46457	14
34	GONDIA	82335	82335	0
<b>Total</b>		<b>1078075</b>	<b>988671</b>	<b>89404</b>

# प्रधानमंत्री आवास योजना ग्रामीण : Sanction (Awaas+)


SNo	Name	GP having awaasplus data	Job card Mapped GP	Gramsabh a Done	Target 21-22	Sanction	Remaining Sanction
	<b>Total</b>	<b>27288</b>	<b>18900</b>	<b>7249</b>	<b>308910</b>	<b>23</b>	<b>308887</b>
1	<b>YAVATMAL</b>	<b>1192</b>	<b>411</b>	<b>103</b>	<b>22290</b>	<b>0</b>	<b>22290</b>
2	<b>NANDED</b>	<b>1296</b>	<b>406</b>	<b>0</b>	<b>19791</b>	<b>0</b>	<b>19791</b>
3	<b>NASHIK</b>	<b>1379</b>	<b>1288</b>	<b>861</b>	<b>18668</b>	<b>0</b>	<b>18668</b>
4	<b>JALGAON</b>	<b>1147</b>	<b>434</b>	<b>230</b>	<b>17733</b>	<b>0</b>	<b>17733</b>
5	<b>NANDURBAR</b>	<b>581</b>	<b>36</b>	<b>0</b>	<b>16583</b>	<b>0</b>	<b>16583</b>
6	<b>DHULE</b>	<b>538</b>	<b>423</b>	<b>0</b>	<b>15601</b>	<b>2</b>	<b>15599</b>
7	<b>AHMEDNAGAR</b>	<b>1306</b>	<b>1211</b>	<b>0</b>	<b>13435</b>	<b>0</b>	<b>13435</b>
8	<b>BULDHANA</b>	<b>838</b>	<b>420</b>	<b>1</b>	<b>13071</b>	<b>0</b>	<b>13071</b>
9	<b>AMRAVATI</b>	<b>836</b>	<b>613</b>	<b>48</b>	<b>12958</b>	<b>0</b>	<b>12958</b>
10	<b>AURANGABAD</b>	<b>858</b>	<b>207</b>	<b>1</b>	<b>12436</b>	<b>0</b>	<b>12436</b>
11	<b>BEED</b>	<b>1030</b>	<b>746</b>	<b>0</b>	<b>12076</b>	<b>0</b>	<b>12076</b>
12	<b>GONDIA</b>	<b>539</b>	<b>494</b>	<b>472</b>	<b>10380</b>	<b>0</b>	<b>10380</b>
13	<b>CHANDRAPUR</b>	<b>802</b>	<b>659</b>	<b>234</b>	<b>10377</b>	<b>0</b>	<b>10377</b>
14	<b>JALNA</b>	<b>778</b>	<b>165</b>	<b>0</b>	<b>9757</b>	<b>0</b>	<b>9757</b>
15	<b>WASHIM</b>	<b>494</b>	<b>437</b>	<b>0</b>	<b>8970</b>	<b>0</b>	<b>8970</b>
16	<b>PALGHAR</b>	<b>458</b>	<b>179</b>	<b>140</b>	<b>8340</b>	<b>0</b>	<b>8340</b>
17	<b>LATUR</b>	<b>765</b>	<b>560</b>	<b>235</b>	<b>7789</b>	<b>0</b>	<b>7789</b>

## प्रधानमंत्री आवास योजना ग्रामीण : Sanction (Awaas+)

SNo	Name	GP having awaasplus data	Job card Mapped GP	Gramsabha Done	Target 21-22	Sanction	Remaining Sanction
18	SOLAPUR	1020	808	27	7739	0	7739
19	BHANDARA	528	251	3	7737	0	7737
20	GADCHIROLI	450	416	235	7362	0	7362
21	PARBHANI	703	436	270	7275	0	7275
22	HINGOLI	562	471	9	6727	0	6727
23	AKOLA	521	142	0	5962	0	5962
24	OSMANABAD	618	617	308	5748	0	5748
25	SANGLI	698	581	65	4499	0	4499
26	KOLHAPUR	1016	1016	710	4082	0	4082
27	NAGPUR	711	555	530	3949	2	3947
28	WARDHA	510	506	510	3813	0	3813
29	PUNE	1275	954	778	3582	3	3579
30	SATARA	1482	1482	313	3046	0	3046
31	THANE	409	324	29	2615	0	2615
32	RATNAGIRI	842	633	337	2132	0	2132
33	RAIGAD	680	680	610	1759	16	1743
34	SINDHUDURG	426	339	374	628	0	628
	<b>Total</b>	<b>27288</b>	<b>18900</b>	<b>7433</b>	<b>308910</b>	<b>23</b>	<b>308887</b>

ग्रामसभामधून ग्रामपंचायतनिहाय अल्पसंख्याक लाभार्थी निश्चित न झाल्यामुळे ८३०११ इतके उद्दिष्ट जिल्हानिहाय दाखवता येत नाही

# प्रधानमंत्री आवास योजना ग्रामीण : अभियान प्रगती (२० नोव्हेंबर ते ७ डिसेंबर २०२१)

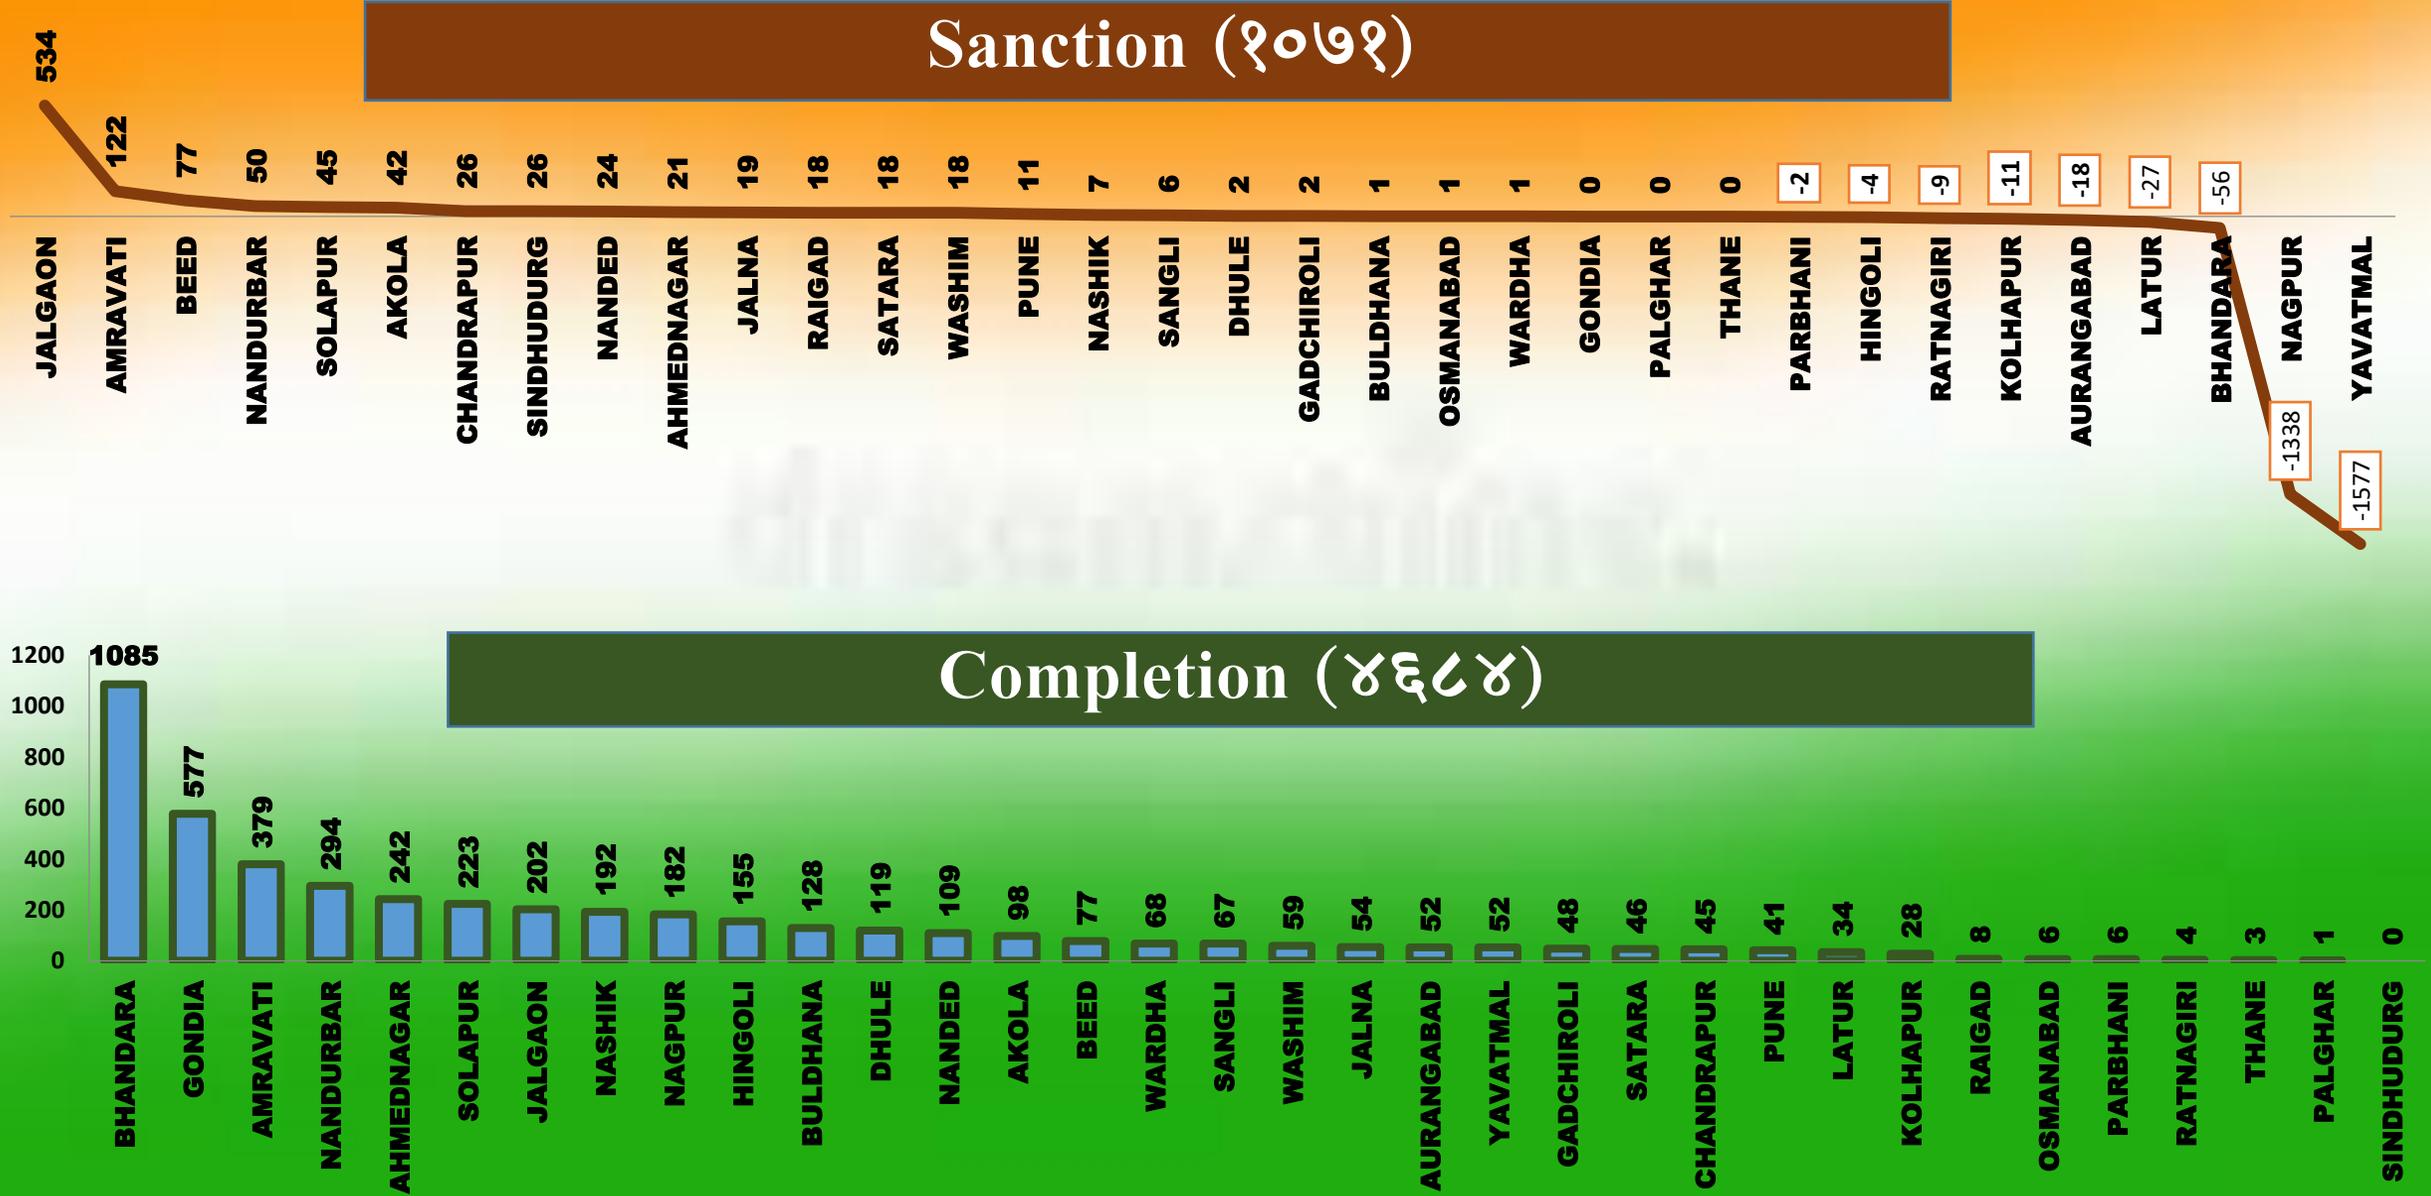

# प्रधानमंत्री आवास योजना ग्रामीण : अभियान प्रगती- Sanction

Sr. No.	District	Target (PWL+Awaas+)	Sanctions 07.12.2021	ABHIYAN			
				Sanction Target on 20 Nov	Sanctions 20 Nov to 07 dec.	Abhiyan %	Remaining
	<b>Total</b>	<b>1387381</b>	<b>988691</b>	<b>400502</b>	<b>1071</b>	<b>0.27</b>	<b>398690</b>
<b>1</b>	<b>JALGAON</b>	<b>79037</b>	<b>55965</b>	<b>24485</b>	<b>534</b>	<b>2.2</b>	<b>23072</b>
<b>2</b>	<b>AMRAVATI</b>	<b>101865</b>	<b>69221</b>	<b>34079</b>	<b>122</b>	<b>0.4</b>	<b>32644</b>
<b>3</b>	<b>BEED</b>	<b>31035</b>	<b>18445</b>	<b>12867</b>	<b>77</b>	<b>0.6</b>	<b>12590</b>
<b>4</b>	<b>NANDURBAR</b>	<b>119358</b>	<b>99930</b>	<b>19624</b>	<b>50</b>	<b>0.3</b>	<b>19428</b>
<b>5</b>	<b>SOLAPUR</b>	<b>51658</b>	<b>36502</b>	<b>15276</b>	<b>45</b>	<b>0.3</b>	<b>15156</b>
<b>6</b>	<b>AKOLA</b>	<b>50292</b>	<b>38622</b>	<b>11828</b>	<b>42</b>	<b>0.4</b>	<b>11670</b>
<b>7</b>	<b>CHANDRAPUR</b>	<b>41737</b>	<b>28936</b>	<b>12843</b>	<b>26</b>	<b>0.2</b>	<b>12801</b>
<b>8</b>	<b>SINDHUDURG</b>	<b>4542</b>	<b>3694</b>	<b>879</b>	<b>26</b>	<b>3.0</b>	<b>848</b>
<b>9</b>	<b>NANDED</b>	<b>67149</b>	<b>45118</b>	<b>22076</b>	<b>24</b>	<b>0.1</b>	<b>22031</b>
<b>10</b>	<b>AHMEDNAGAR</b>	<b>61168</b>	<b>41926</b>	<b>19304</b>	<b>21</b>	<b>0.1</b>	<b>19242</b>
<b>11</b>	<b>JALNA</b>	<b>23057</b>	<b>11676</b>	<b>11424</b>	<b>19</b>	<b>0.2</b>	<b>11381</b>
<b>12</b>	<b>RAIGAD</b>	<b>9497</b>	<b>7763</b>	<b>1754</b>	<b>18</b>	<b>1.0</b>	<b>1734</b>
<b>13</b>	<b>SATARA</b>	<b>16117</b>	<b>11077</b>	<b>5103</b>	<b>18</b>	<b>0.4</b>	<b>5040</b>
<b>14</b>	<b>WASHIM</b>	<b>19289</b>	<b>9082</b>	<b>10260</b>	<b>18</b>	<b>0.2</b>	<b>10207</b>
<b>15</b>	<b>PUNE</b>	<b>22334</b>	<b>15301</b>	<b>7052</b>	<b>11</b>	<b>0.2</b>	<b>7033</b>
<b>16</b>	<b>NASHIK</b>	<b>88692</b>	<b>68568</b>	<b>20217</b>	<b>7</b>	<b>0.0</b>	<b>20124</b>
<b>17</b>	<b>SANGLI</b>	<b>22837</b>	<b>16007</b>	<b>6852</b>	<b>6</b>	<b>0.1</b>	<b>6830</b>
<b>18</b>	<b>DHULE</b>	<b>62072</b>	<b>46459</b>	<b>15615</b>	<b>2</b>	<b>0.0</b>	<b>15613</b>

# प्रधानमंत्री आवास योजना ग्रामीण : अभियान प्रगती- Sanction

Sr. No.	District	Target (PWL+Awaas+)	Sanctions 07.12.2021	ABHIYAN			
				Sanction Target on 20 Nov	Sanctions 20 Nov to 07 dec.	Abhiyan %	Remaining
19	GADCHIROLI	29651	21840	7999	2	0.0	7811
20	BULDHANA	40821	23916	16927	1	0.0	16905
21	OSMANABAD	11787	5328	6460	1	0.0	6459
22	WARDHA	19976	13131	6847	1	0.0	6845
23	GONDIA	92715	82335	10380	0	0.0	10380
24	PALGHAR	34010	25650	8360	0	0.0	8360
25	THANE	9347	6708	2639	0	0.0	2639
26	PARBHANI	14270	6763	7513	-2	0.0	7507
27	HINGOLI	16803	9514	7315	-4	-0.1	7289
28	RATNAGIRI	8128	5963	2173	-9	-0.4	2165
29	KOLHAPUR	18410	12990	5450	-11	-0.2	5420
30	AURANGABAD	34534	22067	12478	-18	-0.1	12467
31	LATUR	18643	9254	9437	-27	-0.3	9389
32	BHANDARA	62541	51959	10732	-56	-0.5	10582
33	NAGPUR	42189	29851	11075	-1338	-12.1	12338
34	YAVATMAL	61820	37130	23179	-1577	-6.8	24690
	<b>Total</b>	<b>1387381</b>	<b>988691</b>	<b>400502</b>	<b>1071</b>	<b>-0.5</b>	<b>398690</b>

ग्रामपंचायतनिहाय अल्पसंख्याक लाभार्थी अद्याप वेगळे न झाल्यामुळे ८३०११ इतके उद्दिष्ट अद्याप वितरीत करण्यात आलेले नाही

# प्रधानमंत्री आवास योजना ग्रामीण : अभियान प्रगती- Completion

Sr. No.	District	Sanction	Completion 07.12.2021	ABHIYAN			
				Target on 20 Nov 2021	Completion 20 Nov 2021 to 07 Dec. 2021	%	Remaining
	<b>Total</b>	<b>988691</b>	<b>743326</b>	<b>252020</b>	<b>4684</b>	<b>1.85</b>	<b>245365</b>
<b>1</b>	<b>BHANDARA</b>	<b>51959</b>	<b>31998</b>	<b>21102</b>	<b>1085</b>	<b>5.14</b>	<b>19961</b>
<b>2</b>	<b>GONDIA</b>	<b>82335</b>	<b>69835</b>	<b>13077</b>	<b>577</b>	<b>4.41</b>	<b>12500</b>
<b>3</b>	<b>AMRAVATI</b>	<b>69221</b>	<b>51701</b>	<b>17777</b>	<b>379</b>	<b>2.13</b>	<b>17520</b>
<b>4</b>	<b>NANDURBAR</b>	<b>99930</b>	<b>75003</b>	<b>25171</b>	<b>294</b>	<b>1.16</b>	<b>24927</b>
<b>5</b>	<b>AHMEDNAGAR</b>	<b>41926</b>	<b>32535</b>	<b>9612</b>	<b>242</b>	<b>2.51</b>	<b>9391</b>
<b>6</b>	<b>SOLAPUR</b>	<b>36502</b>	<b>25095</b>	<b>11585</b>	<b>223</b>	<b>1.92</b>	<b>11407</b>
<b>7</b>	<b>JALGAON</b>	<b>55965</b>	<b>39033</b>	<b>16600</b>	<b>202</b>	<b>1.21</b>	<b>16932</b>
<b>8</b>	<b>NASHIK</b>	<b>68568</b>	<b>57568</b>	<b>11185</b>	<b>192</b>	<b>1.71</b>	<b>11000</b>
<b>9</b>	<b>NAGPUR</b>	<b>29851</b>	<b>23148</b>	<b>8223</b>	<b>182</b>	<b>2.21</b>	<b>6703</b>
<b>10</b>	<b>HINGOLI</b>	<b>9514</b>	<b>8030</b>	<b>1643</b>	<b>155</b>	<b>9.43</b>	<b>1484</b>
<b>11</b>	<b>BULDHANA</b>	<b>23916</b>	<b>17825</b>	<b>6218</b>	<b>128</b>	<b>2.05</b>	<b>6091</b>
<b>12</b>	<b>DHULE</b>	<b>46459</b>	<b>38241</b>	<b>8335</b>	<b>119</b>	<b>1.42</b>	<b>8218</b>
<b>13</b>	<b>NANDED</b>	<b>45118</b>	<b>26771</b>	<b>18432</b>	<b>109</b>	<b>0.59</b>	<b>18347</b>
<b>14</b>	<b>AKOLA</b>	<b>38622</b>	<b>28527</b>	<b>10151</b>	<b>98</b>	<b>0.96</b>	<b>10095</b>
<b>15</b>	<b>BEED</b>	<b>18445</b>	<b>12089</b>	<b>6356</b>	<b>77</b>	<b>1.21</b>	<b>6356</b>
<b>16</b>	<b>WARDHA</b>	<b>13131</b>	<b>10544</b>	<b>2654</b>	<b>68</b>	<b>2.56</b>	<b>2587</b>
<b>17</b>	<b>SANGLI</b>	<b>16007</b>	<b>10640</b>	<b>5428</b>	<b>67</b>	<b>1.23</b>	<b>5367</b>

# प्रधानमंत्री आवास योजना ग्रामीण : अभियान प्रगती- Completion

Sr. No.	District	Sanction	Completion 07.12.2021	ABHIYAN			
				Target on 20 Nov 2021	Completion 20 Nov 2021 to 07 Dec. 2021	%	Remaining
18	WASHIM	9082	6248	2875	59	2.05	2834
19	JALNA	11676	8361	3350	54	1.61	3315
20	AURANGABAD	22067	15913	6224	52	0.83	6154
21	YAVATMAL	37130	25829	12930	52	0.40	11301
22	GADCHIROLI	21840	15676	6210	48	0.77	6164
23	SATARA	11077	8064	3041	46	1.51	3013
24	CHANDRAPUR	28936	21841	7114	45	0.63	7095
25	PUNE	15301	10618	4713	41	0.87	4683
26	LATUR	9254	7159	2156	34	1.57	2095
27	KOLHAPUR	12990	10245	2784	28	1.00	2745
28	RAIGAD	7763	7068	685	8	1.16	695
29	OSMANABAD	5328	4048	1285	6	0.46	1280
30	PARBHANI	6763	5225	1546	6	0.38	1538
31	RATNAGIRI	5963	5400	576	4	0.69	563
32	THANE	6708	6228	483	3	0.62	480
33	PALGHAR	25650	23546	2105	1	0.04	2104
34	SINDHUDURG	3694	3274	394	0	0	420
	<b>Total</b>	<b>988691</b>	<b>743326</b>	<b>252020</b>	<b>4684</b>	<b>1.85</b>	<b>245365</b>

# राज्यपुरस्कृत आवास योजना ग्रामीण : अभियान प्रगती (२० नोव्हेंबर ते ७ डिसेंबर २०२१)

## Sanctions (८१९)



## Completion (१९०२)



# राज्यपुरस्कृत आवास योजना ग्रामीण : अभियान प्रगती- Sanction

Sr. No.	District	Target	Sanctions 07.12.2021	ABHIYAN			
				Sanction Target on 20 Nov	Sanctions 20 Nov 2021 to 07 dec. 2021	Abhiyan %	Remaining
	<b>Total</b>	<b>449509</b>	<b>419833</b>	<b>30338</b>	<b>819</b>	<b>2.7</b>	<b>29676</b>
<b>1</b>	<b>BEED</b>	<b>16485</b>	<b>15102</b>	<b>1638</b>	<b>255</b>	<b>15.6</b>	<b>1383</b>
<b>2</b>	<b>JALNA</b>	<b>9609</b>	<b>9179</b>	<b>614</b>	<b>184</b>	<b>30.0</b>	<b>430</b>
<b>3</b>	<b>NANDED</b>	<b>18260</b>	<b>15741</b>	<b>2649</b>	<b>130</b>	<b>4.9</b>	<b>2519</b>
<b>4</b>	<b>LATUR</b>	<b>20102</b>	<b>19598</b>	<b>621</b>	<b>117</b>	<b>18.8</b>	<b>504</b>
<b>5</b>	<b>CHANDRAPUR</b>	<b>25562</b>	<b>21838</b>	<b>3783</b>	<b>59</b>	<b>1.6</b>	<b>3724</b>
<b>6</b>	<b>HINGOLI</b>	<b>10195</b>	<b>9450</b>	<b>776</b>	<b>31</b>	<b>4.0</b>	<b>745</b>
<b>7</b>	<b>PUNE</b>	<b>10938</b>	<b>10350</b>	<b>603</b>	<b>15</b>	<b>2.5</b>	<b>588</b>
<b>8</b>	<b>AKOLA</b>	<b>14458</b>	<b>13691</b>	<b>779</b>	<b>12</b>	<b>1.5</b>	<b>767</b>
<b>9</b>	<b>YAVATMAL</b>	<b>20141</b>	<b>19139</b>	<b>1008</b>	<b>6</b>	<b>0.6</b>	<b>1002</b>
<b>10</b>	<b>AURANGABAD</b>	<b>17952</b>	<b>17530</b>	<b>424</b>	<b>2</b>	<b>0.5</b>	<b>422</b>
<b>11</b>	<b>NASHIK</b>	<b>20372</b>	<b>18961</b>	<b>1413</b>	<b>2</b>	<b>0.1</b>	<b>1411</b>
<b>12</b>	<b>GADCHIROLI</b>	<b>13305</b>	<b>11138</b>	<b>2168</b>	<b>1</b>	<b>0.0</b>	<b>2167</b>
<b>13</b>	<b>JALGAON</b>	<b>18210</b>	<b>17342</b>	<b>716</b>	<b>1</b>	<b>0.1</b>	<b>868</b>
<b>14</b>	<b>NANDURBAR</b>	<b>13581</b>	<b>9885</b>	<b>3697</b>	<b>1</b>	<b>0.0</b>	<b>3696</b>
<b>15</b>	<b>OSMANABAD</b>	<b>15354</b>	<b>15193</b>	<b>162</b>	<b>1</b>	<b>0.6</b>	<b>161</b>
<b>16</b>	<b>PARBHANI</b>	<b>14649</b>	<b>14515</b>	<b>135</b>	<b>1</b>	<b>0.7</b>	<b>134</b>
<b>17</b>	<b>SOLAPUR</b>	<b>15517</b>	<b>15284</b>	<b>234</b>	<b>1</b>	<b>0.4</b>	<b>233</b>

# राज्यपुरस्कृत आवास योजना ग्रामीण : अभियान प्रगती- Sanction

Sr. No.	District	Target	Sanctions 07.12.2021	ABHIYAN			
				Sanction Target on 20 Nov	Sanctions 20 Nov 2021 to 07 dec. 2021	Abhiyan %	Remaining
18	AHMEDNAGAR	28964	28550	414	0	0.0	414
19	AMRAVATI	15147	14366	781	0	0.0	781
20	BHANDARA	15736	14846	890	0	0.0	890
21	BULDHANA	12418	12189	229	0	0.0	229
22	DHULE	13841	12319	1522	0	0.0	1522
23	KOLHAPUR	10860	10843	17	0	0.0	17
24	NAGPUR	9927	9258	669	0	0.0	669
25	PALGHAR	8133	6344	1789	0	0.0	1789
26	RAIGAD	4377	3814	563	0	0.0	563
27	RATNAGIRI	5923	5863	60	0	0.0	60
28	SANGLI	7082	7038	44	0	0.0	44
29	SATARA	9599	9545	54	0	0.0	54
30	SINDHUDURG	1852	1845	7	0	0.0	7
31	THANE	4068	3490	578	0	0.0	578
32	WARDHA	8510	8310	200	0	0.0	200
33	WASHIM	8031	7712	319	0	0.0	319
34	GONDIA	10351	9565	782	-4	-0.5	786
	<b>Total</b>	<b>449509</b>	<b>419833</b>	<b>30338</b>	<b>819</b>	<b>2.7</b>	<b>29676</b>

# राज्यपुरस्कृत आवास योजना ग्रामीण : अभियान प्रगती- Completion

Sr.N	District	Sanction	Completion 07.12.2021	ABHIYAN			
				Target on 20 Nov	Completion 20 Nov 2021 to 07 Dec. 2021	%	Remaining
	<b>Total</b>	<b>419833</b>	<b>295941</b>	<b>124979</b>	<b>1902</b>	<b>1.5</b>	<b>123892</b>
<b>1</b>	<b>BHANDARA</b>	<b>14846</b>	<b>9867</b>	<b>5235</b>	<b>256</b>	<b>4.9</b>	<b>4979</b>
<b>2</b>	<b>NASHIK</b>	<b>18961</b>	<b>13817</b>	<b>5278</b>	<b>136</b>	<b>2.6</b>	<b>5144</b>
<b>3</b>	<b>AURANGABAD</b>	<b>17530</b>	<b>10360</b>	<b>7281</b>	<b>113</b>	<b>1.6</b>	<b>7170</b>
<b>4</b>	<b>HINGOLI</b>	<b>9450</b>	<b>7711</b>	<b>1808</b>	<b>100</b>	<b>5.5</b>	<b>1739</b>
<b>5</b>	<b>CHANDRAPUR</b>	<b>21838</b>	<b>12658</b>	<b>9217</b>	<b>96</b>	<b>1.0</b>	<b>9180</b>
<b>6</b>	<b>AHMEDNAGAR</b>	<b>28550</b>	<b>22138</b>	<b>6503</b>	<b>91</b>	<b>1.4</b>	<b>6412</b>
<b>7</b>	<b>OSMANABAD</b>	<b>15193</b>	<b>6220</b>	<b>9057</b>	<b>85</b>	<b>0.9</b>	<b>8973</b>
<b>8</b>	<b>AMRAVATI</b>	<b>14366</b>	<b>10975</b>	<b>3474</b>	<b>83</b>	<b>2.4</b>	<b>3391</b>
<b>9</b>	<b>LATUR</b>	<b>19598</b>	<b>12702</b>	<b>6857</b>	<b>78</b>	<b>1.1</b>	<b>6896</b>
<b>10</b>	<b>BEED</b>	<b>15102</b>	<b>8330</b>	<b>6581</b>	<b>64</b>	<b>1.0</b>	<b>6772</b>
<b>11</b>	<b>GADCHIROLI</b>	<b>11138</b>	<b>7428</b>	<b>3771</b>	<b>62</b>	<b>1.6</b>	<b>3710</b>
<b>12</b>	<b>JALGAON</b>	<b>17342</b>	<b>12515</b>	<b>4888</b>	<b>62</b>	<b>1.3</b>	<b>4827</b>
<b>13</b>	<b>JALNA</b>	<b>9179</b>	<b>4523</b>	<b>4533</b>	<b>61</b>	<b>1.3</b>	<b>4656</b>
<b>14</b>	<b>BULDHANA</b>	<b>12189</b>	<b>9269</b>	<b>2973</b>	<b>53</b>	<b>1.8</b>	<b>2920</b>
<b>15</b>	<b>GONDIA</b>	<b>9565</b>	<b>7748</b>	<b>1874</b>	<b>53</b>	<b>2.8</b>	<b>1817</b>
<b>16</b>	<b>NANDED</b>	<b>15741</b>	<b>8228</b>	<b>7436</b>	<b>53</b>	<b>0.7</b>	<b>7513</b>
<b>17</b>	<b>WARDHA</b>	<b>8310</b>	<b>6536</b>	<b>1821</b>	<b>47</b>	<b>2.6</b>	<b>1774</b>

# राज्यपुरस्कृत आवास योजना ग्रामीण : अभियान प्रगती- Completion

	District	Sanction	Completion 07.12.2021	ABHIYAN			
				Target on 20 Nov	Completion 20 Nov 2021 to 07 Dec. 2021	%	Remaining
18	YAVATMAL	19139	13451	5729	47	0.8	5688
19	PARBHANI	14515	10980	3577	43	1.2	3535
20	WASHIM	7712	4750	3003	41	1.4	2962
21	SATARA	9545	7796	1787	38	2.1	1749
22	NANDURBAR	9885	7562	2358	36	1.5	2323
23	AKOLA	13691	9141	4573	35	0.8	4550
24	NAGPUR	9258	7782	1509	33	2.2	1476
25	PUNE	10350	7661	2707	33	1.2	2689
26	SOLAPUR	15284	12585	2730	32	1.2	2699
27	DHULE	12319	10259	2083	23	1.1	2060
28	SANGLI	7038	5025	2026	13	0.6	2013
29	RAIGAD	3814	3473	353	12	3.4	341
30	RATNAGIRI	5863	5246	627	10	1.6	617
31	SINDHUDURG	1845	1665	184	4	2.2	180
32	KOLHAPUR	10843	9089	1757	3	0.2	1754
33	PALGHAR	6344	5238	1109	3	0.3	1106
34	THANE	3490	3213	280	3	1.1	277
	<b>Total</b>	<b>419833</b>	<b>295941</b>	<b>124979</b>	<b>1902</b>	<b>1.5</b>	<b>123892</b>

# PMAY-G Sanction and 1st Instalment Release Status

#SNo	District_Name	Total houses sanctioned	Houses with 1st installment released	Average time taken for 1st installment release (in days)	Houses Pending for 1st installment				
					No. of houses Pending	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
	<b>Total/Avg</b>	<b>987509</b>	<b>967714</b>	<b>58</b>	<b>19795</b>	<b>408</b>	<b>683</b>	<b>758</b>	<b>17946</b>
<b>1</b>	<b>SINDHUDURG</b>	<b>3694</b>	<b>3664</b>	<b>21</b>	<b>30</b>	<b>4</b>	<b>16</b>	<b>4</b>	<b>6</b>
<b>2</b>	<b>NASHIK</b>	<b>68486</b>	<b>68031</b>	<b>31</b>	<b>455</b>	<b>14</b>	<b>4</b>	<b>2</b>	<b>435</b>
<b>3</b>	<b>THANE</b>	<b>6122</b>	<b>6074</b>	<b>33</b>	<b>48</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>48</b>
<b>4</b>	<b>DHULE</b>	<b>46424</b>	<b>46333</b>	<b>40</b>	<b>91</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>91</b>
<b>5</b>	<b>HINGOLI</b>	<b>9514</b>	<b>9476</b>	<b>40</b>	<b>38</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>35</b>
<b>6</b>	<b>SOLAPUR</b>	<b>36503</b>	<b>35515</b>	<b>42</b>	<b>988</b>	<b>34</b>	<b>16</b>	<b>13</b>	<b>925</b>
<b>7</b>	<b>KOLHAPUR</b>	<b>12990</b>	<b>12662</b>	<b>43</b>	<b>328</b>	<b>0</b>	<b>0</b>	<b>3</b>	<b>325</b>
<b>8</b>	<b>PUNE</b>	<b>15295</b>	<b>14465</b>	<b>43</b>	<b>830</b>	<b>6</b>	<b>2</b>	<b>4</b>	<b>818</b>
<b>9</b>	<b>AHMEDNAGAR</b>	<b>41926</b>	<b>41885</b>	<b>44</b>	<b>41</b>	<b>2</b>	<b>0</b>	<b>9</b>	<b>30</b>
<b>10</b>	<b>OSMANABAD</b>	<b>5284</b>	<b>5228</b>	<b>44</b>	<b>56</b>	<b>2</b>	<b>1</b>	<b>4</b>	<b>49</b>
<b>11</b>	<b>JALNA</b>	<b>11676</b>	<b>11341</b>	<b>50</b>	<b>335</b>	<b>14</b>	<b>5</b>	<b>20</b>	<b>296</b>
<b>12</b>	<b>RAIGAD</b>	<b>7791</b>	<b>7682</b>	<b>50</b>	<b>109</b>	<b>44</b>	<b>6</b>	<b>7</b>	<b>52</b>
<b>13</b>	<b>AKOLA</b>	<b>38622</b>	<b>37880</b>	<b>51</b>	<b>742</b>	<b>22</b>	<b>0</b>	<b>30</b>	<b>690</b>
<b>14</b>	<b>BULDHANA</b>	<b>23899</b>	<b>23586</b>	<b>51</b>	<b>313</b>	<b>0</b>	<b>1</b>	<b>2</b>	<b>310</b>
<b>15</b>	<b>LATUR</b>	<b>9089</b>	<b>8864</b>	<b>53</b>	<b>225</b>	<b>0</b>	<b>0</b>	<b>7</b>	<b>218</b>
<b>16</b>	<b>JALGAON</b>	<b>55963</b>	<b>54399</b>	<b>54</b>	<b>1564</b>	<b>100</b>	<b>337</b>	<b>158</b>	<b>969</b>
<b>17</b>	<b>AMRAVATI</b>	<b>69223</b>	<b>67808</b>	<b>55</b>	<b>1415</b>	<b>36</b>	<b>92</b>	<b>98</b>	<b>1189</b>

# PMAY-G Sanction and 1st instalment release Status

#SNo	District_Name	Total houses sanctioned	Houses with 1st installment released	Average time taken for 1st installment release (in days)	Houses Pending for 1st installment				
					No. of houses Pending	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
18	CHANDRAPUR	28953	28583	55	370	19	11	49	291
19	NANDURBAR	99929	96468	57	3461	0	60	83	3318
20	RATNAGIRI	5963	5931	57	32	0	0	0	32
21	WASHIM	9082	8785	58	297	0	4	26	267
22	PARBHANI	6763	6679	59	84	1	0	0	83
23	AURANGABAD	22067	21096	60	971	0	0	2	969
24	BEED	18443	17882	60	561	30	36	94	401
25	WARDHA	13131	13099	60	32	0	1	0	31
26	SANGLI	15995	15521	62	474	0	7	0	467
27	BHANDARA	51902	51047	63	855	0	7	8	840
28	YAVATMAL	36934	36227	63	707	0	2	4	701
29	GADCHIROLI	21840	21590	66	250	2	0	13	235
30	SATARA	11014	9731	68	1283	4	48	5	1226
31	GONDIA	82335	81635	79	700	0	0	0	700
32	NANDED	45118	43572	90	1546	4	21	102	1419
33	PALGHAR	25650	25571	94	79	0	0	0	79
34	NAGPUR	29889	29404	105	485	69	5	10	401
<b>Total/Avg</b>		<b>987509</b>	<b>967714</b>	<b>58</b>	<b>19795</b>	<b>408</b>	<b>683</b>	<b>758</b>	<b>17946</b>

# PMAY-G Sanction and House completion Status

#SNo	District_Name	Total houses sanctioned	Total houses completed	Average time taken for houses completion (in days)	Houses Pending for Completion				
					No. of houses Incomplete	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
	<b>Total/Avg</b>	<b>987509</b>	<b>742423</b>	<b>357</b>	<b>245075</b>	<b>419</b>	<b>815</b>	<b>924</b>	<b>242917</b>
<b>1</b>	<b>SINDHUDURG</b>	<b>3694</b>	<b>3276</b>	<b>280</b>	<b>418</b>	<b>4</b>	<b>23</b>	<b>14</b>	<b>377</b>
<b>2</b>	<b>GONDIA</b>	<b>82335</b>	<b>69899</b>	<b>288</b>	<b>12436</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>12436</b>
<b>3</b>	<b>SATARA</b>	<b>11014</b>	<b>8006</b>	<b>293</b>	<b>3008</b>	<b>4</b>	<b>48</b>	<b>5</b>	<b>2951</b>
<b>4</b>	<b>SOLAPUR</b>	<b>36503</b>	<b>25095</b>	<b>312</b>	<b>11408</b>	<b>34</b>	<b>16</b>	<b>14</b>	<b>11344</b>
<b>5</b>	<b>NASHIK</b>	<b>68486</b>	<b>57510</b>	<b>317</b>	<b>10975</b>	<b>14</b>	<b>5</b>	<b>2</b>	<b>10954</b>
<b>6</b>	<b>HINGOLI</b>	<b>9514</b>	<b>8030</b>	<b>320</b>	<b>1484</b>	<b>1</b>	<b>2</b>	<b>6</b>	<b>1475</b>
<b>7</b>	<b>BULDHANA</b>	<b>23899</b>	<b>17809</b>	<b>325</b>	<b>6090</b>	<b>0</b>	<b>1</b>	<b>2</b>	<b>6087</b>
<b>8</b>	<b>RATNAGIRI</b>	<b>5963</b>	<b>5401</b>	<b>331</b>	<b>562</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>562</b>
<b>9</b>	<b>WARDHA</b>	<b>13131</b>	<b>10546</b>	<b>339</b>	<b>2585</b>	<b>0</b>	<b>1</b>	<b>1</b>	<b>2583</b>
<b>10</b>	<b>AMRAVATI</b>	<b>69223</b>	<b>51701</b>	<b>341</b>	<b>17521</b>	<b>36</b>	<b>114</b>	<b>132</b>	<b>17239</b>
<b>11</b>	<b>SANGLI</b>	<b>15995</b>	<b>10628</b>	<b>341</b>	<b>5366</b>	<b>0</b>	<b>7</b>	<b>0</b>	<b>5359</b>
<b>12</b>	<b>BEED</b>	<b>18443</b>	<b>12088</b>	<b>342</b>	<b>6355</b>	<b>33</b>	<b>39</b>	<b>106</b>	<b>6177</b>
<b>13</b>	<b>NAGPUR</b>	<b>29889</b>	<b>23163</b>	<b>345</b>	<b>6726</b>	<b>69</b>	<b>7</b>	<b>15</b>	<b>6635</b>
<b>14</b>	<b>JALGAON</b>	<b>55963</b>	<b>39034</b>	<b>347</b>	<b>16929</b>	<b>104</b>	<b>422</b>	<b>217</b>	<b>16186</b>
<b>15</b>	<b>THANE</b>	<b>6122</b>	<b>5648</b>	<b>349</b>	<b>474</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>474</b>
<b>16</b>	<b>BHANDARA</b>	<b>51902</b>	<b>31941</b>	<b>353</b>	<b>19961</b>	<b>0</b>	<b>10</b>	<b>9</b>	<b>19942</b>
<b>17</b>	<b>CHANDRAPUR</b>	<b>28953</b>	<b>21841</b>	<b>354</b>	<b>7111</b>	<b>22</b>	<b>11</b>	<b>57</b>	<b>7021</b>

# PMAY-G Sanction and House completion Status

#SNo	District_Name	Total houses sanctioned	Total houses completed	Average time taken for houses completion (in days)	Houses Pending for Completion				
					No. of houses Incomplete	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
18	DHULE	46424	38208	354	8216	0	0	0	8216
19	WASHIM	9082	6248	355	2830	0	4	27	2799
20	OSMANABAD	5284	4005	359	1279	2	1	4	1272
21	JALNA	11676	8368	364	3308	14	5	21	3268
22	RAIGAD	7791	7069	365	722	44	6	7	665
23	YAVATMAL	36934	25824	365	11110	1	6	4	11099
24	AHMEDNAGAR	41926	32542	367	9384	2	1	21	9360
25	AURANGABAD	22067	15913	367	6153	0	0	2	6151
26	KOLHAPUR	12990	10247	372	2743	0	0	6	2737
27	AKOLA	38622	28527	383	10095	22	0	30	10043
28	PUNE	15295	10616	387	4679	6	2	14	4657
29	PARBHANI	6763	5226	389	1537	1	0	2	1534
30	PALGHAR	25650	23546	391	2104	0	0	0	2104
31	LATUR	9089	6999	426	2090	0	0	7	2083
32	NANDED	45118	26776	426	18340	4	24	102	18210
33	NANDURBAR	99929	75017	433	24912	0	60	84	24768
34	GADCHIROLI	21840	15676	458	6164	2	0	13	6149
	<b>Total/Avg</b>	<b>987509</b>	<b>742423</b>	<b>357</b>	<b>245075</b>	<b>419</b>	<b>815</b>	<b>924</b>	<b>242917</b>

# PMAY-G 1<sup>st</sup> Instalment Released and Completion

#SNo	District	1st installment released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
	<b>Total/Avg</b>	<b>968781</b>	<b>743271</b>	<b>304</b>	<b>225500</b>	<b>676</b>	<b>1258</b>	<b>449</b>	<b>223117</b>
<b>1</b>	<b>GONDIA</b>	<b>81635</b>	<b>69812</b>	<b>213</b>	<b>11823</b>	<b>3</b>	<b>16</b>	<b>0</b>	<b>11804</b>
<b>2</b>	<b>SATARA</b>	<b>9792</b>	<b>8064</b>	<b>235</b>	<b>1728</b>	<b>2</b>	<b>8</b>	<b>6</b>	<b>1712</b>
<b>3</b>	<b>NAGPUR</b>	<b>29404</b>	<b>23157</b>	<b>249</b>	<b>6247</b>	<b>19</b>	<b>24</b>	<b>83</b>	<b>6121</b>
<b>4</b>	<b>SINDHUDURG</b>	<b>3664</b>	<b>3276</b>	<b>257</b>	<b>388</b>	<b>4</b>	<b>12</b>	<b>7</b>	<b>365</b>
<b>5</b>	<b>SOLAPUR</b>	<b>35515</b>	<b>25093</b>	<b>273</b>	<b>10422</b>	<b>13</b>	<b>31</b>	<b>48</b>	<b>10330</b>
<b>6</b>	<b>RATNAGIRI</b>	<b>5931</b>	<b>5401</b>	<b>277</b>	<b>530</b>	<b>2</b>	<b>3</b>	<b>0</b>	<b>525</b>
<b>7</b>	<b>HINGOLI</b>	<b>9476</b>	<b>8028</b>	<b>278</b>	<b>1448</b>	<b>0</b>	<b>16</b>	<b>5</b>	<b>1427</b>
<b>8</b>	<b>WARDHA</b>	<b>13099</b>	<b>10546</b>	<b>279</b>	<b>2553</b>	<b>0</b>	<b>3</b>	<b>5</b>	<b>2545</b>
<b>9</b>	<b>BULDHANA</b>	<b>23603</b>	<b>17819</b>	<b>280</b>	<b>5784</b>	<b>26</b>	<b>11</b>	<b>0</b>	<b>5747</b>
<b>10</b>	<b>SANGLI</b>	<b>15533</b>	<b>10635</b>	<b>280</b>	<b>4897</b>	<b>91</b>	<b>8</b>	<b>0</b>	<b>4798</b>
<b>11</b>	<b>BEED</b>	<b>17884</b>	<b>12088</b>	<b>285</b>	<b>5796</b>	<b>36</b>	<b>48</b>	<b>21</b>	<b>5691</b>
<b>12</b>	<b>NASHIK</b>	<b>68112</b>	<b>57586</b>	<b>288</b>	<b>10525</b>	<b>10</b>	<b>6</b>	<b>13</b>	<b>10496</b>
<b>13</b>	<b>AMRAVATI</b>	<b>67808</b>	<b>51700</b>	<b>291</b>	<b>16107</b>	<b>41</b>	<b>151</b>	<b>60</b>	<b>15855</b>
<b>14</b>	<b>BHANDARA</b>	<b>51104</b>	<b>31997</b>	<b>294</b>	<b>19107</b>	<b>30</b>	<b>212</b>	<b>34</b>	<b>18831</b>
<b>15</b>	<b>JALGAON</b>	<b>54399</b>	<b>39027</b>	<b>298</b>	<b>15372</b>	<b>178</b>	<b>206</b>	<b>13</b>	<b>14975</b>
<b>16</b>	<b>PALGHAR</b>	<b>25571</b>	<b>23545</b>	<b>302</b>	<b>2026</b>	<b>4</b>	<b>1</b>	<b>0</b>	<b>2021</b>
<b>17</b>	<b>CHANDRAPUR</b>	<b>28583</b>	<b>21840</b>	<b>303</b>	<b>6742</b>	<b>39</b>	<b>152</b>	<b>10</b>	<b>6541</b>

# PMAY-G 1<sup>st</sup> Instalment Released and Completion

#SNo	District	1st installment released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
18	WASHIM	8785	6247	305	2534	23	26	0	2485
19	AURANGABAD	21096	15908	313	5188	2	6	7	5173
20	THANE	6659	6228	313	431	0	0	0	431
21	DHULE	46366	38239	315	8127	0	8	9	8110
22	RAIGAD	7682	7069	315	613	3	2	0	608
23	YAVATMAL	36234	25830	316	10404	63	69	11	10261
24	OSMANABAD	5272	4048	318	1224	0	1	0	1223
25	JALNA	11341	8365	319	2976	12	47	5	2912
26	AHMEDNAGAR	41885	32540	324	9345	6	13	34	9292
27	KOLHAPUR	12662	10241	329	2421	6	1	0	2414
28	PARBHANI	6679	5222	336	1457	1	6	0	1450
29	AKOLA	37880	28527	338	9353	8	47	4	9294
30	PUNE	14468	10618	350	3850	15	3	41	3791
31	NANDED	43572	26772	356	16798	8	73	16	16701
32	LATUR	9029	7160	377	1869	0	0	1	1868
33	NANDURBAR	96468	74968	384	21500	29	37	15	21419
34	GADCHIROLI	21590	15675	399	5915	2	11	1	5901
	<b>Total/Avg</b>	<b>968781</b>	<b>743271</b>	<b>304</b>	<b>225500</b>	<b>676</b>	<b>1258</b>	<b>449</b>	<b>223117</b>

# PMAY-G 2<sup>nd</sup> Instalment Released and Completion

#SNo	District	2nd installme nt released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
	<b>Total</b>	<b>847377</b>	<b>739873</b>	<b>155</b>	<b>107504</b>	<b>1154</b>	<b>2053</b>	<b>1002</b>	<b>103295</b>
<b>1</b>	<b>SANGLI</b>	<b>11729</b>	<b>10589</b>	<b>100</b>	<b>1140</b>	<b>187</b>	<b>6</b>	<b>2</b>	<b>945</b>
<b>2</b>	<b>GONDIA</b>	<b>75814</b>	<b>68815</b>	<b>102</b>	<b>6999</b>	<b>33</b>	<b>198</b>	<b>49</b>	<b>6719</b>
<b>3</b>	<b>BEED</b>	<b>14662</b>	<b>12002</b>	<b>104</b>	<b>2660</b>	<b>25</b>	<b>150</b>	<b>18</b>	<b>2467</b>
<b>4</b>	<b>HINGOLI</b>	<b>8386</b>	<b>7952</b>	<b>104</b>	<b>434</b>	<b>6</b>	<b>33</b>	<b>7</b>	<b>388</b>
<b>5</b>	<b>SINDHUDURG</b>	<b>3420</b>	<b>3266</b>	<b>113</b>	<b>154</b>	<b>0</b>	<b>0</b>	<b>6</b>	<b>148</b>
<b>6</b>	<b>NAGPUR</b>	<b>25614</b>	<b>23088</b>	<b>121</b>	<b>2526</b>	<b>38</b>	<b>69</b>	<b>56</b>	<b>2363</b>
<b>7</b>	<b>PARBHANI</b>	<b>5740</b>	<b>5138</b>	<b>123</b>	<b>602</b>	<b>2</b>	<b>11</b>	<b>1</b>	<b>588</b>
<b>8</b>	<b>WASHIM</b>	<b>7391</b>	<b>6222</b>	<b>128</b>	<b>1169</b>	<b>30</b>	<b>22</b>	<b>1</b>	<b>1116</b>
<b>9</b>	<b>JALGAON</b>	<b>43215</b>	<b>38790</b>	<b>133</b>	<b>4425</b>	<b>47</b>	<b>187</b>	<b>104</b>	<b>4087</b>
<b>10</b>	<b>RATNAGIRI</b>	<b>5658</b>	<b>5397</b>	<b>134</b>	<b>261</b>	<b>7</b>	<b>3</b>	<b>2</b>	<b>249</b>
<b>11</b>	<b>SATARA</b>	<b>8876</b>	<b>8017</b>	<b>134</b>	<b>859</b>	<b>3</b>	<b>18</b>	<b>21</b>	<b>817</b>
<b>12</b>	<b>OSMANABAD</b>	<b>4421</b>	<b>3999</b>	<b>135</b>	<b>422</b>	<b>0</b>	<b>16</b>	<b>4</b>	<b>402</b>
<b>13</b>	<b>SOLAPUR</b>	<b>28845</b>	<b>24978</b>	<b>137</b>	<b>3867</b>	<b>29</b>	<b>38</b>	<b>208</b>	<b>3592</b>
<b>14</b>	<b>JALNA</b>	<b>9568</b>	<b>8301</b>	<b>139</b>	<b>1267</b>	<b>11</b>	<b>23</b>	<b>23</b>	<b>1210</b>
<b>15</b>	<b>BULDHANA</b>	<b>21163</b>	<b>17724</b>	<b>140</b>	<b>3439</b>	<b>1</b>	<b>23</b>	<b>0</b>	<b>3415</b>
<b>16</b>	<b>NANDED</b>	<b>30654</b>	<b>26595</b>	<b>140</b>	<b>4059</b>	<b>1</b>	<b>59</b>	<b>25</b>	<b>3974</b>
<b>17</b>	<b>RAIGAD</b>	<b>7295</b>	<b>7041</b>	<b>141</b>	<b>254</b>	<b>5</b>	<b>18</b>	<b>0</b>	<b>231</b>

# PMAY-G 2<sup>nd</sup> Instalment Released and Completion

#SNo	District	2nd instalment released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8-15 days	No. of houses with delay of 16-30 days	No. of houses with delay of more than 30 days
18	CHANDRAPUR	25376	21819	145	3557	22	56	17	3462
19	KOLHAPUR	10881	10192	147	689	13	8	8	660
20	AURANGABAD	18361	15831	148	2530	36	62	8	2424
21	WARDHA	11931	10509	149	1422	10	6	5	1401
22	AHMEDNAGAR	37315	32432	150	4883	66	92	121	4604
23	BHANDARA	42043	31977	156	10066	197	204	41	9624
24	AMRAVATI	58683	51559	157	7124	61	253	43	6767
25	NASHIK	63602	57516	157	6086	114	80	64	5828
26	PALGHAR	24771	23447	164	1324	1	1	0	1322
27	YAVATMAL	30910	25773	167	5137	16	21	6	5094
28	LATUR	7938	7106	174	832	13	14	1	804
29	THANE	6432	6198	174	234	0	2	0	232
30	DHULE	42129	38101	175	4028	12	172	43	3801
31	AKOLA	33467	28502	178	4965	22	55	14	4874
32	PUNE	12192	10537	178	1655	18	38	94	1505
33	GADCHIROLI	19313	15629	184	3684	59	19	6	3600
34	NANDURBAR	89582	74831	240	14751	69	96	4	14582
	<b>Total</b>	<b>847377</b>	<b>739873</b>	<b>155</b>	<b>107504</b>	<b>1154</b>	<b>2053</b>	<b>1002</b>	<b>103295</b>

# PMAY-G 3<sup>rd</sup> Instalment Released and Completion

#SNo	District_Name	3rd installmen t released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8- 15 days	No. of houses with delay of 16- 30 days	No. of houses with delay of more than 30 days
	<b>Total/Avg</b>	<b>798628</b>	<b>733075</b>	<b>52</b>	<b>65553</b>	<b>1186</b>	<b>2875</b>	<b>1281</b>	<b>60211</b>
<b>1</b>	<b>OSMANABAD</b>	<b>4043</b>	<b>3850</b>	<b>-40</b>	<b>193</b>	<b>2</b>	<b>32</b>	<b>9</b>	<b>150</b>
<b>2</b>	<b>BEED</b>	<b>12989</b>	<b>11661</b>	<b>-22</b>	<b>1328</b>	<b>19</b>	<b>141</b>	<b>49</b>	<b>1119</b>
<b>3</b>	<b>PARBHANI</b>	<b>5298</b>	<b>5063</b>	<b>-16</b>	<b>235</b>	<b>6</b>	<b>10</b>	<b>4</b>	<b>215</b>
<b>4</b>	<b>HINGOLI</b>	<b>7914</b>	<b>7752</b>	<b>-11</b>	<b>162</b>	<b>4</b>	<b>29</b>	<b>2</b>	<b>127</b>
<b>5</b>	<b>LATUR</b>	<b>7455</b>	<b>6994</b>	<b>-8</b>	<b>461</b>	<b>5</b>	<b>19</b>	<b>0</b>	<b>437</b>
<b>6</b>	<b>JALNA</b>	<b>8800</b>	<b>8144</b>	<b>-5</b>	<b>656</b>	<b>30</b>	<b>43</b>	<b>15</b>	<b>568</b>
<b>7</b>	<b>WASHIM</b>	<b>6818</b>	<b>6130</b>	<b>-4</b>	<b>688</b>	<b>33</b>	<b>38</b>	<b>0</b>	<b>617</b>
<b>8</b>	<b>SANGLI</b>	<b>10695</b>	<b>10382</b>	<b>-1</b>	<b>313</b>	<b>14</b>	<b>8</b>	<b>2</b>	<b>289</b>
<b>9</b>	<b>KOLHAPUR</b>	<b>10438</b>	<b>10020</b>	<b>1</b>	<b>418</b>	<b>10</b>	<b>9</b>	<b>34</b>	<b>365</b>
<b>10</b>	<b>NANDED</b>	<b>27283</b>	<b>25861</b>	<b>5</b>	<b>1422</b>	<b>5</b>	<b>38</b>	<b>27</b>	<b>1352</b>
<b>11</b>	<b>RAIGAD</b>	<b>7094</b>	<b>6991</b>	<b>10</b>	<b>103</b>	<b>4</b>	<b>11</b>	<b>0</b>	<b>88</b>
<b>12</b>	<b>SATARA</b>	<b>8585</b>	<b>7976</b>	<b>11</b>	<b>609</b>	<b>9</b>	<b>28</b>	<b>38</b>	<b>534</b>
<b>13</b>	<b>JALGAON</b>	<b>40441</b>	<b>38172</b>	<b>19</b>	<b>2269</b>	<b>39</b>	<b>218</b>	<b>137</b>	<b>1875</b>
<b>14</b>	<b>SINDHUDURG</b>	<b>3318</b>	<b>3232</b>	<b>24</b>	<b>86</b>	<b>0</b>	<b>2</b>	<b>2</b>	<b>82</b>
<b>15</b>	<b>THANE</b>	<b>6259</b>	<b>6163</b>	<b>29</b>	<b>96</b>	<b>0</b>	<b>3</b>	<b>0</b>	<b>93</b>
<b>16</b>	<b>PUNE</b>	<b>11283</b>	<b>10397</b>	<b>30</b>	<b>886</b>	<b>19</b>	<b>51</b>	<b>72</b>	<b>744</b>
<b>17</b>	<b>BULDHANA</b>	<b>20011</b>	<b>17618</b>	<b>35</b>	<b>2393</b>	<b>3</b>	<b>43</b>	<b>0</b>	<b>2347</b>

# PMAY-G 3<sup>rd</sup> Instalment Released and Completion

#SNo	District_Name	3rd installmen t released	Total houses completed	Average time taken till houses completed (in days)	No of houses Pending for House completion				
					No. of houses	No. of houses with delay of 0-7 days	No. of houses with delay of 8- 15 days	No. of houses with delay of 16- 30 days	No. of houses with delay of more than 30 days
18	AURANGABAD	17130	15651	36	1479	53	98	15	1313
19	SOLAPUR	26306	24612	36	1694	20	42	187	1445
20	GONDIA	72378	67609	41	4769	49	274	30	4416
21	AHMEDNAGAR	34939	32252	42	2687	64	174	180	2269
22	NASHIK	61104	57255	50	3849	132	118	82	3517
23	RATNAGIRI	5586	5385	50	201	10	9	1	181
24	CHANDRAPUR	24424	21703	51	2721	23	72	28	2598
25	NAGPUR	24803	23018	56	1785	41	51	114	1579
26	PALGHAR	24269	23401	61	868	0	4	0	864
27	YAVATMAL	29000	25608	62	3392	41	50	4	3297
28	DHULE	39988	37866	67	2122	24	164	79	1855
29	AKOLA	31596	28435	69	3161	19	80	10	3052
30	GADCHIROLI	17643	15554	72	2089	51	54	9	1975
31	WARDHA	11628	10497	76	1131	15	1	21	1094
32	AMRAVATI	56352	51467	82	4885	46	238	49	4552
33	BHANDARA	39476	31909	84	7567	249	418	72	6828
34	NANDURBAR	83282	74447	120	8835	147	305	9	8374
	<b>Total/Avg</b>	<b>798628</b>	<b>733075</b>	<b>52</b>	<b>65553</b>	<b>1186</b>	<b>2875</b>	<b>1281</b>	<b>60211</b>

# PMAY-G Overridden Cases Status

SNo	District Name	Total Mismatched	Mismatched Verified	Remaining Mismatch
1	NANDURBAR	67266	12968	54298
2	AMRAVATI	49033	13360	35673
3	GONDIA	51756	28458	23298
4	AHMEDNAGAR	30823	8062	22761
5	JALGAON	35994	13285	22709
6	DHULE	27547	5204	22343
7	NANDED	35211	12888	22323
8	NASHIK	29850	8259	21591
9	YAVATMAL	26410	7867	18543
10	AKOLA	24290	8125	16165
11	SOLAPUR	23539	8152	15387
12	BULDHANA	18210	5562	12648
13	BHANDARA	35060	23021	12039
14	NAGPUR	16299	5613	10686
15	AURANGABAD	14715	4438	10277
16	CHANDRAPUR	17639	7432	10207
17	GADCHIROLI	13990	4116	9874

#SNo	District Name	Total Mismatched	Mismatched Verified	Remaining Mismatch
18	PALGHAR	12565	2705	9860
19	BEED	9247	2263	6984
20	JALNA	10373	3450	6923
21	SANGLI	10153	4125	6028
22	WASHIM	8182	2165	6017
23	PUNE	8243	2613	5630
24	SATARA	7011	1773	5238
25	KOLHAPUR	7221	2023	5198
26	PARBHANI	6175	1856	4319
27	LATUR	5519	1334	4185
28	HINGOLI	5572	1407	4165
29	THANE	4079	370	3709
30	OSMANABAD	3489	909	2580
31	RAIGAD	3211	821	2390
32	WARDHA	7156	4785	2371
33	RATNAGIRI	2858	914	1944
34	SINDHUDURG	1068	298	770
	<b>Total</b>	<b>629754</b>	<b>210621</b>	<b>419133</b>

# IAY Single Page entry Status

#SNo	District	New Registration	Amount Pending For New Registration	Update	Amount Pending For Existing Registration	#SNo	District	New Registration	Amount Pending For New Registration	Update	Amount Pending For Existing Registration
1	GADCHIROLI	1620	1618	3523	3480	18	SANGLI	3	3	153	148
2	AHMEDNAGAR	70	69	2338	2274	19	WARDHA	14	7	170	148
3	NASHIK	1080	1074	2176	2125	20	SOLAPUR	10	9	138	131
4	AMRAVATI	183	182	1652	1641	21	SATARA	111	78	115	110
5	NANDED	4	4	1611	1601	22	BULDHANA	0	0	162	100
6	LATUR	69	69	1283	1090	23	WASHIM	3	2	96	95
7	CHANDRAPUR	101	100	1077	1048	24	RATNAGIRI	3	3	95	91
8	AURANGABAD	945	936	1009	995	25	KOLHAPUR	11	10	83	83
9	DHULE	283	283	939	925	26	BHANDARA	51	51	75	75
10	YAVATMAL	70	70	945	895	27	HINGOLI	0	0	96	73
11	NANDURBAR	179	88	884	829	28	PUNE	0	0	80	70
12	GONDIA	95	95	677	674	29	BEED	1	1	69	67
13	OSMANABAD	83	83	606	595	30	PALGHAR	0	0	38	38
14	JALNA	1	1	521	518	31	RAIGAD	0	0	81	27
15	AKOLA	71	71	519	511	32	NAGPUR	24	24	13	11
16	PARBHANI	11	11	319	305	33	SINDHUDURG	0	0	7	6
17	JALGAON	30	28	270	260	34	THANE	0	0	0	0
							<b>Total</b>	<b>5126</b>	<b>4970</b>	<b>21820</b>	<b>21039</b>



## ग्राम विकास विभाग

स्वातंत्र्याचा अमृत महोत्सव अंतर्गत

# महा आवास अभियान २.० (२०२१-२२)

महाराष्ट्र शासनाचा एकच ध्यास...२०२२ पर्यंत सर्वांसाठी आवास!!



राज्य व्यवस्थापन कक्ष-ग्रामीण गृहनिर्माण  
महाराष्ट्र राज्य
