



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०६.०४.२०२३

प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४११८९५	३०	१०२३३८१	६०५	०	०	०
राज्य योजना	५४८१४९	२८३	३९८८२०	२२७	०	०	०
एकूण	१९६००४४	३१३	१४२२२०१	८३२	०	०	०


PMAY-G Completion Progress Bar

72.5%



State Schemes Progress Bar

72.8%


PMAY-G: Incomplete Houses bifurcation




State Schemes: Incomplete Houses bifurcation

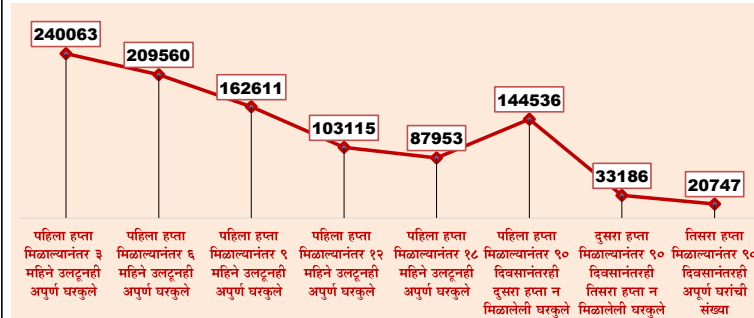


Abhiyan Achievement Day 137

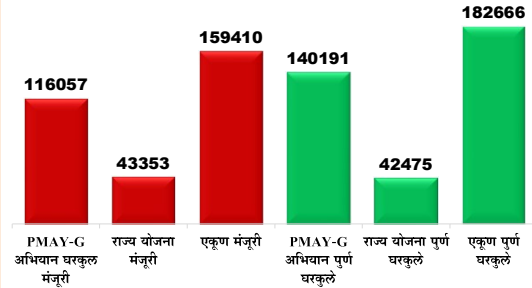

PMAY-G : House completion (Abhiyan Achievement)

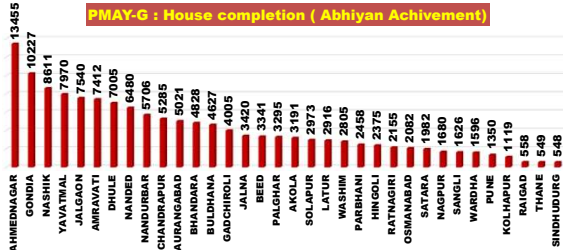

State Schemes : House completion (Abhiyan Achievement)

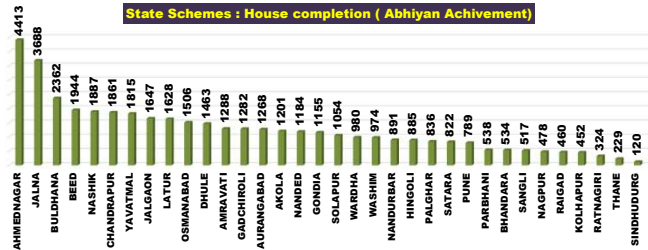


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण

४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.



State Schemes Remaining 1st Installments Bottom 10 Dist




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	05.04.2023	06.04.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	238112	237476	237493	17	619
2	NASHIK DIV.	414649	413722	413720	12	929
3	NAGPUR DIV.	292238	291654	291648	1	590
4	AMRAVATI DIV.	274992	274538	274537	0	455
5	KONKAN DIV.	69718	69656	69647	0	71
6	PUNE DIV.	125258	124948	124850	0	408
Total		1414967	1411994	1411895	30	3072

Sr. No.	District	Target (PWL+Awaas Plus)	05.04.2023	06.04.2023	Daily Achievement	Remaining
1	NANDURBAR	119440	118923	118935	12	505
2	NANDED	69546	69460	69471	11	75
3	JALNA	24039	24031	24033	2	6
4	LATUR	20708	20562	20564	2	144
5	OSMANABAD	14509	14366	14368	2	141
6	NAGPUR	37144	37132	37133	1	11
7	AKOLA	48797	48778	48778	0	19
8	AURANGABAD	36795	36661	36661	0	134
9	BEED	35310	35256	35256	0	54
10	BULDHANA	44765	44724	44724	0	41
11	DHULE	64954	64903	64903	0	51
12	GADCHIROLI	31681	31603	31603	0	78
13	GONDIA	96489	96141	96141	0	348
14	HINGOLI	18108	18083	18083	0	25
15	KOLHAPUR	17685	17685	17685	0	0
16	NASHIK	89710	89695	89695	0	15
17	PALGHAR	35233	35183	35183	0	50
18	PARBHANI	19097	19057	19057	0	40
19	PUNE	20544	20531	20531	0	13
20	SINDHUDURG	5142	5142	5142	0	0
21	THANE	9606	9599	9599	0	7
22	WARDHA	18645	18621	18621	0	24
23	WASHIM	20409	20389	20389	0	20
24	YAVATMAL	65362	65196	65196	0	166
25	AMRAVATI	95659	95451	95450	-1	209
26	SATARA	15378	15374	15373	-1	5
27	BHANDARA	65120	65101	65099	-2	21
28	RATNAGIRI	9904	9901	9899	-2	5
29	CHANDRAPUR	43159	43056	43051	-5	108
30	SOLAPUR	49629	49417	49412	-5	217
31	JALGAON	79751	79432	79426	-6	325
32	RAIGAD	9833	9831	9824	-7	9
33	AHMEDNAGAR	60794	60769	60761	-8	33
34	SANGLI	22022	21941	21849	-92	173
Total		1414967	1411994	1411895	30	3072

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
RATNAGIRI	5
SATARA	5
JALNA	6
THANE	7
RAIGAD	9
NAGPUR	11
PUNE	13
NASHIK	15
AKOLA	19
WASHIM	20
BHANDARA	21
WARDHA	24
HINGOLI	25
AHMEDNAGAR	33
PARBHANI	40
BULDHANA	41
PALGHAR	50
DHULE	51
BEED	54
NANDED	75
GADCHIROLI	78
CHANDRAPUR	108
AURANGABAD	134
OSMANABAD	141
LATUR	144
YAVATMAL	166
SANGLI	173
AMRAVATI	209
SOLAPUR	217
JALGAON	325
GONDIA	348
NANDURBAR	505

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	224	33	0
9	THANE	127	74	53	127	43	84	0
10	NANDED	362	277	85	362	242	120	0
11	BEED	212	101	111	212	71	141	0
12	SANGLI	454	143	311	437	141	296	17
13	PARBHANI	332	15	317	332	13	319	0
14	SATARA	1311	582	729	1311	631	680	0
15	NASHIK	1804	1454	350	1617	715	902	187
16	HINGOLI	1713	787	926	1713	466	1247	0
17	JALNA	1413	165	1248	1413	85	1328	0
18	WARDHA	2819	1284	1535	2819	1216	1603	0
19	GONDIA	2450	2450	0	2450	765	1685	0
20	NAGPUR	5134	3397	1737	5122	3398	1724	12
21	CHANDRAPUR	2791	1463	1328	2791	919	1872	0
22	PUNE	2925	992	1933	2925	885	2040	0
23	LATUR	2341	13	2328	2341	5	2336	0
24	OSMANABAD	2470	104	2366	2470	56	2414	0
25	YAVATMAL	3589	1144	2445	3582	1094	2488	7
26	BHANDARA	5823	3230	2593	5823	3213	2610	0
27	WASHIM	3477	865	2612	3477	850	2627	0
28	AURANGABAD	3328	1779	1549	3328	288	3040	0
29	AKOLA	7074	3842	3232	7074	3844	3230	0
30	AHMEDNAGAR	7762	4828	2934	7759	3030	4729	3
31	JALGAON	22889	20580	2309	21515	16308	5207	1374
32	SOLAPUR	7960	2595	5365	7851	793	7058	109
33	BULDHANA	15139	8455	6684	14894	6912	7982	245
34	AMRAVATI	23044	13116	9928	20784	339	20445	2260
Total		129486	74478	55008	125272	47032	78240	4214

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.04.2023	06.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AMRAVATI DIV.	274537	183008	183162	154	91375	190	698
2	NASHIK DIV.	413720	325681	325831	150	87889	309	671
3	NAGPUR DIV.	291648	235631	235749	118	55899	202	427
4	KONKAN DIV.	69647	56433	56513	80	13134	52	100
5	AURANGABAD DIV.	237493	135577	135654	77	101839	205	777
6	PUNE DIV.	124850	86446	86472	26	38378	66	293
Total		1411895	1022776	1023381	605	388514	1023	2966

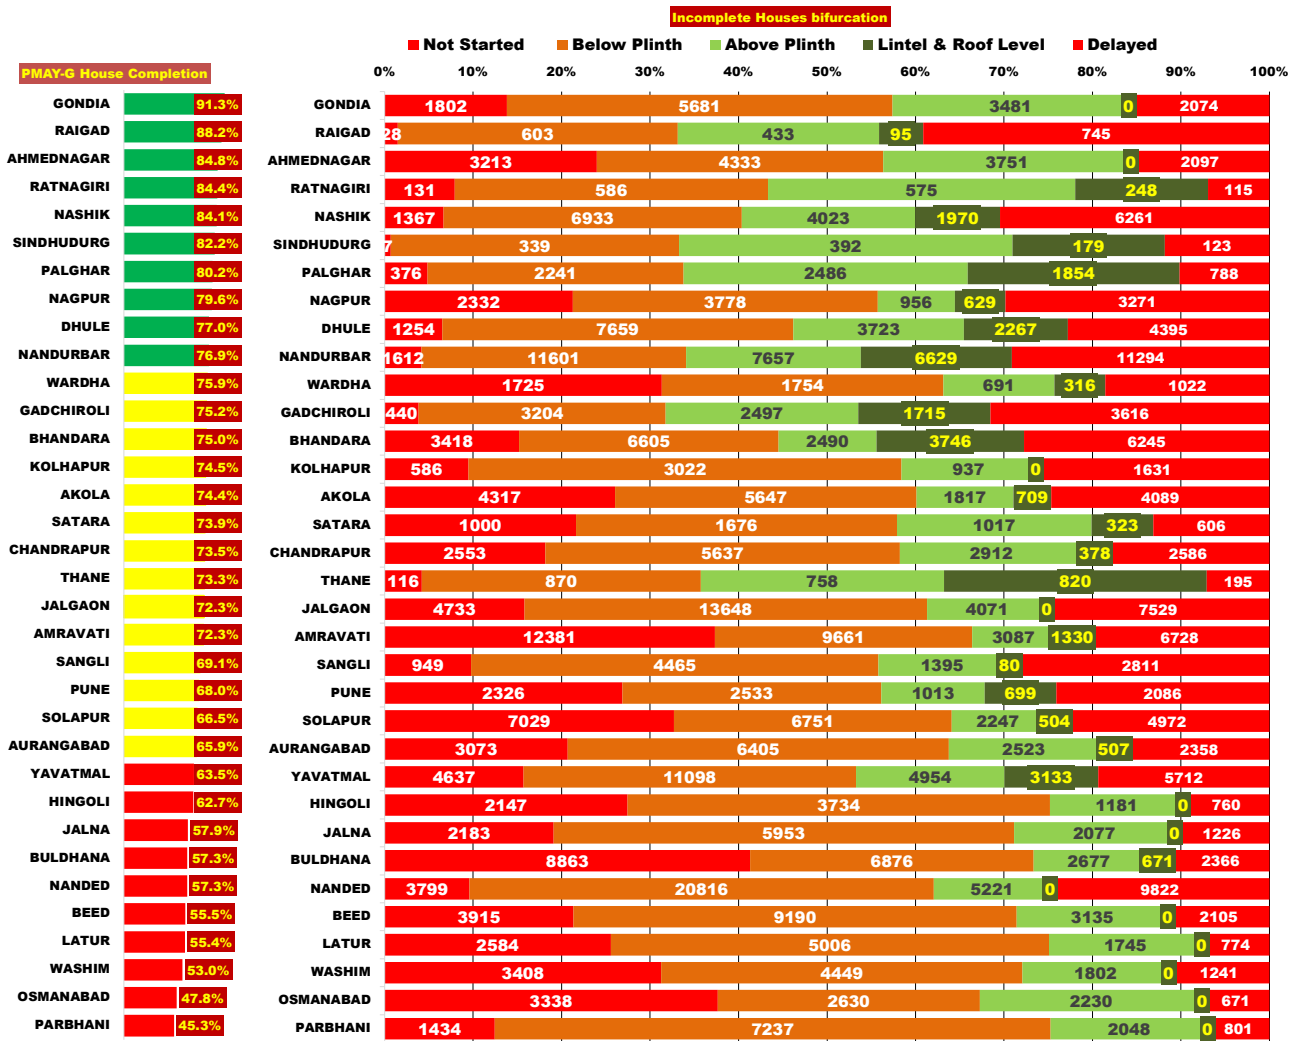

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.04.2023	06.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.06.23
1	YAVATMAL	65196	41316	41378	62	23818	58	182
2	NANDURBAR	118935	91381	91436	55	27499	42	210
3	BHANDARA	65099	48791	48840	49	16259	35	124
4	NASHIK	89695	75364	75402	38	14293	63	109
5	AHMEDNAGAR	60761	51506	51535	29	9226	98	70
6	BULDHANA	44724	25619	25648	29	19076	34	146
7	GADCHIROLI	31603	23743	23772	29	7831	29	60
8	WASHIM	20389	10782	10811	29	9578	20	73
9	RATNAGIRI	9899	8331	8359	28	1540	16	12
10	AMRAVATI	95450	69013	69037	24	26413	54	202
11	LATUR	20564	11368	11390	22	9174	21	70
12	JALGAON	79426	57437	57458	21	21968	55	168
13	PALGHAR	35183	28207	28226	19	6957	24	53
14	NANDED	69471	39774	39790	16	29681	47	227
15	RAIGAD	9824	8652	8668	16	1156	4	9
16	NAGPUR	37133	29559	29573	14	7560	12	58
17	SOLAPUR	49412	32867	32881	14	16531	22	126
18	CHANDRAPUR	43051	31611	31624	13	11427	39	87
19	BEED	35256	19558	19569	11	15687	24	120
20	AKOLA	48778	36278	36288	10	12490	23	95
21	OSMANABAD	14368	6852	6862	10	7506	15	57
22	PARBHANI	19057	8621	8631	10	10426	18	80
23	THANE	9599	7025	7035	10	2564	4	20
24	GONDIA	96141	87797	87805	8	8336	75	64
25	DHULE	64903	49993	50000	7	14903	51	114
26	SANGLI	21849	15086	15093	7	6756	12	52
27	SINDHUDURG	5142	4218	4225	7	917	4	7
28	WARDHA	18621	14130	14135	5	4486	12	34
29	KOLHAPUR	17685	13177	13181	4	4504	8	34
30	HINGOLI	18083	11330	11333	3	6750	17	52
31	JALNA	24033	13923	13926	3	10107	25	77
32	AURANGABAD	36661	24151	24153	2	12508	37	95
33	PUNE	20531	13959	13960	1	6571	10	50
34	SATARA	15373	11357	11357	0	4016	14	31
Total		1411895	1022776	1023381	605	388514	1023	2966

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	05.04.2023	06.04.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	141360	109340	109547	207	31813
2	AURANGABAD DIV.	199331	163407	163450	43	35881
3	AMRAVATI DIV.	109702	93324	93340	16	16362
4	NAGPUR DIV.	118393	88482	88498	16	29895
5	KONKAN DIV.	34729	30337	30338	1	4391
6	PUNE DIV.	65334	62976	62976	0	2358
Total		668849	547866	548149	283	120700


Sr. No.	District	Target	05.04.2023	06.04.2023	Daily_Achievement	Remaining
1	DHULE	21790	17425	17547	122	4243
2	NASHIK	32035	22281	22366	85	9669
3	NANDED	26760	20078	20102	24	6658
4	CHANDRAPUR	40285	23394	23410	16	16875
5	AMRAVATI	23224	19607	19621	14	3603
6	JALNA	20446	19142	19155	13	1291
7	PARBHANI	19784	17474	17479	5	2305
8	BULDHANA	21616	19964	19966	2	1650
9	BEED	26878	24782	24783	1	2095
10	PALGHAR	11792	10584	10585	1	1207
11	AHMEDNAGAR	35298	32971	32971	0	2327
12	AKOLA	23681	17687	17687	0	5994
13	AURANGABAD	26141	23795	23795	0	2346
14	BHANDARA	17590	15181	15181	0	2409
15	GADCHIROLI	16834	15168	15168	0	1666
16	GONDIA	14246	12687	12687	0	1559
17	HINGOLI	27298	15130	15130	0	12168
18	JALGAON	25659	22528	22528	0	3131
19	KOLHAPUR	12565	12528	12528	0	37
20	LATUR	27171	26027	26027	0	1144
21	NAGPUR	16291	10882	10882	0	5409
22	NANDURBAR	26578	14135	14135	0	12443
23	OSMANABAD	24853	16979	16979	0	7874
24	PUNE	14672	12770	12770	0	1902
25	RAIGAD	7406	6220	6220	0	1186
26	RATNAGIRI	7126	6677	6677	0	449
27	SANGLI	8732	8600	8600	0	132
28	SATARA	10647	10633	10633	0	14
29	SINDHUDURG	2141	2107	2107	0	34
30	SOLAPUR	18718	18445	18445	0	273
31	THANE	6264	4749	4749	0	1515
32	WARDHA	13147	11170	11170	0	1977
33	WASHIM	11500	10050	10050	0	1450
34	YAVATMAL	29681	26016	26016	0	3665
Total		668849	547866	548149	283	120700

Remaining Sanction RANK

SATARA	14
SINDHUDURG	34
KOLHAPUR	37
SANGLI	132
SOLAPUR	273
RATNAGIRI	449
LATUR	1144
RAIGAD	1186
PALGHAR	1207
JALNA	1291
WASHIM	1450
THANE	1515
GONDIA	1559
BULDHANA	1650
GADCHIROLI	1666
PUNE	1902
WARDHA	1977
BEED	2095
PARBHANI	2305
AHMEDNAGAR	2327
AURANGABAD	2346
BHANDARA	2409
JALGAON	3131
AMRAVATI	3603
YAVATMAL	3665
DHULE	4243
NAGPUR	5409
AKOLA	5994
NANDED	6658
OSMANABAD	7874
NASHIK	9669
HINGOLI	12168
NANDURBAR	12443
CHANDRAPUR	16875

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.04.2023	06.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AURANGABAD DIV.	163450	102684	102747	63	60703	92	463
2	AMRAVATI DIV.	93340	63780	63838	58	29502	56	225
3	NAGPUR DIV.	88498	68797	68835	38	19663	46	150
4	NASHIK DIV.	109547	88324	88358	34	21189	75	162
5	KONKAN DIV.	30338	23325	23343	18	6995	14	53
6	PUNE DIV.	62976	51683	51699	16	11277	27	86
Total		548149	398593	398820	227	149329	310	1140

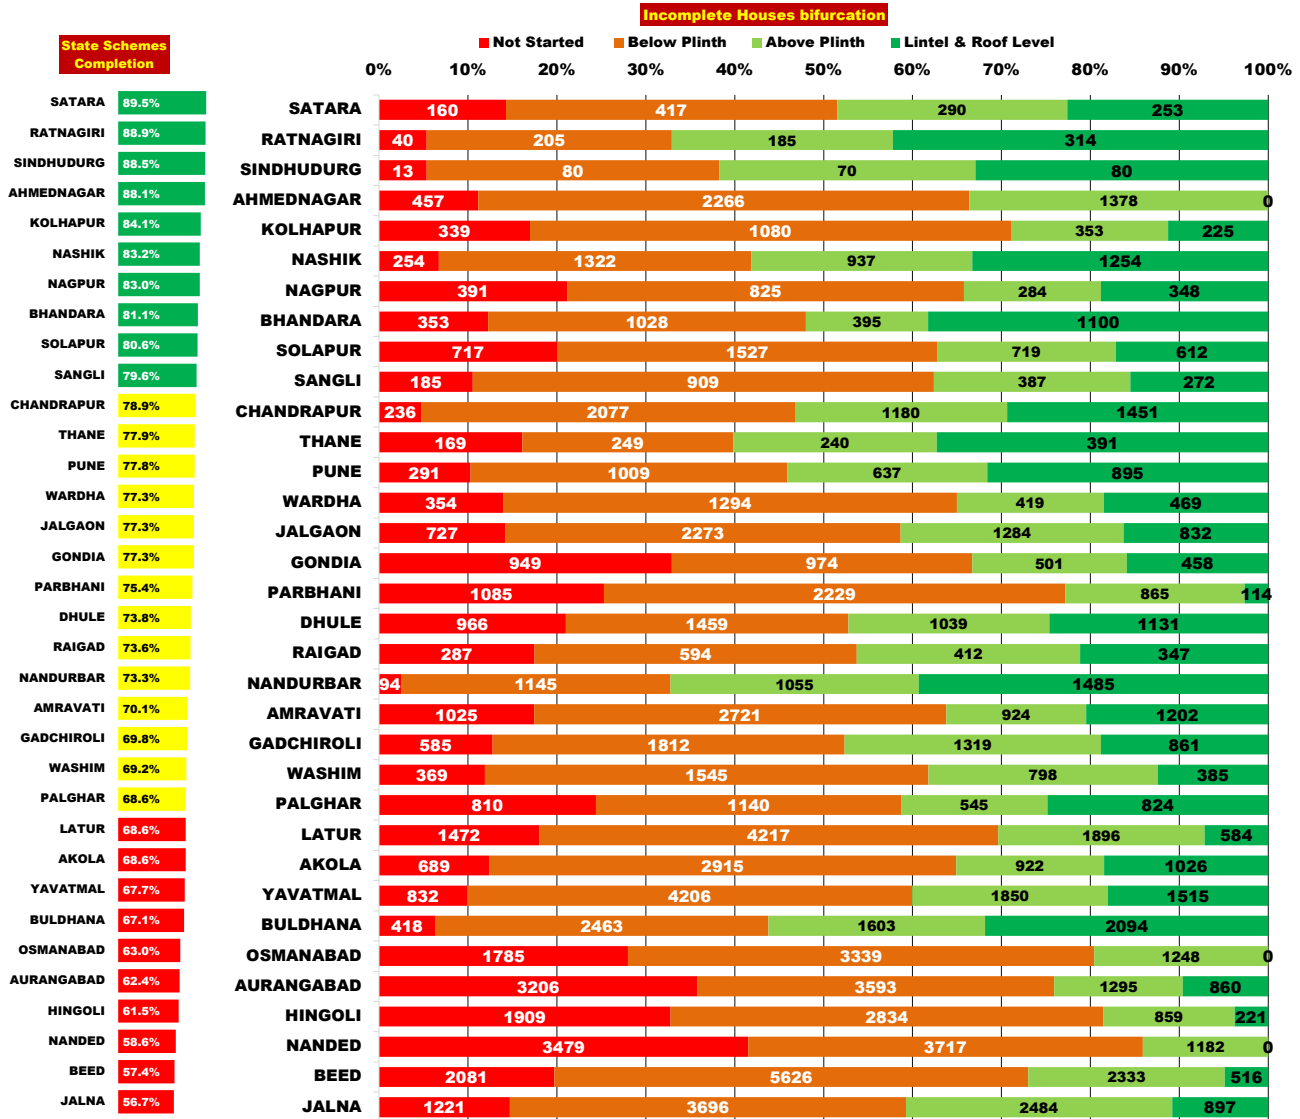

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.04.2023	06.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	BEED	24783	14200	14227	27	10556	14	81
2	BULDHANA	19966	13367	13388	21	6578	17	50
3	AMRAVATI	19621	13733	13749	16	5872	9	45
4	AHMEDNAGAR	32971	29026	29039	13	3932	32	30
5	WASHIM	10050	6941	6953	12	3097	7	24
6	WARDHA	11170	8623	8634	11	2536	7	19
7	NANDED	20102	11764	11773	9	8329	9	64
8	BHANDARA	15181	12297	12305	8	2876	4	22
9	CHANDRAPUR	23410	18458	18466	8	4944	14	38
10	LATUR	26027	17850	17858	8	8169	12	62
11	SANGLI	8600	6839	6847	8	1753	4	13
12	YAVATMAL	26016	17605	17613	8	8403	13	64
13	NASHIK	22366	18592	18599	7	3767	14	29
14	AURANGABAD	23795	14835	14841	6	8954	9	68
15	DHULE	17547	12946	12952	6	4595	11	35
16	GADCHIROLI	15168	10585	10591	6	4577	9	35
17	HINGOLI	15130	9301	9307	6	5823	6	44
18	OSMANABAD	16979	10692	10698	6	6281	11	48
19	PALGHAR	10585	7260	7266	6	3319	6	25
20	RATNAGIRI	6677	5927	5933	6	744	2	6
21	NANDURBAR	14135	10351	10356	5	3779	7	29
22	GONDIA	12687	9802	9805	3	2882	8	22
23	JALGAON	22528	17409	17412	3	5116	12	39
24	KOLHAPUR	12528	10528	10531	3	1997	3	15
25	RAIGAD	6220	4577	4580	3	1640	3	13
26	SOLAPUR	18445	14867	14870	3	3575	8	27
27	NAGPUR	10882	9032	9034	2	1848	3	14
28	PUNE	12770	9936	9938	2	2832	6	22
29	THANE	4749	3698	3700	2	1049	2	8
30	AKOLA	17687	12134	12135	1	5552	9	42
31	JALNA	19155	10856	10857	1	8298	27	63
32	SINDHUDURG	2107	1863	1864	1	243	1	2
33	PARBHANI	17479	13186	13186	0	4293	4	33
34	SATARA	10633	9513	9513	0	1120	6	9
	Total	548149	398593	398820	227	149329	310	1140

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	12179	0	44174	0	23225
2	AMRAVATI DIV.	0	33542	0	37731	0	14337
3	AURANGABAD DIV.	0	22443	0	60971	0	20160
4	NAGPUR DIV.	0	12057	0	26659	0	13027
5	KONKAN DIV.	0	655	0	4639	0	4644
6	PUNE DIV.	0	11757	0	18447	0	6609
Total		0	92633	0	192621	0	82002

PMAY-G 1st Ins Pending

SINDHUDURG	7
RAIGAD	25
THANE	116
RATNAGIRI	131
PALGHAR	376
GADCHIROLI	415
KOLHAPUR	586
SANGLI	816
SATARA	1000
DHULE	1254
NASHIK	1367
PARBHANI	1434
NANDURBAR	1612
WARDHA	1725
GONDIA	1802
HINGOLI	2147
JALNA	2153
NAGPUR	2197
PUNE	2326
CHANDRAPUR	2500
LATUR	2584
AURANGABAD	3073
AHMEDNAGAR	3213
OSMANABAD	3338
WASHIM	3405
BHANDARA	3418
NANDED	3799
BEED	3915
AKOLA	4317
YAVATMAL	4633
JALGAON	4733
SOLAPUR	7029
BULDHANA	8852
AMRAVATI	12335

PMAY-G 2nd Ins Pending

SINDHUDURG	339
RATNAGIRI	586
RAIGAD	603
THANE	870
SATARA	1676
WARDHA	1754
PALGHAR	2241
PUNE	2533
OSMANABAD	2630
KOLHAPUR	3022
GADCHIROLI	3204
HINGOLI	3734
NAGPUR	3778
AHMEDNAGAR	4333
WASHIM	4449
SANGLI	4465
LATUR	5006
CHANDRAPUR	5637
AKOLA	5647
GONDIA	5681
JALNA	5953
AURANGABAD	6405
BHANDARA	6605
SOLAPUR	6751
BULDHANA	6876
NASHIK	6933
PARBHANI	7237
DHULE	7659
BEED	9190
AMRAVATI	9661
YAVATMAL	11098
NANDURBAR	11601
JALGAON	13648
NANDED	20816

PMAY-G 3rd Ins Pending

SINDHUDURG	392
RAIGAD	433
RATNAGIRI	575
WARDHA	691
THANE	758
KOLHAPUR	937
NAGPUR	956
PUNE	1013
SATARA	1017
HINGOLI	1181
SANGLI	1395
LATUR	1745
WASHIM	1802
AKOLA	1817
PARBHANI	2048
JALNA	2077
OSMANABAD	2230
SOLAPUR	2247
PALGHAR	2486
BHANDARA	2490
GADCHIROLI	2497
AURANGABAD	2523
BULDHANA	2677
CHANDRAPUR	2912
AMRAVATI	3087
BEED	3135
GONDIA	3481
DHULE	3723
AHMEDNAGAR	3751
NASHIK	4023
JALGAON	4071
YAVATMAL	4954
NANDED	5221
NANDURBAR	7657

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3213	0	4333	0	3751
2	AKOLA	0	4317	0	5647	0	1817
3	AMRAVATI	0	12335	0	9661	0	3087
4	AURANGABAD	0	3073	0	6405	0	2523
5	BEED	0	3915	0	9190	0	3135
6	BHANDARA	0	3418	0	6605	0	2490
7	BULDHANA	0	8852	0	6876	0	2677
8	CHANDRAPUR	0	2500	0	5637	0	2912
9	DHULE	0	1254	0	7659	0	3723
10	GADCHIROLI	0	415	0	3204	0	2497
11	GONDIA	0	1802	0	5681	0	3481
12	HINGOLI	0	2147	0	3734	0	1181
13	JALGAON	0	4733	0	13648	0	4071
14	JALNA	0	2153	0	5953	0	2077
15	KOLHAPUR	0	586	0	3022	0	937
16	LATUR	0	2584	0	5006	0	1745
17	NAGPUR	0	2197	0	3778	0	956
18	NANDED	0	3799	0	20816	0	5221
19	NANDURBAR	0	1612	0	11601	0	7657
20	NASHIK	0	1367	0	6933	0	4023
21	OSMANABAD	0	3338	0	2630	0	2230
22	PALGHAR	0	376	0	2241	0	2486
23	PARBHANI	0	1434	0	7237	0	2048
24	PUNE	0	2326	0	2533	0	1013
25	SANGLI	0	816	0	4465	0	1395
26	SINDHUDURG	0	7	0	339	0	392
27	SOLAPUR	0	7029	0	6751	0	2247
28	THANE	0	116	0	870	0	758
29	WARDHA	0	1725	0	1754	0	691
30	WASHIM	0	3405	0	4449	0	1802
31	YAVATMAL	0	4633	0	11098	0	4954
32	RAIGAD	-2	25	0	603	0	433
33	RATNAGIRI	-5	131	0	586	0	575
34	SATARA	-14	1000	0	1676	0	1017
	Total	0	92633	0	192621	0	82002

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2498	0	8465	0	5693
2	AMRAVATI DIV.	0	3333	0	13850	0	6097
3	AURANGABAD DIV.	0	16238	0	29251	0	12162
4	NAGPUR DIV.	0	2868	0	8010	0	4098
5	KONKAN DIV.	0	1319	0	2268	0	1452
6	PUNE DIV.	0	1692	0	4942	0	2386
Total		0	27948	0	66786	0	31888

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	40
NANDURBAR	94
SATARA	160
THANE	169
SANGLI	185
CHANDRAPUR	236
NASHIK	254
RAIGAD	287
PUNE	291
KOLHAPUR	339
BHANDARA	353
WARDHA	354
WASHIM	369
NAGPUR	391
BULDHANA	418
AHMEDNAGAR	457
GADCHIROLI	585
AKOLA	689
SOLAPUR	717
JALGAON	727
PALGHAR	810
YAVATMAL	832
GONDIA	949
DHULE	966
AMRAVATI	1025
PARBHANI	1085
JALNA	1221
LATUR	1472
OSMANABAD	1785
HINGOLI	1909
BEED	2081
AURANGABAD	3206
NANDED	3479

State Schemes 2nd Ins Pending

SINDHUDURG	80
RATNAGIRI	205
THANE	249
SATARA	417
RAIGAD	594
NAGPUR	825
SANGLI	909
GONDIA	974
PUNE	1009
BHANDARA	1028
KOLHAPUR	1080
PALGHAR	1140
NANDURBAR	1145
WARDHA	1294
NASHIK	1322
DHULE	1459
SOLAPUR	1527
WASHIM	1545
GADCHIROLI	1812
CHANDRAPUR	2077
PARBHANI	2229
AHMEDNAGAR	2266
JALGAON	2273
BULDHANA	2463
AMRAVATI	2721
HINGOLI	2834
AKOLA	2915
OSMANABAD	3339
AURANGABAD	3593
JALNA	3696
NANDED	3717
YAVATMAL	4206
LATUR	4217
BEED	5626

State Schemes 3rd Ins Pending

SINDHUDURG	70
RATNAGIRI	185
THANE	240
NAGPUR	284
SATARA	290
KOLHAPUR	353
SANGLI	387
BHANDARA	395
RAIGAD	412
WARDHA	419
GONDIA	501
PALGHAR	545
PUNE	637
SOLAPUR	719
WASHIM	798
HINGOLI	859
PARBHANI	865
AKOLA	922
AMRAVATI	924
NASHIK	937
DHULE	1039
NANDURBAR	1055
CHANDRAPUR	1180
NANDED	1182
OSMANABAD	1248
JALGAON	1284
AURANGABAD	1295
GADCHIROLI	1319
AHMEDNAGAR	1378
BULDHANA	1603
YAVATMAL	1850
LATUR	1896
BEED	2333
JALNA	2484

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	457	0	2266	0	1378
2	AKOLA	0	689	0	2915	0	922
3	AMRAVATI	0	1025	0	2721	0	924
4	AURANGABAD	0	3206	0	3593	0	1295
5	BEED	0	2081	0	5626	0	2333
6	BHANDARA	0	353	0	1028	0	395
7	BULDHANA	0	418	0	2463	0	1603
8	CHANDRAPUR	0	236	0	2077	0	1180
9	DHULE	0	966	0	1459	0	1039
10	GADCHIROLI	0	585	0	1812	0	1319
11	GONDIA	0	949	0	974	0	501
12	HINGOLI	0	1909	0	2834	0	859
13	JALGAON	0	727	0	2273	0	1284
14	JALNA	0	1221	0	3696	0	2484
15	KOLHAPUR	0	339	0	1080	0	353
16	LATUR	0	1472	0	4217	0	1896
17	NAGPUR	0	391	0	825	0	284
18	NANDED	0	3479	0	3717	0	1182
19	NANDURBAR	0	94	0	1145	0	1055
20	NASHIK	0	254	0	1322	0	937
21	OSMANABAD	0	1785	0	3339	0	1248
22	PALGHAR	0	810	0	1140	0	545
23	PARBHANI	0	1085	0	2229	0	865
24	PUNE	0	291	0	1009	0	637
25	SANGLI	0	185	0	909	0	387
26	SINDHUDURG	0	13	0	80	0	70
27	SOLAPUR	0	717	0	1527	0	719
28	THANE	0	169	0	249	0	240
29	WARDHA	0	354	0	1294	0	419
30	WASHIM	0	369	0	1545	0	798
31	YAVATMAL	0	832	0	4206	0	1850
32	RAIGAD	-1	287	0	594	0	412
33	SATARA	-1	160	0	417	0	290
34	RATNAGIRI	-5	40	0	205	0	185
	Total	0	27948	0	66786	0	31888

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

