



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १०.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४११७५५	१८	१०२४५४४	२१४	०	०	०
राज्य योजना	५४९११७	०	३९९१२८	०	०	०	०
एकूण	१९६०८७२	१८	१४२३६७२	२१४	०	०	०

PMAY-G Completion Progress Bar

72.6%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.7%


State Schemes: Incomplete Houses bifurcation

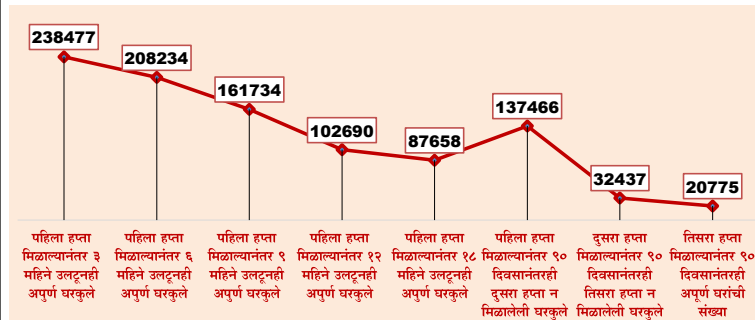


Abhiyan Achievement Day 141

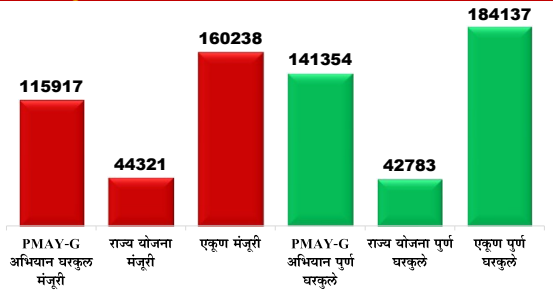

PMAY-G : House completion (Abhiyan Achievement)

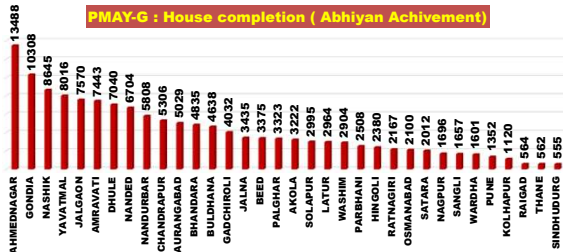

State Schemes : House completion (Abhiyan Achievement)

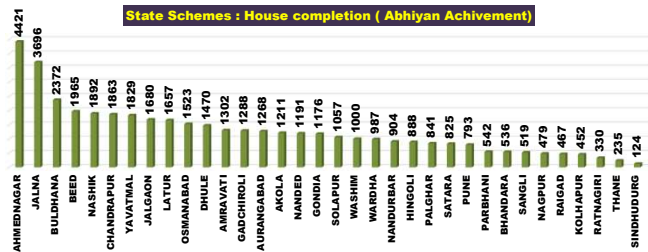


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.



State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	09.04.2023	10.04.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	238112	237493	237509	16	603
2	NASHIK DIV.	414649	413720	413721	1	928
3	AMRAVATI DIV.	274992	274544	274545	1	447
4	NAGPUR DIV.	292198	291604	291604	0	594
5	KONKAN DIV.	69716	69646	69646	0	70
6	PUNE DIV.	125231	124730	124730	0	501
Total		1414898	1411737	1411755	18	3143

Sr. No.	District	Target (PWL+Awaas Plus)	09.04.2023	10.04.2023	Daily Achievement	Remaining
1	OSMANABAD	14509	14369	14382	13	127
2	NANDED	69546	69471	69474	3	72
3	JALGAON	79751	79425	79426	1	325
4	WASHIM	20409	20393	20394	1	15
5	AHMEDNAGAR	60794	60762	60762	0	32
6	AKOLA	48797	48778	48778	0	19
7	AMRAVATI	95659	95453	95453	0	206
8	AURANGABAD	36795	36661	36661	0	134
9	BEED	35310	35254	35254	0	56
10	BHANDARA	65120	65100	65100	0	20
11	BULDHANA	44765	44724	44724	0	41
12	CHANDRAPUR	43125	43012	43012	0	113
13	DHULE	64954	64903	64903	0	51
14	GADCHIROLI	31681	31603	31603	0	78
15	GONDIA	96489	96141	96141	0	348
16	HINGOLI	18108	18083	18083	0	25
17	JALNA	24039	24033	24033	0	6
18	KOLHAPUR	17685	17685	17685	0	0
19	LATUR	20708	20564	20564	0	144
20	NAGPUR	37138	37127	37127	0	11
21	NANDURBAR	119440	118935	118935	0	505
22	NASHIK	89710	89695	89695	0	15
23	PALGHAR	35233	35183	35183	0	50
24	PARBHANI	19097	19058	19058	0	39
25	PUNE	20544	20531	20531	0	13
26	RAIGAD	9831	9822	9822	0	9
27	RATNAGIRI	9904	9900	9900	0	4
28	SANGLI	22022	21849	21849	0	173
29	SATARA	15378	15373	15373	0	5
30	SINDHUDURG	5142	5142	5142	0	0
31	SOLAPUR	49602	49292	49292	0	310
32	THANE	9606	9599	9599	0	7
33	WARDHA	18645	18621	18621	0	24
34	YAVATMAL	65362	65196	65196	0	166
Total		1414898	1411737	1411755	18	3143

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
RATNAGIRI	4
SATARA	5
JALNA	6
THANE	7
RAIGAD	9
NAGPUR	11
PUNE	13
NASHIK	15
WASHIM	15
AKOLA	19
BHANDARA	20
WARDHA	24
HINGOLI	25
AHMEDNAGAR	32
PARBHANI	39
BULDHANA	41
PALGHAR	50
DHULE	51
BEED	56
NANDED	72
GADCHIROLI	78
CHANDRAPUR	113
OSMANABAD	127
AURANGABAD	134
LATUR	144
YAVATMAL	166
SANGLI	173
AMRAVATI	206
SOLAPUR	310
JALGAON	325
GONDIA	348
NANDURBAR	505

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	224	33	0
9	THANE	127	74	53	127	43	84	0
10	NANDED	362	277	85	362	242	120	0
11	BEED	212	101	111	212	72	140	0
12	SANGLI	437	143	294	437	141	296	0
13	PARBHANI	332	15	317	332	13	319	0
14	SATARA	1311	582	729	1311	631	680	0
15	NASHIK	1642	1454	188	1617	715	902	25
16	HINGOLI	1713	787	926	1713	466	1247	0
17	JALNA	1413	165	1248	1413	85	1328	0
18	WARDHA	2819	1284	1535	2819	1216	1603	0
19	GONDIA	2450	2450	0	2450	765	1685	0
20	NAGPUR	5134	3397	1737	5117	3400	1717	17
21	CHANDRAPUR	2791	1463	1328	2743	918	1825	48
22	PUNE	2925	992	1933	2925	885	2040	0
23	LATUR	2341	13	2328	2341	5	2336	0
24	OSMANABAD	2470	104	2366	2470	56	2414	0
25	YAVATMAL	3589	1144	2445	3582	1094	2488	7
26	BHANDARA	5825	3230	2595	5825	3213	2612	0
27	WASHIM	3477	865	2612	3477	850	2627	0
28	AURANGABAD	3328	1779	1549	3328	288	3040	0
29	AKOLA	7074	3842	3232	7074	3844	3230	0
30	AHMEDNAGAR	7762	4828	2934	7759	3158	4601	3
31	JALGAON	22889	20580	2309	21977	16486	5491	912
32	SOLAPUR	7960	2595	5365	7847	793	7054	113
33	BULDHANA	15256	8455	6801	15256	6912	8344	0
34	AMRAVATI	21560	11238	10322	21560	339	21221	0
Total		127942	72600	55342	126817	47340	79477	1125

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	09.04.2023	10.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AURANGABAD DIV.	237509	135935	136056	121	101453	202	799
2	NASHIK DIV.	413721	326014	326065	51	87656	302	690
3	AMRAVATI DIV.	274545	183353	183380	27	91165	186	718
4	PUNE DIV.	124730	86546	86558	12	38172	65	301
5	NAGPUR DIV.	291604	235903	235906	3	55698	197	439
6	KONKAN DIV.	69646	56579	56579	0	13067	51	103
Total		1411755	1024330	1024544	214	387211	1003	3049

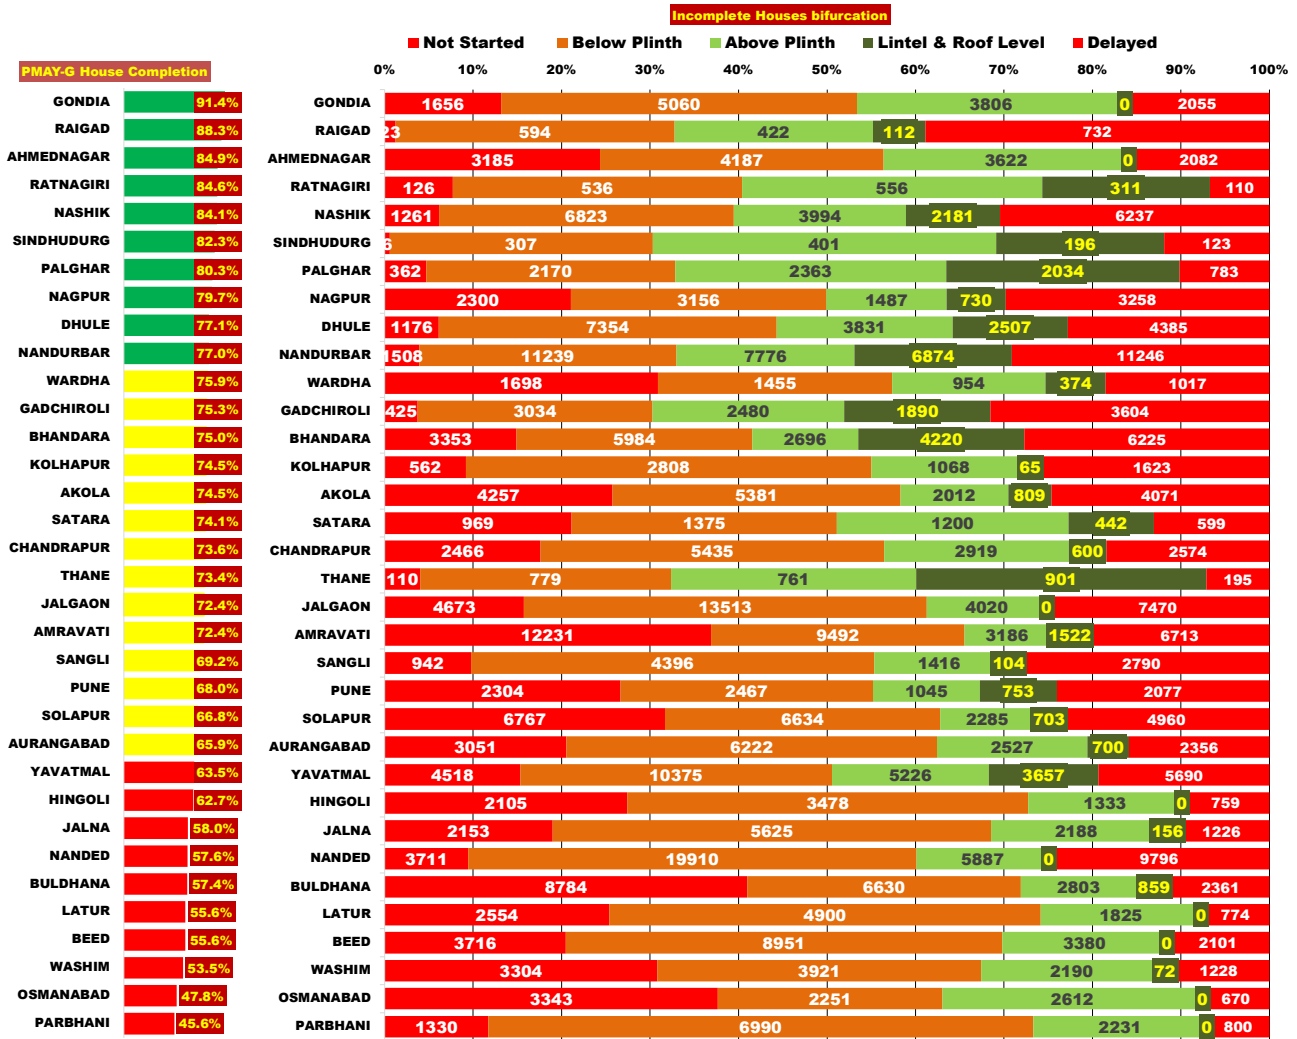

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	09.04.2023	10.04.2023	Daily_Achievement	Remaining	Avg. Completed From 20.11.22 to Today	Per Day	To be Completed in Per Day till 15.08.23
1	NANDED	69474	39908	40014	106	29460	48		232
2	NANDURBAR	118935	91508	91538	30	27397	41		216
3	JALGAON	79426	57471	57488	17	21938	54		173
4	WASHIM	20394	10893	10910	17	9484	21		75
5	SANGLI	21849	15112	15124	12	6725	12		53
6	AKOLA	48778	36311	36319	8	12459	23		98
7	BEED	35254	19597	19603	6	15651	24		123
8	HINGOLI	18083	11334	11338	4	6745	17		53
9	NASHIK	89695	75432	75436	4	14259	61		112
10	PARBHANI	19058	8678	8681	3	10377	18		82
11	NAGPUR	37127	29587	29589	2	7538	12		59
12	AMRAVATI	95453	69067	69068	1	26385	53		208
13	GONDIA	96141	87885	87886	1	8255	73		65
14	JALNA	24033	13940	13941	1	10092	24		79
15	LATUR	20564	11437	11438	1	9126	21		72
16	YAVATMAL	65196	41423	41424	1	23772	57		187
17	AHMEDNAGAR	60762	51568	51568	0	9194	96		72
18	AURANGABAD	36661	24161	24161	0	12500	36		98
19	BHANDARA	65100	48847	48847	0	16253	34		128
20	BULDHANA	44724	25659	25659	0	19065	33		150
21	CHANDRAPUR	43012	31645	31645	0	11367	38		90
22	DHULE	64903	50035	50035	0	14868	50		117
23	GADCHIROLI	31603	23799	23799	0	7804	29		61
24	KOLHAPUR	17685	13182	13182	0	4503	8		35
25	OSMANABAD	14382	6880	6880	0	7502	15		59
26	PALGHAR	35183	28254	28254	0	6929	24		55
27	PUNE	20531	13962	13962	0	6569	10		52
28	RAIGAD	9822	8674	8674	0	1148	4		9
29	RATNAGIRI	9900	8371	8371	0	1529	15		12
30	SATARA	15373	11387	11387	0	3986	14		31
31	SINDHUDURG	5142	4232	4232	0	910	4		7
32	SOLAPUR	49292	32903	32903	0	16389	21		129
33	THANE	9599	7048	7048	0	2551	4		20
34	WARDHA	18621	14140	14140	0	4481	11		35
Total		1411755	1024330	1024544	214	387211	1003		3049

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	09.04.2023	10.04.2023	Daily_Achievement	Remaining
1	KONKAN DIV.	34729	30424	30424	0	4305
2	PUNE DIV.	65334	62976	62976	0	2358
3	NASHIK DIV.	141360	109755	109755	0	31605
4	AURANGABAD DIV.	199331	163848	163848	0	35483
5	AMRAVATI DIV.	109702	93436	93436	0	16266
6	NAGPUR DIV.	118393	88678	88678	0	29715
Total		668849	549117	549117	0	119732


Sr. No.	District	Target	09.04.2023	10.04.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	35298	32971	32971	0	2327
2	AKOLA	23681	17687	17687	0	5994
3	AMRAVATI	23224	19675	19675	0	3549
4	AURANGABAD	26141	23795	23795	0	2346
5	BEED	26878	24783	24783	0	2095
6	BHANDARA	17590	15213	15213	0	2377
7	BULDHANA	21616	19966	19966	0	1650
8	CHANDRAPUR	40285	23410	23410	0	16875
9	DHULE	21790	17602	17602	0	4188
10	GADCHIROLI	16834	15186	15186	0	1648
11	GONDIA	14246	12682	12682	0	1564
12	HINGOLI	27298	15305	15305	0	11993
13	JALGAON	25659	22532	22532	0	3127
14	JALNA	20446	19155	19155	0	1291
15	KOLHAPUR	12565	12528	12528	0	37
16	LATUR	27171	26068	26068	0	1103
17	NAGPUR	16291	11017	11017	0	5274
18	NANDED	26760	20284	20284	0	6476
19	NANDURBAR	26578	14135	14135	0	12443
20	NASHIK	32035	22515	22515	0	9520
21	OSMANABAD	24853	16979	16979	0	7874
22	PALGHAR	11792	10585	10585	0	1207
23	PARBHANI	19784	17479	17479	0	2305
24	PUNE	14672	12770	12770	0	1902
25	RAIGAD	7406	6221	6221	0	1185
26	RATNAGIRI	7126	6677	6677	0	449
27	SANGLI	8732	8600	8600	0	132
28	SATARA	10647	10633	10633	0	14
29	SINDHUDURG	2141	2107	2107	0	34
30	SOLAPUR	18718	18445	18445	0	273
31	THANE	6264	4834	4834	0	1430
32	WARDHA	13147	11170	11170	0	1977
33	WASHIM	11500	10050	10050	0	1450
34	YAVATMAL	29681	26058	26058	0	3623
Total		668849	549117	549117	0	119732

Remaining Sanction RANK

SATARA	14
SINDHUDURG	34
KOLHAPUR	37
SANGLI	132
SOLAPUR	273
RATNAGIRI	449
LATUR	1103
RAIGAD	1185
PALGHAR	1207
JALNA	1291
THANE	1430
WASHIM	1450
GONDIA	1564
GADCHIROLI	1648
BULDHANA	1650
PUNE	1902
WARDHA	1977
BEED	2095
PARBHANI	2305
AHMEDNAGAR	2327
AURANGABAD	2346
BHANDARA	2377
JALGAON	3127
AMRAVATI	3549
YAVATMAL	3623
DHULE	4188
NAGPUR	5274
AKOLA	5994
NANDED	6476
OSMANABAD	7874
NASHIK	9520
HINGOLI	11993
NANDURBAR	12443
CHANDRAPUR	16875

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	09.04.2023	10.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	KONKAN DIV.	30424	23371	23371	0	7053	14	56
2	PUNE DIV.	62976	51711	51711	0	11265	26	89
3	NASHIK DIV.	109755	88424	88424	0	21331	74	168
4	AURANGABAD DIV.	163848	102836	102836	0	61012	90	480
5	AMRAVATI DIV.	93436	63912	63912	0	29524	55	232
6	NAGPUR DIV.	88678	68874	68874	0	19804	45	156
Total		549117	399128	399128	0	149989	303	1181

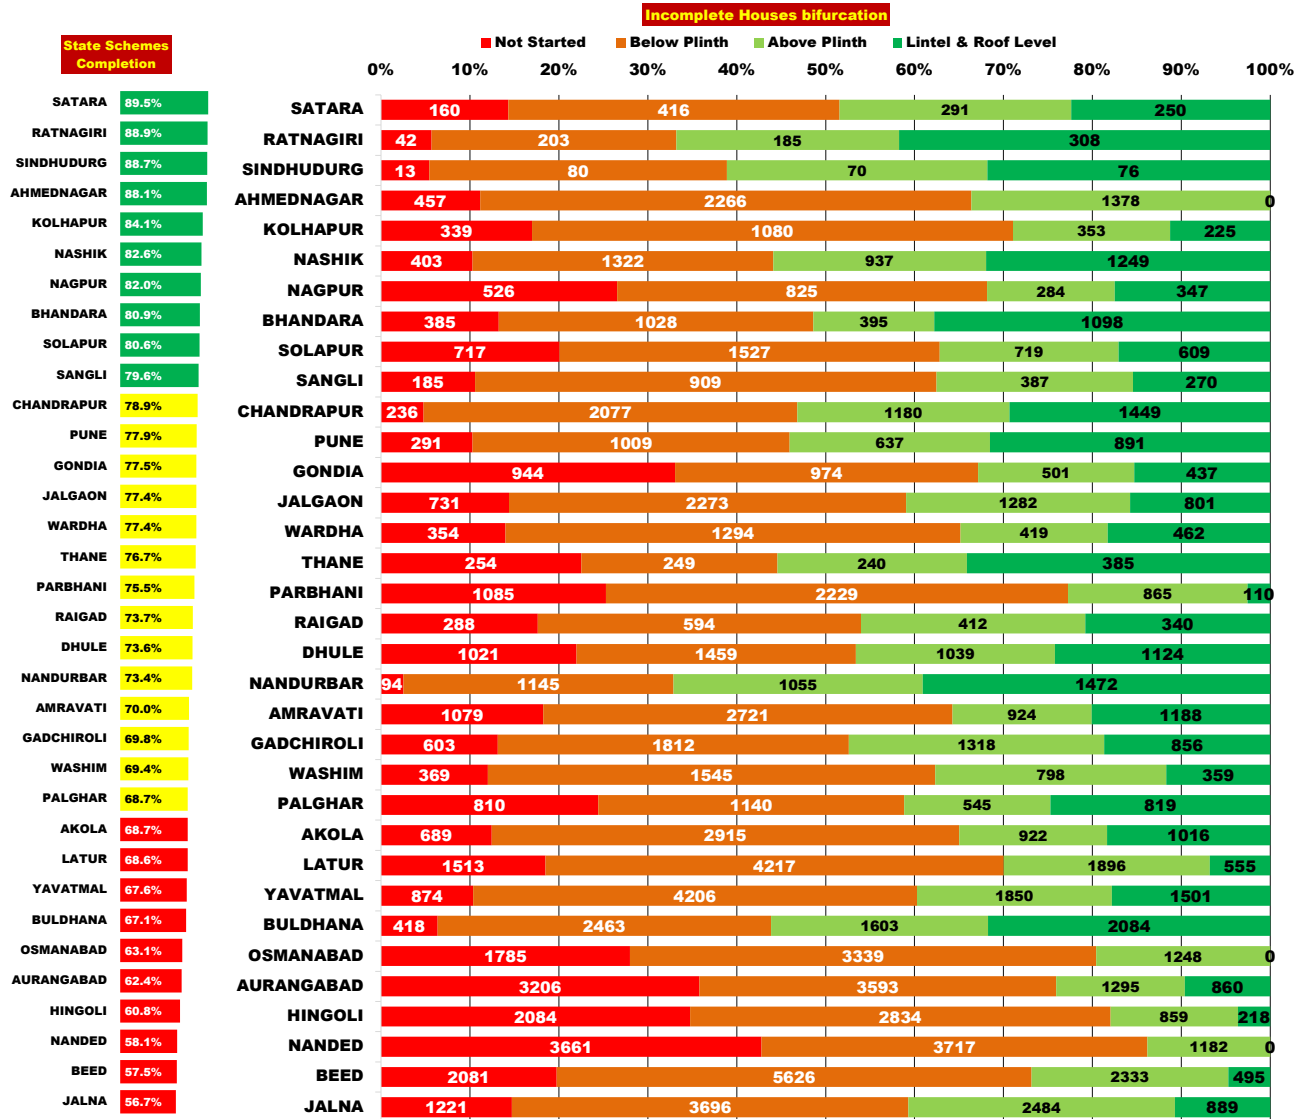

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	09.04.2023	10.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AHMEDNAGAR	32971	29047	29047	0	3924	31	31
2	AKOLA	17687	12145	12145	0	5542	9	44
3	AMRAVATI	19675	13763	13763	0	5912	9	47
4	AURANGABAD	23795	14841	14841	0	8954	9	71
5	BEED	24783	14248	14248	0	10535	14	83
6	BHANDARA	15213	12307	12307	0	2906	4	23
7	BULDHANA	19966	13398	13398	0	6568	17	52
8	CHANDRAPUR	23410	18468	18468	0	4942	13	39
9	DHULE	17602	12959	12959	0	4643	10	37
10	GADCHIROLI	15186	10597	10597	0	4589	9	36
11	GONDIA	12682	9826	9826	0	2856	8	22
12	HINGOLI	15305	9310	9310	0	5995	6	47
13	JALGAON	22532	17445	17445	0	5087	12	40
14	JALNA	19155	10865	10865	0	8290	26	65
15	KOLHAPUR	12528	10531	10531	0	1997	3	16
16	LATUR	26068	17887	17887	0	8181	12	64
17	NAGPUR	11017	9035	9035	0	1982	3	16
18	NANDED	20284	11780	11780	0	8504	8	67
19	NANDURBAR	14135	10369	10369	0	3766	6	30
20	NASHIK	22515	18604	18604	0	3911	13	31
21	OSMANABAD	16979	10715	10715	0	6264	11	49
22	PALGHAR	10585	7271	7271	0	3314	6	26
23	PARBHANI	17479	13190	13190	0	4289	4	34
24	PUNE	12770	9942	9942	0	2828	6	22
25	RAIGAD	6221	4587	4587	0	1634	3	13
26	RATNAGIRI	6677	5939	5939	0	738	2	6
27	SANGLI	8600	6849	6849	0	1751	4	14
28	SATARA	10633	9516	9516	0	1117	6	9
29	SINDHUDURG	2107	1868	1868	0	239	1	2
30	SOLAPUR	18445	14873	14873	0	3572	7	28
31	THANE	4834	3706	3706	0	1128	2	9
32	WARDHA	11170	8641	8641	0	2529	7	20
33	WASHIM	10050	6979	6979	0	3071	7	24
34	YAVATMAL	26058	17627	17627	0	8431	13	66
	Total	549117	399128	399128	0	149989	303	1181

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	11803	0	43116	0	23243
2	AMRAVATI DIV.	0	33030	0	35799	0	15417
3	AURANGABAD DIV.	0	21933	0	58327	0	21983
4	NAGPUR DIV.	0	11685	0	24124	0	14342
5	KONKAN DIV.	0	624	0	4386	0	4503
6	PUNE DIV.	0	11411	0	17680	0	7014
	Total	0	90486	0	183432	0	86502

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	20
THANE	110
RATNAGIRI	126
PALGHAR	362
GADCHIROLI	400
KOLHAPUR	562
SANGLI	809
SATARA	969
DHULE	1176
NASHIK	1261
PARBHANI	1330
NANDURBAR	1508
GONDIA	1656
WARDHA	1698
HINGOLI	2105
JALNA	2123
NAGPUR	2165
PUNE	2304
CHANDRAPUR	2413
LATUR	2554
AURANGABAD	3051
AHMEDNAGAR	3185
WASHIM	3301
OSMANABAD	3343
BHANDARA	3353
NANDED	3711
BEED	3716
AKOLA	4257
YAVATMAL	4514
JALGAON	4673
SOLAPUR	6767
BULDHANA	8773
AMRAVATI	12185

PMAY-G 2nd Ins Pending

SINDHUDURG	307
RATNAGIRI	536
RAIGAD	594
THANE	779
SATARA	1375
WARDHA	1455
PALGHAR	2170
OSMANABAD	2251
PUNE	2467
KOLHAPUR	2808
GADCHIROLI	3034
NAGPUR	3156
HINGOLI	3478
WASHIM	3921
AHMEDNAGAR	4187
SANGLI	4396
LATUR	4900
GONDIA	5060
AKOLA	5381
CHANDRAPUR	5435
JALNA	5625
BHANDARA	5984
AURANGABAD	6222
BULDHANA	6630
SOLAPUR	6634
NASHIK	6823
PARBHANI	6990
DHULE	7354
BEED	8951
AMRAVATI	9492
YAVATMAL	10375
NANDURBAR	11239
JALGAON	13513
NANDED	19910

PMAY-G 3rd Ins Pending

SINDHUDURG	401
RAIGAD	422
RATNAGIRI	556
THANE	761
WARDHA	954
PUNE	1045
KOLHAPUR	1068
SATARA	1200
HINGOLI	1333
SANGLI	1416
NAGPUR	1487
LATUR	1825
AKOLA	2012
JALNA	2188
WASHIM	2190
PARBHANI	2231
SOLAPUR	2285
PALGHAR	2363
GADCHIROLI	2480
AURANGABAD	2527
OSMANABAD	2612
BHANDARA	2696
BULDHANA	2803
CHANDRAPUR	2919
AMRAVATI	3186
BEED	3380
AHMEDNAGAR	3622
GONDIA	3806
DHULE	3831
NASHIK	3994
JALGAON	4020
YAVATMAL	5226
NANDED	5887
NANDURBAR	7776

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3185	0	4187	0	3622
2	AKOLA	0	4257	0	5381	0	2012
3	AMRAVATI	0	12185	0	9492	0	3186
4	AURANGABAD	0	3051	0	6222	0	2527
5	BEED	0	3716	0	8951	0	3380
6	BHANDARA	0	3353	0	5984	0	2696
7	BULDHANA	0	8773	0	6630	0	2803
8	CHANDRAPUR	0	2413	0	5435	0	2919
9	DHULE	0	1176	0	7354	0	3831
10	GADCHIROLI	0	400	0	3034	0	2480
11	GONDIA	0	1656	0	5060	0	3806
12	HINGOLI	0	2105	0	3478	0	1333
13	JALGAON	0	4673	0	13513	0	4020
14	JALNA	0	2123	0	5625	0	2188
15	KOLHAPUR	0	562	0	2808	0	1068
16	LATUR	0	2554	0	4900	0	1825
17	NAGPUR	0	2165	0	3156	0	1487
18	NANDED	0	3711	0	19910	0	5887
19	NANDURBAR	0	1508	0	11239	0	7776
20	NASHIK	0	1261	0	6823	0	3994
21	OSMANABAD	0	3343	0	2251	0	2612
22	PALGHAR	0	362	0	2170	0	2363
23	PARBHANI	0	1330	0	6990	0	2231
24	PUNE	0	2304	0	2467	0	1045
25	RAIGAD	0	20	0	594	0	422
26	RATNAGIRI	0	126	0	536	0	556
27	SANGLI	0	809	0	4396	0	1416
28	SATARA	0	969	0	1375	0	1200
29	SINDHUDURG	0	6	0	307	0	401
30	SOLAPUR	0	6767	0	6634	0	2285
31	THANE	0	110	0	779	0	761
32	WARDHA	0	1698	0	1455	0	954
33	WASHIM	0	3301	0	3921	0	2190
34	YAVATMAL	0	4514	0	10375	0	5226
	Total	0	90486	0	183432	0	86502

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2706	0	8465	0	5691
2	AMRAVATI DIV.	0	3429	0	13850	0	6097
3	AURANGABAD DIV.	0	16636	0	29251	0	12162
4	NAGPUR DIV.	0	3048	0	8010	0	4097
5	KONKAN DIV.	0	1407	0	2266	0	1452
6	PUNE DIV.	0	1692	0	4941	0	2387
Total		0	28918	0	66783	0	31886

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	42
NANDURBAR	94
SATARA	160
SANGLI	185
CHANDRAPUR	236
THANE	254
RAIGAD	288
PUNE	291
KOLHAPUR	339
WARDHA	354
WASHIM	369
BHANDARA	385
NASHIK	403
BULDHANA	418
AHMEDNAGAR	457
NAGPUR	526
GADCHIROLI	603
AKOLA	689
SOLAPUR	717
JALGAON	731
PALGHAR	810
YAVATMAL	874
GONDIA	944
DHULE	1021
AMRAVATI	1079
PARBHANI	1085
JALNA	1221
LATUR	1513
OSMANABAD	1785
BEED	2081
HINGOLI	2084
AURANGABAD	3206
NANDED	3661

State Schemes 2nd Ins Pending

SINDHUDURG	80
RATNAGIRI	203
THANE	249
SATARA	416
RAIGAD	594
NAGPUR	825
SANGLI	909
GONDIA	974
PUNE	1009
BHANDARA	1028
KOLHAPUR	1080
PALGHAR	1140
NANDURBAR	1145
WARDHA	1294
NASHIK	1322
DHULE	1459
SOLAPUR	1527
WASHIM	1545
GADCHIROLI	1812
CHANDRAPUR	2077
PARBHANI	2229
AHMEDNAGAR	2266
JALGAON	2273
BULDHANA	2463
AMRAVATI	2721
HINGOLI	2834
AKOLA	2915
OSMANABAD	3339
AURANGABAD	3593
JALNA	3696
NANDED	3717
YAVATMAL	4206
LATUR	4217
BEED	5626

State Schemes 3rd Ins Pending

SINDHUDURG	70
RATNAGIRI	185
THANE	240
NAGPUR	284
SATARA	291
KOLHAPUR	353
SANGLI	387
BHANDARA	395
RAIGAD	412
WARDHA	419
GONDIA	501
PALGHAR	545
PUNE	637
SOLAPUR	719
WASHIM	798
HINGOLI	859
PARBHANI	865
AKOLA	922
AMRAVATI	924
NASHIK	937
DHULE	1039
NANDURBAR	1055
CHANDRAPUR	1180
NANDED	1182
OSMANABAD	1248
JALGAON	1282
AURANGABAD	1295
GADCHIROLI	1318
AHMEDNAGAR	1378
BULDHANA	1603
YAVATMAL	1850
LATUR	1896
BEED	2333
JALNA	2484

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	457	0	2266	0	1378
2	AKOLA	0	689	0	2915	0	922
3	AMRAVATI	0	1079	0	2721	0	924
4	AURANGABAD	0	3206	0	3593	0	1295
5	BEED	0	2081	0	5626	0	2333
6	BHANDARA	0	385	0	1028	0	395
7	BULDHANA	0	418	0	2463	0	1603
8	CHANDRAPUR	0	236	0	2077	0	1180
9	DHULE	0	1021	0	1459	0	1039
10	GADCHIROLI	0	603	0	1812	0	1318
11	GONDIA	0	944	0	974	0	501
12	HINGOLI	0	2084	0	2834	0	859
13	JALGAON	0	731	0	2273	0	1282
14	JALNA	0	1221	0	3696	0	2484
15	KOLHAPUR	0	339	0	1080	0	353
16	LATUR	0	1513	0	4217	0	1896
17	NAGPUR	0	526	0	825	0	284
18	NANDED	0	3661	0	3717	0	1182
19	NANDURBAR	0	94	0	1145	0	1055
20	NASHIK	0	403	0	1322	0	937
21	OSMANABAD	0	1785	0	3339	0	1248
22	PALGHAR	0	810	0	1140	0	545
23	PARBHANI	0	1085	0	2229	0	865
24	PUNE	0	291	0	1009	0	637
25	RAIGAD	0	288	0	594	0	412
26	RATNAGIRI	0	42	0	203	0	185
27	SANGLI	0	185	0	909	0	387
28	SATARA	0	160	0	416	0	291
29	SINDHUDURG	0	13	0	80	0	70
30	SOLAPUR	0	717	0	1527	0	719
31	THANE	0	254	0	249	0	240
32	WARDHA	0	354	0	1294	0	419
33	WASHIM	0	369	0	1545	0	798
34	YAVATMAL	0	874	0	4206	0	1850
	Total	0	28918	0	66783	0	31886

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

