



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १५.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४११४३७	१	१०३२२५५	७१०	०	०	०
राज्य योजना	५५१६०२	१	४०१०३५	१११	०	०	०
एकूण	१९६३०३९	२	१४३३२९०	८२१	०	०	०

PMAY-G Completion Progress Bar

73.1%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.7%


State Schemes: Incomplete Houses bifurcation

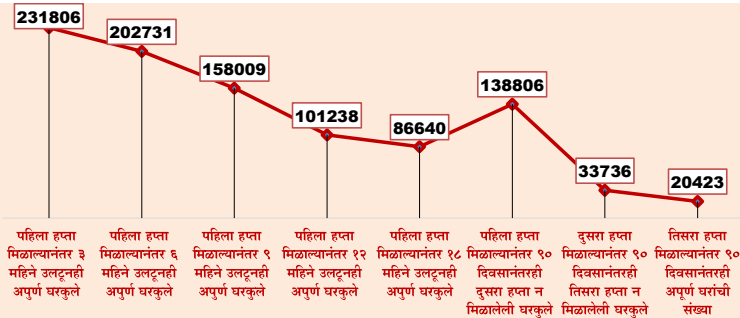


Abhiyan Achievement Day 146

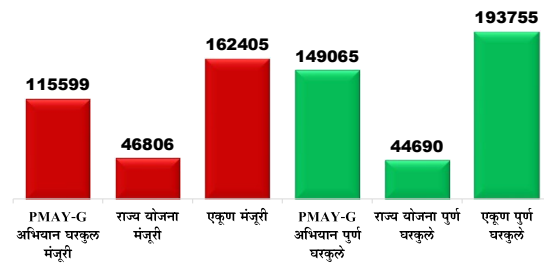

PMAY-G : House completion ( Abhiyan Achievement)

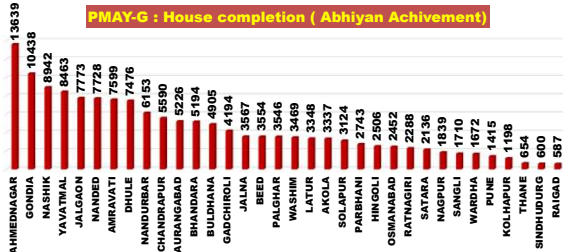

State Schemes : House completion ( Abhiyan Achievement)

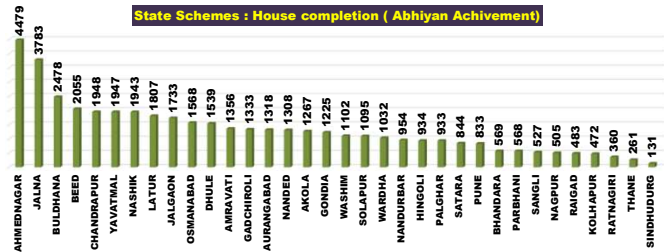


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण

४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


**PMAY-G Delayed Houses TOP 10 Dist.**




**State Schemes Sanction TOP 10 Dist.**




**PMAY-G Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Delayed Houses Bottom 10 Dist.**




**State Schemes Sanction Bottom 10 Dist.**




**PMAY-G Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Completion TOP 10 Dist.**




**State Schemes Completion TOP 10 Dist.**




**PMAY-G Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G Completion Bottom 10 Dist.**




**State Schemes Completion Bottom 10 Dist.**




**State Schemes Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Top 10 Dist.**




**State Schemes Daily Completion Top 10 Dist.**




**State Schemes Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Bottom 10 Dist.**




**State Schemes Daily Completion Bottom 10 Dist.**




**State Schemes Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G : Current Pace of Completion Per Day (Abhiyan)**




**State Schemes : Current Pace of Completion Per Day (Abhiyan)**



**PMAY-G Required Pace of Completion Per Day**



**State Schemes Required Pace of Completion Per Day**



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	14.04.2023	15.04.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414777	413710	413711	1	1066
2	AMRAVATI DIV.	275036	274527	274527	0	509
3	AURANGABAD DIV.	238110	237492	237492	0	618
4	NAGPUR DIV.	292190	291578	291576	0	614
5	KONKAN DIV.	69788	69637	69637	0	151
6	PUNE DIV.	125100	124494	124494	0	606
<b>Total</b>		<b>1415001</b>	<b>1411438</b>	<b>1411437</b>	<b>1</b>	<b>3564</b>

Sr. No.	District	Target (PWL+Awaas Plus)	14.04.2023	15.04.2023	Daily_Achievement	Remaining
1	JALGAON	79749	79422	79423	1	326
2	AHMEDNAGAR	60793	60752	60752	0	41
3	AKOLA	48797	48778	48778	0	19
4	AMRAVATI	95712	95460	95460	0	252
5	AURANGABAD	36795	36666	36666	0	129
6	BEED	35310	35254	35254	0	56
7	BULDHANA	44768	44731	44731	0	37
8	CHANDRAPUR	43124	43010	43010	0	114
9	DHULE	64979	64903	64903	0	76
10	GADCHIROLI	31698	31611	31611	0	87
11	GONDIA	96492	96142	96142	0	350
12	HINGOLI	18109	18083	18083	0	26
13	JALNA	24039	24007	24007	0	32
14	KOLHAPUR	17685	17685	17685	0	0
15	LATUR	20708	20564	20564	0	144
16	NAGPUR	37113	37100	37100	0	13
17	NANDED	69546	69474	69474	0	72
18	NANDURBAR	119521	118941	118941	0	580
19	NASHIK	89735	89692	89692	0	43
20	OSMANABAD	14506	14384	14384	0	122
21	PALGHAR	35312	35184	35184	0	128
22	PARBHANI	19097	19060	19060	0	37
23	PUNE	20544	20531	20531	0	13
24	RAIGAD	9831	9822	9822	0	9
25	RATNAGIRI	9897	9890	9890	0	7
26	SANGLI	21932	21780	21780	0	152
27	SATARA	15363	15361	15361	0	2
28	SINDHUDURG	5142	5142	5142	0	0
29	SOLAPUR	49576	49137	49137	0	439
30	THANE	9606	9599	9599	0	7
31	WARDHA	18645	18621	18621	0	24
32	WASHIM	20404	20397	20397	0	7
33	YAVATMAL	65355	65161	65161	0	194
34	BHANDARA	65118	65094	65092	-2	26
<b>Total</b>		<b>1415001</b>	<b>1411438</b>	<b>1411437</b>	<b>1</b>	<b>3564</b>

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
SATARA	2
RATNAGIRI	7
THANE	7
WASHIM	7
RAIGAD	9
NAGPUR	13
PUNE	13
AKOLA	19
WARDHA	24
BHANDARA	26
HINGOLI	26
JALNA	32
BULDHANA	37
PARBHANI	37
AHMEDNAGAR	41
NASHIK	43
BEED	56
NANDED	72
DHULE	76
GADCHIROLI	87
CHANDRAPUR	114
OSMANABAD	122
PALGHAR	128
AURANGABAD	129
LATUR	144
SANGLI	152
YAVATMAL	194
AMRAVATI	252
JALGAON	326
GONDIA	350
SOLAPUR	439
NANDURBAR	580

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	224	33	0
9	THANE	127	74	53	127	43	84	0
10	NANDED	362	277	85	362	242	120	0
11	BEED	212	101	111	212	72	140	0
12	SANGLI	437	143	294	431	141	290	6
13	PARBHANI	332	15	317	332	13	319	0
14	SATARA	1311	582	729	1311	630	681	0
15	NASHIK	1642	1454	188	1642	715	927	0
16	HINGOLI	1713	787	926	1713	466	1247	0
17	JALNA	1413	165	1248	1381	85	1296	32
18	WARDHA	2819	1284	1535	2819	1216	1603	0
19	GONDIA	2450	2450	0	2450	765	1685	0
20	NAGPUR	5134	3397	1737	5088	3400	1688	46
21	CHANDRAPUR	2791	1463	1328	2752	965	1787	39
22	PUNE	2925	992	1933	2925	885	2040	0
23	LATUR	2341	13	2328	2341	5	2336	0
24	OSMANABAD	2470	104	2366	2470	56	2414	0
25	YAVATMAL	3437	1119	2318	3575	1094	2481	-138
26	BHANDARA	5825	3230	2595	5820	3213	2607	5
27	WASHIM	3477	865	2612	3477	850	2627	0
28	AURANGABAD	3328	1779	1549	3328	288	3040	0
29	AKOLA	7074	3842	3232	7074	3844	3230	0
30	AHMEDNAGAR	7762	4828	2934	7757	3286	4471	5
31	JALGAON	22889	20580	2309	22681	16486	6195	208
32	SOLAPUR	7960	2595	5365	7854	793	7061	106
33	BULDHANA	15256	8455	6801	15256	6953	8303	0
34	AMRAVATI	21560	11238	10322	21560	3318	18242	0
	<b>Total</b>	<b>127790</b>	<b>72575</b>	<b>55215</b>	<b>127481</b>	<b>50534</b>	<b>76947</b>	<b>309</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	14.04.2023	15.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AURANGABAD DIV.	237492	138459	138685	226	98807	213	810
2	AMRAVATI DIV.	274527	184746	184930	184	89597	190	734
3	NASHIK DIV.	413711	327345	327497	152	86214	301	707
4	NAGPUR DIV.	291576	237002	237055	53	54521	198	447
5	KONKAN DIV.	69637	57035	57083	48	12554	53	103
6	PUNE DIV.	124494	86958	87005	47	37489	66	307
<b>Total</b>		<b>1411437</b>	<b>1031545</b>	<b>1032255</b>	<b>710</b>	<b>379182</b>	<b>1021</b>	<b>3108</b>

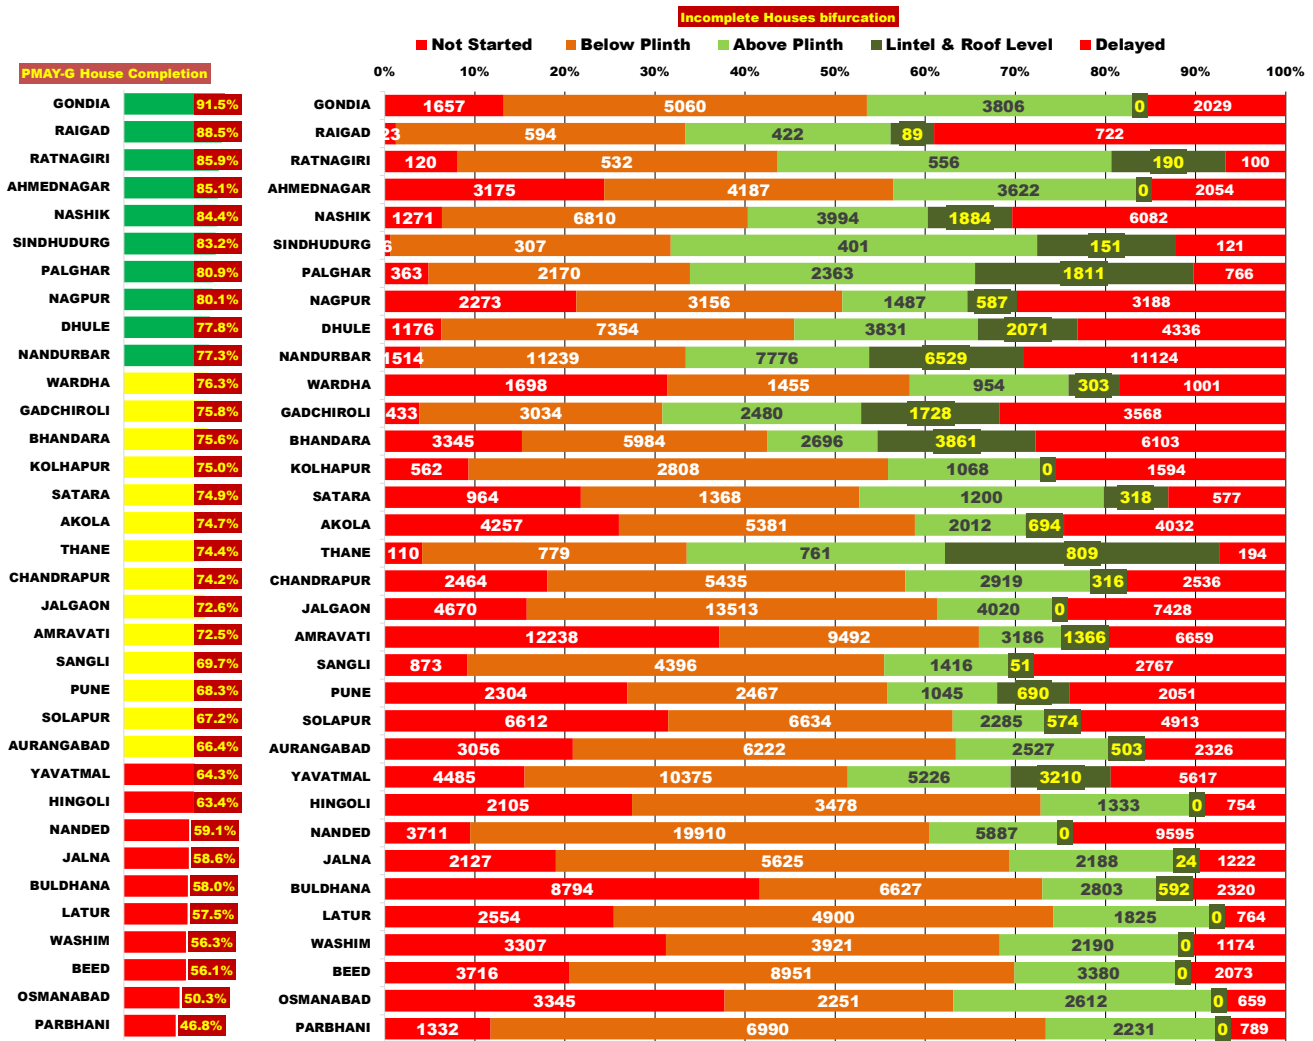

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	14.04.2023	15.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	WASHIM	20397	11330	11475	145	8922	24	73
2	OSMANABAD	14384	7125	7232	107	7152	17	59
3	DHULE	64903	50382	50471	89	14432	51	118
4	NANDED	69474	40963	41038	75	28436	53	233
5	JALGAON	79423	57656	57691	35	21732	53	178
6	CHANDRAPUR	43010	31898	31929	31	11081	38	91
7	SATARA	15361	11480	11511	31	3850	15	32
8	NANDURBAR	118941	91861	91883	22	27058	42	222
9	BULDHANA	44731	25906	25926	20	18805	34	154
10	RATNAGIRI	9890	8473	8492	19	1398	16	11
11	LATUR	20564	11807	11822	15	8742	23	72
12	PALGHAR	35184	28463	28477	14	6707	24	55
13	SOLAPUR	49137	33018	33032	14	16105	21	132
14	JALNA	24007	14060	14073	13	9934	24	81
15	YAVATMAL	65161	41859	41871	12	23290	58	191
16	GONDIA	96142	88005	88016	11	8126	71	67
17	THANE	9599	7130	7140	10	2459	4	20
18	BEED	35254	19774	19782	8	15472	24	127
19	AURANGABAD	36666	24351	24358	7	12308	36	101
20	AHMEDNAGAR	60752	51713	51719	6	9033	93	74
21	BHANDARA	65092	49200	49206	6	15886	36	130
22	SINDHUDURG	5142	4272	4277	5	865	4	7
23	AKOLA	48778	36430	36434	4	12344	23	101
24	WARDHA	18621	14207	14211	4	4410	11	36
25	AMRAVATI	95460	69221	69224	3	26236	52	215
26	KOLHAPUR	17685	13258	13260	2	4425	8	36
27	NAGPUR	37100	29731	29732	1	7368	13	60
28	PARBHANI	19060	8915	8916	1	10144	19	83
29	GADCHIROLI	31611	23961	23961	0	7650	29	63
30	HINGOLI	18083	11464	11464	0	6619	17	54
31	NASHIK	89692	75733	75733	0	13959	61	114
32	PUNE	20531	14025	14025	0	6506	10	53
33	RAIGAD	9822	8697	8697	0	1125	4	9
34	SANGLI	21780	15177	15177	0	6603	12	54
<b>Total</b>		<b>1411437</b>	<b>1031545</b>	<b>1032255</b>	<b>710</b>	<b>379182</b>	<b>1021</b>	<b>3108</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	14.04.2023	15.04.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	109702	93509	93510	1	16192
2	KONKAN DIV.	34729	30943	30943	0	3786
3	PUNE DIV.	65334	62993	62993	0	2341
4	NASHIK DIV.	141360	110133	110133	0	31227
5	AURANGABAD DIV.	199331	164369	164368	0	34963
6	NAGPUR DIV.	118393	89655	89655	0	28738
<b>Total</b>		<b>668849</b>	<b>551602</b>	<b>551602</b>	<b>1</b>	<b>117247</b>


Sr. No.	District	Target	14.04.2023	15.04.2023	Daily_Achievement	Remaining
1	WASHIM	11500	10054	10055	1	1445
2	AHMEDNAGAR	35298	32973	32973	0	2325
3	AKOLA	23681	17691	17691	0	5990
4	AMRAVATI	23224	19699	19699	0	3525
5	AURANGABAD	26141	23795	23795	0	2346
6	BEED	26878	24796	24796	0	2082
7	BHANDARA	17590	15392	15392	0	2198
8	BULDHANA	21616	19967	19967	0	1649
9	CHANDRAPUR	40285	24080	24080	0	16205
10	DHULE	21790	17708	17708	0	4082
11	GADCHIROLI	16834	15197	15197	0	1637
12	GONDIA	14246	12795	12795	0	1451
13	HINGOLI	27298	15306	15306	0	11992
14	JALGAON	25659	22535	22535	0	3124
15	JALNA	20446	19183	19183	0	1263
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	26113	26113	0	1058
18	NAGPUR	16291	11021	11021	0	5270
19	NANDED	26760	20607	20607	0	6153
20	NANDURBAR	26578	14135	14135	0	12443
21	NASHIK	32035	22782	22782	0	9253
22	OSMANABAD	24853	16979	16979	0	7874
23	PALGHAR	11792	10974	10974	0	818
24	PUNE	14672	12770	12770	0	1902
25	RAIGAD	7406	6228	6228	0	1178
26	RATNAGIRI	7126	6677	6677	0	449
27	SANGLI	8732	8603	8603	0	129
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2107	2107	0	34
30	SOLAPUR	18718	18445	18445	0	273
31	THANE	6264	4957	4957	0	1307
32	WARDHA	13147	11170	11170	0	1977
33	YAVATMAL	29681	26098	26098	0	3583
34	PARBHANI	19784	17590	17589	-1	2195
<b>Total</b>		<b>668849</b>	<b>551602</b>	<b>551602</b>	<b>1</b>	<b>117247</b>

Remaining Sanction RANK

SATARA	0
SINDHUDURG	34
KOLHAPUR	37
SANGLI	129
SOLAPUR	273
RATNAGIRI	449
PALGHAR	818
LATUR	1058
RAIGAD	1178
JALNA	1263
THANE	1307
WASHIM	1445
GONDIA	1451
GADCHIROLI	1637
BULDHANA	1649
PUNE	1902
WARDHA	1977
BEED	2082
PARBHANI	2195
BHANDARA	2198
AHMEDNAGAR	2325
AURANGABAD	2346
JALGAON	3124
AMRAVATI	3525
YAVATMAL	3583
DHULE	4082
NAGPUR	5270
AKOLA	5990
NANDED	6153
OSMANABAD	7874
NASHIK	9253
HINGOLI	11992
NANDURBAR	12443
CHANDRAPUR	16205

## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	14.04.2023	15.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	AURANGABAD DIV.	164368	103413	103447	34	60921	91	499
2	AMRAVATI DIV.	93510	64325	64348	23	29162	56	239
3	NASHIK DIV.	110133	88684	88705	21	21428	73	176
4	KONKAN DIV.	30943	23528	23542	14	7401	15	61
5	PUNE DIV.	62993	51824	51836	12	11157	26	91
6	NAGPUR DIV.	89655	69150	69157	7	20498	45	168
<b>Total</b>		<b>551602</b>	<b>400924</b>	<b>401035</b>	<b>111</b>	<b>150567</b>	<b>306</b>	<b>1234</b>

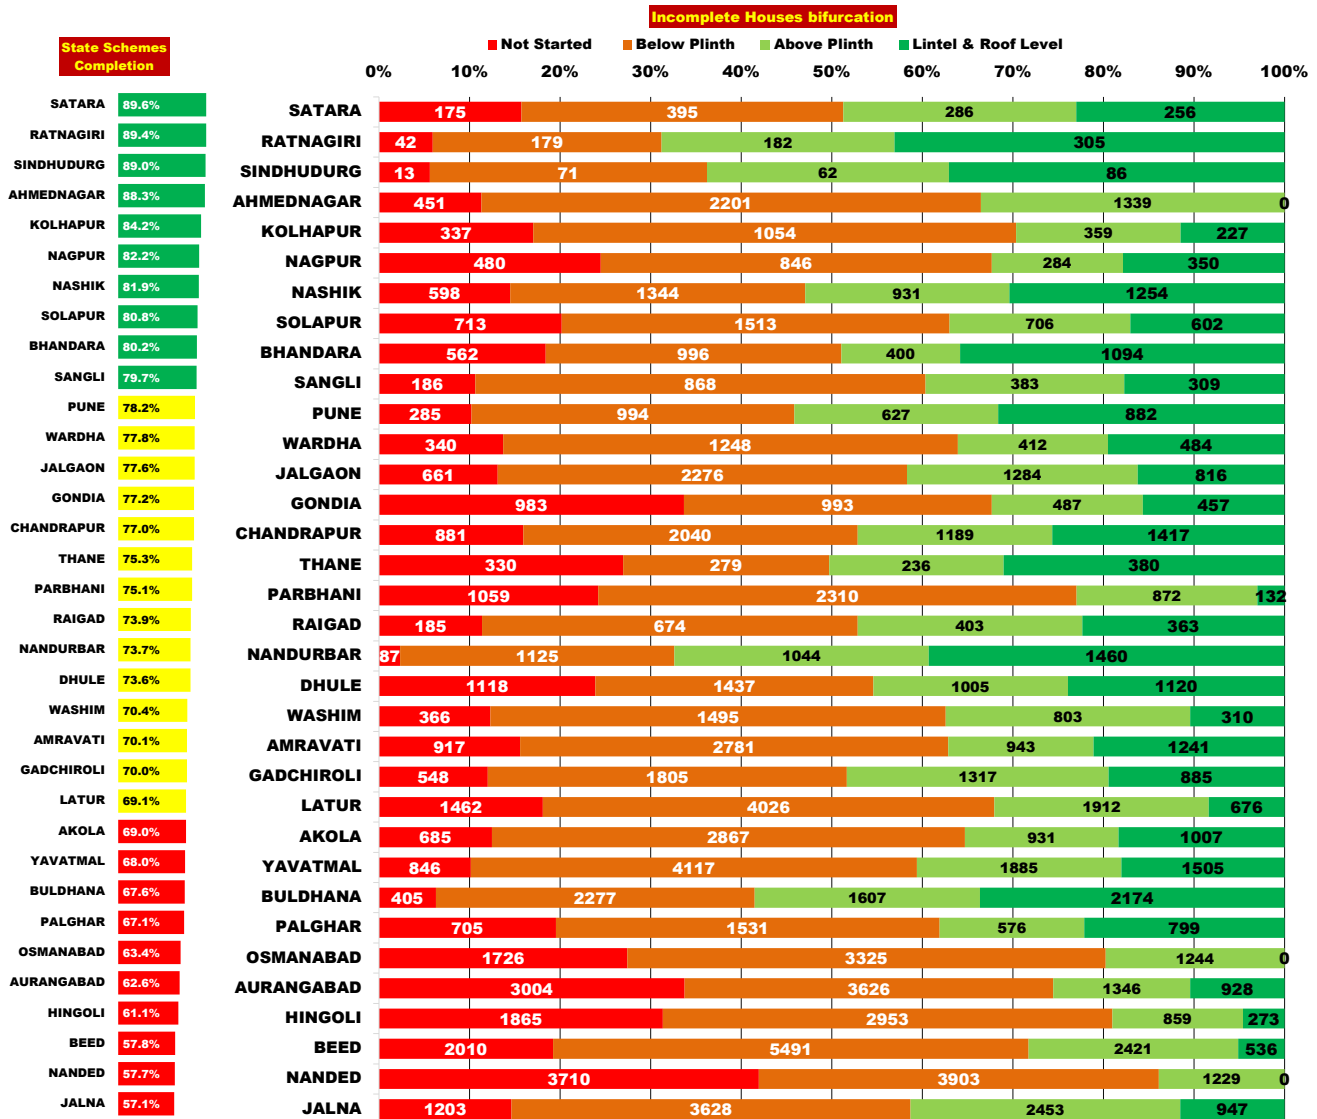



राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	14.04.2023	15.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 15.08.23
1	WASHIM	10055	7068	7081	13	2974	8	24
2	NANDED	20607	11885	11897	12	8710	9	71
3	DHULE	17708	13018	13028	10	4680	11	38
4	OSMANABAD	16979	10750	10760	10	6219	11	51
5	THANE	4957	3722	3732	10	1225	2	10
6	SOLAPUR	18445	14902	14911	9	3534	8	29
7	AMRAVATI	19699	13810	13817	7	5882	9	48
8	LATUR	26113	18032	18037	5	8076	12	66
9	NANDURBAR	14135	10414	10419	5	3716	7	30
10	AHMEDNAGAR	32973	29101	29105	4	3868	31	32
11	AURANGABAD	23795	14887	14891	4	8904	9	73
12	YAVATMAL	26098	17742	17745	3	8353	13	68
13	BHANDARA	15392	12338	12340	2	3052	4	25
14	CHANDRAPUR	24080	18551	18553	2	5527	13	45
15	JALGAON	22535	17496	17498	2	5037	12	41
16	JALNA	19183	10950	10952	2	8231	26	67
17	NAGPUR	11021	9059	9061	2	1960	3	16
18	PALGHAR	10974	7361	7363	2	3611	6	30
19	SATARA	10647	9533	9535	2	1112	6	9
20	HINGOLI	15306	9355	9356	1	5950	6	49
21	KOLHAPUR	12528	10550	10551	1	1977	3	16
22	RAIGAD	6228	4602	4603	1	1625	3	13
23	RATNAGIRI	6677	5968	5969	1	708	2	6
24	WARDHA	11170	8685	8686	1	2484	7	20
25	AKOLA	17691	12201	12201	0	5490	9	45
26	BEED	24796	14338	14338	0	10458	14	86
27	BULDHANA	19967	13504	13504	0	6463	17	53
28	GADCHIROLI	15197	10642	10642	0	4555	9	37
29	GONDIA	12795	9875	9875	0	2920	8	24
30	NASHIK	22782	18655	18655	0	4127	13	34
31	PARBHANI	17589	13216	13216	0	4373	4	36
32	PUNE	12770	9982	9982	0	2788	6	23
33	SANGLI	8603	6857	6857	0	1746	4	14
34	SINDHUDURG	2107	1875	1875	0	232	1	2
<b>Total</b>		<b>551602</b>	<b>400924</b>	<b>401035</b>	<b>111</b>	<b>150567</b>	<b>306</b>	<b>1234</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	11806	0	43103	0	23243
2	AMRAVATI DIV.	0	33015	0	35796	0	15417
3	AURANGABAD DIV.	0	21916	0	58327	0	21983
4	NAGPUR DIV.	0	11657	0	24124	0	14342
5	KONKAN DIV.	0	619	0	4382	0	4503
6	PUNE DIV.	0	11182	0	17673	0	7014
	<b>Total</b>	<b>0</b>	<b>90195</b>	<b>0</b>	<b>183405</b>	<b>0</b>	<b>86502</b>

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	20
THANE	110
RATNAGIRI	120
PALGHAR	363
GADCHIROLI	408
KOLHAPUR	562
SANGLI	740
SATARA	964
DHULE	1176
NASHIK	1271
PARBHANI	1332
NANDURBAR	1514
GONDIA	1657
WARDHA	1698
JALNA	2097
HINGOLI	2105
NAGPUR	2138
PUNE	2304
CHANDRAPUR	2411
LATUR	2554
AURANGABAD	3056
AHMEDNAGAR	3175
WASHIM	3304
OSMANABAD	3345
BHANDARA	3345
NANDED	3711
BEED	3716
AKOLA	4257
YAVATMAL	4479
JALGAON	4670
SOLAPUR	6612
BULDHANA	8783
AMRAVATI	12192

PMAY-G 2nd Ins Pending

SINDHUDURG	307
RATNAGIRI	532
RAIGAD	594
THANE	779
SATARA	1368
WARDHA	1455
PALGHAR	2170
OSMANABAD	2251
PUNE	2467
KOLHAPUR	2808
GADCHIROLI	3034
NAGPUR	3156
HINGOLI	3478
WASHIM	3921
AHMEDNAGAR	4187
SANGLI	4396
LATUR	4900
GONDIA	5060
AKOLA	5381
CHANDRAPUR	5435
JALNA	5625
BHANDARA	5984
AURANGABAD	6222
BULDHANA	6627
SOLAPUR	6634
NASHIK	6810
PARBHANI	6990
DHULE	7354
BEED	8951
AMRAVATI	9492
YAVATMAL	10375
NANDURBAR	11239
JALGAON	13513
NANDED	19910

PMAY-G 3rd Ins Pending

SINDHUDURG	401
RAIGAD	422
RATNAGIRI	556
THANE	761
WARDHA	954
PUNE	1045
KOLHAPUR	1068
SATARA	1200
HINGOLI	1333
SANGLI	1416
NAGPUR	1487
LATUR	1825
AKOLA	2012
JALNA	2188
WASHIM	2190
PARBHANI	2231
SOLAPUR	2285
PALGHAR	2363
GADCHIROLI	2480
AURANGABAD	2527
OSMANABAD	2612
BHANDARA	2696
BULDHANA	2803
CHANDRAPUR	2919
AMRAVATI	3186
BEED	3380
AHMEDNAGAR	3622
GONDIA	3806
DHULE	3831
NASHIK	3994
JALGAON	4020
YAVATMAL	5226
NANDED	5887
NANDURBAR	7776

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3175	0	4187	0	3622
2	AKOLA	0	4257	0	5381	0	2012
3	AMRAVATI	0	12192	0	9492	0	3186
4	AURANGABAD	0	3056	0	6222	0	2527
5	BEED	0	3716	0	8951	0	3380
6	BHANDARA	0	3345	0	5984	0	2696
7	BULDHANA	0	8783	0	6627	0	2803
8	CHANDRAPUR	0	2411	0	5435	0	2919
9	DHULE	0	1176	0	7354	0	3831
10	GADCHIROLI	0	408	0	3034	0	2480
11	GONDIA	0	1657	0	5060	0	3806
12	HINGOLI	0	2105	0	3478	0	1333
13	JALGAON	0	4670	0	13513	0	4020
14	JALNA	0	2097	0	5625	0	2188
15	KOLHAPUR	0	562	0	2808	0	1068
16	LATUR	0	2554	0	4900	0	1825
17	NAGPUR	0	2138	0	3156	0	1487
18	NANDED	0	3711	0	19910	0	5887
19	NANDURBAR	0	1514	0	11239	0	7776
20	NASHIK	0	1271	0	6810	0	3994
21	OSMANABAD	0	3345	0	2251	0	2612
22	PALGHAR	0	363	0	2170	0	2363
23	PARBHANI	0	1332	0	6990	0	2231
24	PUNE	0	2304	0	2467	0	1045
25	RAIGAD	0	20	0	594	0	422
26	RATNAGIRI	0	120	0	532	0	556
27	SANGLI	0	740	0	4396	0	1416
28	SATARA	0	964	0	1368	0	1200
29	SINDHUDURG	0	6	0	307	0	401
30	SOLAPUR	0	6612	0	6634	0	2285
31	THANE	0	110	0	779	0	761
32	WARDHA	0	1698	0	1455	0	954
33	WASHIM	0	3304	0	3921	0	2190
34	YAVATMAL	0	4479	0	10375	0	5226
	<b>Total</b>	<b>0</b>	<b>90195</b>	<b>0</b>	<b>183405</b>	<b>0</b>	<b>86502</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2915	0	8383	0	5603
2	AMRAVATI DIV.	0	3219	0	13537	0	6169
3	AURANGABAD DIV.	0	16039	0	29262	0	12336
4	NAGPUR DIV.	0	3794	0	7928	0	4089
5	KONKAN DIV.	0	1275	0	2734	0	1459
6	PUNE DIV.	0	1696	0	4824	0	2361
<b>Total</b>		<b>0</b>	<b>28938</b>	<b>0</b>	<b>66668</b>	<b>0</b>	<b>32017</b>

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	42
NANDURBAR	87
SATARA	175
RAIGAD	185
SANGLI	186
PUNE	285
THANE	330
KOLHAPUR	337
WARDHA	340
WASHIM	366
BULDHANA	405
AHMEDNAGAR	451
NAGPUR	480
GADCHIROLI	548
BHANDARA	562
NASHIK	598
JALGAON	661
AKOLA	685
PALGHAR	705
SOLAPUR	713
YAVATMAL	846
CHANDRAPUR	881
AMRAVATI	917
GONDIA	983
PARBHANI	1059
DHULE	1118
JALNA	1203
LATUR	1462
OSMANABAD	1726
HINGOLI	1865
BEED	2010
AURANGABAD	3004
NANDED	3710

State Schemes 2nd Ins Pending

SINDHUDURG	71
RATNAGIRI	179
THANE	279
SATARA	395
RAIGAD	674
NAGPUR	846
SANGLI	868
GONDIA	993
PUNE	994
BHANDARA	996
KOLHAPUR	1054
NANDURBAR	1125
WARDHA	1248
NASHIK	1344
DHULE	1437
WASHIM	1495
SOLAPUR	1513
PALGHAR	1531
GADCHIROLI	1805
CHANDRAPUR	2040
AHMEDNAGAR	2201
JALGAON	2276
BULDHANA	2277
PARBHANI	2310
AMRAVATI	2781
AKOLA	2867
HINGOLI	2953
OSMANABAD	3325
AURANGABAD	3626
JALNA	3628
NANDED	3903
LATUR	4026
YAVATMAL	4117
BEED	5491

State Schemes 3rd Ins Pending

SINDHUDURG	62
RATNAGIRI	182
THANE	236
NAGPUR	284
SATARA	286
KOLHAPUR	359
SANGLI	383
BHANDARA	400
RAIGAD	403
WARDHA	412
GONDIA	487
PALGHAR	576
PUNE	627
SOLAPUR	706
WASHIM	803
HINGOLI	859
PARBHANI	872
NASHIK	931
AKOLA	931
AMRAVATI	943
DHULE	1005
NANDURBAR	1044
CHANDRAPUR	1189
NANDED	1229
OSMANABAD	1244
JALGAON	1284
GADCHIROLI	1317
AHMEDNAGAR	1339
AURANGABAD	1346
BULDHANA	1607
YAVATMAL	1885
LATUR	1912
BEED	2421
JALNA	2453

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	451	0	2201	0	1339
2	AKOLA	0	685	0	2867	0	931
3	AMRAVATI	0	917	0	2781	0	943
4	AURANGABAD	0	3004	0	3626	0	1346
5	BEED	0	2010	0	5491	0	2421
6	BHANDARA	0	562	0	996	0	400
7	BULDHANA	0	405	0	2277	0	1607
8	CHANDRAPUR	0	881	0	2040	0	1189
9	DHULE	0	1118	0	1437	0	1005
10	GADCHIROLI	0	548	0	1805	0	1317
11	GONDIA	0	983	0	993	0	487
12	HINGOLI	0	1865	0	2953	0	859
13	JALGAON	0	661	0	2276	0	1284
14	JALNA	0	1203	0	3628	0	2453
15	KOLHAPUR	0	337	0	1054	0	359
16	LATUR	0	1462	0	4026	0	1912
17	NAGPUR	0	480	0	846	0	284
18	NANDED	0	3710	0	3903	0	1229
19	NANDURBAR	0	87	0	1125	0	1044
20	NASHIK	0	598	0	1344	0	931
21	OSMANABAD	0	1726	0	3325	0	1244
22	PALGHAR	0	705	0	1531	0	576
23	PARBHANI	0	1059	0	2310	0	872
24	PUNE	0	285	0	994	0	627
25	RAIGAD	0	185	0	674	0	403
26	RATNAGIRI	0	42	0	179	0	182
27	SANGLI	0	186	0	868	0	383
28	SATARA	0	175	0	395	0	286
29	SINDHUDURG	0	13	0	71	0	62
30	SOLAPUR	0	713	0	1513	0	706
31	THANE	0	330	0	279	0	236
32	WARDHA	0	340	0	1248	0	412
33	WASHIM	0	366	0	1495	0	803
34	YAVATMAL	0	846	0	4117	0	1885
	<b>Total</b>	<b>0</b>	<b>28938</b>	<b>0</b>	<b>66668</b>	<b>0</b>	<b>32017</b>

## प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

