



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १८.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४११६३	७९	१०३३९८३	९८७	०	०	०
राज्य योजना	५५२३०६	५८६	४०१४७१	२८९	३९	७०	८९
एकूण	१९६३९६९	६६५	१४३५४५४	१२७६	३९	७०	८९

PMAY-G Completion Progress Bar

73.3%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.7%


State Schemes: Incomplete Houses bifurcation

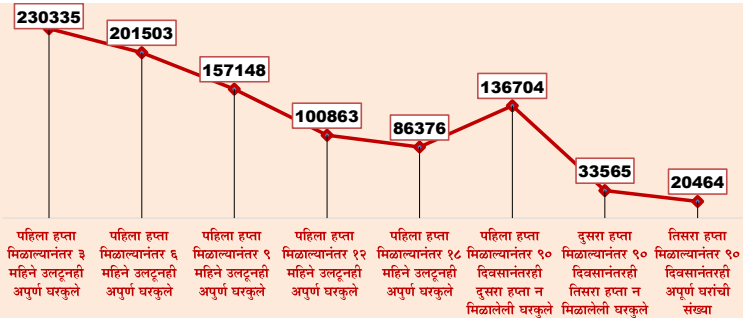


Abhiyan Achievement Day 149

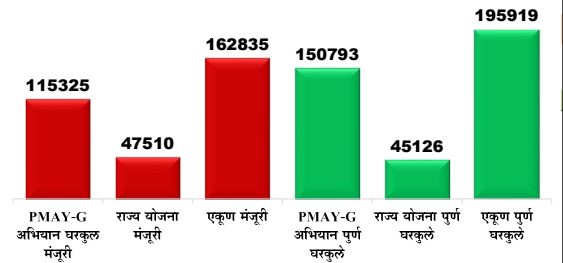

PMAY-G : House completion ( Abhiyan Achievement)

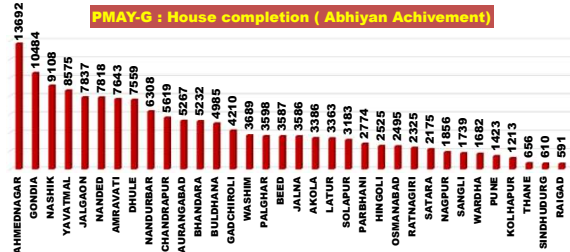

State Schemes : House completion ( Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


**PMAY-G Delayed Houses TOP 10 Dist.**




**State Schemes Sanction TOP 10 Dist.**




**PMAY-G Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Delayed Houses Bottom 10 Dist.**




**State Schemes Sanction Bottom 10 Dist.**




**PMAY-G Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Completion TOP 10 Dist.**




**State Schemes Completion TOP 10 Dist.**




**PMAY-G Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G Completion Bottom 10 Dist.**




**State Schemes Completion Bottom 10 Dist.**




**State Schemes Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Top 10 Dist.**




**State Schemes Daily Completion Top 10 Dist.**




**State Schemes Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Bottom 10 Dist.**




**State Schemes Daily Completion Bottom 10 Dist.**




**State Schemes Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G : Current Pace of Completion Per Day (Abhiyan)**




**State Schemes : Current Pace of Completion Per Day (Abhiyan)**



**PMAY-G Required Pace of Completion Per Day**



**State Schemes Required Pace of Completion Per Day**



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	17.04.2023	18.04.2023	Daily Achievement	Remaining
1	NASHIK DIV.	414776	413711	413738	27	1038
2	AURANGABAD DIV.	238076	237478	237451	26	625
3	AMRAVATI DIV.	275030	274528	274549	21	481
4	NAGPUR DIV.	292185	291576	291579	3	606
5	KONKAN DIV.	69786	69637	69638	1	148
6	PUNE DIV.	124989	124494	124208	1	781
<b>Total</b>		<b>1414842</b>	<b>1411424</b>	<b>1411163</b>	<b>79</b>	<b>3679</b>

Sr. No.	District	Target (PWL+Awaas Plus)	17.04.2023	18.04.2023	Daily Achievement	Remaining
1	YAVATMAL	65355	65161	65180	19	175
2	JALNA	24039	24007	24022	15	17
3	NASHIK	89735	89692	89705	13	30
4	DHULE	64979	64903	64915	12	64
5	OSMANABAD	14506	14384	14394	10	112
6	AHMEDNAGAR	60792	60752	60754	2	38
7	AMRAVATI	95712	95460	95462	2	250
8	NAGPUR	37113	37100	37102	2	11
9	BEED	35310	35254	35255	1	55
10	GADCHIROLI	31698	31611	31612	1	86
11	PALGHAR	35312	35184	35185	1	127
12	SANGLI	21932	21780	21781	1	151
13	AKOLA	48792	48778	48778	0	14
14	AURANGABAD	36795	36666	36666	0	129
15	BHANDARA	65113	65092	65092	0	21
16	BULDHANA	44767	44732	44732	0	35
17	CHANDRAPUR	43124	43010	43010	0	114
18	GONDIA	96492	96142	96142	0	350
19	HINGOLI	18109	18083	18083	0	26
20	JALGAON	79749	79423	79423	0	326
21	KOLHAPUR	17685	17685	17685	0	0
22	NANDED	69533	69460	69460	0	73
23	NANDURBAR	119521	118941	118941	0	580
24	PARBHANI	19097	19060	19060	0	37
25	PUNE	20544	20531	20531	0	13
26	RAIGAD	9831	9822	9822	0	9
27	RATNAGIRI	9896	9890	9890	0	6
28	SINDHUDURG	5142	5142	5142	0	0
29	THANE	9605	9599	9599	0	6
30	WARDHA	18645	18621	18621	0	24
31	WASHIM	20404	20397	20397	0	7
32	SATARA	15360	15361	15357	-4	3
33	LATUR	20687	20564	20511	-53	176
34	SOLAPUR	49468	49137	48854	-283	614
<b>Total</b>		<b>1414842</b>	<b>1411424</b>	<b>1411163</b>	<b>79</b>	<b>3679</b>

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
SATARA	3
RATNAGIRI	6
THANE	6
WASHIM	7
RAIGAD	9
NAGPUR	11
PUNE	13
AKOLA	14
JALNA	17
BHANDARA	21
WARDHA	24
HINGOLI	26
NASHIK	30
BULDHANA	35
PARBHANI	37
AHMEDNAGAR	38
BEED	55
DHULE	64
NANDED	73
GADCHIROLI	86
OSMANABAD	112
CHANDRAPUR	114
PALGHAR	127
AURANGABAD	129
SANGLI	151
YAVATMAL	175
LATUR	176
AMRAVATI	250
JALGAON	326
GONDIA	350
NANDURBAR	580
SOLAPUR	614

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	224	33	0
9	THANE	127	74	53	127	43	84	0
10	NANDED	362	277	85	362	242	120	0
11	BEED	212	101	111	212	72	140	0
12	SANGLI	437	143	294	431	141	290	6
13	PARBHANI	332	15	317	332	13	319	0
14	SATARA	1311	582	729	1309	630	679	2
15	NASHIK	1642	1454	188	1779	715	1064	-137
16	HINGOLI	1713	787	926	1713	466	1247	0
17	JALNA	1413	165	1248	1381	85	1296	32
18	WARDHA	2819	1284	1535	2819	1216	1603	0
19	GONDIA	2450	2450	0	2450	765	1685	0
20	NAGPUR	5134	3397	1737	5088	3400	1688	46
21	CHANDRAPUR	2791	1463	1328	2752	965	1787	39
22	PUNE	2925	992	1933	2925	885	2040	0
23	LATUR	2320	13	2307	2320	6	2314	0
24	OSMANABAD	2470	104	2366	2470	56	2414	0
25	YAVATMAL	3437	1119	2318	3575	1094	2481	-138
26	BHANDARA	5825	3230	2595	5820	3213	2607	5
27	WASHIM	3477	865	2612	3477	850	2627	0
28	AURANGABAD	3328	1779	1549	3328	288	3040	0
29	AKOLA	7074	3842	3232	7074	3844	3230	0
30	AHMEDNAGAR	7762	4828	2934	7757	3286	4471	5
31	JALGAON	22889	20580	2309	22764	16486	6278	125
32	SOLAPUR	7960	2595	5365	7660	792	6868	300
33	BULDHANA	15256	8455	6801	15256	6953	8303	0
34	AMRAVATI	21560	11238	10322	21560	5844	15716	0
	<b>Total</b>	<b>127769</b>	<b>72575</b>	<b>55194</b>	<b>127484</b>	<b>53060</b>	<b>74424</b>	<b>285</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	17.04.2023	18.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK DIV.	413738	327645	328018	373	85720	299	1786
2	AMRAVATI DIV.	274549	185214	185435	221	89114	190	1857
3	AURANGABAD DIV.	237451	138840	138976	136	98475	211	2052
4	NAGPUR DIV.	291579	237079	237211	132	54368	195	1133
5	PUNE DIV.	124208	87075	87155	80	37053	65	772
6	KONKAN DIV.	69638	57143	57188	45	12450	52	259
<b>Total</b>		<b>1411163</b>	<b>1032996</b>	<b>1033983</b>	<b>987</b>	<b>377180</b>	<b>1012</b>	<b>7858</b>

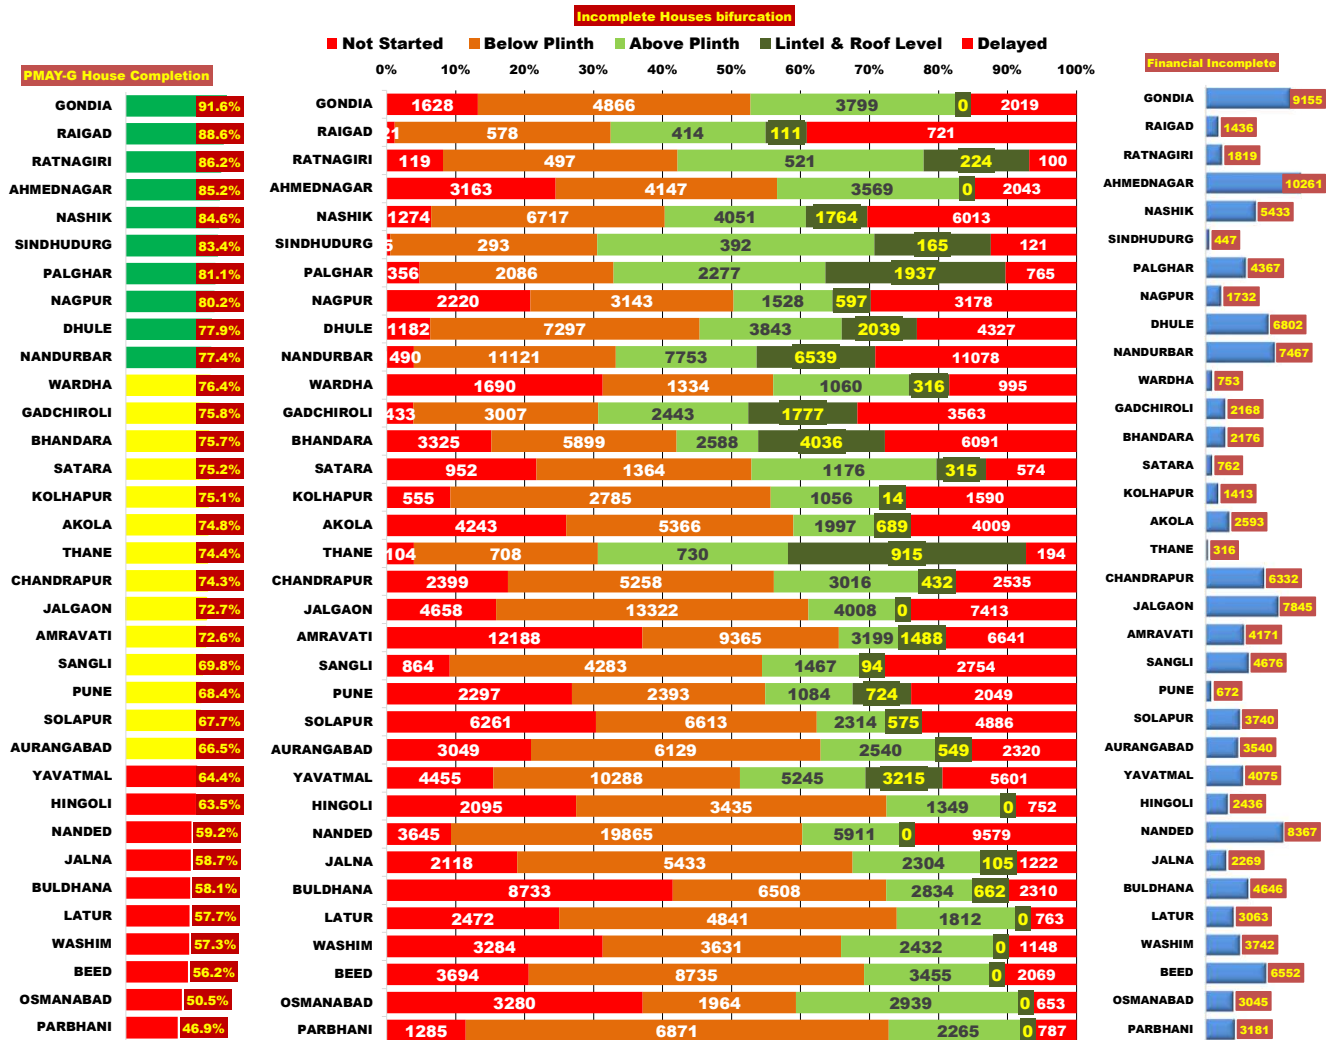

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	17.04.2023	18.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDURBAR	118941	91901	92038	137	26903	42	560
2	NASHIK	89705	75809	75899	90	13806	61	288
3	YAVATMAL	65180	41905	41983	78	23197	58	483
4	DHULE	64915	50478	50554	76	14361	51	299
5	WASHIM	20397	11642	11695	53	8702	25	181
6	AHMEDNAGAR	60754	51732	51772	40	8982	92	187
7	BHANDARA	65092	49206	49244	38	15848	35	330
8	AMRAVATI	95462	69231	69268	37	26194	51	546
9	SOLAPUR	48854	33054	33091	37	15763	21	328
10	AKOLA	48778	36448	36483	35	12295	23	256
11	AURANGABAD	36666	24364	24399	35	12267	35	256
12	GONDIA	96142	88030	88062	32	8080	70	168
13	JALGAON	79423	57725	57755	30	21668	53	451
14	NANDED	69460	41103	41128	25	28332	52	590
15	CHANDRAPUR	43010	31936	31958	22	11052	38	230
16	BULDHANA	44732	25988	26006	18	18726	33	390
17	OSMANABAD	14394	7257	7275	18	7119	17	148
18	NAGPUR	37102	29732	29749	17	7353	12	153
19	RATNAGIRI	9890	8512	8529	17	1361	16	28
20	SATARA	15357	11534	11550	16	3807	15	79
21	GADCHIROLI	31612	23962	23977	15	7635	28	159
22	JALNA	24022	14077	14092	15	9930	24	207
23	LATUR	20511	11822	11837	15	8674	23	181
24	PALGHAR	35185	28514	28529	15	6656	24	139
25	BEED	35255	19802	19815	13	15440	24	322
26	PARBHANI	19060	8935	8947	12	10113	19	211
27	KOLHAPUR	17685	13265	13275	10	4410	8	92
28	SANGLI	21781	15196	15206	10	6575	12	137
29	SINDHUDURG	5142	4277	4287	10	855	4	18
30	WARDHA	18621	14213	14221	8	4400	11	92
31	PUNE	20531	14026	14033	7	6498	10	135
32	HINGOLI	18083	11480	11483	3	6600	17	138
33	RAIGAD	9822	8698	8701	3	1121	4	23
34	THANE	9599	7142	7142	0	2457	4	51
<b>Total</b>		<b>1411163</b>	<b>1032996</b>	<b>1033983</b>	<b>987</b>	<b>377180</b>	<b>1012</b>	<b>7858</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	17.04.2023	18.04.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118393	89655	89925	270	28468
2	AURANGABAD DIV.	199331	164457	164623	166	34708
3	NASHIK DIV.	141360	110162	110309	147	31051
4	AMRAVATI DIV.	109702	93510	93513	3	16189
5	KONKAN DIV.	34732	30943	30943	0	3789
6	PUNE DIV.	65334	62993	62993	0	2341
<b>Total</b>		<b>668852</b>	<b>551720</b>	<b>552306</b>	<b>586</b>	<b>116546</b>


Sr. No.	District	Target	17.04.2023	18.04.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	24080	24275	195	16010
2	HINGOLI	27298	15306	15467	161	11831
3	DHULE	21790	17708	17854	146	3936
4	NAGPUR	16291	11021	11073	52	5218
5	WARDHA	13147	11170	11193	23	1954
6	BEED	26878	24796	24798	2	2080
7	BULDHANA	21616	19967	19969	2	1647
8	JALNA	20446	19183	19185	2	1261
9	AMRAVATI	23224	19699	19700	1	3524
10	LATUR	27171	26113	26114	1	1057
11	NASHIK	32035	22811	22812	1	9223
12	AHMEDNAGAR	35298	32973	32973	0	2325
13	AKOLA	23681	17691	17691	0	5990
14	AURANGABAD	26141	23795	23795	0	2346
15	BHANDARA	17590	15392	15392	0	2198
16	GADCHIROLI	16834	15197	15197	0	1637
17	GONDIA	14246	12795	12795	0	1451
18	JALGAON	25659	22535	22535	0	3124
19	KOLHAPUR	12565	12528	12528	0	37
20	NANDED	26760	20698	20698	0	6062
21	NANDURBAR	26578	14135	14135	0	12443
22	OSMANABAD	24853	16979	16979	0	7874
23	PALGHAR	11792	10974	10974	0	818
24	PARBHANI	19784	17587	17587	0	2197
25	PUNE	14672	12770	12770	0	1902
26	RAIGAD	7406	6228	6228	0	1178
27	RATNAGIRI	7129	6677	6677	0	452
28	SANGLI	8732	8603	8603	0	129
29	SATARA	10647	10647	10647	0	0
30	SINDHUDURG	2141	2107	2107	0	34
31	SOLAPUR	18718	18445	18445	0	273
32	THANE	6264	4957	4957	0	1307
33	WASHIM	11500	10055	10055	0	1445
34	YAVATMAL	29681	26098	26098	0	3583
<b>Total</b>		<b>668852</b>	<b>551720</b>	<b>552306</b>	<b>586</b>	<b>116546</b>

Remaining Sanction RANK

SATARA	0
SINDHUDURG	34
KOLHAPUR	37
SANGLI	129
SOLAPUR	273
RATNAGIRI	452
PALGHAR	818
LATUR	1057
RAIGAD	1178
JALNA	1261
THANE	1307
WASHIM	1445
GONDIA	1451
GADCHIROLI	1637
BULDHANA	1647
PUNE	1902
WARDHA	1954
BEED	2080
PARBHANI	2197
BHANDARA	2198
AHMEDNAGAR	2325
AURANGABAD	2346
JALGAON	3124
AMRAVATI	3524
YAVATMAL	3583
DHULE	3936
NAGPUR	5218
AKOLA	5990
NANDED	6062
OSMANABAD	7874
NASHIK	9223
HINGOLI	11831
NANDURBAR	12443
CHANDRAPUR	16010

## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	17.04.2023	18.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI DIV.	93513	64406	64494	88	29019	56	605
2	AURANGABAD DIV.	164623	103494	103560	66	61063	90	1272
3	NASHIK DIV.	110309	88720	88779	59	21530	72	449
4	NAGPUR DIV.	89925	69163	69208	45	20717	45	432
5	PUNE DIV.	62993	51846	51862	16	11131	25	232
6	KONKAN DIV.	30943	23553	23568	15	7375	15	154
<b>Total</b>		<b>552306</b>	<b>401182</b>	<b>401471</b>	<b>289</b>	<b>150835</b>	<b>303</b>	<b>3142</b>

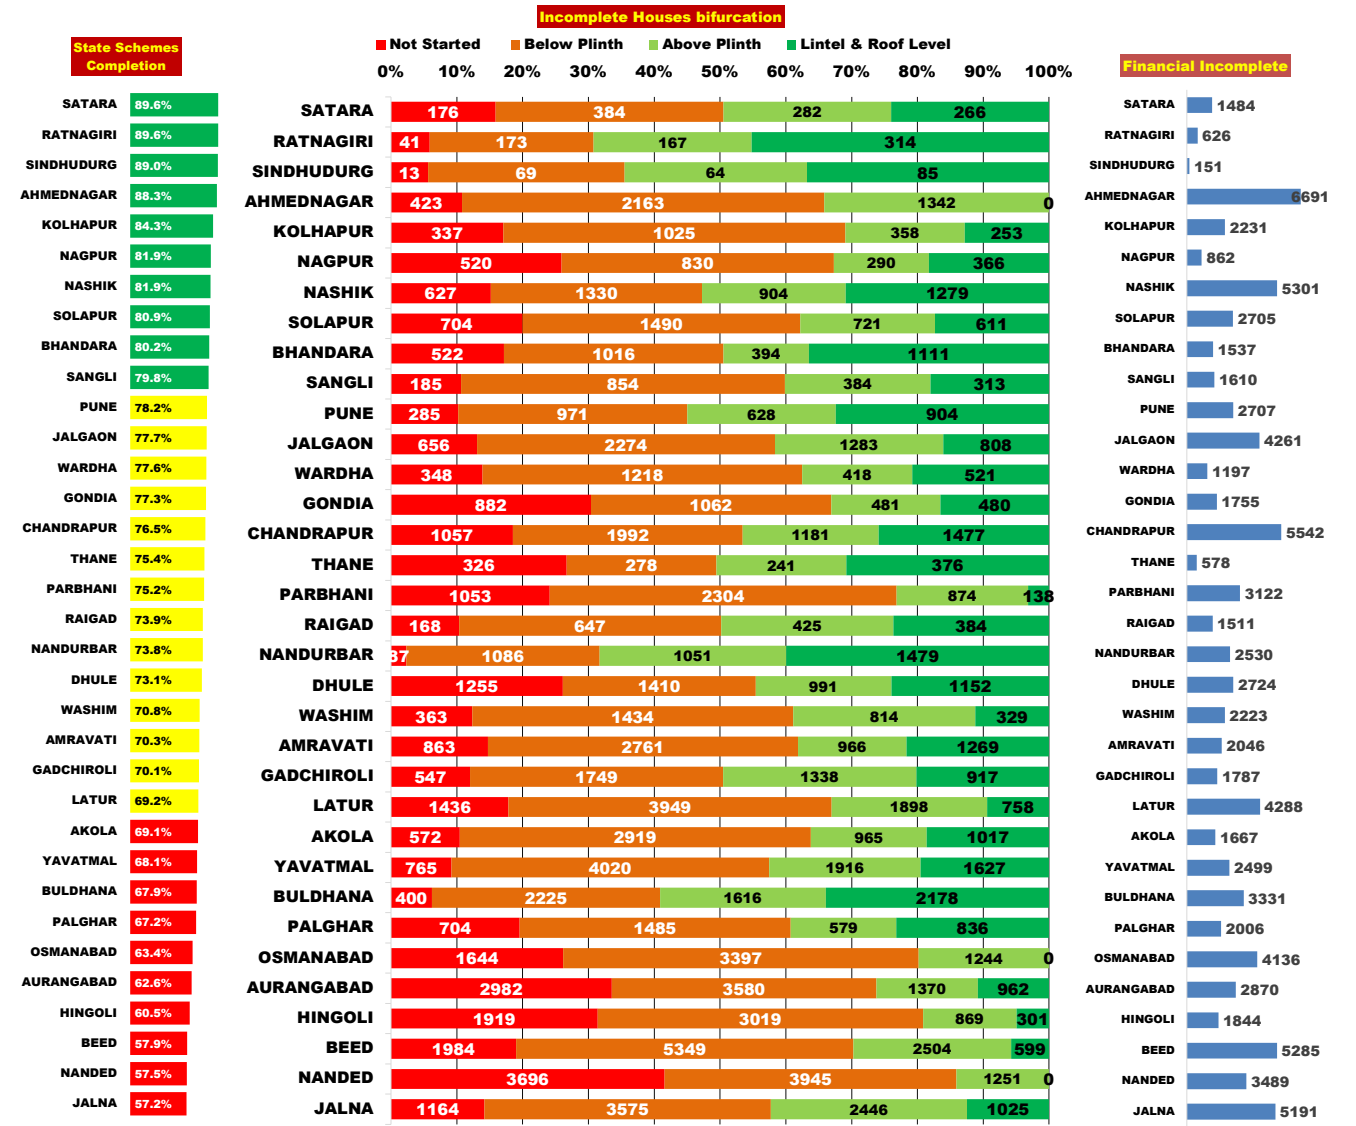



राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	17.04.2023	18.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	BULDHANA	19969	13519	13550	31	6419	17	134
2	LATUR	26114	18047	18073	26	8041	12	168
3	AMRAVATI	19700	13822	13841	19	5859	9	122
4	JALNA	19185	10956	10975	19	8210	26	171
5	DHULE	17854	13028	13046	18	4808	10	100
6	YAVATMAL	26098	17755	17770	15	8328	13	174
7	GONDIA	12795	9876	9890	14	2905	8	61
8	AKOLA	17691	12206	12218	12	5473	9	114
9	NANDURBAR	14135	10420	10432	12	3703	6	77
10	WASHIM	10055	7104	7115	11	2940	8	61
11	CHANDRAPUR	24275	18558	18568	10	5707	13	119
12	JALGAON	22535	17504	17514	10	5021	12	105
13	NASHIK	22812	18662	18672	10	4140	13	86
14	AHMEDNAGAR	32973	29106	29115	9	3858	30	80
15	BHANDARA	15392	12340	12349	9	3043	4	63
16	AURANGABAD	23795	14893	14901	8	8894	9	185
17	SANGLI	8603	6859	6867	8	1736	4	36
18	BEED	24798	14355	14362	7	10436	14	217
19	PALGHAR	10974	7363	7370	7	3604	6	75
20	NAGPUR	11073	9061	9067	6	2006	3	42
21	GADCHIROLI	15197	10642	10646	4	4551	9	95
22	SOLAPUR	18445	14915	14919	4	3526	7	73
23	THANE	4957	3732	3736	4	1221	2	25
24	HINGOLI	15467	9356	9359	3	6108	6	127
25	SATARA	10647	9536	9539	3	1108	6	23
26	NANDED	20698	11903	11905	2	8793	9	183
27	RATNAGIRI	6677	5980	5982	2	695	3	14
28	WARDHA	11193	8686	8688	2	2505	7	52
29	KOLHAPUR	12528	10554	10555	1	1973	3	41
30	PARBHANI	17587	13217	13218	1	4369	4	91
31	RAIGAD	6228	4603	4604	1	1624	3	34
32	SINDHUDURG	2107	1875	1876	1	231	1	5
33	OSMANABAD	16979	10767	10767	0	6212	11	129
34	PUNE	12770	9982	9982	0	2788	6	58
<b>Total</b>		<b>552306</b>	<b>401182</b>	<b>401471</b>	<b>289</b>	<b>150835</b>	<b>303</b>	<b>3142</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	11767	0	42604	0	23224
2	AMRAVATI DIV.	0	32837	0	35158	0	15707
3	AURANGABAD DIV.	0	21608	0	57273	0	22575
4	NAGPUR DIV.	0	11482	0	23507	0	14434
5	KONKAN DIV.	0	602	0	4162	0	4334
6	PUNE DIV.	0	10796	0	17438	0	7097
	<b>Total</b>	<b>0</b>	<b>89092</b>	<b>0</b>	<b>180142</b>	<b>0</b>	<b>87371</b>

PMAY-G 1st Ins Pending

SINDHUDURG	5
RAIGAD	18
THANE	104
RATNAGIRI	119
PALGHAR	356
GADCHIROLI	408
KOLHAPUR	555
SANGLI	731
SATARA	952
DHULE	1182
NASHIK	1274
PARBHANI	1285
NANDURBAR	1490
GONDIA	1628
WARDHA	1690
NAGPUR	2085
JALNA	2088
HINGOLI	2095
PUNE	2297
CHANDRAPUR	2346
LATUR	2472
AURANGABAD	3049
AHMEDNAGAR	3163
OSMANABAD	3280
WASHIM	3281
BHANDARA	3325
NANDED	3645
BEED	3694
AKOLA	4243
YAVATMAL	4449
JALGAON	4658
SOLAPUR	6261
BULDHANA	8722
AMRAVATI	12142

PMAY-G 2nd Ins Pending

SINDHUDURG	293
RATNAGIRI	497
RAIGAD	578
THANE	708
WARDHA	1334
SATARA	1364
OSMANABAD	1964
PALGHAR	2086
PUNE	2393
KOLHAPUR	2785
GADCHIROLI	3007
NAGPUR	3143
HINGOLI	3435
WASHIM	3631
AHMEDNAGAR	4147
SANGLI	4283
LATUR	4841
GONDIA	4866
CHANDRAPUR	5258
AKOLA	5366
JALNA	5433
BHANDARA	5899
AURANGABAD	6129
BULDHANA	6508
SOLAPUR	6613
NASHIK	6717
PARBHANI	6871
DHULE	7297
BEED	8735
AMRAVATI	9365
YAVATMAL	10288
NANDURBAR	11121
JALGAON	13322
NANDED	19865

PMAY-G 3rd Ins Pending

SINDHUDURG	392
RAIGAD	414
RATNAGIRI	521
THANE	730
KOLHAPUR	1056
WARDHA	1060
PUNE	1084
SATARA	1176
HINGOLI	1349
SANGLI	1467
NAGPUR	1528
LATUR	1812
AKOLA	1997
PARBHANI	2265
PALGHAR	2277
JALNA	2304
SOLAPUR	2314
WASHIM	2432
GADCHIROLI	2443
AURANGABAD	2540
BHANDARA	2588
BULDHANA	2834
OSMANABAD	2939
CHANDRAPUR	3016
AMRAVATI	3199
BEED	3455
AHMEDNAGAR	3569
GONDIA	3799
DHULE	3843
JALGAON	4008
NASHIK	4051
YAVATMAL	5245
NANDED	5911
NANDURBAR	7753

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3163	0	4147	0	3569
2	AKOLA	0	4243	0	5366	0	1997
3	AURANGABAD	0	3049	0	6129	0	2540
4	BEED	0	3694	0	8735	0	3455
5	BHANDARA	0	3325	0	5899	0	2588
6	BULDHANA	0	8722	0	6508	0	2834
7	CHANDRAPUR	0	2346	0	5258	0	3016
8	DHULE	0	1182	0	7297	0	3843
9	GADCHIROLI	0	408	0	3007	0	2443
10	GONDIA	0	1628	0	4866	0	3799
11	HINGOLI	0	2095	0	3435	0	1349
12	JALGAON	0	4658	0	13322	0	4008
13	JALNA	0	2088	0	5433	0	2304
14	KOLHAPUR	0	555	0	2785	0	1056
15	LATUR	0	2472	0	4841	0	1812
16	NAGPUR	0	2085	0	3143	0	1528
17	NANDED	0	3645	0	19865	0	5911
18	NANDURBAR	0	1490	0	11121	0	7753
19	NASHIK	0	1274	0	6717	0	4051
20	OSMANABAD	0	3280	0	1964	0	2939
21	PALGHAR	0	356	0	2086	0	2277
22	PARBHANI	0	1285	0	6871	0	2265
23	PUNE	0	2297	0	2393	0	1084
24	RAIGAD	0	18	0	578	0	414
25	RATNAGIRI	0	119	0	497	0	521
26	SANGLI	0	731	0	4283	0	1467
27	SINDHUDURG	0	5	0	293	0	392
28	SOLAPUR	0	6261	0	6613	0	2314
29	THANE	0	104	0	708	0	730
30	WARDHA	0	1690	0	1334	0	1060
31	WASHIM	0	3281	0	3631	0	2432
32	YAVATMAL	0	4449	0	10288	0	5245
33	AMRAVATI	-1	12142	0	9365	0	3199
34	SATARA	-1	952	0	1364	0	1176
	<b>Total</b>	<b>0</b>	<b>89092</b>	<b>0</b>	<b>180142</b>	<b>0</b>	<b>87371</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AMRAVATI DIV.	37	2963	56	13359	47	6277
2	KONKAN DIV.	1	1252	6	2652	23	1476
3	NAGPUR DIV.	1	3876	5	7867	3	4102
4	PUNE DIV.	0	1687	2	4724	4	2373
5	NASHIK DIV.	0	3048	1	8263	4	5571
6	AURANGABAD DIV.	0	15878	0	29118	0	12456
<b>Total</b>		<b>39</b>	<b>28704</b>	<b>70</b>	<b>65983</b>	<b>81</b>	<b>32255</b>

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	41
NANDURBAR	87
RAIGAD	168
SATARA	176
SANGLI	185
PUNE	285
THANE	326
KOLHAPUR	337
WARDHA	348
WASHIM	363
BULDHANA	400
AHMEDNAGAR	423
NAGPUR	520
BHANDARA	522
GADCHIROLI	547
AKOLA	572
NASHIK	627
JALGAON	656
PALGHAR	704
SOLAPUR	704
YAVATMAL	765
AMRAVATI	863
GONDIA	882
PARBHANI	1053
CHANDRAPUR	1057
JALNA	1164
DHULE	1255
LATUR	1436
OSMANABAD	1644
HINGOLI	1919
BEED	1984
AURANGABAD	2982
NANDED	3696

State Schemes 2nd Ins Pending

SINDHUDURG	69
RATNAGIRI	173
THANE	278
SATARA	384
RAIGAD	647
NAGPUR	830
SANGLI	854
PUNE	971
BHANDARA	1016
KOLHAPUR	1025
GONDIA	1062
NANDURBAR	1086
WARDHA	1218
NASHIK	1330
DHULE	1410
WASHIM	1434
PALGHAR	1485
SOLAPUR	1490
GADCHIROLI	1749
CHANDRAPUR	1992
AHMEDNAGAR	2163
BULDHANA	2225
JALGAON	2274
PARBHANI	2304
AMRAVATI	2761
AKOLA	2919
HINGOLI	3019
OSMANABAD	3397
JALNA	3575
AURANGABAD	3580
NANDED	3945
LATUR	3949
YAVATMAL	4020
BEED	5349

State Schemes 3rd Ins Pending

SINDHUDURG	64
RATNAGIRI	167
THANE	241
SATARA	282
NAGPUR	290
KOLHAPUR	358
SANGLI	384
BHANDARA	394
WARDHA	418
RAIGAD	425
GONDIA	481
PALGHAR	579
PUNE	628
SOLAPUR	721
WASHIM	814
HINGOLI	869
PARBHANI	874
NASHIK	904
AKOLA	965
AMRAVATI	966
DHULE	991
NANDURBAR	1051
CHANDRAPUR	1181
OSMANABAD	1244
NANDED	1251
JALGAON	1283
GADCHIROLI	1338
AHMEDNAGAR	1342
AURANGABAD	1370
BULDHANA	1616
LATUR	1898
YAVATMAL	1916
JALNA	2446
BEED	2504

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	YAVATMAL	24	765	52	4020	47	1916
2	AMRAVATI	13	863	3	2761	0	966
3	PALGHAR	1	704	4	1485	9	579
4	RAIGAD	0	168	2	647	11	425
5	KOLHAPUR	0	337	2	1025	4	358
6	WARDHA	0	348	3	1218	1	418
7	CHANDRAPUR	1	1057	0	1992	2	1181
8	NASHIK	0	627	1	1330	2	904
9	RATNAGIRI	0	41	0	173	3	167
10	DHULE	0	1255	0	1410	2	991
11	NAGPUR	0	520	2	830	0	290
12	BULDHANA	0	400	1	2225	0	1616
13	AHMEDNAGAR	0	423	0	2163	0	1342
14	AKOLA	0	572	0	2919	0	965
15	AURANGABAD	0	2982	0	3580	0	1370
16	BEED	0	1984	0	5349	0	2504
17	BHANDARA	0	522	0	1016	0	394
18	GADCHIROLI	0	547	0	1749	0	1338
19	GONDIA	0	882	0	1062	0	481
20	HINGOLI	0	1919	0	3019	0	869
21	JALGAON	0	656	0	2274	0	1283
22	JALNA	0	1164	0	3575	0	2446
23	LATUR	0	1436	0	3949	0	1898
24	NANDED	0	3696	0	3945	0	1251
25	NANDURBAR	0	87	0	1086	0	1051
26	OSMANABAD	0	1644	0	3397	0	1244
27	PARBHANI	0	1053	0	2304	0	874
28	PUNE	0	285	0	971	0	628
29	SANGLI	0	185	0	854	0	384
30	SINDHUDURG	0	13	0	69	0	64
31	SOLAPUR	0	704	0	1490	0	721
32	THANE	0	326	0	278	0	241
33	WASHIM	0	363	0	1434	0	814
34	SATARA	-1	176	0	384	0	282
	<b>Total</b>	<b>39</b>	<b>28704</b>	<b>70</b>	<b>65983</b>	<b>81</b>	<b>32255</b>

## प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

