



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २०.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

| योजना | एकूण मंजूरी | दैनिक मंजूरी | एकूण पूर्ण | दैनिक पूर्ण घरकुले | दैनिक पहिला हप्ता वितरित | दैनिक दुसरा हप्ता वितरित | दैनिक तिसरा हप्ता वितरित |
|---------------------------------|-------------|--------------|------------|--------------------|--------------------------|--------------------------|--------------------------|
| प्रधानमंत्री आवास योजना ग्रामीण | १४१०९१९ | ५४ | १०३५३८७ | ७२६ | ० | ० | ० |
| राज्य योजना | ५५३८८४ | ४८९ | ४०२१४० | ३९८ | ० | -१ | ० |
| एकूण | १९६४८०३ | ५४३ | १४३७५२७ | ११२४ | ० | -१ | ० |

PMAY-G Completion Progress Bar

73.4%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.6%


State Schemes: Incomplete Houses bifurcation

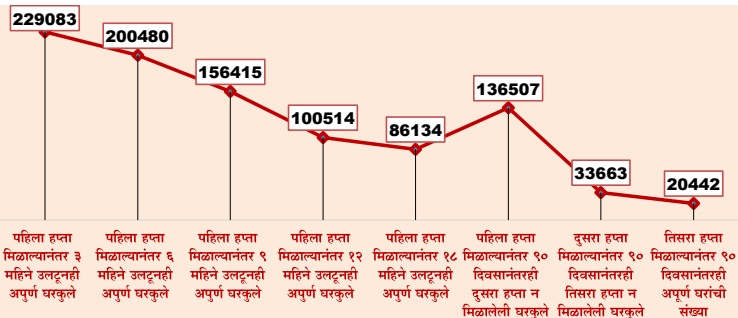

Abhiyan Achievement Day 151

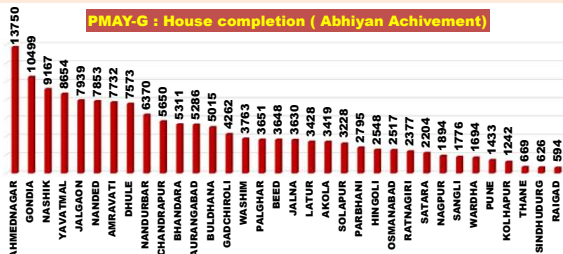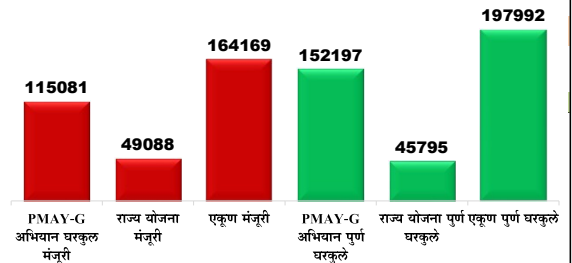

State Schemes: House completion (Abhiyan Achievement)



राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण

४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

| Sr. No. | Division | Target (PWL+Awaas Plus) | 19.04.2023 | 20.04.2023 | Daily Achievement | Remaining |
|--------------|-----------------|-------------------------|----------------|----------------|-------------------|-------------|
| 1 | AMRAVATI DIV. | 275030 | 274552 | 274560 | 27 | 470 |
| 2 | NASHIK DIV. | 414763 | 413720 | 413737 | 17 | 1026 |
| 3 | AURANGABAD DIV. | 238068 | 237409 | 237416 | 7 | 652 |
| 4 | NAGPUR DIV. | 292127 | 291575 | 291513 | 3 | 614 |
| 5 | KONKAN DIV. | 69785 | 69638 | 69636 | 0 | 149 |
| 6 | PUNE DIV. | 124898 | 124215 | 124057 | 0 | 841 |
| Total | | 1414671 | 1411109 | 1410919 | 54 | 3752 |

| Sr. No. | District | Target (PWL+Awaas Plus) | 19.04.2023 | 20.04.2023 | Daily Achievement | Remaining |
|--------------|------------|-------------------------|----------------|----------------|-------------------|-------------|
| 1 | YAVATMAL | 65355 | 65182 | 65206 | 24 | 149 |
| 2 | NANDURBAR | 119521 | 118941 | 118949 | 8 | 572 |
| 3 | OSMANABAD | 14506 | 14394 | 14401 | 7 | 105 |
| 4 | AHMEDNAGAR | 60792 | 60758 | 60761 | 3 | 31 |
| 5 | CHANDRAPUR | 43124 | 43010 | 43013 | 3 | 111 |
| 6 | JALGAON | 79749 | 79446 | 79449 | 3 | 300 |
| 7 | NASHIK | 89722 | 89658 | 89661 | 3 | 61 |
| 8 | WASHIM | 20404 | 20397 | 20399 | 2 | 5 |
| 9 | AMRAVATI | 95712 | 95463 | 95464 | 1 | 248 |
| 10 | AKOLA | 48792 | 48778 | 48778 | 0 | 14 |
| 11 | AURANGABAD | 36795 | 36666 | 36666 | 0 | 129 |
| 12 | BEED | 35310 | 35253 | 35253 | 0 | 57 |
| 13 | DHULE | 64979 | 64917 | 64917 | 0 | 62 |
| 14 | GADCHIROLI | 31698 | 31618 | 31618 | 0 | 80 |
| 15 | GONDIA | 96492 | 96142 | 96142 | 0 | 350 |
| 16 | HINGOLI | 18109 | 18083 | 18083 | 0 | 26 |
| 17 | JALNA | 24039 | 24022 | 24022 | 0 | 17 |
| 18 | KOLHAPUR | 17685 | 17685 | 17685 | 0 | 0 |
| 19 | LATUR | 20679 | 20471 | 20471 | 0 | 208 |
| 20 | NANDED | 69533 | 69460 | 69460 | 0 | 73 |
| 21 | PALGHAR | 35312 | 35185 | 35185 | 0 | 127 |
| 22 | PARBHANI | 19097 | 19060 | 19060 | 0 | 37 |
| 23 | PUNE | 20544 | 20531 | 20531 | 0 | 13 |
| 24 | RAIGAD | 9831 | 9822 | 9822 | 0 | 9 |
| 25 | SANGLI | 21932 | 21782 | 21782 | 0 | 150 |
| 26 | SINDHUDURG | 5142 | 5142 | 5142 | 0 | 0 |
| 27 | THANE | 9605 | 9599 | 9599 | 0 | 6 |
| 28 | RATNAGIRI | 9895 | 9890 | 9888 | -2 | 7 |
| 29 | WARDHA | 18644 | 18621 | 18617 | -4 | 27 |
| 30 | BHANDARA | 65091 | 65082 | 65066 | -16 | 25 |
| 31 | BULDHANA | 44767 | 44732 | 44713 | -19 | 54 |
| 32 | SATARA | 15353 | 15355 | 15328 | -27 | 25 |
| 33 | NAGPUR | 37078 | 37102 | 37057 | -45 | 21 |
| 34 | SOLAPUR | 49384 | 48862 | 48731 | -131 | 653 |
| Total | | 1414671 | 1411109 | 1410919 | 54 | 3752 |

Remaining Sanction RANK


| | |
|------------|-----|
| KOLHAPUR | 0 |
| SINDHUDURG | 0 |
| WASHIM | 5 |
| THANE | 6 |
| RATNAGIRI | 7 |
| RAIGAD | 9 |
| PUNE | 13 |
| AKOLA | 14 |
| JALNA | 17 |
| NAGPUR | 21 |
| BHANDARA | 25 |
| SATARA | 25 |
| HINGOLI | 26 |
| WARDHA | 27 |
| AHMEDNAGAR | 31 |
| PARBHANI | 37 |
| BULDHANA | 54 |
| BEED | 57 |
| NASHIK | 61 |
| DHULE | 62 |
| NANDED | 73 |
| GADCHIROLI | 80 |
| OSMANABAD | 105 |
| CHANDRAPUR | 111 |
| PALGHAR | 127 |
| AURANGABAD | 129 |
| YAVATMAL | 149 |
| SANGLI | 150 |
| LATUR | 208 |
| AMRAVATI | 248 |
| JALGAON | 300 |
| GONDIA | 350 |
| NANDURBAR | 572 |
| SOLAPUR | 653 |

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

| Sr. No. | District | Google Sheet Report | | | AwaasSoft Report | | | |
|---------|--------------|---------------------|---------------|--------------|--|--------------------------------------|--------------------|-------------------------------|
| | | Total Landless | Provided land | Remaining | Landless beneficiaries tagged in AwaasSoft | Landless beneficiaries provided land | Remaining Landless | Remaining Tag (provided land) |
| 1 | DHULE | 18 | 18 | 0 | 18 | 18 | 0 | 0 |
| 2 | GADCHIROLI | 8 | 8 | 0 | 8 | 8 | 0 | 0 |
| 3 | NANDURBAR | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 4 | PALGHAR | 11 | 11 | 0 | 11 | 11 | 0 | 0 |
| 5 | RAIGAD | 6 | 6 | 0 | 6 | 6 | 0 | 0 |
| 6 | RATNAGIRI | 23 | 23 | 0 | 23 | 23 | 0 | 0 |
| 7 | SINDHUDURG | 420 | 420 | 0 | 420 | 420 | 0 | 0 |
| 8 | KOLHAPUR | 257 | 257 | 0 | 257 | 224 | 33 | 33 |
| 9 | THANE | 127 | 74 | 53 | 127 | 43 | 84 | 31 |
| 10 | NANDED | 362 | 277 | 85 | 362 | 242 | 120 | 35 |
| 11 | BEED | 212 | 101 | 111 | 212 | 72 | 140 | 29 |
| 12 | SANGLI | 431 | 143 | 288 | 431 | 141 | 290 | 2 |
| 13 | PARBHANI | 332 | 15 | 317 | 332 | 13 | 319 | 2 |
| 14 | SATARA | 1309 | 598 | 711 | 1307 | 628 | 679 | -30 |
| 15 | NASHIK | 1804 | 1454 | 350 | 1804 | 715 | 1089 | 739 |
| 16 | HINGOLI | 1713 | 787 | 926 | 1713 | 466 | 1247 | 321 |
| 17 | JALNA | 1413 | 165 | 1248 | 1381 | 85 | 1296 | 80 |
| 18 | WARDHA | 2819 | 1284 | 1535 | 2814 | 1216 | 1598 | 68 |
| 19 | NAGPUR | 5134 | 3397 | 1737 | 5065 | 3414 | 1651 | -17 |
| 20 | GONDIA | 2450 | 2450 | 0 | 2450 | 765 | 1685 | 1685 |
| 21 | CHANDRAPUR | 2791 | 1463 | 1328 | 2752 | 965 | 1787 | 498 |
| 22 | PUNE | 2925 | 992 | 1933 | 2925 | 885 | 2040 | 107 |
| 23 | LATUR | 2299 | 68 | 2231 | 2299 | 66 | 2233 | 2 |
| 24 | OSMANABAD | 2470 | 104 | 2366 | 2470 | 56 | 2414 | 48 |
| 25 | YAVATMAL | 3437 | 1119 | 2318 | 3575 | 1094 | 2481 | 25 |
| 26 | BHANDARA | 5825 | 3230 | 2595 | 5800 | 3213 | 2587 | 17 |
| 27 | WASHIM | 3477 | 865 | 2612 | 3477 | 850 | 2627 | 15 |
| 28 | AURANGABAD | 3328 | 1779 | 1549 | 3328 | 288 | 3040 | 1491 |
| 29 | AKOLA | 7074 | 3842 | 3232 | 7074 | 3844 | 3230 | -2 |
| 30 | AHMEDNAGAR | 7762 | 4828 | 2934 | 7756 | 3365 | 4391 | 1463 |
| 31 | JALGAON | 22889 | 20580 | 2309 | 22881 | 17556 | 5325 | 3024 |
| 32 | SOLAPUR | 7960 | 2595 | 5365 | 7511 | 792 | 6719 | 1803 |
| 33 | BULDHANA | 15256 | 8455 | 6801 | 15235 | 6953 | 8282 | 1502 |
| 34 | AMRAVATI | 21560 | 11238 | 10322 | 21560 | 9827 | 11733 | 1411 |
| | Total | 127902 | 72646 | 55256 | 127384 | 58264 | 69120 | 14431 |

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | Division | Sanction | 19.04.2023 | 20.04.2023 | Daily Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|-----------------|----------------|----------------|----------------|-------------------|---------------|---|--|
| 1 | AMRAVATI DIV. | 274560 | 185558 | 185740 | 182 | 88820 | 189 | 1931 |
| 2 | AURANGABAD DIV. | 237416 | 139111 | 139266 | 155 | 98150 | 210 | 2134 |
| 3 | NASHIK DIV. | 413737 | 328172 | 328313 | 141 | 85424 | 297 | 1857 |
| 4 | NAGPUR DIV. | 291513 | 237339 | 237438 | 99 | 54075 | 194 | 1176 |
| 5 | KONKAN DIV. | 69636 | 57244 | 57325 | 81 | 12311 | 52 | 268 |
| 6 | PUNE DIV. | 124057 | 87237 | 87305 | 68 | 36752 | 65 | 799 |
| Total | | 1410919 | 1034661 | 1035387 | 726 | 375532 | 1008 | 8164 |

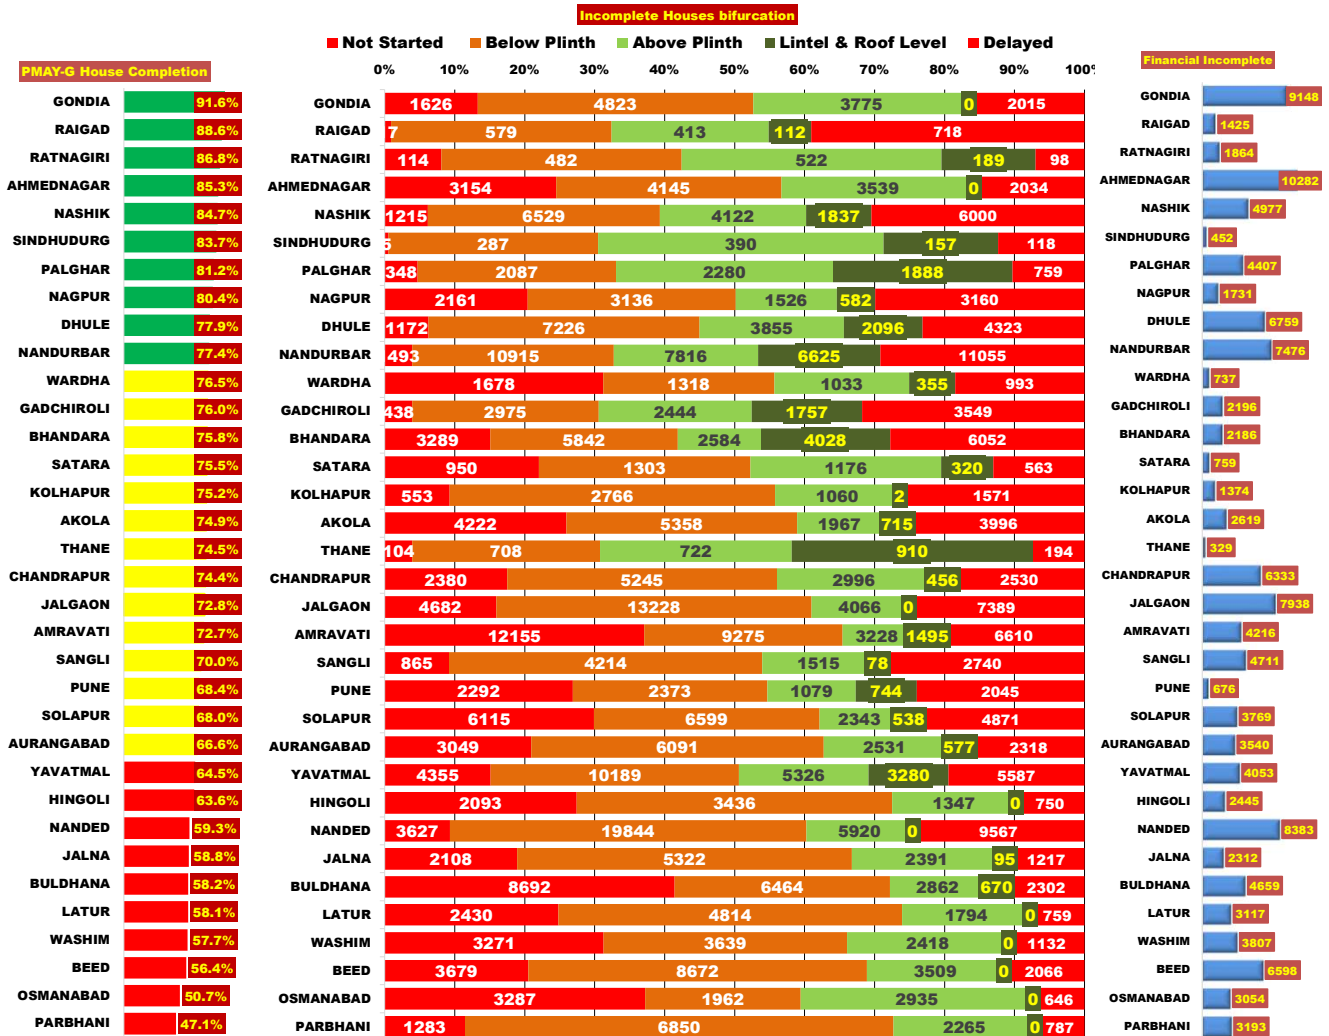

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | District | Sanction | 19.04.2023 | 20.04.2023 | Daily Achievement | Remaining | Aug. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|------------|----------------|----------------|----------------|-------------------|---------------|---|--|
| 1 | AMRAVATI | 95464 | 69290 | 69357 | 67 | 26107 | 51 | 568 |
| 2 | JALGAON | 79449 | 57806 | 57857 | 51 | 21592 | 53 | 469 |
| 3 | YAVATMAL | 65206 | 42011 | 42062 | 51 | 23144 | 57 | 503 |
| 4 | PALGHAR | 35185 | 28546 | 28582 | 36 | 6603 | 24 | 144 |
| 5 | JALNA | 24022 | 14101 | 14136 | 35 | 9886 | 24 | 215 |
| 6 | LATUR | 20471 | 11868 | 11902 | 34 | 8569 | 23 | 186 |
| 7 | BHANDARA | 65066 | 49291 | 49323 | 32 | 15743 | 35 | 342 |
| 8 | NANDED | 69460 | 41131 | 41163 | 32 | 28297 | 52 | 615 |
| 9 | NANDURBAR | 118949 | 92068 | 92100 | 32 | 26849 | 42 | 584 |
| 10 | NASHIK | 89661 | 75926 | 75958 | 32 | 13703 | 61 | 298 |
| 11 | RATNAGIRI | 9888 | 8549 | 8581 | 32 | 1307 | 16 | 28 |
| 12 | WASHIM | 20399 | 11737 | 11769 | 32 | 8630 | 25 | 188 |
| 13 | GADCHIROLI | 31618 | 24001 | 24029 | 28 | 7589 | 28 | 165 |
| 14 | BEED | 35253 | 19849 | 19876 | 27 | 15377 | 24 | 334 |
| 15 | AHMEDNAGAR | 60761 | 51806 | 51830 | 24 | 8931 | 91 | 194 |
| 16 | NAGPUR | 37057 | 29763 | 29787 | 24 | 7270 | 13 | 158 |
| 17 | SATARA | 15328 | 11555 | 11579 | 24 | 3749 | 15 | 82 |
| 18 | KOLHAPUR | 17685 | 13285 | 13304 | 19 | 4381 | 8 | 95 |
| 19 | AKOLA | 48778 | 36498 | 36516 | 18 | 12262 | 23 | 267 |
| 20 | BULDHANA | 44713 | 26022 | 26036 | 14 | 18677 | 33 | 406 |
| 21 | SANGLI | 21782 | 15229 | 15243 | 14 | 6539 | 12 | 142 |
| 22 | AURANGABAD | 36666 | 24405 | 24418 | 13 | 12248 | 35 | 266 |
| 23 | HINGOLI | 18083 | 11497 | 11506 | 9 | 6577 | 17 | 143 |
| 24 | SINDHUDURG | 5142 | 4295 | 4303 | 8 | 839 | 4 | 18 |
| 25 | CHANDRAPUR | 43013 | 31982 | 31989 | 7 | 11024 | 37 | 240 |
| 26 | PUNE | 20531 | 14037 | 14043 | 6 | 6488 | 9 | 141 |
| 27 | WARDHA | 18617 | 14227 | 14233 | 6 | 4384 | 11 | 95 |
| 28 | PARBHANI | 19060 | 8963 | 8968 | 5 | 10092 | 19 | 219 |
| 29 | SOLAPUR | 48731 | 33131 | 33136 | 5 | 15595 | 21 | 339 |
| 30 | RAIGAD | 9822 | 8701 | 8704 | 3 | 1118 | 4 | 24 |
| 31 | DHULE | 64917 | 50566 | 50568 | 2 | 14349 | 50 | 312 |
| 32 | GONDIA | 96142 | 88075 | 88077 | 2 | 8065 | 70 | 175 |
| 33 | THANE | 9599 | 7153 | 7155 | 2 | 2444 | 4 | 53 |
| 34 | OSMANABAD | 14401 | 7297 | 7297 | 0 | 7104 | 17 | 154 |
| Total | | 1410919 | 1034661 | 1035387 | 726 | 375532 | 1008 | 8164 |

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

| Sr. No. | Division | Target | 19.04.2023 | 20.04.2023 | Daily_Achievement | Remaining |
|--------------|-----------------|---------------|---------------|---------------|-------------------|---------------|
| 1 | AURANGABAD DIV. | 199331 | 164874 | 165164 | 290 | 34167 |
| 2 | NASHIK DIV. | 141360 | 110372 | 110459 | 87 | 30901 |
| 3 | NAGPUR DIV. | 118393 | 90499 | 90571 | 72 | 27822 |
| 4 | KONKAN DIV. | 34732 | 31020 | 31053 | 33 | 3679 |
| 5 | AMRAVATI DIV. | 109702 | 93636 | 93640 | 7 | 16062 |
| 6 | PUNE DIV. | 65334 | 62997 | 62997 | 0 | 2337 |
| Total | | 668852 | 553398 | 553884 | 489 | 114968 |


| Sr. No. | District | Target | 19.04.2023 | 20.04.2023 | Daily_Achievement | Remaining |
|--------------|------------|---------------|---------------|---------------|-------------------|---------------|
| 1 | BEED | 26878 | 24843 | 24991 | 148 | 1887 |
| 2 | DHULE | 21790 | 17895 | 17980 | 85 | 3810 |
| 3 | LATUR | 27171 | 26136 | 26198 | 62 | 973 |
| 4 | CHANDRAPUR | 40285 | 24745 | 24804 | 59 | 15481 |
| 5 | OSMANABAD | 24853 | 16980 | 17039 | 59 | 7814 |
| 6 | PALGHAR | 11792 | 10974 | 11002 | 28 | 790 |
| 7 | NANDED | 26760 | 20818 | 20838 | 20 | 5922 |
| 8 | NAGPUR | 16291 | 11118 | 11130 | 12 | 5161 |
| 9 | THANE | 6264 | 4960 | 4965 | 5 | 1299 |
| 10 | AKOLA | 23681 | 17691 | 17695 | 4 | 5986 |
| 11 | NASHIK | 32035 | 22829 | 22831 | 2 | 9204 |
| 12 | WASHIM | 11500 | 10055 | 10057 | 2 | 1443 |
| 13 | BULDHANA | 21616 | 19970 | 19971 | 1 | 1645 |
| 14 | GONDIA | 14246 | 12854 | 12855 | 1 | 1391 |
| 15 | PARBHANI | 19784 | 17623 | 17624 | 1 | 2160 |
| 16 | AHMEDNAGAR | 35298 | 32973 | 32973 | 0 | 2325 |
| 17 | AMRAVATI | 23224 | 19808 | 19808 | 0 | 3416 |
| 18 | AURANGABAD | 26141 | 23801 | 23801 | 0 | 2340 |
| 19 | BHANDARA | 17590 | 15392 | 15392 | 0 | 2198 |
| 20 | GADCHIROLI | 16834 | 15197 | 15197 | 0 | 1637 |
| 21 | HINGOLI | 27298 | 15467 | 15467 | 0 | 11831 |
| 22 | JALGAON | 25659 | 22538 | 22538 | 0 | 3121 |
| 23 | JALNA | 20446 | 19206 | 19206 | 0 | 1240 |
| 24 | KOLHAPUR | 12565 | 12528 | 12528 | 0 | 37 |
| 25 | NANDURBAR | 26578 | 14137 | 14137 | 0 | 12441 |
| 26 | PUNE | 14672 | 12774 | 12774 | 0 | 1898 |
| 27 | RAIGAD | 7406 | 6302 | 6302 | 0 | 1104 |
| 28 | RATNAGIRI | 7129 | 6677 | 6677 | 0 | 452 |
| 29 | SANGLI | 8732 | 8603 | 8603 | 0 | 129 |
| 30 | SATARA | 10647 | 10647 | 10647 | 0 | 0 |
| 31 | SINDHUDURG | 2141 | 2107 | 2107 | 0 | 34 |
| 32 | SOLAPUR | 18718 | 18445 | 18445 | 0 | 273 |
| 33 | WARDHA | 13147 | 11193 | 11193 | 0 | 1954 |
| 34 | YAVATMAL | 29681 | 26112 | 26109 | -3 | 3572 |
| Total | | 668852 | 553398 | 553884 | 489 | 114968 |

Remaining Sanction RANK

| | |
|------------|-------|
| SATARA | 0 |
| SINDHUDURG | 34 |
| KOLHAPUR | 37 |
| SANGLI | 129 |
| SOLAPUR | 273 |
| RATNAGIRI | 452 |
| PALGHAR | 790 |
| LATUR | 973 |
| RAIGAD | 1104 |
| JALNA | 1240 |
| THANE | 1299 |
| GONDIA | 1391 |
| WASHIM | 1443 |
| GADCHIROLI | 1637 |
| BULDHANA | 1645 |
| BEED | 1887 |
| PUNE | 1898 |
| WARDHA | 1954 |
| PARBHANI | 2160 |
| BHANDARA | 2198 |
| AHMEDNAGAR | 2325 |
| AURANGABAD | 2340 |
| JALGAON | 3121 |
| AMRAVATI | 3416 |
| YAVATMAL | 3572 |
| DHULE | 3810 |
| NAGPUR | 5161 |
| NANDED | 5922 |
| AKOLA | 5986 |
| OSMANABAD | 7814 |
| NASHIK | 9204 |
| HINGOLI | 11831 |
| NANDURBAR | 12441 |
| CHANDRAPUR | 15481 |

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | Division | Sanction | 19.04.2023 | 20.04.2023 | Daily_Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|-----------------|---------------|---------------|---------------|-------------------|---------------|---|--|
| 1 | AURANGABAD DIV. | 165164 | 103632 | 103768 | 136 | 61396 | 90 | 1335 |
| 2 | AMRAVATI DIV. | 93640 | 64561 | 64657 | 96 | 28983 | 56 | 630 |
| 3 | NASHIK DIV. | 110459 | 88822 | 88892 | 70 | 21567 | 72 | 469 |
| 4 | NAGPUR DIV. | 90571 | 69253 | 69293 | 40 | 21278 | 45 | 463 |
| 5 | KONKAN DIV. | 31053 | 23589 | 23620 | 31 | 7433 | 15 | 162 |
| 6 | PUNE DIV. | 62997 | 51885 | 51910 | 25 | 11087 | 25 | 241 |
| Total | | 553884 | 401742 | 402140 | 398 | 151744 | 303 | 3299 |

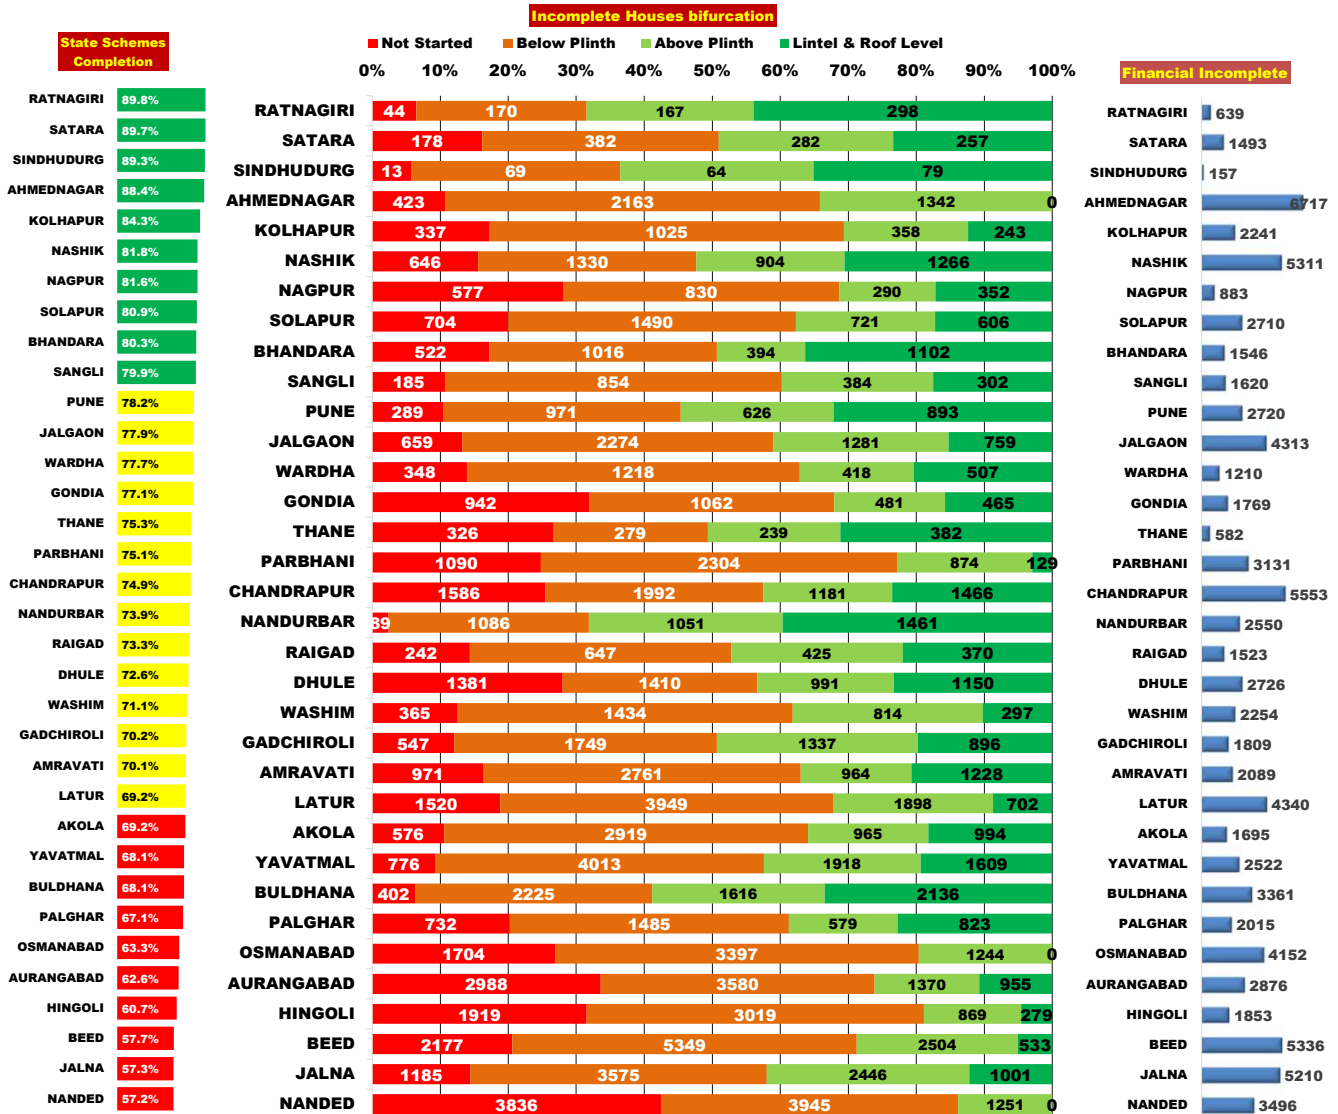

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | District | Sanction | 19.04.2023 | 20.04.2023 | Daily Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|---------|--------------|---------------|---------------|---------------|-------------------|---------------|---|--|
| 1 | BEED | 24991 | 14379 | 14428 | 49 | 10563 | 14 | 230 |
| 2 | LATUR | 26198 | 18082 | 18129 | 47 | 8069 | 13 | 175 |
| 3 | JALGAON | 22538 | 17528 | 17565 | 37 | 4973 | 12 | 108 |
| 4 | AMRAVATI | 19808 | 13852 | 13884 | 32 | 5924 | 9 | 129 |
| 5 | BULDHANA | 19971 | 13573 | 13592 | 19 | 6379 | 17 | 139 |
| 6 | AKOLA | 17695 | 12226 | 12241 | 15 | 5454 | 9 | 119 |
| 7 | NANDURBAR | 14137 | 10435 | 10450 | 15 | 3687 | 7 | 80 |
| 8 | WASHIM | 10057 | 7132 | 7147 | 15 | 2910 | 8 | 63 |
| 9 | YAVATMAL | 26109 | 17778 | 17793 | 15 | 8316 | 13 | 181 |
| 10 | JALNA | 19206 | 10985 | 10999 | 14 | 8207 | 25 | 178 |
| 11 | RAIGAD | 6302 | 4605 | 4618 | 13 | 1684 | 3 | 37 |
| 12 | GADCHIROLI | 15197 | 10656 | 10668 | 12 | 4529 | 9 | 98 |
| 13 | AHMEDNAGAR | 32973 | 29133 | 29144 | 11 | 3829 | 30 | 83 |
| 14 | NAGPUR | 11130 | 9070 | 9081 | 11 | 2049 | 3 | 45 |
| 15 | PUNE | 12774 | 9987 | 9995 | 8 | 2779 | 6 | 60 |
| 16 | GONDIA | 12855 | 9898 | 9905 | 7 | 2950 | 8 | 64 |
| 17 | HINGOLI | 15467 | 9374 | 9381 | 7 | 6086 | 6 | 132 |
| 18 | NANDED | 20838 | 11905 | 11912 | 7 | 8926 | 9 | 194 |
| 19 | WARDHA | 11193 | 8695 | 8702 | 7 | 2491 | 7 | 54 |
| 20 | KOLHAPUR | 12528 | 10559 | 10565 | 6 | 1963 | 3 | 43 |
| 21 | NASHIK | 22831 | 18679 | 18685 | 6 | 4146 | 13 | 90 |
| 22 | OSMANABAD | 17039 | 10778 | 10784 | 6 | 6255 | 11 | 136 |
| 23 | PALGHAR | 11002 | 7377 | 7383 | 6 | 3619 | 6 | 79 |
| 24 | RATNAGIRI | 6677 | 5992 | 5998 | 6 | 679 | 3 | 15 |
| 25 | SINDHUDURG | 2107 | 1876 | 1882 | 6 | 225 | 1 | 5 |
| 26 | SANGLI | 8603 | 6873 | 6878 | 5 | 1725 | 4 | 38 |
| 27 | SATARA | 10647 | 9543 | 9548 | 5 | 1099 | 6 | 24 |
| 28 | AURANGABAD | 23801 | 14904 | 14908 | 4 | 8893 | 9 | 193 |
| 29 | CHANDRAPUR | 24804 | 18577 | 18579 | 2 | 6225 | 13 | 135 |
| 30 | PARBHANI | 17624 | 13225 | 13227 | 2 | 4397 | 4 | 96 |
| 31 | BHANDARA | 15392 | 12357 | 12358 | 1 | 3034 | 4 | 66 |
| 32 | DHULE | 17980 | 13047 | 13048 | 1 | 4932 | 10 | 107 |
| 33 | SOLAPUR | 18445 | 14923 | 14924 | 1 | 3521 | 7 | 77 |
| 34 | THANE | 4965 | 3739 | 3739 | 0 | 1226 | 2 | 27 |
| | Total | 553884 | 401742 | 402140 | 398 | 151744 | 303 | 3299 |

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | Division | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|---------|-----------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | NASHIK DIV. | 0 | 11716 | 0 | 42043 | 0 | 23398 |
| 2 | AMRAVATI DIV. | 0 | 32629 | 0 | 34925 | 0 | 15801 |
| 3 | AURANGABAD DIV. | 0 | 21526 | 0 | 56991 | 0 | 22692 |
| 4 | NAGPUR DIV. | 0 | 11359 | 0 | 23339 | 0 | 14358 |
| 5 | KONKAN DIV. | 0 | 585 | 0 | 4143 | 0 | 4327 |
| 6 | PUNE DIV. | 0 | 10642 | 0 | 17255 | 0 | 7173 |
| | Total | 0 | 88457 | 0 | 178696 | 0 | 87749 |

PMAY-G 1st Ins Pending

| | |
|------------|-------|
| SINDHUDURG | 5 |
| RAIGAD | 14 |
| THANE | 104 |
| RATNAGIRI | 114 |
| PALGHAR | 348 |
| GADCHIROLI | 413 |
| KOLHAPUR | 553 |
| SANGLI | 732 |
| SATARA | 950 |
| DHULE | 1172 |
| NASHIK | 1215 |
| PARBHANI | 1283 |
| NANDURBAR | 1493 |
| GONDIA | 1626 |
| WARDHA | 1678 |
| NAGPUR | 2026 |
| JALNA | 2078 |
| HINGOLI | 2093 |
| PUNE | 2292 |
| CHANDRAPUR | 2327 |
| LATUR | 2430 |
| AURANGABAD | 3049 |
| AHMEDNAGAR | 3154 |
| WASHIM | 3268 |
| OSMANABAD | 3287 |
| BHANDARA | 3289 |
| NANDED | 3627 |
| BEED | 3679 |
| AKOLA | 4222 |
| YAVATMAL | 4349 |
| JALGAON | 4682 |
| SOLAPUR | 6115 |
| BULDHANA | 8681 |
| AMRAVATI | 12109 |

PMAY-G 2nd Ins Pending

| | |
|------------|-------|
| SINDHUDURG | 287 |
| RATNAGIRI | 482 |
| RAIGAD | 579 |
| THANE | 708 |
| SATARA | 1303 |
| WARDHA | 1318 |
| OSMANABAD | 1962 |
| PALGHAR | 2087 |
| PUNE | 2373 |
| KOLHAPUR | 2766 |
| GADCHIROLI | 2975 |
| NAGPUR | 3136 |
| HINGOLI | 3436 |
| WASHIM | 3639 |
| AHMEDNAGAR | 4145 |
| SANGLI | 4214 |
| LATUR | 4814 |
| GONDIA | 4823 |
| CHANDRAPUR | 5245 |
| JALNA | 5322 |
| AKOLA | 5358 |
| BHANDARA | 5842 |
| AURANGABAD | 6091 |
| BULDHANA | 6464 |
| NASHIK | 6529 |
| SOLAPUR | 6599 |
| PARBHANI | 6850 |
| DHULE | 7226 |
| BEED | 8672 |
| AMRAVATI | 9275 |
| YAVATMAL | 10189 |
| NANDURBAR | 10915 |
| JALGAON | 13228 |
| NANDED | 19844 |

PMAY-G 3rd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 390 |
| RAIGAD | 413 |
| RATNAGIRI | 522 |
| THANE | 722 |
| WARDHA | 1033 |
| KOLHAPUR | 1060 |
| PUNE | 1079 |
| SATARA | 1176 |
| HINGOLI | 1347 |
| SANGLI | 1515 |
| NAGPUR | 1526 |
| LATUR | 1794 |
| AKOLA | 1967 |
| PARBHANI | 2265 |
| PALGHAR | 2280 |
| SOLAPUR | 2343 |
| JALNA | 2391 |
| WASHIM | 2418 |
| GADCHIROLI | 2444 |
| AURANGABAD | 2531 |
| BHANDARA | 2584 |
| BULDHANA | 2862 |
| OSMANABAD | 2935 |
| CHANDRAPUR | 2996 |
| AMRAVATI | 3228 |
| BEED | 3509 |
| AHMEDNAGAR | 3539 |
| GONDIA | 3775 |
| DHULE | 3855 |
| JALGAON | 4066 |
| NASHIK | 4122 |
| YAVATMAL | 5326 |
| NANDED | 5920 |
| NANDURBAR | 7816 |

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | District | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|---------|--------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | AHMEDNAGAR | 0 | 3154 | 0 | 4145 | 0 | 3539 |
| 2 | AKOLA | 0 | 4222 | 0 | 5358 | 0 | 1967 |
| 3 | AMRAVATI | 0 | 12109 | 0 | 9275 | 0 | 3228 |
| 4 | AURANGABAD | 0 | 3049 | 0 | 6091 | 0 | 2531 |
| 5 | BEED | 0 | 3679 | 0 | 8672 | 0 | 3509 |
| 6 | BHANDARA | 0 | 3289 | 0 | 5842 | 0 | 2584 |
| 7 | BULDHANA | 0 | 8681 | 0 | 6464 | 0 | 2862 |
| 8 | CHANDRAPUR | 0 | 2327 | 0 | 5245 | 0 | 2996 |
| 9 | DHULE | 0 | 1172 | 0 | 7226 | 0 | 3855 |
| 10 | GADCHIROLI | 0 | 413 | 0 | 2975 | 0 | 2444 |
| 11 | GONDIA | 0 | 1626 | 0 | 4823 | 0 | 3775 |
| 12 | HINGOLI | 0 | 2093 | 0 | 3436 | 0 | 1347 |
| 13 | JALGAON | 0 | 4682 | 0 | 13228 | 0 | 4066 |
| 14 | JALNA | 0 | 2078 | 0 | 5322 | 0 | 2391 |
| 15 | KOLHAPUR | 0 | 553 | 0 | 2766 | 0 | 1060 |
| 16 | LATUR | 0 | 2430 | 0 | 4814 | 0 | 1794 |
| 17 | NAGPUR | 0 | 2026 | 0 | 3136 | 0 | 1526 |
| 18 | NANDED | 0 | 3627 | 0 | 19844 | 0 | 5920 |
| 19 | NANDURBAR | 0 | 1493 | 0 | 10915 | 0 | 7816 |
| 20 | NASHIK | 0 | 1215 | 0 | 6529 | 0 | 4122 |
| 21 | OSMANABAD | 0 | 3287 | 0 | 1962 | 0 | 2935 |
| 22 | PALGHAR | 0 | 348 | 0 | 2087 | 0 | 2280 |
| 23 | PARBHANI | 0 | 1283 | 0 | 6850 | 0 | 2265 |
| 24 | PUNE | 0 | 2292 | 0 | 2373 | 0 | 1079 |
| 25 | RAIGAD | 0 | 14 | 0 | 579 | 0 | 413 |
| 26 | SANGLI | 0 | 732 | 0 | 4214 | 0 | 1515 |
| 27 | SINDHUDURG | 0 | 5 | 0 | 287 | 0 | 390 |
| 28 | SOLAPUR | 0 | 6115 | 0 | 6599 | 0 | 2343 |
| 29 | THANE | 0 | 104 | 0 | 708 | 0 | 722 |
| 30 | WARDHA | 0 | 1678 | 0 | 1318 | 0 | 1033 |
| 31 | WASHIM | 0 | 3268 | 0 | 3639 | 0 | 2418 |
| 32 | YAVATMAL | 0 | 4349 | 0 | 10189 | 0 | 5326 |
| 33 | RATNAGIRI | -5 | 114 | 0 | 482 | 0 | 522 |
| 34 | SATARA | -30 | 950 | 0 | 1303 | 0 | 1176 |
| | Total | 0 | 88457 | 0 | 178696 | 0 | 87749 |

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | Division | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|--------------|-----------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | NASHIK DIV. | 0 | 3198 | 0 | 8263 | 0 | 5569 |
| 2 | AMRAVATI DIV. | 0 | 3090 | 0 | 13352 | 0 | 6277 |
| 3 | AURANGABAD DIV. | 0 | 16419 | 0 | 29118 | 0 | 12456 |
| 4 | NAGPUR DIV. | 0 | 4522 | 0 | 7867 | 0 | 4101 |
| 5 | KONKAN DIV. | 0 | 1357 | -1 | 2650 | 0 | 1474 |
| 6 | PUNE DIV. | 0 | 1693 | 0 | 4722 | 0 | 2371 |
| Total | | 0 | 30279 | -1 | 65972 | 0 | 32248 |

State Schemes 1st Ins Pending

| | |
|------------|------|
| SINDHUDURG | 13 |
| RATNAGIRI | 44 |
| NANDURBAR | 89 |
| SATARA | 178 |
| SANGLI | 185 |
| RAIGAD | 242 |
| PUNE | 289 |
| THANE | 326 |
| KOLHAPUR | 337 |
| WARDHA | 348 |
| WASHIM | 365 |
| BULDHANA | 402 |
| AHMEDNAGAR | 423 |
| BHANDARA | 522 |
| GADCHIROLI | 547 |
| AKOLA | 576 |
| NAGPUR | 577 |
| NASHIK | 646 |
| JALGAON | 659 |
| SOLAPUR | 704 |
| PALGHAR | 732 |
| YAVATMAL | 776 |
| GONDIA | 942 |
| AMRAVATI | 971 |
| PARBHANI | 1090 |
| JALNA | 1185 |
| DHULE | 1381 |
| LATUR | 1520 |
| CHANDRAPUR | 1586 |
| OSMANABAD | 1704 |
| HINGOLI | 1919 |
| BEED | 2177 |
| AURANGABAD | 2988 |
| NANDED | 3836 |

State Schemes 2nd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 69 |
| RATNAGIRI | 170 |
| THANE | 279 |
| SATARA | 382 |
| RAIGAD | 647 |
| NAGPUR | 830 |
| SANGLI | 854 |
| PUNE | 971 |
| BHANDARA | 1016 |
| KOLHAPUR | 1025 |
| GONDIA | 1062 |
| NANDURBAR | 1086 |
| WARDHA | 1218 |
| NASHIK | 1330 |
| DHULE | 1410 |
| WASHIM | 1434 |
| PALGHAR | 1485 |
| SOLAPUR | 1490 |
| GADCHIROLI | 1749 |
| CHANDRAPUR | 1992 |
| AHMEDNAGAR | 2163 |
| BULDHANA | 2225 |
| JALGAON | 2274 |
| PARBHANI | 2304 |
| AMRAVATI | 2761 |
| AKOLA | 2919 |
| HINGOLI | 3019 |
| OSMANABAD | 3397 |
| JALNA | 3575 |
| AURANGABAD | 3580 |
| NANDED | 3945 |
| LATUR | 3949 |
| YAVATMAL | 4013 |
| BEED | 5349 |

State Schemes 3rd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 64 |
| RATNAGIRI | 167 |
| THANE | 239 |
| SATARA | 282 |
| NAGPUR | 290 |
| KOLHAPUR | 358 |
| SANGLI | 384 |
| BHANDARA | 394 |
| WARDHA | 418 |
| RAIGAD | 425 |
| GONDIA | 481 |
| PALGHAR | 579 |
| PUNE | 626 |
| SOLAPUR | 721 |
| WASHIM | 814 |
| HINGOLI | 869 |
| PARBHANI | 874 |
| NASHIK | 904 |
| AMRAVATI | 964 |
| AKOLA | 965 |
| DHULE | 991 |
| NANDURBAR | 1051 |
| CHANDRAPUR | 1181 |
| OSMANABAD | 1244 |
| NANDED | 1251 |
| JALGAON | 1281 |
| GADCHIROLI | 1337 |
| AHMEDNAGAR | 1342 |
| AURANGABAD | 1370 |
| BULDHANA | 1616 |
| LATUR | 1898 |
| YAVATMAL | 1918 |
| JALNA | 2446 |
| BEED | 2504 |

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

| Sr. No. | District | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|---------|--------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | AHMEDNAGAR | 0 | 423 | 0 | 2163 | 0 | 1342 |
| 2 | AKOLA | 0 | 576 | 0 | 2919 | 0 | 965 |
| 3 | AMRAVATI | 0 | 971 | 0 | 2761 | 0 | 964 |
| 4 | AURANGABAD | 0 | 2988 | 0 | 3580 | 0 | 1370 |
| 5 | BEED | 0 | 2177 | 0 | 5349 | 0 | 2504 |
| 6 | BHANDARA | 0 | 522 | 0 | 1016 | 0 | 394 |
| 7 | BULDHANA | 0 | 402 | 0 | 2225 | 0 | 1616 |
| 8 | CHANDRAPUR | 0 | 1586 | 0 | 1992 | 0 | 1181 |
| 9 | DHULE | 0 | 1381 | 0 | 1410 | 0 | 991 |
| 10 | GADCHIROLI | 0 | 547 | 0 | 1749 | 0 | 1337 |
| 11 | GONDIA | 0 | 942 | 0 | 1062 | 0 | 481 |
| 12 | HINGOLI | 0 | 1919 | 0 | 3019 | 0 | 869 |
| 13 | JALGAON | 0 | 659 | 0 | 2274 | 0 | 1281 |
| 14 | JALNA | 0 | 1185 | 0 | 3575 | 0 | 2446 |
| 15 | KOLHAPUR | 0 | 337 | 0 | 1025 | 0 | 358 |
| 16 | LATUR | 0 | 1520 | 0 | 3949 | 0 | 1898 |
| 17 | NAGPUR | 0 | 577 | 0 | 830 | 0 | 290 |
| 18 | NANDED | 0 | 3836 | 0 | 3945 | 0 | 1251 |
| 19 | NANDURBAR | 0 | 89 | 0 | 1086 | 0 | 1051 |
| 20 | NASHIK | 0 | 646 | 0 | 1330 | 0 | 904 |
| 21 | OSMANABAD | 0 | 1704 | 0 | 3397 | 0 | 1244 |
| 22 | PALGHAR | 0 | 732 | 0 | 1485 | 0 | 579 |
| 23 | PARBHANI | 0 | 1090 | 0 | 2304 | 0 | 874 |
| 24 | PUNE | 0 | 289 | 0 | 971 | 0 | 626 |
| 25 | RAIGAD | 0 | 242 | 0 | 647 | 0 | 425 |
| 26 | SANGLI | 0 | 185 | 0 | 854 | 0 | 384 |
| 27 | SINDHUDURG | 0 | 13 | 0 | 69 | 0 | 64 |
| 28 | SOLAPUR | 0 | 704 | 0 | 1490 | 0 | 721 |
| 29 | THANE | 0 | 326 | 0 | 279 | 0 | 239 |
| 30 | WARDHA | 0 | 348 | 0 | 1218 | 0 | 418 |
| 31 | WASHIM | 0 | 365 | 0 | 1434 | 0 | 814 |
| 32 | YAVATMAL | 0 | 776 | 0 | 4013 | 0 | 1918 |
| 33 | SATARA | -2 | 178 | 0 | 382 | 0 | 282 |
| 34 | RATNAGIRI | -3 | 44 | -1 | 170 | 0 | 167 |
| | Total | 0 | 30279 | 0 | 65972 | 0 | 32248 |

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

