



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २१.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

| योजना | एकूण मंजूरी | दैनिक मंजूरी | एकूण पूर्ण | दैनिक पूर्ण घरकुले | दैनिक पहिला हप्ता वितरित | दैनिक दुसरा हप्ता वितरित | दैनिक तिसरा हप्ता वितरित |
|---------------------------------|-------------|--------------|------------|--------------------|--------------------------|--------------------------|--------------------------|
| प्रधानमंत्री आवास योजना ग्रामीण | १४१०८७१ | ४८ | १०३६०३९ | ६५२ | ३६४ | १६७५ | २३९३ |
| राज्य योजना | ५५४१२७ | २४३ | ४०२४८१ | ३४१ | १२१६ | ८३५ | ७५७ |
| एकूण | १९६४९९८ | २९१ | १४३८५२० | ९९३ | १५८० | २५१० | ३१५० |

PMAY-G Completion Progress Bar

73.4%



PMAY-G: Incomplete Houses bifurcation






State Schemes Progress Bar

72.6%

State Schemes: Incomplete Houses bifurcation

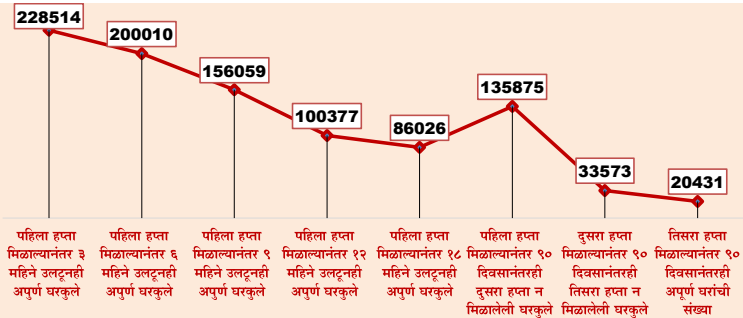


Abhiyan Achievement Day 152

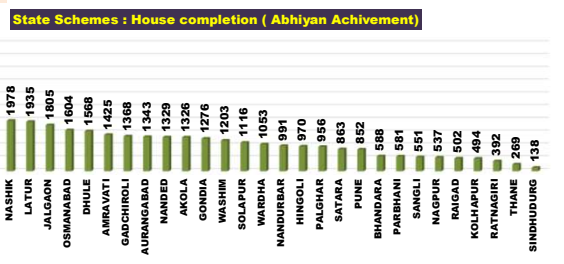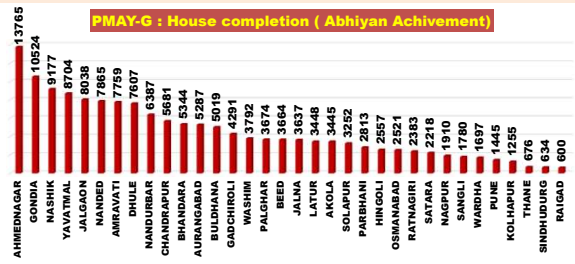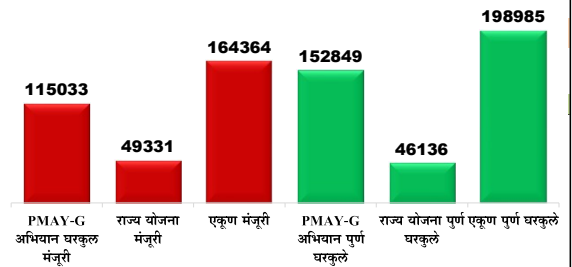


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण
४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

| Sr. No. | Division | Target (PWL+Awaas Plus) | 20.04.2023 | 21.04.2023 | Daily_Achievement | Remaining |
|--------------|-----------------|-------------------------|----------------|----------------|-------------------|-------------|
| 1 | AMRAVATI DIV. | 275030 | 274560 | 274579 | 19 | 451 |
| 2 | PUNE DIV. | 124898 | 124057 | 123986 | 13 | 912 |
| 3 | NASHIK DIV. | 414763 | 413737 | 413748 | 12 | 1015 |
| 4 | NAGPUR DIV. | 292127 | 291513 | 291506 | 4 | 621 |
| 5 | AURANGABAD DIV. | 238068 | 237416 | 237416 | 0 | 652 |
| 6 | KONKAN DIV. | 69785 | 69636 | 69636 | 0 | 149 |
| Total | | 1414671 | 1410919 | 1410871 | 48 | 3800 |

| Sr. No. | District | Target (PWL+Awaas Plus) | 20.04.2023 | 21.04.2023 | Daily_Achievement | Remaining |
|--------------|------------|-------------------------|----------------|----------------|-------------------|-------------|
| 1 | YAVATMAL | 65355 | 65206 | 65220 | 14 | 135 |
| 2 | SATARA | 15353 | 15328 | 15341 | 13 | 12 |
| 3 | NANDURBAR | 119521 | 118949 | 118959 | 10 | 562 |
| 4 | AMRAVATI | 95712 | 95464 | 95466 | 2 | 246 |
| 5 | NAGPUR | 37078 | 37057 | 37059 | 2 | 19 |
| 6 | WASHIM | 20404 | 20399 | 20401 | 2 | 3 |
| 7 | AHMEDNAGAR | 60792 | 60761 | 60762 | 1 | 30 |
| 8 | BULDHANA | 44767 | 44713 | 44714 | 1 | 53 |
| 9 | GADCHIROLI | 31698 | 31618 | 31619 | 1 | 79 |
| 10 | GONDIA | 96492 | 96142 | 96143 | 1 | 349 |
| 11 | JALGAON | 79749 | 79449 | 79450 | 1 | 299 |
| 12 | AKOLA | 48792 | 48778 | 48778 | 0 | 14 |
| 13 | AURANGABAD | 36795 | 36666 | 36666 | 0 | 129 |
| 14 | BEED | 35310 | 35253 | 35253 | 0 | 57 |
| 15 | BHANDARA | 65091 | 65066 | 65066 | 0 | 25 |
| 16 | CHANDRAPUR | 43124 | 43013 | 43013 | 0 | 111 |
| 17 | DHULE | 64979 | 64917 | 64917 | 0 | 62 |
| 18 | HINGOLI | 18109 | 18083 | 18083 | 0 | 26 |
| 19 | JALNA | 24039 | 24022 | 24022 | 0 | 17 |
| 20 | KOLHAPUR | 17685 | 17685 | 17685 | 0 | 0 |
| 21 | LATUR | 20679 | 20471 | 20471 | 0 | 208 |
| 22 | NANDED | 69533 | 69460 | 69460 | 0 | 73 |
| 23 | OSMANABAD | 14506 | 14401 | 14401 | 0 | 105 |
| 24 | PALGHAR | 35312 | 35185 | 35185 | 0 | 127 |
| 25 | PARBHANI | 19097 | 19060 | 19060 | 0 | 37 |
| 26 | PUNE | 20544 | 20531 | 20531 | 0 | 13 |
| 27 | RAIGAD | 9831 | 9822 | 9822 | 0 | 9 |
| 28 | RATNAGIRI | 9895 | 9888 | 9888 | 0 | 7 |
| 29 | SANGLI | 21932 | 21782 | 21782 | 0 | 150 |
| 30 | SINDHUDURG | 5142 | 5142 | 5142 | 0 | 0 |
| 31 | THANE | 9605 | 9599 | 9599 | 0 | 6 |
| 32 | NASHIK | 89722 | 89661 | 89660 | -1 | 62 |
| 33 | WARDHA | 18644 | 18617 | 18606 | -11 | 38 |
| 34 | SOLAPUR | 49384 | 48731 | 48647 | -84 | 737 |
| Total | | 1414671 | 1410919 | 1410871 | 48 | 3800 |

Remaining Sanction RANK


| | |
|------------|-----|
| KOLHAPUR | 0 |
| SINDHUDURG | 0 |
| WASHIM | 3 |
| THANE | 6 |
| RATNAGIRI | 7 |
| RAIGAD | 9 |
| SATARA | 12 |
| PUNE | 13 |
| AKOLA | 14 |
| JALNA | 17 |
| NAGPUR | 19 |
| BHANDARA | 25 |
| HINGOLI | 26 |
| AHMEDNAGAR | 30 |
| PARBHANI | 37 |
| WARDHA | 38 |
| BULDHANA | 53 |
| BEED | 57 |
| DHULE | 62 |
| NASHIK | 62 |
| NANDED | 73 |
| GADCHIROLI | 79 |
| OSMANABAD | 105 |
| CHANDRAPUR | 111 |
| PALGHAR | 127 |
| AURANGABAD | 129 |
| YAVATMAL | 135 |
| SANGLI | 150 |
| LATUR | 208 |
| AMRAVATI | 246 |
| JALGAON | 299 |
| GONDIA | 349 |
| NANDURBAR | 562 |
| SOLAPUR | 737 |

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

| Sr. No. | District | Google Sheet Report | | | AwaasSoft Report | | | |
|---------|--------------|---------------------|---------------|--------------|--|--------------------------------------|--------------------|-------------------------------|
| | | Total Landless | Provided land | Remaining | Landless beneficiaries tagged in AwaasSoft | Landless beneficiaries provided land | Remaining Landless | Remaining Tag (provided land) |
| 1 | DHULE | 18 | 18 | 0 | 18 | 18 | 0 | 0 |
| 2 | GADCHIROLI | 8 | 8 | 0 | 8 | 8 | 0 | 0 |
| 3 | NANDURBAR | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 4 | PALGHAR | 11 | 11 | 0 | 11 | 11 | 0 | 0 |
| 5 | RAIGAD | 6 | 6 | 0 | 6 | 6 | 0 | 0 |
| 6 | RATNAGIRI | 23 | 23 | 0 | 23 | 23 | 0 | 0 |
| 7 | SINDHUDURG | 420 | 420 | 0 | 420 | 420 | 0 | 0 |
| 8 | KOLHAPUR | 257 | 257 | 0 | 257 | 227 | 30 | 30 |
| 9 | THANE | 127 | 74 | 53 | 127 | 43 | 84 | 31 |
| 10 | NANDED | 362 | 277 | 85 | 362 | 242 | 120 | 35 |
| 11 | BEED | 212 | 101 | 111 | 212 | 72 | 140 | 29 |
| 12 | SANGLI | 431 | 143 | 288 | 431 | 141 | 290 | 2 |
| 13 | PARBHANI | 332 | 15 | 317 | 332 | 13 | 319 | 2 |
| 14 | SATARA | 1309 | 598 | 711 | 1305 | 628 | 677 | -30 |
| 15 | NASHIK | 1804 | 1454 | 350 | 1803 | 715 | 1088 | 739 |
| 16 | HINGOLI | 1713 | 787 | 926 | 1713 | 466 | 1247 | 321 |
| 17 | JALNA | 1413 | 165 | 1248 | 1381 | 85 | 1296 | 80 |
| 18 | WARDHA | 2819 | 1284 | 1535 | 2803 | 1214 | 1589 | 70 |
| 19 | NAGPUR | 5134 | 3397 | 1737 | 5054 | 3412 | 1642 | -15 |
| 20 | GONDIA | 2450 | 2450 | 0 | 2450 | 765 | 1685 | 1685 |
| 21 | CHANDRAPUR | 2791 | 1463 | 1328 | 2752 | 968 | 1784 | 495 |
| 22 | PUNE | 2925 | 992 | 1933 | 2924 | 885 | 2039 | 107 |
| 23 | LATUR | 2299 | 68 | 2231 | 2299 | 66 | 2233 | 2 |
| 24 | OSMANABAD | 2470 | 104 | 2366 | 2470 | 56 | 2414 | 48 |
| 25 | YAVATMAL | 3437 | 1119 | 2318 | 3575 | 1134 | 2441 | -15 |
| 26 | BHANDARA | 5825 | 3230 | 2595 | 5800 | 3213 | 2587 | 17 |
| 27 | WASHIM | 3477 | 865 | 2612 | 3477 | 850 | 2627 | 15 |
| 28 | AURANGABAD | 3328 | 1779 | 1549 | 3328 | 288 | 3040 | 1491 |
| 29 | AKOLA | 7074 | 3842 | 3232 | 7074 | 3844 | 3230 | -2 |
| 30 | AHMEDNAGAR | 7762 | 4828 | 2934 | 7756 | 3374 | 4382 | 1454 |
| 31 | JALGAON | 22889 | 20580 | 2309 | 22881 | 17556 | 5325 | 3024 |
| 32 | SOLAPUR | 7960 | 2595 | 5365 | 7463 | 792 | 6671 | 1803 |
| 33 | BULDHANA | 15256 | 8455 | 6801 | 15229 | 6953 | 8276 | 1502 |
| 34 | AMRAVATI | 21560 | 11238 | 10322 | 21560 | 10040 | 11520 | 1198 |
| | Total | 127902 | 72646 | 55256 | 127304 | 58528 | 68776 | 14180 |

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | Division | Sanction | 20.04.2023 | 21.04.2023 | Daily Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|-----------------|----------------|----------------|----------------|-------------------|---------------|---|--|
| 1 | NASHIK DIV. | 413748 | 328313 | 328488 | 175 | 85260 | 296 | 1895 |
| 2 | NAGPUR DIV. | 291506 | 237438 | 237575 | 137 | 53931 | 194 | 1198 |
| 3 | AMRAVATI DIV. | 274579 | 185740 | 185876 | 136 | 88703 | 189 | 1971 |
| 4 | AURANGABAD DIV. | 237416 | 139266 | 139353 | 87 | 98063 | 209 | 2179 |
| 5 | PUNE DIV. | 123986 | 87305 | 87372 | 67 | 36614 | 65 | 814 |
| 6 | KONKAN DIV. | 69636 | 57325 | 57375 | 50 | 12261 | 52 | 272 |
| Total | | 1410871 | 1035387 | 1036039 | 652 | 374832 | 1006 | 8330 |

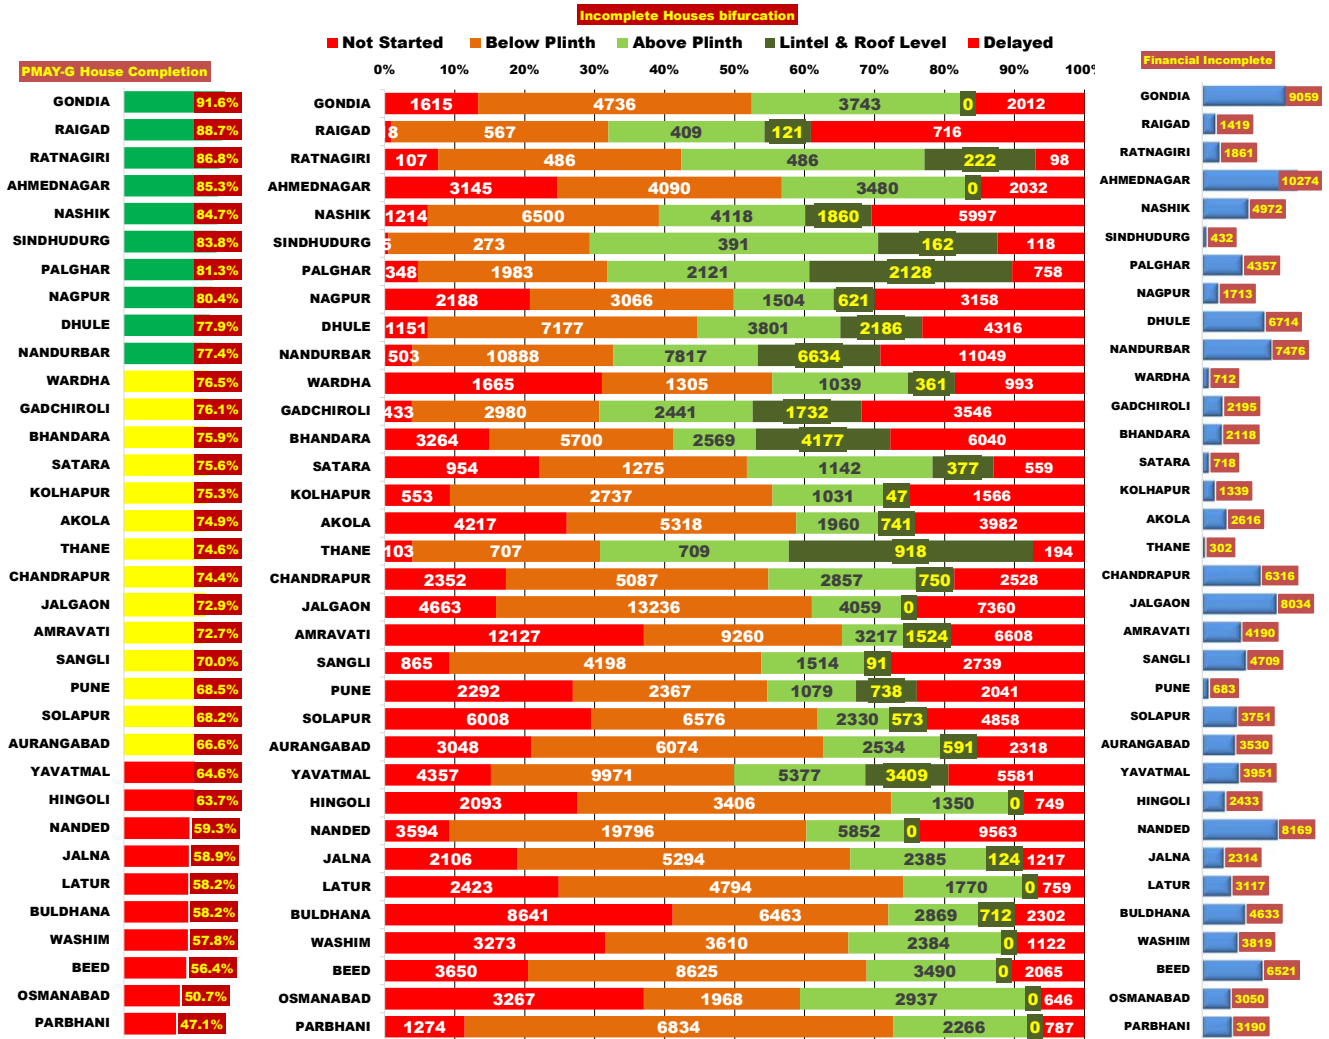

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | District | Sanction | 20.04.2023 | 21.04.2023 | Daily Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|------------|----------------|----------------|----------------|-------------------|---------------|---|--|
| 1 | JALGAON | 79450 | 57857 | 57956 | 99 | 21494 | 53 | 478 |
| 2 | YAVATMAL | 65220 | 42062 | 42112 | 50 | 23108 | 57 | 514 |
| 3 | DHULE | 64917 | 50568 | 50602 | 34 | 14315 | 50 | 318 |
| 4 | BHANDARA | 65066 | 49323 | 49356 | 33 | 15710 | 35 | 349 |
| 5 | CHANDRAPUR | 43013 | 31989 | 32020 | 31 | 10993 | 37 | 244 |
| 6 | GADCHIROLI | 31619 | 24029 | 24058 | 29 | 7561 | 28 | 168 |
| 7 | WASHIM | 20401 | 11769 | 11798 | 29 | 8603 | 25 | 191 |
| 8 | AMRAVATI | 95466 | 69357 | 69384 | 27 | 26082 | 51 | 580 |
| 9 | AKOLA | 48778 | 36516 | 36542 | 26 | 12236 | 23 | 272 |
| 10 | GONDIA | 96143 | 88077 | 88102 | 25 | 8041 | 69 | 179 |
| 11 | SOLAPUR | 48647 | 33136 | 33160 | 24 | 15487 | 21 | 344 |
| 12 | PALGHAR | 35185 | 28582 | 28605 | 23 | 6580 | 24 | 146 |
| 13 | LATUR | 20471 | 11902 | 11922 | 20 | 8549 | 23 | 190 |
| 14 | PARBHANI | 19060 | 8968 | 8986 | 18 | 10074 | 19 | 224 |
| 15 | NANDURBAR | 118959 | 92100 | 92117 | 17 | 26842 | 42 | 596 |
| 16 | BEED | 35253 | 19876 | 19892 | 16 | 15361 | 24 | 341 |
| 17 | NAGPUR | 37059 | 29787 | 29803 | 16 | 7256 | 13 | 161 |
| 18 | AHMEDNAGAR | 60762 | 51830 | 51845 | 15 | 8917 | 91 | 198 |
| 19 | SATARA | 15341 | 11579 | 11593 | 14 | 3748 | 15 | 83 |
| 20 | KOLHAPUR | 17685 | 13304 | 13317 | 13 | 4368 | 8 | 97 |
| 21 | NANDED | 69460 | 41163 | 41175 | 12 | 28285 | 52 | 629 |
| 22 | PUNE | 20531 | 14043 | 14055 | 12 | 6476 | 10 | 144 |
| 23 | NASHIK | 89660 | 75958 | 75968 | 10 | 13692 | 60 | 304 |
| 24 | HINGOLI | 18083 | 11506 | 11515 | 9 | 6568 | 17 | 146 |
| 25 | SINDHUDURG | 5142 | 4303 | 4311 | 8 | 831 | 4 | 18 |
| 26 | JALNA | 24022 | 14136 | 14143 | 7 | 9879 | 24 | 220 |
| 27 | THANE | 9599 | 7155 | 7162 | 7 | 2437 | 4 | 54 |
| 28 | RAIGAD | 9822 | 8704 | 8710 | 6 | 1112 | 4 | 25 |
| 29 | RATNAGIRI | 9888 | 8581 | 8587 | 6 | 1301 | 16 | 29 |
| 30 | BULDHANA | 44714 | 26036 | 26040 | 4 | 18674 | 33 | 415 |
| 31 | OSMANABAD | 14401 | 7297 | 7301 | 4 | 7100 | 17 | 158 |
| 32 | SANGLI | 21782 | 15243 | 15247 | 4 | 6535 | 12 | 145 |
| 33 | WARDHA | 18606 | 14233 | 14236 | 3 | 4370 | 11 | 97 |
| 34 | AURANGABAD | 36666 | 24418 | 24419 | 1 | 12247 | 35 | 272 |
| Total | | 1410871 | 1035387 | 1036039 | 652 | 374832 | 1006 | 8330 |

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

| Sr. No. | Division | Target | 20.04.2023 | 21.04.2023 | Daily_Achievement | Remaining |
|--------------|-----------------|---------------|---------------|---------------|-------------------|---------------|
| 1 | NAGPUR DIV. | 118393 | 90571 | 90687 | 116 | 27706 |
| 2 | AURANGABAD DIV. | 199331 | 165164 | 165274 | 110 | 34057 |
| 3 | NASHIK DIV. | 141360 | 110459 | 110467 | 8 | 30893 |
| 4 | AMRAVATI DIV. | 109702 | 93640 | 93648 | 8 | 16054 |
| 5 | KONKAN DIV. | 34732 | 31053 | 31054 | 1 | 3678 |
| 6 | PUNE DIV. | 65334 | 62997 | 62997 | 0 | 2337 |
| Total | | 668852 | 553884 | 554127 | 243 | 114725 |


| Sr. No. | District | Target | 20.04.2023 | 21.04.2023 | Daily_Achievement | Remaining |
|--------------|------------|---------------|---------------|---------------|-------------------|---------------|
| 1 | BHANDARA | 17590 | 15392 | 15464 | 72 | 2126 |
| 2 | HINGOLI | 27298 | 15467 | 15514 | 47 | 11784 |
| 3 | AURANGABAD | 26141 | 23801 | 23842 | 41 | 2299 |
| 4 | CHANDRAPUR | 40285 | 24804 | 24843 | 39 | 15442 |
| 5 | JALNA | 20446 | 19206 | 19227 | 21 | 1219 |
| 6 | NASHIK | 32035 | 22831 | 22839 | 8 | 9196 |
| 7 | GADCHIROLI | 16834 | 15197 | 15202 | 5 | 1632 |
| 8 | AMRAVATI | 23224 | 19808 | 19812 | 4 | 3412 |
| 9 | BULDHANA | 21616 | 19971 | 19975 | 4 | 1641 |
| 10 | LATUR | 27171 | 26198 | 26199 | 1 | 972 |
| 11 | THANE | 6264 | 4965 | 4966 | 1 | 1298 |
| 12 | AHMEDNAGAR | 35298 | 32973 | 32973 | 0 | 2325 |
| 13 | AKOLA | 23681 | 17695 | 17695 | 0 | 5986 |
| 14 | BEED | 26878 | 24991 | 24991 | 0 | 1887 |
| 15 | DHULE | 21790 | 17980 | 17980 | 0 | 3810 |
| 16 | GONDIA | 14246 | 12855 | 12855 | 0 | 1391 |
| 17 | JALGAON | 25659 | 22538 | 22538 | 0 | 3121 |
| 18 | KOLHAPUR | 12565 | 12528 | 12528 | 0 | 37 |
| 19 | NAGPUR | 16291 | 11130 | 11130 | 0 | 5161 |
| 20 | NANDED | 26760 | 20838 | 20838 | 0 | 5922 |
| 21 | NANDURBAR | 26578 | 14137 | 14137 | 0 | 12441 |
| 22 | OSMANABAD | 24853 | 17039 | 17039 | 0 | 7814 |
| 23 | PALGHAR | 11792 | 11002 | 11002 | 0 | 790 |
| 24 | PARBHANI | 19784 | 17624 | 17624 | 0 | 2160 |
| 25 | PUNE | 14672 | 12774 | 12774 | 0 | 1898 |
| 26 | RAIGAD | 7406 | 6302 | 6302 | 0 | 1104 |
| 27 | RATNAGIRI | 7129 | 6677 | 6677 | 0 | 452 |
| 28 | SANGLI | 8732 | 8603 | 8603 | 0 | 129 |
| 29 | SATARA | 10647 | 10647 | 10647 | 0 | 0 |
| 30 | SINDHUDURG | 2141 | 2107 | 2107 | 0 | 34 |
| 31 | SOLAPUR | 18718 | 18445 | 18445 | 0 | 273 |
| 32 | WARDHA | 13147 | 11193 | 11193 | 0 | 1954 |
| 33 | WASHIM | 11500 | 10057 | 10057 | 0 | 1443 |
| 34 | YAVATMAL | 29681 | 26109 | 26109 | 0 | 3572 |
| Total | | 668852 | 553884 | 554127 | 243 | 114725 |

Remaining Sanction RANK

| | |
|------------|-------|
| SATARA | 0 |
| SINDHUDURG | 34 |
| KOLHAPUR | 37 |
| SANGLI | 129 |
| SOLAPUR | 273 |
| RATNAGIRI | 452 |
| PALGHAR | 790 |
| LATUR | 972 |
| RAIGAD | 1104 |
| JALNA | 1219 |
| THANE | 1298 |
| GONDIA | 1391 |
| WASHIM | 1443 |
| GADCHIROLI | 1632 |
| BULDHANA | 1641 |
| BEED | 1887 |
| PUNE | 1898 |
| WARDHA | 1954 |
| BHANDARA | 2126 |
| PARBHANI | 2160 |
| AURANGABAD | 2299 |
| AHMEDNAGAR | 2325 |
| JALGAON | 3121 |
| AMRAVATI | 3412 |
| YAVATMAL | 3572 |
| DHULE | 3810 |
| NAGPUR | 5161 |
| NANDED | 5922 |
| AKOLA | 5986 |
| OSMANABAD | 7814 |
| NASHIK | 9196 |
| HINGOLI | 11784 |
| NANDURBAR | 12441 |
| CHANDRAPUR | 15442 |

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | Division | Sanction | 20.04.2023 | 21.04.2023 | Daily_Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|-----------------|---------------|---------------|---------------|-------------------|---------------|---|--|
| 1 | AURANGABAD DIV. | 165274 | 103768 | 103887 | 119 | 61387 | 91 | 1364 |
| 2 | AMRAVATI DIV. | 93648 | 64657 | 64741 | 84 | 28907 | 56 | 642 |
| 3 | NAGPUR DIV. | 90687 | 69293 | 69354 | 61 | 21333 | 45 | 474 |
| 4 | NASHIK DIV. | 110467 | 88892 | 88927 | 35 | 21540 | 72 | 479 |
| 5 | PUNE DIV. | 62997 | 51910 | 51941 | 31 | 11056 | 26 | 246 |
| 6 | KONKAN DIV. | 31054 | 23620 | 23631 | 11 | 7423 | 15 | 165 |
| Total | | 554127 | 402140 | 402481 | 341 | 151646 | 304 | 3370 |

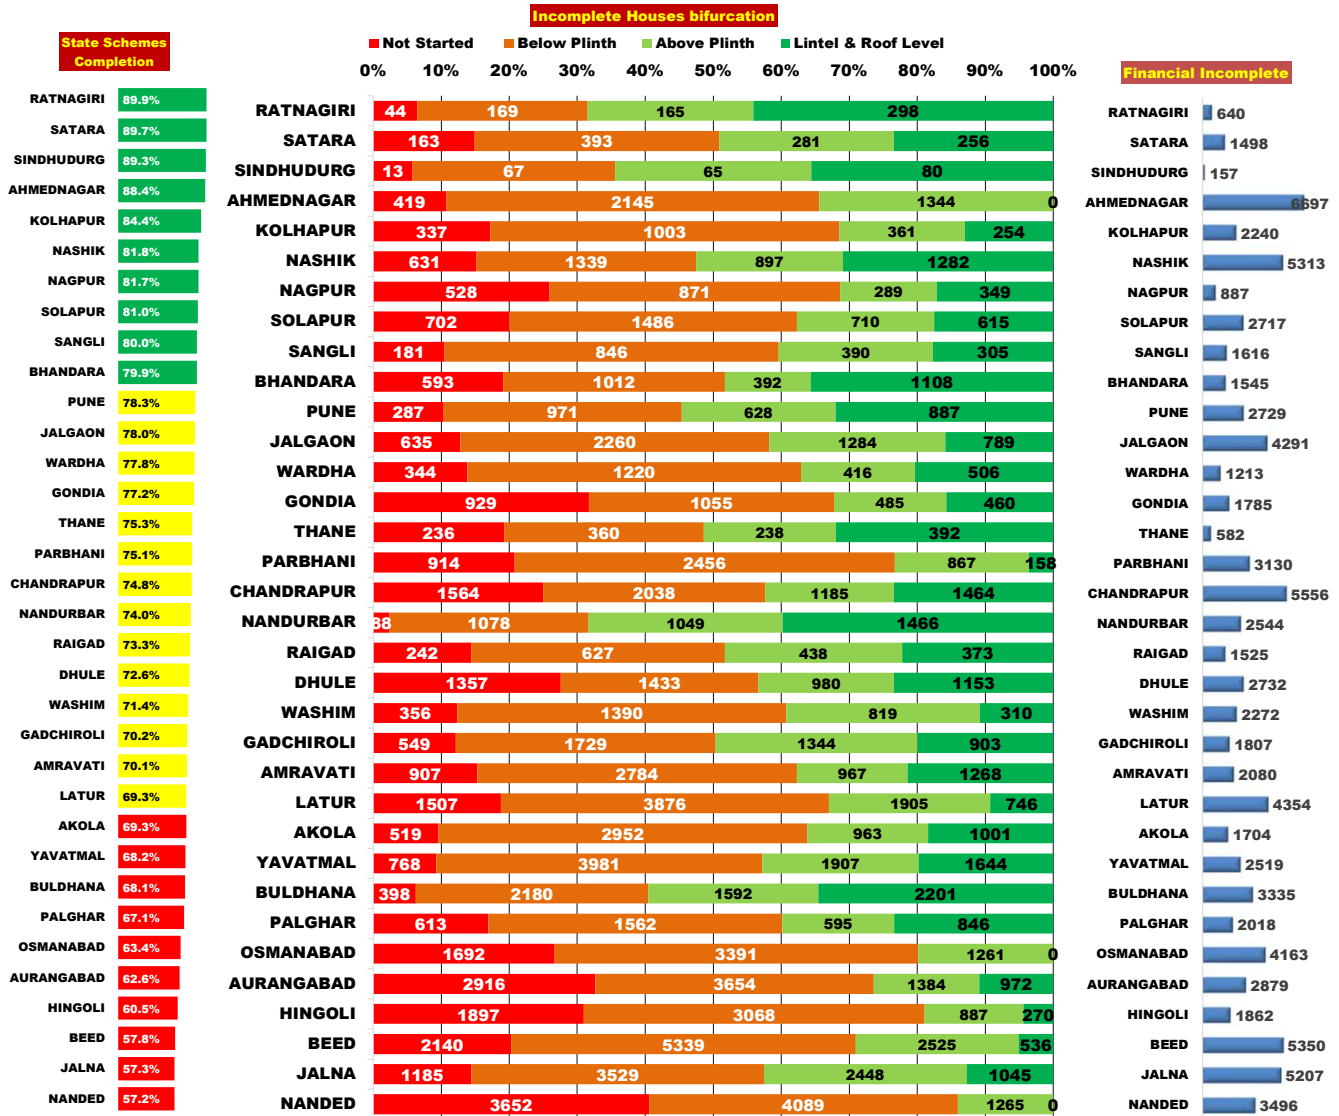

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

| Sr. No. | District | Sanction | 20.04.2023 | 21.04.2023 | Daily Achievement | Remaining | Avg. Completed Per Day From 20.11.22 to Today | To be Completed in Per Day till 05.06.23 |
|--------------|------------|---------------|---------------|---------------|-------------------|---------------|---|--|
| 1 | LATUR | 26199 | 18129 | 18165 | 36 | 8034 | 13 | 179 |
| 2 | WASHIM | 10057 | 7147 | 7182 | 35 | 2875 | 8 | 64 |
| 3 | BEED | 24991 | 14428 | 14451 | 23 | 10540 | 14 | 234 |
| 4 | GONDIA | 12855 | 9905 | 9926 | 21 | 2929 | 8 | 65 |
| 5 | JALNA | 19227 | 10999 | 11020 | 21 | 8207 | 25 | 182 |
| 6 | AKOLA | 17695 | 12241 | 12260 | 19 | 5435 | 9 | 121 |
| 7 | YAVATMAL | 26109 | 17793 | 17809 | 16 | 8300 | 13 | 184 |
| 8 | CHANDRAPUR | 24843 | 18579 | 18592 | 13 | 6251 | 13 | 139 |
| 9 | BULDHANA | 19975 | 13592 | 13604 | 12 | 6371 | 17 | 142 |
| 10 | NAGPUR | 11130 | 9081 | 9093 | 12 | 2037 | 4 | 45 |
| 11 | OSMANABAD | 17039 | 10784 | 10796 | 12 | 6243 | 11 | 139 |
| 12 | HINGOLI | 15514 | 9381 | 9392 | 11 | 6122 | 6 | 136 |
| 13 | AHMEDNAGAR | 32973 | 29144 | 29154 | 10 | 3819 | 30 | 85 |
| 14 | DHULE | 17980 | 13048 | 13057 | 9 | 4923 | 10 | 109 |
| 15 | GADCHIROLI | 15202 | 10668 | 10677 | 9 | 4525 | 9 | 101 |
| 16 | AURANGABAD | 23842 | 14908 | 14916 | 8 | 8926 | 9 | 198 |
| 17 | KOLHAPUR | 12528 | 10565 | 10573 | 8 | 1955 | 3 | 43 |
| 18 | SOLAPUR | 18445 | 14924 | 14932 | 8 | 3513 | 7 | 78 |
| 19 | NANDED | 20838 | 11912 | 11918 | 6 | 8920 | 9 | 198 |
| 20 | NANDURBAR | 14137 | 10450 | 10456 | 6 | 3681 | 7 | 82 |
| 21 | PUNE | 12774 | 9995 | 10001 | 6 | 2773 | 6 | 62 |
| 22 | SATARA | 10647 | 9548 | 9554 | 6 | 1093 | 6 | 24 |
| 23 | JALGAON | 22538 | 17565 | 17570 | 5 | 4968 | 12 | 110 |
| 24 | NASHIK | 22839 | 18685 | 18690 | 5 | 4149 | 13 | 92 |
| 25 | WARDHA | 11193 | 8702 | 8707 | 5 | 2486 | 7 | 55 |
| 26 | RAIGAD | 6302 | 4618 | 4622 | 4 | 1680 | 3 | 37 |
| 27 | PALGHAR | 11002 | 7383 | 7386 | 3 | 3616 | 6 | 80 |
| 28 | RATNAGIRI | 6677 | 5998 | 6001 | 3 | 676 | 3 | 15 |
| 29 | SANGLI | 8603 | 6878 | 6881 | 3 | 1722 | 4 | 38 |
| 30 | AMRAVATI | 19812 | 13884 | 13886 | 2 | 5926 | 9 | 132 |
| 31 | PARBHANI | 17624 | 13227 | 13229 | 2 | 4395 | 4 | 98 |
| 32 | BHANDARA | 15464 | 12358 | 12359 | 1 | 3105 | 4 | 69 |
| 33 | THANE | 4966 | 3739 | 3740 | 1 | 1226 | 2 | 27 |
| 34 | SINDHUDURG | 2107 | 1882 | 1882 | 0 | 225 | 1 | 5 |
| Total | | 554127 | 402140 | 402481 | 341 | 151646 | 304 | 3370 |

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | Division | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|--------------|-----------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | NAGPUR DIV. | 73 | 11316 | 501 | 22874 | 706 | 14153 |
| 2 | AMRAVATI DIV. | 99 | 32549 | 402 | 34622 | 396 | 15807 |
| 3 | AURANGABAD DIV. | 101 | 21425 | 301 | 56791 | 409 | 22584 |
| 4 | NASHIK DIV. | 51 | 11676 | 203 | 41891 | 326 | 23275 |
| 5 | KONKAN DIV. | 8 | 578 | 134 | 4016 | 345 | 4116 |
| 6 | PUNE DIV. | 32 | 10539 | 134 | 17153 | 211 | 7096 |
| Total | | 364 | 88083 | 1675 | 177347 | 2393 | 87031 |

PMAY-G 1st Ins Pending

| | |
|------------|-------|
| SINDHUDURG | 5 |
| RAIGAD | 15 |
| THANE | 103 |
| RATNAGIRI | 107 |
| PALGHAR | 348 |
| GADCHIROLI | 408 |
| KOLHAPUR | 553 |
| SANGLI | 732 |
| SATARA | 954 |
| DHULE | 1151 |
| NASHIK | 1214 |
| PARBHANI | 1274 |
| NANDURBAR | 1503 |
| GONDIA | 1615 |
| WARDHA | 1665 |
| NAGPUR | 2065 |
| JALNA | 2076 |
| HINGOLI | 2093 |
| PUNE | 2292 |
| CHANDRAPUR | 2299 |
| LATUR | 2423 |
| AURANGABAD | 3048 |
| AHMEDNAGAR | 3145 |
| BHANDARA | 3264 |
| OSMANABAD | 3267 |
| WASHIM | 3270 |
| NANDED | 3594 |
| BEED | 3650 |
| AKOLA | 4217 |
| YAVATMAL | 4351 |
| JALGAON | 4663 |
| SOLAPUR | 6008 |
| BULDHANA | 8630 |
| AMRAVATI | 12081 |

PMAY-G 2nd Ins Pending

| | |
|------------|-------|
| SINDHUDURG | 273 |
| RATNAGIRI | 486 |
| RAIGAD | 567 |
| THANE | 707 |
| SATARA | 1275 |
| WARDHA | 1305 |
| OSMANABAD | 1968 |
| PALGHAR | 1983 |
| PUNE | 2367 |
| KOLHAPUR | 2737 |
| GADCHIROLI | 2980 |
| NAGPUR | 3066 |
| HINGOLI | 3406 |
| WASHIM | 3610 |
| AHMEDNAGAR | 4090 |
| SANGLI | 4198 |
| GONDIA | 4736 |
| LATUR | 4794 |
| CHANDRAPUR | 5087 |
| JALNA | 5294 |
| AKOLA | 5318 |
| BHANDARA | 5700 |
| AURANGABAD | 6074 |
| BULDHANA | 6463 |
| NASHIK | 6500 |
| SOLAPUR | 6576 |
| PARBHANI | 6834 |
| DHULE | 7177 |
| BEED | 8625 |
| AMRAVATI | 9260 |
| YAVATMAL | 9971 |
| NANDURBAR | 10888 |
| JALGAON | 13236 |
| NANDED | 19796 |

PMAY-G 3rd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 391 |
| RAIGAD | 409 |
| RATNAGIRI | 486 |
| THANE | 709 |
| KOLHAPUR | 1031 |
| WARDHA | 1039 |
| PUNE | 1079 |
| SATARA | 1142 |
| HINGOLI | 1350 |
| NAGPUR | 1504 |
| SANGLI | 1514 |
| LATUR | 1770 |
| AKOLA | 1960 |
| PALGHAR | 2121 |
| PARBHANI | 2266 |
| SOLAPUR | 2330 |
| WASHIM | 2384 |
| JALNA | 2385 |
| GADCHIROLI | 2441 |
| AURANGABAD | 2534 |
| BHANDARA | 2569 |
| CHANDRAPUR | 2857 |
| BULDHANA | 2869 |
| OSMANABAD | 2937 |
| AMRAVATI | 3217 |
| AHMEDNAGAR | 3480 |
| BEED | 3490 |
| GONDIA | 3743 |
| DHULE | 3801 |
| JALGAON | 4059 |
| NASHIK | 4118 |
| YAVATMAL | 5377 |
| NANDED | 5852 |
| NANDURBAR | 7817 |

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | District | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|---------|--------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | CHANDRAPUR | 28 | 2299 | 186 | 5087 | 325 | 2857 |
| 2 | YAVATMAL | 12 | 4351 | 230 | 9971 | 179 | 5377 |
| 3 | BHANDARA | 25 | 3264 | 167 | 5700 | 182 | 2569 |
| 4 | PALGHAR | 0 | 348 | 104 | 1983 | 263 | 2121 |
| 5 | NANDED | 33 | 3594 | 81 | 19796 | 149 | 5852 |
| 6 | GONDIA | 12 | 1615 | 99 | 4736 | 131 | 3743 |
| 7 | DHULE | 21 | 1151 | 70 | 7177 | 124 | 3801 |
| 8 | BEED | 29 | 3650 | 76 | 8625 | 95 | 3490 |
| 9 | AHMEDNAGAR | 10 | 3145 | 65 | 4090 | 124 | 3480 |
| 10 | BULDHANA | 52 | 8630 | 53 | 6463 | 46 | 2869 |
| 11 | AMRAVATI | 30 | 12081 | 45 | 9260 | 56 | 3217 |
| 12 | SOLAPUR | 23 | 6008 | 46 | 6576 | 59 | 2330 |
| 13 | SATARA | 9 | 954 | 37 | 1275 | 71 | 1142 |
| 14 | AKOLA | 5 | 4217 | 45 | 5318 | 52 | 1960 |
| 15 | WASHIM | 0 | 3270 | 29 | 3610 | 63 | 2384 |
| 16 | NAGPUR | -37 | 2065 | 33 | 3066 | 55 | 1504 |
| 17 | KOLHAPUR | 0 | 553 | 29 | 2737 | 58 | 1031 |
| 18 | LATUR | 7 | 2423 | 27 | 4794 | 51 | 1770 |
| 19 | JALNA | 2 | 2076 | 30 | 5294 | 36 | 2385 |
| 20 | NASHIK | 0 | 1214 | 29 | 6500 | 33 | 4118 |
| 21 | PARBHANI | 9 | 1274 | 25 | 6834 | 24 | 2266 |
| 22 | HINGOLI | 0 | 2093 | 30 | 3406 | 27 | 1350 |
| 23 | NANDURBAR | 0 | 1503 | 27 | 10888 | 26 | 7817 |
| 24 | JALGAON | 20 | 4663 | 12 | 13236 | 19 | 4059 |
| 25 | RATNAGIRI | 7 | 107 | 3 | 486 | 39 | 486 |
| 26 | OSMANABAD | 20 | 3267 | 14 | 1968 | 12 | 2937 |
| 27 | AURANGABAD | 1 | 3048 | 18 | 6074 | 15 | 2534 |
| 28 | SANGLI | 0 | 732 | 16 | 4198 | 17 | 1514 |
| 29 | SINDHUDURG | 0 | 5 | 14 | 273 | 13 | 391 |
| 30 | RAIGAD | -1 | 15 | 11 | 567 | 15 | 409 |
| 31 | WARDHA | 2 | 1665 | 15 | 1305 | 9 | 1039 |
| 32 | THANE | 1 | 103 | 2 | 707 | 15 | 709 |
| 33 | PUNE | 0 | 2292 | 6 | 2367 | 6 | 1079 |
| 34 | GADCHIROLI | 6 | 408 | 1 | 2980 | 4 | 2441 |
| | Total | 364 | 88083 | 1675 | 177347 | 2393 | 87031 |

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

| Sr. No. | Division | 1st Installment (Daily Achievement) | 1st Installment Remaining | 2nd Installment (Daily Achievement) | 2nd Installment Remaining | 3rd Installment (Daily Achievement) | 3rd Installment Remaining |
|--------------|-----------------|-------------------------------------|---------------------------|-------------------------------------|---------------------------|-------------------------------------|---------------------------|
| 1 | AURANGABAD DIV. | 626 | 15903 | 342 | 29402 | 256 | 12542 |
| 2 | AMRAVATI DIV. | 150 | 2948 | 215 | 13287 | 244 | 6248 |
| 3 | KONKAN DIV. | 210 | 1148 | 75 | 2785 | 48 | 1501 |
| 4 | NAGPUR DIV. | 131 | 4507 | 73 | 7925 | 63 | 4111 |
| 5 | NASHIK DIV. | 76 | 3130 | 84 | 8255 | 99 | 5554 |
| 6 | PUNE DIV. | 23 | 1670 | 46 | 4699 | 47 | 2370 |
| Total | | 1216 | 29306 | 835 | 66353 | 757 | 32326 |

State Schemes 1st Ins Pending

| | |
|------------|------|
| SINDHUDURG | 13 |
| RATNAGIRI | 44 |
| NANDURBAR | 88 |
| SATARA | 163 |
| SANGLI | 181 |
| THANE | 236 |
| RAIGAD | 242 |
| PUNE | 287 |
| KOLHAPUR | 337 |
| WARDHA | 344 |
| WASHIM | 356 |
| BULDHANA | 398 |
| AHMEDNAGAR | 419 |
| AKOLA | 519 |
| NAGPUR | 528 |
| GADCHIROLI | 549 |
| BHANDARA | 593 |
| PALGHAR | 613 |
| NASHIK | 631 |
| JALGAON | 635 |
| SOLAPUR | 702 |
| YAVATMAL | 768 |
| AMRAVATI | 907 |
| PARBHANI | 914 |
| GONDIA | 929 |
| JALNA | 1185 |
| DHULE | 1357 |
| LATUR | 1507 |
| CHANDRAPUR | 1564 |
| OSMANABAD | 1692 |
| HINGOLI | 1897 |
| BEED | 2140 |
| AURANGABAD | 2916 |
| NANDED | 3652 |

State Schemes 2nd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 67 |
| RATNAGIRI | 169 |
| THANE | 360 |
| SATARA | 393 |
| RAIGAD | 627 |
| SANGLI | 846 |
| NAGPUR | 871 |
| PUNE | 971 |
| KOLHAPUR | 1003 |
| BHANDARA | 1012 |
| GONDIA | 1055 |
| NANDURBAR | 1078 |
| WARDHA | 1220 |
| NASHIK | 1339 |
| WASHIM | 1390 |
| DHULE | 1433 |
| SOLAPUR | 1486 |
| PALGHAR | 1562 |
| GADCHIROLI | 1729 |
| CHANDRAPUR | 2038 |
| AHMEDNAGAR | 2145 |
| BULDHANA | 2180 |
| JALGAON | 2260 |
| PARBHANI | 2456 |
| AMRAVATI | 2784 |
| AKOLA | 2952 |
| HINGOLI | 3068 |
| OSMANABAD | 3391 |
| JALNA | 3529 |
| AURANGABAD | 3654 |
| LATUR | 3876 |
| YAVATMAL | 3981 |
| NANDED | 4089 |
| BEED | 5339 |

State Schemes 3rd Ins Pending

| | |
|------------|------|
| SINDHUDURG | 65 |
| RATNAGIRI | 165 |
| THANE | 238 |
| SATARA | 281 |
| NAGPUR | 289 |
| KOLHAPUR | 361 |
| SANGLI | 390 |
| BHANDARA | 392 |
| WARDHA | 416 |
| RAIGAD | 438 |
| GONDIA | 485 |
| PALGHAR | 595 |
| PUNE | 628 |
| SOLAPUR | 710 |
| WASHIM | 819 |
| PARBHANI | 867 |
| HINGOLI | 887 |
| NASHIK | 897 |
| AKOLA | 963 |
| AMRAVATI | 967 |
| DHULE | 980 |
| NANDURBAR | 1049 |
| CHANDRAPUR | 1185 |
| OSMANABAD | 1261 |
| NANDED | 1265 |
| JALGAON | 1284 |
| GADCHIROLI | 1344 |
| AHMEDNAGAR | 1344 |
| AURANGABAD | 1384 |
| BULDHANA | 1592 |
| LATUR | 1905 |
| YAVATMAL | 1907 |
| JALNA | 2448 |
| BEED | 2525 |

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

| Sr. No. | District | 1st Installment (Daily Achivement) | 1st Installment Remaining | 2nd Installment (Daily Achivement) | 2nd Installment Remaining | 3rd Installment (Daily Achivement) | 3rd Installment Remaining |
|---------|--------------|------------------------------------|---------------------------|------------------------------------|---------------------------|------------------------------------|---------------------------|
| 1 | NANDED | 184 | 3652 | 40 | 4089 | 26 | 1265 |
| 2 | PARBHANI | 176 | 914 | 24 | 2456 | 31 | 867 |
| 3 | PALGHAR | 119 | 613 | 42 | 1562 | 26 | 595 |
| 4 | LATUR | 14 | 1507 | 87 | 3876 | 80 | 1905 |
| 5 | AURANGABAD | 113 | 2916 | 39 | 3654 | 25 | 1384 |
| 6 | AMRAVATI | 68 | 907 | 45 | 2784 | 42 | 967 |
| 7 | JALNA | 21 | 1185 | 67 | 3529 | 65 | 2448 |
| 8 | BULDHANA | 8 | 398 | 53 | 2180 | 77 | 1592 |
| 9 | THANE | 91 | 236 | 10 | 360 | 11 | 238 |
| 10 | BEED | 37 | 2140 | 47 | 5339 | 26 | 2525 |
| 11 | WASHIM | 9 | 356 | 53 | 1390 | 48 | 819 |
| 12 | AKOLA | 57 | 519 | 24 | 2952 | 26 | 963 |
| 13 | YAVATMAL | 8 | 768 | 40 | 3981 | 51 | 1907 |
| 14 | JALGAON | 24 | 635 | 38 | 2260 | 35 | 1284 |
| 15 | HINGOLI | 69 | 1897 | 20 | 3068 | 2 | 887 |
| 16 | CHANDRAPUR | 61 | 1564 | 15 | 2038 | 11 | 1185 |
| 17 | NAGPUR | 49 | 528 | 8 | 871 | 9 | 289 |
| 18 | NASHIK | 23 | 631 | 14 | 1339 | 21 | 897 |
| 19 | GONDIA | 13 | 929 | 20 | 1055 | 16 | 485 |
| 20 | AHMEDNAGAR | 4 | 419 | 22 | 2145 | 20 | 1344 |
| 21 | GADCHIROLI | 3 | 549 | 23 | 1729 | 16 | 1344 |
| 22 | KOLHAPUR | 0 | 337 | 22 | 1003 | 19 | 361 |
| 23 | DHULE | 24 | 1357 | 1 | 1433 | 12 | 980 |
| 24 | OSMANABAD | 12 | 1692 | 18 | 3391 | 1 | 1261 |
| 25 | RAIGAD | 0 | 242 | 20 | 627 | 7 | 438 |
| 26 | SOLAPUR | 2 | 702 | 6 | 1486 | 17 | 710 |
| 27 | SATARA | 15 | 163 | 4 | 393 | 5 | 281 |
| 28 | SANGLI | 4 | 181 | 12 | 846 | 6 | 390 |
| 29 | NANDURBAR | 1 | 88 | 9 | 1078 | 11 | 1049 |
| 30 | BHANDARA | 1 | 593 | 5 | 1012 | 7 | 392 |
| 31 | WARDHA | 4 | 344 | 2 | 1220 | 4 | 416 |
| 32 | PUNE | 2 | 287 | 2 | 971 | 0 | 628 |
| 33 | RATNAGIRI | 0 | 44 | 1 | 169 | 3 | 165 |
| 34 | SINDHUDURG | 0 | 13 | 2 | 67 | 1 | 65 |
| | Total | 1216 | 29306 | 835 | 66353 | 757 | 32326 |

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

