



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २२.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१०८४०	४०	१०३६६१९	५८०	३३	५८	११०
राज्य योजना	५५५५१६	१३९९	४०२७२८	२४७	३१७	५२५	५३१
एकूण	१९६६३५६	१४३९	१४३९३४७	८२७	३५०	५८३	६४१

PMAY-G Completion Progress Bar

73.5%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

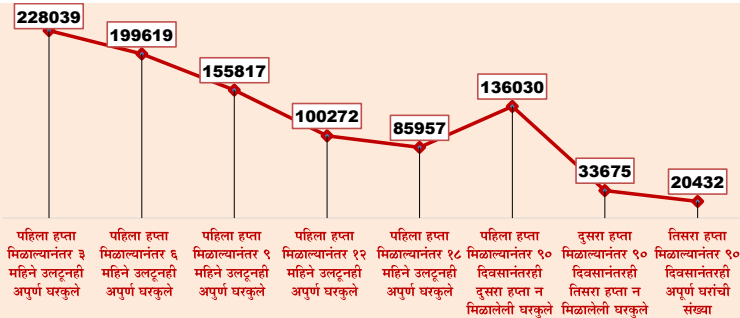

Abhiyan Achievement Day 153

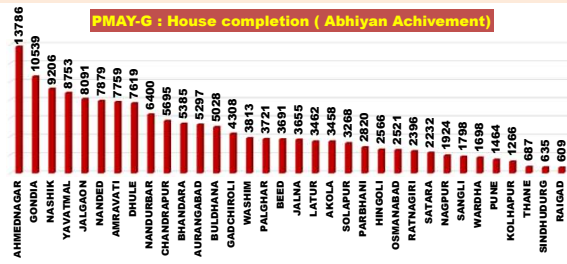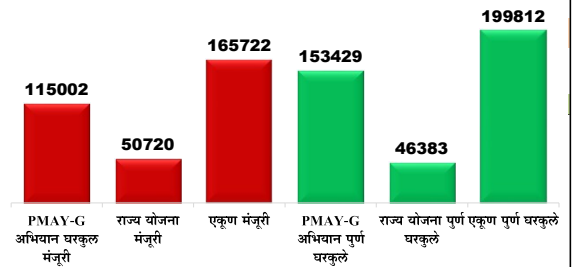


State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण
४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	21.04.2023	22.04.2023	Daily_Achievement	Remaining
1	PUNE DIV.	124804	123986	123978	26	826
2	NASHIK DIV.	414760	413748	413753	5	1007
3	AMRAVATI DIV.	275029	274579	274584	5	445
4	AURANGABAD DIV.	238068	237416	237420	4	648
5	NAGPUR DIV.	292090	291506	291469	0	621
6	KONKAN DIV.	69785	69636	69636	0	149
Total		1414536	1410871	1410840	40	3696

Sr. No.	District	Target (PWL+Awaas Plus)	21.04.2023	22.04.2023	Daily_Achievement	Remaining
1	SOLAPUR	49338	48647	48670	23	668
2	YAVATMAL	65355	65220	65225	5	130
3	LATUR	20679	20471	20475	4	204
4	NASHIK	89720	89660	89663	3	57
5	SATARA	15348	15341	15344	3	4
6	AHMEDNAGAR	60792	60762	60763	1	29
7	JALGAON	79748	79450	79451	1	297
8	AKOLA	48792	48778	48778	0	14
9	AMRAVATI	95712	95466	95466	0	246
10	AURANGABAD	36795	36666	36666	0	129
11	BEED	35310	35253	35253	0	57
12	BULDHANA	44766	44714	44714	0	52
13	DHULE	64979	64917	64917	0	62
14	GADCHIROLI	31698	31619	31619	0	79
15	HINGOLI	18109	18083	18083	0	26
16	JALNA	24039	24022	24022	0	17
17	KOLHAPUR	17685	17685	17685	0	0
18	NANDED	69533	69460	69460	0	73
19	NANDURBAR	119521	118959	118959	0	562
20	OSMANABAD	14506	14401	14401	0	105
21	PALGHAR	35312	35185	35185	0	127
22	PARBHANI	19097	19060	19060	0	37
23	PUNE	20543	20531	20531	0	12
24	RAIGAD	9831	9822	9822	0	9
25	RATNAGIRI	9895	9888	9888	0	7
26	SINDHUDURG	5142	5142	5142	0	0
27	THANE	9605	9599	9599	0	6
28	WARDHA	18633	18606	18606	0	27
29	WASHIM	20404	20401	20401	0	3
30	GONDIA	96492	96143	96142	-1	350
31	BHANDARA	65086	65066	65056	-10	30
32	NAGPUR	37059	37059	37047	-12	12
33	CHANDRAPUR	43122	43013	42999	-14	123
34	SANGLI	21890	21782	21748	-34	142
Total		1414536	1410871	1410840	40	3696

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
WASHIM	3
SATARA	4
THANE	6
RATNAGIRI	7
RAIGAD	9
NAGPUR	12
PUNE	12
AKOLA	14
JALNA	17
HINGOLI	26
WARDHA	27
AHMEDNAGAR	29
BHANDARA	30
PARBHANI	37
BULDHANA	52
BEED	57
NASHIK	57
DHULE	62
NANDED	73
GADCHIROLI	79
OSMANABAD	105
CHANDRAPUR	123
PALGHAR	127
AURANGABAD	129
YAVATMAL	130
SANGLI	142
LATUR	204
AMRAVATI	246
JALGAON	297
GONDIA	350
NANDURBAR	562
SOLAPUR	668

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	43	84	31
10	NANDED	362	277	85	362	242	120	35
11	BEED	212	101	111	212	72	140	29
12	SANGLI	431	143	288	430	141	289	2
13	PARBHANI	332	15	317	332	13	319	2
14	SATARA	1309	598	711	1304	628	676	-30
15	NASHIK	1804	1454	350	1804	715	1089	739
16	HINGOLI	1713	787	926	1713	466	1247	321
17	JALNA	1413	165	1248	1381	85	1296	80
18	WARDHA	2819	1284	1535	2803	1214	1589	70
19	NAGPUR	5134	3397	1737	5054	3412	1642	-15
20	GONDIA	2450	2450	0	2450	765	1685	1685
21	CHANDRAPUR	2791	1463	1328	2770	971	1799	492
22	PUNE	2925	992	1933	2924	885	2039	107
23	LATUR	2299	68	2231	2299	66	2233	2
24	OSMANABAD	2470	104	2366	2470	56	2414	48
25	YAVATMAL	3437	1119	2318	3611	1178	2433	-59
26	BHANDARA	5825	3230	2595	5792	3213	2579	17
27	WASHIM	3477	865	2612	3477	850	2627	15
28	AURANGABAD	3328	1779	1549	3328	288	3040	1491
29	AKOLA	7074	3842	3232	7074	3844	3230	-2
30	AHMEDNAGAR	7762	4828	2934	7756	3374	4382	1454
31	JALGAON	22872	21026	1846	22962	17824	5138	3202
32	SOLAPUR	7960	2595	5365	7431	791	6640	1804
33	BULDHANA	15256	8455	6801	15230	6970	8260	1485
34	AMRAVATI	21560	11238	10322	21560	10904	10656	334
	Total	127885	73092	54793	127399	59723	67676	13475

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	21.04.2023	22.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK DIV.	413753	328488	328616	128	85137	295	1935
2	NAGPUR DIV.	291469	237575	237677	102	53792	193	1223
3	AURANGABAD DIV.	237420	139353	139452	99	97968	208	2227
4	AMRAVATI DIV.	274584	185876	185968	92	88616	188	2014
5	KONKAN DIV.	69636	57375	57456	81	12180	53	277
6	PUNE DIV.	123978	87372	87450	78	36528	66	830
Total		1410840	1036039	1036619	580	374221	1003	8505

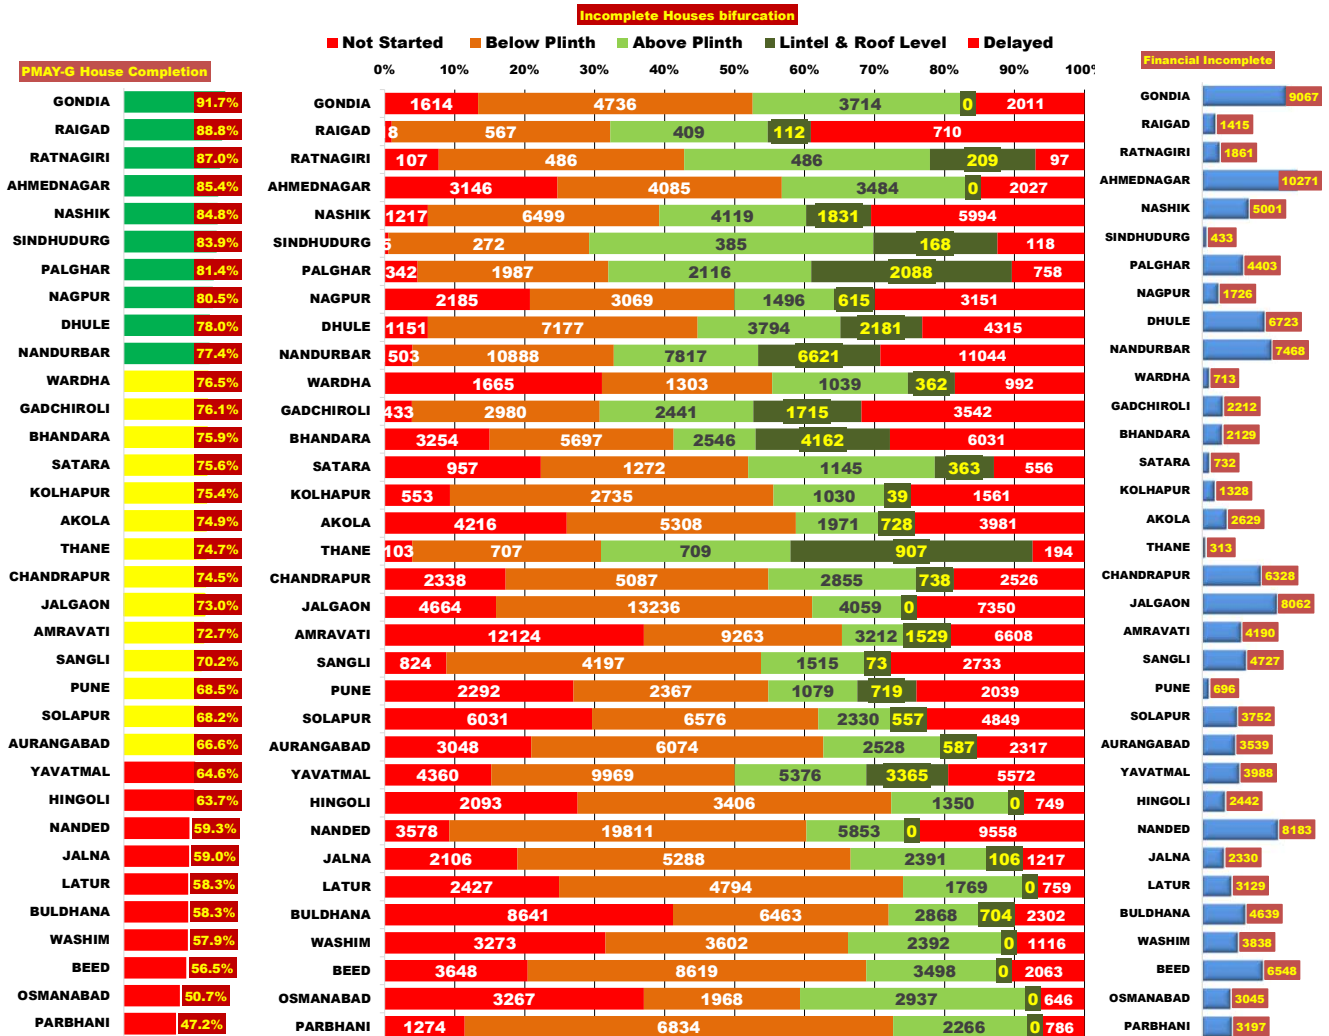

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	21.04.2023	22.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	JALGAON	79451	57956	58009	53	21442	53	487
2	YAVATMAL	65225	42112	42161	49	23064	57	524
3	PALGHAR	35185	28605	28652	47	6533	24	148
4	BHANDARA	65056	49356	49397	41	15659	35	356
5	NASHIK	89663	75968	75997	29	13666	60	311
6	BEED	35253	19892	19919	27	15334	24	349
7	AHMEDNAGAR	60763	51845	51866	21	8897	90	202
8	WASHIM	20401	11798	11819	21	8582	25	195
9	PUNE	20531	14055	14074	19	6457	10	147
10	JALNA	24022	14143	14161	18	9861	24	224
11	SANGLI	21748	15247	15265	18	6483	12	147
12	GADCHIROLI	31619	24058	24075	17	7544	28	171
13	SOLAPUR	48670	33160	33176	16	15494	21	352
14	GONDIA	96142	88102	88117	15	8025	69	182
15	CHANDRAPUR	42999	32020	32034	14	10965	37	249
16	LATUR	20475	11922	11936	14	8539	23	194
17	NAGPUR	37047	29803	29817	14	7230	13	164
18	NANDED	69460	41175	41189	14	28271	51	643
19	SATARA	15344	11593	11607	14	3737	15	85
20	AKOLA	48778	36542	36555	13	12223	23	278
21	NANDURBAR	118959	92117	92130	13	26829	42	610
22	RATNAGIRI	9888	8587	8600	13	1288	16	29
23	DHULE	64917	50602	50614	12	14303	50	325
24	KOLHAPUR	17685	13317	13328	11	4357	8	99
25	THANE	9599	7162	7173	11	2426	4	55
26	AURANGABAD	36666	24419	24429	10	12237	35	278
27	BULDHANA	44714	26040	26049	9	18665	33	424
28	HINGOLI	18083	11515	11524	9	6559	17	149
29	RAIGAD	9822	8710	8719	9	1103	4	25
30	PARBHANI	19060	8986	8993	7	10067	18	229
31	SINDHUDURG	5142	4311	4312	1	830	4	19
32	WARDHA	18606	14236	14237	1	4369	11	99
33	AMRAVATI	95466	69384	69384	0	26082	51	593
34	OSMANABAD	14401	7301	7301	0	7100	16	161
Total		1410840	1036039	1036619	580	374221	1003	8505

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	21.04.2023	22.04.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118393	90687	91848	1170	26545
2	AURANGABAD DIV.	199331	165274	165385	111	33946
3	NASHIK DIV.	141360	110467	110539	72	30821
4	AMRAVATI DIV.	109702	93648	93694	46	16008
5	KONKAN DIV.	34732	31054	31053	0	3679
6	PUNE DIV.	65334	62997	62997	0	2337
Total		668852	554127	555516	1399	113336


Sr. No.	District	Target	21.04.2023	22.04.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	24843	25893	1050	14392
2	BHANDARA	17590	15464	15558	94	2032
3	BEED	26878	24991	25076	85	1802
4	DHULE	21790	17980	18048	68	3742
5	AKOLA	23681	17695	17733	38	5948
6	WARDHA	13147	11193	11218	25	1929
7	NANDED	26760	20838	20860	22	5900
8	BULDHANA	21616	19975	19979	4	1637
9	NASHIK	32035	22839	22843	4	9192
10	YAVATMAL	29681	26109	26113	4	3568
11	PARBHANI	19784	17624	17627	3	2157
12	GADCHIROLI	16834	15202	15203	1	1631
13	JALNA	20446	19227	19228	1	1218
14	AHMEDNAGAR	35298	32973	32973	0	2325
15	AMRAVATI	23224	19812	19812	0	3412
16	AURANGABAD	26141	23842	23842	0	2299
17	HINGOLI	27298	15514	15514	0	11784
18	JALGAON	25659	22538	22538	0	3121
19	KOLHAPUR	12565	12528	12528	0	37
20	LATUR	27171	26199	26199	0	972
21	NAGPUR	16291	11130	11130	0	5161
22	NANDURBAR	26578	14137	14137	0	12441
23	OSMANABAD	24853	17039	17039	0	7814
24	PALGHAR	11792	11002	11002	0	790
25	PUNE	14672	12774	12774	0	1898
26	RAIGAD	7406	6302	6302	0	1104
27	RATNAGIRI	7129	6677	6677	0	452
28	SANGLI	8732	8603	8603	0	129
29	SATARA	10647	10647	10647	0	0
30	SINDHUDURG	2141	2107	2107	0	34
31	SOLAPUR	18718	18445	18445	0	273
32	WASHIM	11500	10057	10057	0	1443
33	THANE	6264	4966	4965	-1	1299
34	GONDIA	14246	12855	12846	-9	1400
Total		668852	554127	555516	1399	113336

Remaining Sanction RANK

SATARA	0
SINDHUDURG	34
KOLHAPUR	37
SANGLI	129
SOLAPUR	273
RATNAGIRI	452
PALGHAR	790
LATUR	972
RAIGAD	1104
JALNA	1218
THANE	1299
GONDIA	1400
WASHIM	1443
GADCHIROLI	1631
BULDHANA	1637
BEED	1802
PUNE	1898
WARDHA	1929
BHANDARA	2032
PARBHANI	2157
AURANGABAD	2299
AHMEDNAGAR	2325
JALGAON	3121
AMRAVATI	3412
YAVATMAL	3568
DHULE	3742
NAGPUR	5161
NANDED	5900
AKOLA	5948
OSMANABAD	7814
NASHIK	9192
HINGOLI	11784
NANDURBAR	12441
CHANDRAPUR	14392

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	21.04.2023	22.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	165385	103887	103957	70	61428	91	1396
2	NAGPUR DIV.	91848	69354	69394	40	22454	45	510
3	KONKAN DIV.	31053	23631	23668	37	7385	15	168
4	AMRAVATI DIV.	93694	64741	64777	36	28917	56	657
5	PUNE DIV.	62997	51941	51976	35	11021	26	250
6	NASHIK DIV.	110539	88927	88956	29	21583	71	491
Total		555516	402481	402728	247	152788	303	3472

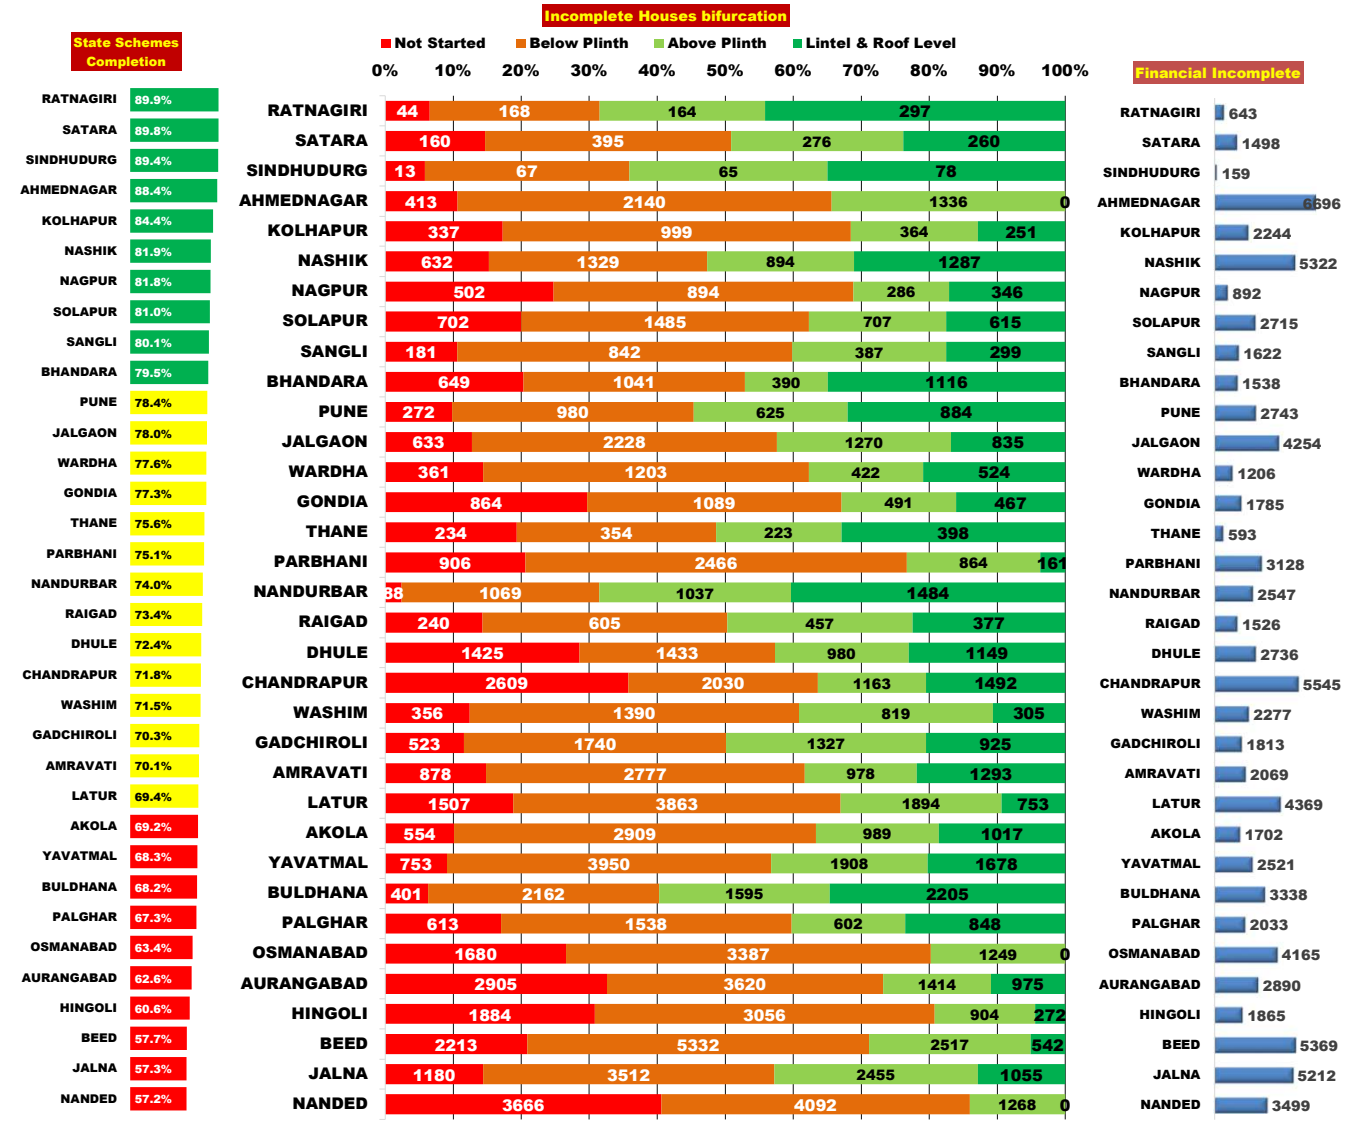

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	21.04.2023	22.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	BEED	25076	14451	14472	21	10604	14	241
2	LATUR	26199	18165	18182	17	8017	13	182
3	THANE	4965	3740	3756	16	1209	2	27
4	PALGHAR	11002	7386	7401	15	3601	6	82
5	YAVATMAL	26113	17809	17824	15	8289	13	188
6	SANGLI	8603	6881	6894	13	1709	4	39
7	AURANGABAD	23842	14916	14928	12	8914	9	203
8	BULDHANA	19979	13604	13616	12	6363	17	145
9	PUNE	12774	10001	10013	12	2761	6	63
10	GADCHIROLI	15203	10677	10688	11	4515	9	103
11	NASHIK	22843	18690	18701	11	4142	13	94
12	AHMEDNAGAR	32973	29154	29163	9	3810	30	87
13	GONDIA	12846	9926	9935	9	2911	8	66
14	NAGPUR	11130	9093	9102	9	2028	4	46
15	CHANDRAPUR	25893	18592	18599	7	7294	13	166
16	HINGOLI	15514	9392	9398	6	6116	6	139
17	JALNA	19228	11020	11026	6	8202	25	186
18	NANDED	20860	11918	11923	5	8937	9	203
19	WASHIM	10057	7182	7187	5	2870	8	65
20	AKOLA	17733	12260	12264	4	5469	9	124
21	DHULE	18048	13057	13061	4	4987	10	113
22	KOLHAPUR	12528	10573	10577	4	1951	3	44
23	SOLAPUR	18445	14932	14936	4	3509	7	80
24	BHANDARA	15558	12359	12362	3	3196	4	73
25	NANDURBAR	14137	10456	10459	3	3678	6	84
26	RATNAGIRI	6677	6001	6004	3	673	3	15
27	JALGAON	22538	17570	17572	2	4966	12	113
28	OSMANABAD	17039	10796	10798	2	6241	10	142
29	SATARA	10647	9554	9556	2	1091	6	25
30	SINDHUDURG	2107	1882	1884	2	223	1	5
31	PARBHANI	17627	13229	13230	1	4397	4	100
32	RAIGAD	6302	4622	4623	1	1679	3	38
33	WARDHA	11218	8707	8708	1	2510	7	57
34	AMRAVATI	19812	13886	13886	0	5926	9	135
	Total	555516	402481	402728	247	152788	303	3472

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NAGPUR DIV.	3	11276	5	22872	67	14091
2	AMRAVATI DIV.	6	32548	23	34605	11	15819
3	AURANGABAD DIV.	18	21411	15	56794	7	22592
4	KONKAN DIV.	6	572	3	4019	14	4105
5	NASHIK DIV.	0	11681	6	41885	8	23273
6	PUNE DIV.	0	10531	6	17147	3	7099
Total		33	88019	58	177322	110	86979

PMAY-G 1st Ins Pending

SINDHUDURG	5
RAIGAD	15
THANE	103
RATNAGIRI	107
PALGHAR	342
GADCHIROLI	408
KOLHAPUR	553
SANGLI	698
SATARA	957
DHULE	1151
NASHIK	1217
PARBHANI	1274
NANDURBAR	1503
GONDIA	1614
WARDHA	1665
NAGPUR	2050
JALNA	2076
HINGOLI	2093
CHANDRAPUR	2285
PUNE	2292
LATUR	2427
AURANGABAD	3048
AHMEDNAGAR	3146
BHANDARA	3254
OSMANABAD	3267
WASHIM	3270
NANDED	3578
BEED	3648
AKOLA	4216
YAVATMAL	4354
JALGAON	4664
SOLAPUR	6031
BULDHANA	8630
AMRAVATI	12078

PMAY-G 2nd Ins Pending

SINDHUDURG	272
RATNAGIRI	486
RAIGAD	567
THANE	707
SATARA	1272
WARDHA	1303
OSMANABAD	1968
PALGHAR	1987
PUNE	2367
KOLHAPUR	2735
GADCHIROLI	2980
NAGPUR	3069
HINGOLI	3406
WASHIM	3602
AHMEDNAGAR	4085
SANGLI	4197
GONDIA	4736
LATUR	4794
CHANDRAPUR	5087
JALNA	5288
AKOLA	5308
BHANDARA	5697
AURANGABAD	6074
BULDHANA	6463
NASHIK	6499
SOLAPUR	6576
PARBHANI	6834
DHULE	7177
BEED	8619
AMRAVATI	9263
YAVATMAL	9969
NANDURBAR	10888
JALGAON	13236
NANDED	19811

PMAY-G 3rd Ins Pending

SINDHUDURG	385
RAIGAD	409
RATNAGIRI	486
THANE	709
KOLHAPUR	1030
WARDHA	1039
PUNE	1079
SATARA	1145
HINGOLI	1350
NAGPUR	1496
SANGLI	1515
LATUR	1769
AKOLA	1971
PALGHAR	2116
PARBHANI	2266
SOLAPUR	2330
JALNA	2391
WASHIM	2392
GADCHIROLI	2441
AURANGABAD	2528
BHANDARA	2546
CHANDRAPUR	2855
BULDHANA	2868
OSMANABAD	2937
AMRAVATI	3212
AHMEDNAGAR	3484
BEED	3498
GONDIA	3714
DHULE	3794
JALGAON	4059
NASHIK	4119
YAVATMAL	5376
NANDED	5853
NANDURBAR	7817

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	BHANDARA	0	3254	3	5697	26	2546
2	GONDIA	0	1614	0	4736	29	3714
3	NANDED	16	3578	1	19811	0	5853
4	PALGHAR	6	342	2	1987	7	2116
5	AKOLA	1	4216	11	5308	0	1971
6	NAGPUR	3	2050	0	3069	8	1496
7	YAVATMAL	2	4354	4	9969	5	5376
8	BEED	2	3648	8	8619	0	3498
9	AMRAVATI	3	12078	0	9263	5	3212
10	SINDHUDURG	0	5	1	272	7	385
11	WASHIM	0	3270	8	3602	0	2392
12	DHULE	0	1151	0	7177	7	3794
13	AHMEDNAGAR	0	3146	5	4085	1	3484
14	AURANGABAD	0	3048	0	6074	6	2528
15	JALNA	0	2076	6	5288	0	2391
16	KOLHAPUR	0	553	2	2735	3	1030
17	WARDHA	0	1665	2	1303	2	1039
18	SATARA	0	957	3	1272	0	1145
19	CHANDRAPUR	0	2285	0	5087	2	2855
20	BULDHANA	0	8630	0	6463	1	2868
21	LATUR	0	2427	0	4794	1	1769
22	NASHIK	0	1217	1	6499	0	4119
23	SANGLI	0	698	1	4197	0	1515
24	GADCHIROLI	0	408	0	2980	0	2441
25	HINGOLI	0	2093	0	3406	0	1350
26	JALGAON	0	4664	0	13236	0	4059
27	NANDURBAR	0	1503	0	10888	0	7817
28	OSMANABAD	0	3267	0	1968	0	2937
29	PARBHANI	0	1274	0	6834	0	2266
30	PUNE	0	2292	0	2367	0	1079
31	RAIGAD	0	15	0	567	0	409
32	RATNAGIRI	0	107	0	486	0	486
33	SOLAPUR	0	6031	0	6576	0	2330
34	THANE	0	103	0	707	0	709
	Total	33	88019	58	177322	110	86979

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NAGPUR DIV.	160	5508	88	7997	120	4079
2	AURANGABAD DIV.	73	15941	147	29328	124	12565
3	AMRAVATI DIV.	52	2942	151	13188	110	6289
4	NASHIK DIV.	11	3191	67	8199	104	5517
5	KONKAN DIV.	3	1144	56	2732	46	1511
6	PUNE DIV.	18	1652	16	4701	27	2359
Total		317	30378	525	66145	531	32320

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	44
NANDURBAR	88
SATARA	160
SANGLI	181
THANE	234
RAIGAD	240
PUNE	272
KOLHAPUR	337
WASHIM	356
WARDHA	361
BULDHANA	401
AHMEDNAGAR	413
NAGPUR	502
GADCHIROLI	523
AKOLA	554
PALGHAR	613
NASHIK	632
JALGAON	633
BHANDARA	649
SOLAPUR	702
YAVATMAL	753
GONDIA	864
AMRAVATI	878
PARBHANI	906
JALNA	1180
DHULE	1425
LATUR	1507
OSMANABAD	1680
HINGOLI	1884
BEED	2213
CHANDRAPUR	2609
AURANGABAD	2905
NANDED	3666

State Schemes 2nd Ins Pending

SINDHUDURG	67
RATNAGIRI	168
THANE	354
SATARA	395
RAIGAD	605
SANGLI	842
NAGPUR	894
PUNE	980
KOLHAPUR	999
BHANDARA	1041
NANDURBAR	1069
GONDIA	1089
WARDHA	1203
NASHIK	1329
WASHIM	1390
DHULE	1433
SOLAPUR	1485
PALGHAR	1538
GADCHIROLI	1740
CHANDRAPUR	2030
AHMEDNAGAR	2140
BULDHANA	2162
JALGAON	2228
PARBHANI	2466
AMRAVATI	2777
AKOLA	2909
HINGOLI	3056
OSMANABAD	3387
JALNA	3512
AURANGABAD	3620
LATUR	3863
YAVATMAL	3950
NANDED	4092
BEED	5332

State Schemes 3rd Ins Pending

SINDHUDURG	65
RATNAGIRI	164
THANE	223
SATARA	276
NAGPUR	286
KOLHAPUR	364
SANGLI	387
BHANDARA	390
WARDHA	422
RAIGAD	457
GONDIA	491
PALGHAR	602
PUNE	625
SOLAPUR	707
WASHIM	819
PARBHANI	864
NASHIK	894
HINGOLI	904
AMRAVATI	978
DHULE	980
AKOLA	989
NANDURBAR	1037
CHANDRAPUR	1163
OSMANABAD	1249
NANDED	1268
JALGAON	1270
GADCHIROLI	1327
AHMEDNAGAR	1336
AURANGABAD	1414
BULDHANA	1595
LATUR	1894
YAVATMAL	1908
JALNA	2455
BEED	2517

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	YAVATMAL	19	753	50	3950	49	1908
2	GONDIA	56	864	22	1089	16	491
3	AMRAVATI	29	878	36	2777	25	978
4	JALGAON	2	633	34	2228	48	1270
5	GADCHIROLI	27	523	16	1740	33	1327
6	AURANGABAD	11	2905	45	3620	15	1414
7	AKOLA	3	554	46	2909	20	989
8	BEED	12	2213	19	5332	27	2517
9	BHANDARA	38	649	9	1041	11	390
10	OSMANABAD	12	1680	16	3387	28	1249
11	CHANDRAPUR	5	2609	13	2030	35	1163
12	WARDHA	8	361	25	1203	19	422
13	HINGOLI	13	1884	25	3056	8	904
14	JALNA	6	1180	23	3512	16	2455
15	PALGHAR	0	613	24	1538	17	602
16	LATUR	0	1507	13	3863	24	1894
17	AHMEDNAGAR	6	413	11	2140	19	1336
18	BULDHANA	1	401	19	2162	16	1595
19	NAGPUR	26	502	3	894	6	286
20	NASHIK	3	632	13	1329	16	894
21	RAIGAD	2	240	24	605	5	457
22	NANDURBAR	0	88	9	1069	21	1037
23	PUNE	15	272	6	980	9	625
24	THANE	1	234	7	354	22	223
25	PARBHANI	11	906	1	2466	4	864
26	NANDED	8	3666	5	4092	2	1268
27	SANGLI	0	181	4	842	7	387
28	SATARA	3	160	1	395	6	276
29	KOLHAPUR	0	337	4	999	1	364
30	SOLAPUR	0	702	1	1485	4	707
31	RATNAGIRI	0	44	1	168	2	164
32	DHULE	0	1425	0	1433	0	980
33	SINDHUDURG	0	13	0	67	0	65
34	WASHIM	0	356	0	1390	0	819
	Total	317	30378	525	66145	531	32320

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

