



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २४.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१०८५३	११	१०३६७७३	१२५	५२	१८३	२११
राज्य योजना	५५५६१४	४६	४०२७२८	०	४३३	१४३	१०४
एकूण	१९६६४६७	५७	१४३९५०१	१२५	४८५	३२६	३१५

PMAY-G Completion Progress Bar

73.5%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

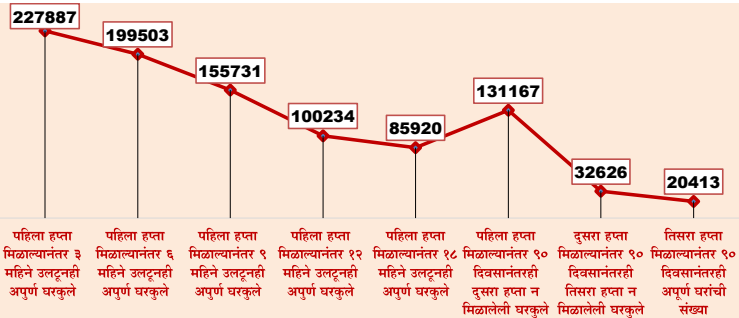

Abhiyan Achievement Day 155

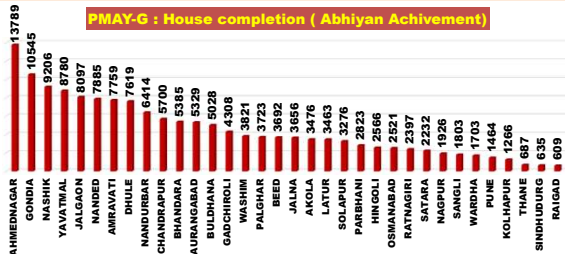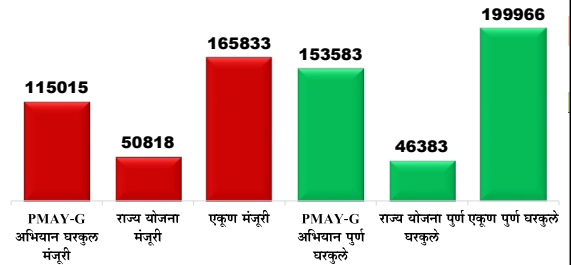

State Schemes: House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.



PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	23.04.2023	24.04.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414760	413758	413768	10	992
2	NAGPUR DIV.	292090	291469	291470	1	620
3	AMRAVATI DIV.	275029	274584	274584	0	445
4	AURANGABAD DIV.	238065	237420	237417	0	648
5	KONKAN DIV.	69785	69636	69636	0	149
6	PUNE DIV.	124804	123978	123978	0	826
Total		1414533	1410845	1410853	11	3680

Sr. No.	District	Target (PWL+Awaas Plus)	23.04.2023	24.04.2023	Daily_Achievement	Remaining
1	NASHIK	89720	89668	89678	10	42
2	GONDIA	96492	96142	96143	1	349
3	AHMEDNAGAR	60792	60763	60763	0	29
4	AKOLA	48792	48778	48778	0	14
5	AMRAVATI	95712	95466	95466	0	246
6	AURANGABAD	36795	36666	36666	0	129
7	BEED	35310	35253	35253	0	57
8	BHANDARA	65086	65056	65056	0	30
9	BULDHANA	44766	44714	44714	0	52
10	CHANDRAPUR	43122	42999	42999	0	123
11	DHULE	64979	64917	64917	0	62
12	GADCHIROLI	31698	31619	31619	0	79
13	HINGOLI	18109	18083	18083	0	26
14	JALGAON	79748	79451	79451	0	297
15	JALNA	24039	24022	24022	0	17
16	KOLHAPUR	17685	17685	17685	0	0
17	LATUR	20679	20475	20475	0	204
18	NAGPUR	37059	37047	37047	0	12
19	NANDED	69533	69460	69460	0	73
20	NANDURBAR	119521	118959	118959	0	562
21	OSMANABAD	14506	14401	14401	0	105
22	PALGHAR	35312	35185	35185	0	127
23	PUNE	20543	20531	20531	0	12
24	RAIGAD	9831	9822	9822	0	9
25	RATNAGIRI	9895	9888	9888	0	7
26	SANGLI	21890	21748	21748	0	142
27	SATARA	15348	15344	15344	0	4
28	SINDHUDURG	5142	5142	5142	0	0
29	SOLAPUR	49338	48670	48670	0	668
30	THANE	9605	9599	9599	0	6
31	WARDHA	18633	18606	18606	0	27
32	WASHIM	20404	20401	20401	0	3
33	YAVATMAL	65355	65225	65225	0	130
34	PARBHANI	19094	19060	19057	-3	37
Total		1414533	1410845	1410853	11	3680

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
WASHIM	3
SATARA	4
THANE	6
RATNAGIRI	7
RAIGAD	9
NAGPUR	12
PUNE	12
AKOLA	14
JALNA	17
HINGOLI	26
WARDHA	27
AHMEDNAGAR	29
BHANDARA	30
PARBHANI	37
NASHIK	42
BULDHANA	52
BEED	57
DHULE	62
NANDED	73
GADCHIROLI	79
OSMANABAD	105
CHANDRAPUR	123
PALGHAR	127
AURANGABAD	129
YAVATMAL	130
SANGLI	142
LATUR	204
AMRAVATI	246
JALGAON	297
GONDIA	349
NANDURBAR	562
SOLAPUR	668

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	43	84	31
10	NANDED	362	277	85	362	242	120	35
11	BEED	212	101	111	212	72	140	29
12	SANGLI	431	143	288	430	141	289	2
13	PARBHANI	332	15	317	331	13	318	2
14	SATARA	1309	598	711	1304	628	676	-30
15	NASHIK	1804	1454	350	1804	715	1089	739
16	HINGOLI	1713	787	926	1713	466	1247	321
17	JALNA	1413	165	1248	1381	85	1296	80
18	WARDHA	2819	1284	1535	2803	1214	1589	70
19	NAGPUR	5134	3397	1737	5054	3412	1642	-15
20	GONDIA	2450	2450	0	2450	765	1685	1685
21	CHANDRAPUR	2791	1463	1328	2770	971	1799	492
22	PUNE	2925	992	1933	2924	885	2039	107
23	LATUR	2299	68	2231	2299	66	2233	2
24	OSMANABAD	2470	104	2366	2470	56	2414	48
25	YAVATMAL	3437	1119	2318	3611	1178	2433	-59
26	BHANDARA	5825	3230	2595	5792	3213	2579	17
27	WASHIM	3477	865	2612	3477	850	2627	15
28	AURANGABAD	3328	1779	1549	3328	288	3040	1491
29	AKOLA	7074	3842	3232	7074	3844	3230	-2
30	AHMEDNAGAR	7762	4828	2934	7756	3374	4382	1454
31	JALGAON	22872	21026	1846	22962	17824	5138	3202
32	SOLAPUR	7960	2595	5365	7431	935	6496	1660
33	BULDHANA	15256	8455	6801	15230	7058	8172	1397
34	AMRAVATI	21560	11238	10322	21560	11221	10339	17
	Total	127885	73092	54793	127398	60272	67126	12926

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	23.04.2023	24.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237417	139456	139496	40	97921	206	2331
2	AMRAVATI DIV.	274584	185989	186021	32	88563	186	2109
3	NASHIK DIV.	413768	328617	328639	22	85129	291	2027
4	NAGPUR DIV.	291470	237678	237695	17	53775	191	1280
5	PUNE DIV.	123978	87451	87463	12	36515	65	869
6	KONKAN DIV.	69636	57457	57459	2	12177	52	290
Total		1410853	1036648	1036773	125	374080	991	8907

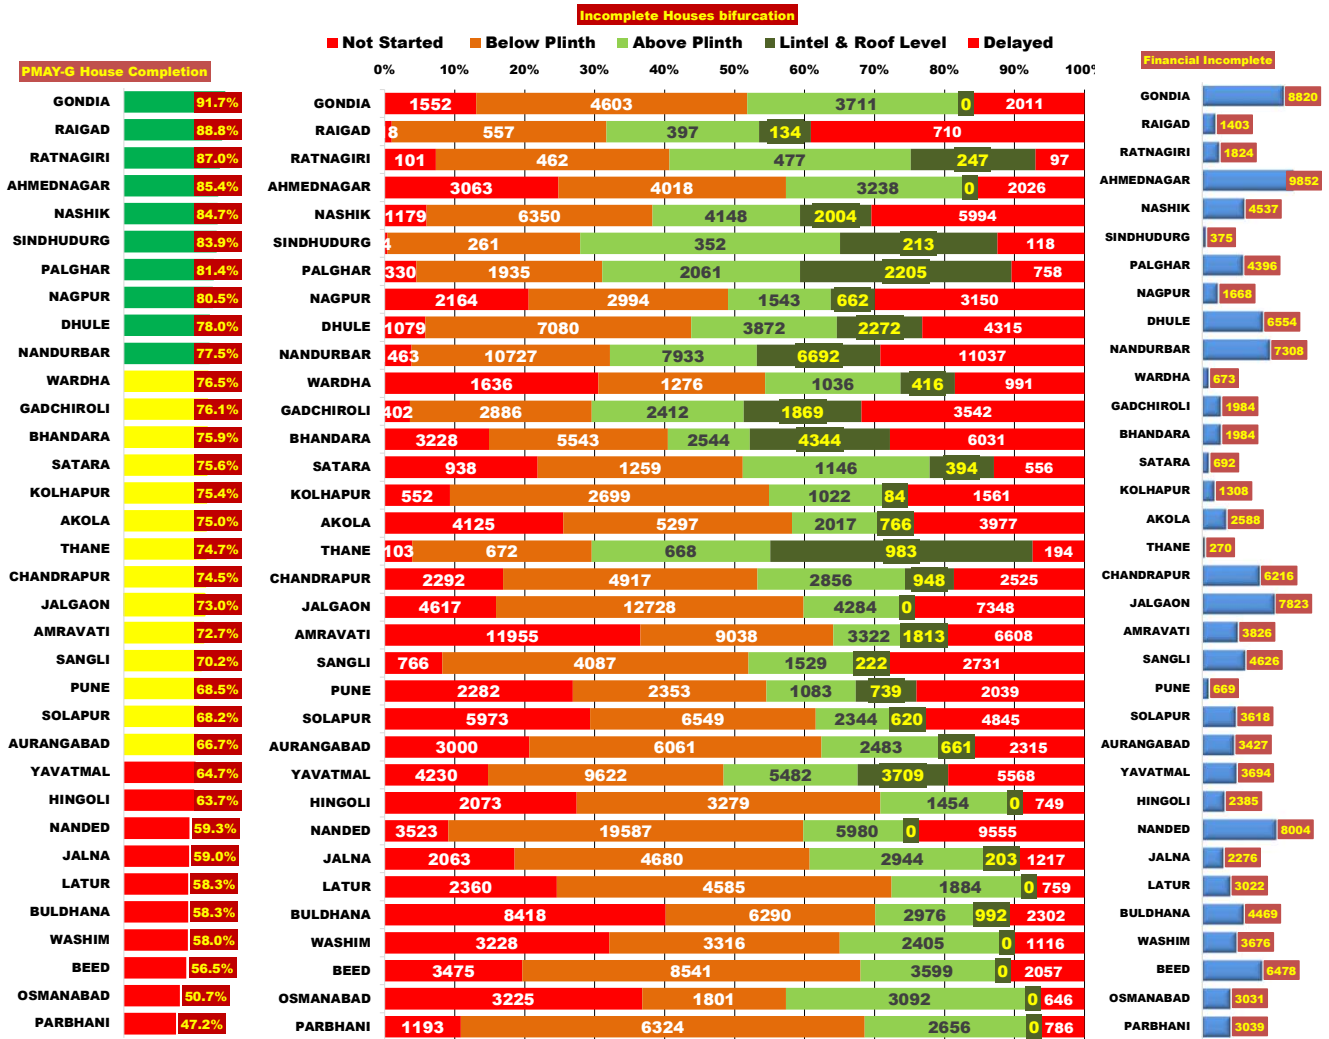

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	23.04.2023	24.04.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD	36666	24429	24461	32	12205	34	291
2	YAVATMAL	65225	42167	42188	21	23037	57	549
3	NANDURBAR	118959	92130	92144	14	26815	41	638
4	AKOLA	48778	36563	36573	10	12205	22	291
5	SOLAPUR	48670	33177	33184	7	15486	21	369
6	GONDIA	96143	88117	88123	6	8020	68	191
7	CHANDRAPUR	42999	32034	32039	5	10960	37	261
8	JALGAON	79451	58010	58015	5	21436	52	510
9	NANDED	69460	41190	41195	5	28265	51	673
10	SANGLI	21748	15265	15270	5	6478	12	154
11	WARDHA	18606	14237	14242	5	4364	11	104
12	AHMEDNAGAR	60763	51866	51869	3	8894	89	212
13	PALGHAR	35185	28652	28654	2	6531	24	156
14	BEED	35253	19919	19920	1	15333	24	365
15	JALNA	24022	14161	14162	1	9860	24	235
16	LATUR	20475	11936	11937	1	8538	22	203
17	NAGPUR	37047	29818	29819	1	7228	12	172
18	WASHIM	20401	11826	11827	1	8574	25	204
19	AMRAVATI	95466	69384	69384	0	26082	50	621
20	BHANDARA	65056	49397	49397	0	15659	35	373
21	BULDHANA	44714	26049	26049	0	18665	32	444
22	DHULE	64917	50614	50614	0	14303	49	341
23	GADCHIROLI	31619	24075	24075	0	7544	28	180
24	HINGOLI	18083	11524	11524	0	6559	17	156
25	KOLHAPUR	17685	13328	13328	0	4357	8	104
26	NASHIK	89678	75997	75997	0	13681	59	326
27	OSMANABAD	14401	7301	7301	0	7100	16	169
28	PARBHANI	19057	8996	8996	0	10061	18	240
29	PUNE	20531	14074	14074	0	6457	9	154
30	RAIGAD	9822	8719	8719	0	1103	4	26
31	RATNAGIRI	9888	8601	8601	0	1287	15	31
32	SATARA	15344	11607	11607	0	3737	14	89
33	SINDHUDURG	5142	4312	4312	0	830	4	20
34	THANE	9599	7173	7173	0	2426	4	58
Total		1410853	1036648	1036773	125	374080	991	8907

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	23.04.2023	24.04.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	199331	165395	165441	46	33890
2	KONKAN DIV.	34732	31053	31053	0	3679
3	PUNE DIV.	65334	62997	62997	0	2337
4	NASHIK DIV.	141360	110541	110541	0	30819
5	AMRAVATI DIV.	109702	93694	93694	0	16008
6	NAGPUR DIV.	118393	91888	91888	0	26505
Total		668852	555568	555614	46	113238


Sr. No.	District	Target	23.04.2023	24.04.2023	Daily_Achievement	Remaining
1	NANDED	26760	20870	20916	46	5844
2	AHMEDNAGAR	35298	32973	32973	0	2325
3	AKOLA	23681	17733	17733	0	5948
4	AMRAVATI	23224	19812	19812	0	3412
5	AURANGABAD	26141	23842	23842	0	2299
6	BEED	26878	25076	25076	0	1802
7	BHANDARA	17590	15558	15558	0	2032
8	BULDHANA	21616	19979	19979	0	1637
9	CHANDRAPUR	40285	25933	25933	0	14352
10	DHULE	21790	18048	18048	0	3742
11	GADCHIROLI	16834	15203	15203	0	1631
12	GONDIA	14246	12846	12846	0	1400
13	HINGOLI	27298	15514	15514	0	11784
14	JALGAON	25659	22540	22540	0	3119
15	JALNA	20446	19228	19228	0	1218
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	26199	26199	0	972
18	NAGPUR	16291	11130	11130	0	5161
19	NANDURBAR	26578	14137	14137	0	12441
20	NASHIK	32035	22843	22843	0	9192
21	OSMANABAD	24853	17039	17039	0	7814
22	PALGHAR	11792	11002	11002	0	790
23	PARBHANI	19784	17627	17627	0	2157
24	PUNE	14672	12774	12774	0	1898
25	RAIGAD	7406	6302	6302	0	1104
26	RATNAGIRI	7129	6677	6677	0	452
27	SANGLI	8732	8603	8603	0	129
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2107	2107	0	34
30	SOLAPUR	18718	18445	18445	0	273
31	THANE	6264	4965	4965	0	1299
32	WARDHA	13147	11218	11218	0	1929
33	WASHIM	11500	10057	10057	0	1443
34	YAVATMAL	29681	26113	26113	0	3568
Total		668852	555568	555614	46	113238

Remaining Sanction RANK

SATARA	0
SINDHUDURG	34
KOLHAPUR	37
SANGLI	129
SOLAPUR	273
RATNAGIRI	452
PALGHAR	790
LATUR	972
RAIGAD	1104
JALNA	1218
THANE	1299
GONDIA	1400
WASHIM	1443
GADCHIROLI	1631
BULDHANA	1637
BEED	1802
PUNE	1898
WARDHA	1929
BHANDARA	2032
PARBHANI	2157
AURANGABAD	2299
AHMEDNAGAR	2325
JALGAON	3119
AMRAVATI	3412
YAVATMAL	3568
DHULE	3742
NAGPUR	5161
NANDED	5844
AKOLA	5948
OSMANABAD	7814
NASHIK	9192
HINGOLI	11784
NANDURBAR	12441
CHANDRAPUR	14352

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	23.04.2023	24.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	KONKAN DIV.	31053	23668	23668	0	7385	15	176
2	PUNE DIV.	62997	51976	51976	0	11021	25	262
3	NASHIK DIV.	110541	88956	88956	0	21585	70	514
4	AURANGABAD DIV.	165441	103957	103957	0	61484	89	1464
5	AMRAVATI DIV.	93694	64777	64777	0	28917	55	689
6	NAGPUR DIV.	91888	69394	69394	0	22494	44	536
Total		555614	402728	402728	0	152886	299	3640

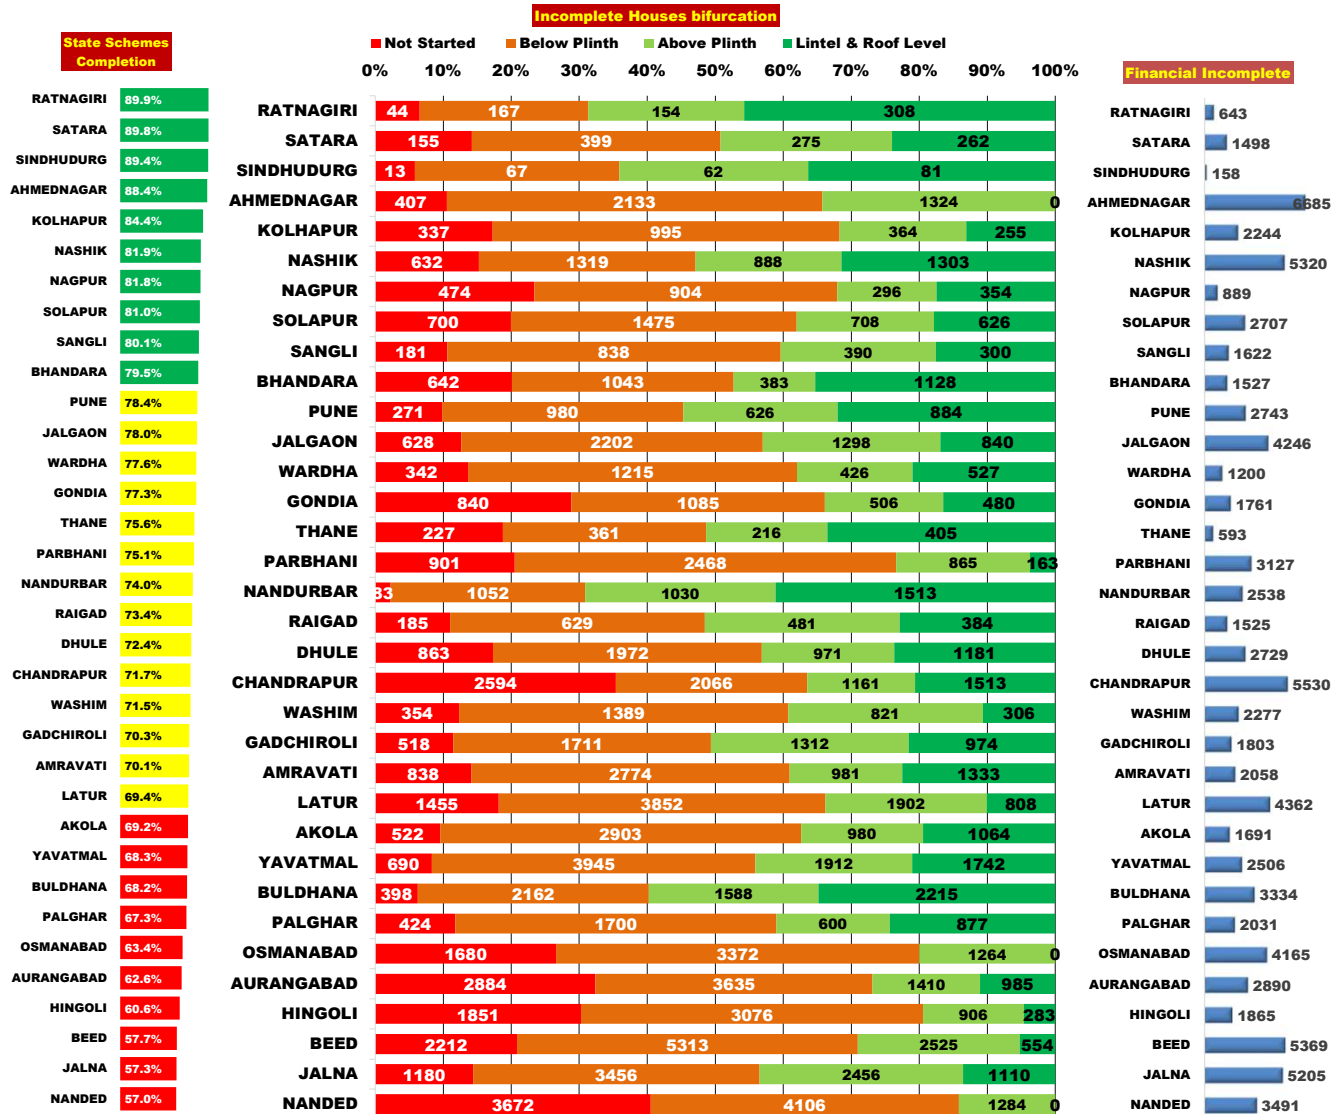

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	23.04.2023	24.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AHMEDNAGAR	32973	29163	29163	0	3810	29	91
2	AKOLA	17733	12264	12264	0	5469	9	130
3	AMRAVATI	19812	13886	13886	0	5926	9	141
4	AURANGABAD	23842	14928	14928	0	8914	9	212
5	BEED	25076	14472	14472	0	10604	14	252
6	BHANDARA	15558	12362	12362	0	3196	4	76
7	BULDHANA	19979	13616	13616	0	6363	17	152
8	CHANDRAPUR	25933	18599	18599	0	7334	13	175
9	DHULE	18048	13061	13061	0	4987	10	119
10	GADCHIROLI	15203	10688	10688	0	4515	9	108
11	GONDIA	12846	9935	9935	0	2911	8	69
12	HINGOLI	15514	9398	9398	0	6116	6	146
13	JALGAON	22540	17572	17572	0	4968	12	118
14	JALNA	19228	11026	11026	0	8202	25	195
15	KOLHAPUR	12528	10577	10577	0	1951	3	46
16	LATUR	26199	18182	18182	0	8017	13	191
17	NAGPUR	11130	9102	9102	0	2028	4	48
18	NANDED	20916	11923	11923	0	8993	9	214
19	NANDURBAR	14137	10459	10459	0	3678	6	88
20	NASHIK	22843	18701	18701	0	4142	13	99
21	OSMANABAD	17039	10798	10798	0	6241	10	149
22	PALGHAR	11002	7401	7401	0	3601	6	86
23	PARBHANI	17627	13230	13230	0	4397	4	105
24	PUNE	12774	10013	10013	0	2761	6	66
25	RAIGAD	6302	4623	4623	0	1679	3	40
26	RATNAGIRI	6677	6004	6004	0	673	3	16
27	SANGLI	8603	6894	6894	0	1709	4	41
28	SATARA	10647	9556	9556	0	1091	6	26
29	SINDHUDURG	2107	1884	1884	0	223	1	5
30	SOLAPUR	18445	14936	14936	0	3509	7	84
31	THANE	4965	3756	3756	0	1209	2	29
32	WARDHA	11218	8708	8708	0	2510	7	60
33	WASHIM	10057	7187	7187	0	2870	8	68
34	YAVATMAL	26113	17824	17824	0	8289	13	197
Total		555614	402728	402728	0	152886	299	3640

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD DIV.	41	20882	83	54858	45	24092
2	NASHIK DIV.	0	11401	65	40903	47	23475
3	AMRAVATI DIV.	3	31890	31	33563	38	16202
4	NAGPUR DIV.	4	11061	0	22219	54	14102
5	KONKAN DIV.	0	553	4	3887	15	3955
6	PUNE DIV.	4	10385	0	16947	12	7124
Total		52	86172	183	172377	211	88950

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	15
RATNAGIRI	101
THANE	103
PALGHAR	330
GADCHIROLI	377
KOLHAPUR	552
SANGLI	640
SATARA	938
DHULE	1079
NASHIK	1179
PARBHANI	1193
NANDURBAR	1463
GONDIA	1552
WARDHA	1636
NAGPUR	2029
JALNA	2033
HINGOLI	2073
CHANDRAPUR	2239
PUNE	2282
LATUR	2360
AURANGABAD	3000
AHMEDNAGAR	3063
OSMANABAD	3225
WASHIM	3225
BHANDARA	3228
BEED	3475
NANDED	3523
AKOLA	4125
YAVATMAL	4224
JALGAON	4617
SOLAPUR	5973
BULDHANA	8407
AMRAVATI	11909

PMAY-G 2nd Ins Pending

SINDHUDURG	261
RATNAGIRI	462
RAIGAD	557
THANE	672
SATARA	1259
WARDHA	1276
OSMANABAD	1801
PALGHAR	1935
PUNE	2353
KOLHAPUR	2699
GADCHIROLI	2886
NAGPUR	2994
HINGOLI	3279
WASHIM	3316
AHMEDNAGAR	4018
SANGLI	4087
LATUR	4585
GONDIA	4603
JALNA	4680
CHANDRAPUR	4917
AKOLA	5297
BHANDARA	5543
AURANGABAD	6061
BULDHANA	6290
PARBHANI	6324
NASHIK	6350
SOLAPUR	6549
DHULE	7080
BEED	8541
AMRAVATI	9038
YAVATMAL	9622
NANDURBAR	10727
JALGAON	12728
NANDED	19587

PMAY-G 3rd Ins Pending

SINDHUDURG	352
RAIGAD	397
RATNAGIRI	477
THANE	668
KOLHAPUR	1022
WARDHA	1036
PUNE	1083
SATARA	1146
HINGOLI	1454
SANGLI	1529
NAGPUR	1543
LATUR	1884
AKOLA	2017
PALGHAR	2061
SOLAPUR	2344
WASHIM	2405
GADCHIROLI	2412
AURANGABAD	2483
BHANDARA	2544
PARBHANI	2656
CHANDRAPUR	2856
JALNA	2944
BULDHANA	2976
OSMANABAD	3092
AHMEDNAGAR	3238
AMRAVATI	3322
BEED	3599
GONDIA	3711
DHULE	3872
NASHIK	4148
JALGAON	4284
YAVATMAL	5482
NANDED	5980
NANDURBAR	7933

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	JALGAON	0	4617	23	12728	28	4284
2	BHANDARA	0	3228	0	5543	46	2544
3	JALNA	12	2033	23	4680	4	2944
4	BEED	1	3475	26	8541	9	3599
5	NANDED	17	3523	8	19587	11	5980
6	PARBHANI	10	1193	23	6324	0	2656
7	NANDURBAR	0	1463	32	10727	0	7933
8	BULDHANA	0	8407	20	6290	10	2976
9	AMRAVATI	3	11909	6	9038	12	3322
10	AHMEDNAGAR	0	3063	0	4018	19	3238
11	THANE	0	103	3	672	14	668
12	LATUR	1	2360	2	4585	12	1884
13	WASHIM	0	3225	0	3316	13	2405
14	AURANGABAD	0	3000	1	6061	9	2483
15	NASHIK	0	1179	10	6350	0	4148
16	KOLHAPUR	0	552	0	2699	6	1022
17	YAVATMAL	0	4224	5	9622	1	5482
18	NAGPUR	1	2029	0	2994	4	1543
19	PUNE	4	2282	0	2353	0	1083
20	SATARA	0	938	0	1259	4	1146
21	GONDIA	0	1552	0	4603	3	3711
22	WARDHA	3	1636	0	1276	0	1036
23	AKOLA	0	4125	0	5297	2	2017
24	CHANDRAPUR	0	2239	0	4917	1	2856
25	PALGHAR	0	330	0	1935	1	2061
26	RAIGAD	0	15	1	557	0	397
27	SANGLI	0	640	0	4087	1	1529
28	SOLAPUR	0	5973	0	6549	1	2344
29	DHULE	0	1079	0	7080	0	3872
30	GADCHIROLI	0	377	0	2886	0	2412
31	HINGOLI	0	2073	0	3279	0	1454
32	OSMANABAD	0	3225	0	1801	0	3092
33	RATNAGIRI	0	101	0	462	0	477
34	SINDHUDURG	0	4	0	261	0	352
	Total	52	86172	183	172377	211	88950

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	236	2613	15	8678	35	5511
2	KONKAN DIV.	92	893	27	2924	7	1513
3	AURANGABAD DIV.	35	15835	40	29278	16	12612
4	AMRAVATI DIV.	44	2802	25	13173	19	6282
5	NAGPUR DIV.	24	5410	30	8024	23	4084
6	PUNE DIV.	2	1644	6	4687	4	2363
Total		433	29197	143	66764	104	32365

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	44
NANDURBAR	83
SATARA	155
SANGLI	181
RAIGAD	185
THANE	227
PUNE	271
KOLHAPUR	337
WARDHA	342
WASHIM	354
BULDHANA	398
AHMEDNAGAR	407
PALGHAR	424
NAGPUR	474
GADCHIROLI	518
AKOLA	522
JALGAON	628
NASHIK	632
BHANDARA	642
YAVATMAL	690
SOLAPUR	700
AMRAVATI	838
GONDIA	840
DHULE	863
PARBHANI	901
JALNA	1180
LATUR	1455
OSMANABAD	1680
HINGOLI	1851
BEED	2212
CHANDRAPUR	2594
AURANGABAD	2884
NANDED	3672

State Schemes 2nd Ins Pending

SINDHUDURG	67
RATNAGIRI	167
THANE	361
SATARA	399
RAIGAD	629
SANGLI	838
NAGPUR	904
PUNE	980
KOLHAPUR	995
BHANDARA	1043
NANDURBAR	1052
GONDIA	1085
WARDHA	1215
NASHIK	1319
WASHIM	1389
SOLAPUR	1475
PALGHAR	1700
GADCHIROLI	1711
DHULE	1972
CHANDRAPUR	2066
AHMEDNAGAR	2133
BULDHANA	2162
JALGAON	2202
PARBHANI	2468
AMRAVATI	2774
AKOLA	2903
HINGOLI	3076
OSMANABAD	3372
JALNA	3456
AURANGABAD	3635
LATUR	3852
YAVATMAL	3945
NANDED	4106
BEED	5313

State Schemes 3rd Ins Pending

SINDHUDURG	62
RATNAGIRI	154
THANE	216
SATARA	275
NAGPUR	296
KOLHAPUR	364
BHANDARA	383
SANGLI	390
WARDHA	426
RAIGAD	481
GONDIA	506
PALGHAR	600
PUNE	626
SOLAPUR	708
WASHIM	821
PARBHANI	865
NASHIK	888
HINGOLI	906
DHULE	971
AKOLA	980
AMRAVATI	981
NANDURBAR	1030
CHANDRAPUR	1161
OSMANABAD	1264
NANDED	1284
JALGAON	1298
GADCHIROLI	1312
AHMEDNAGAR	1324
AURANGABAD	1410
BULDHANA	1588
LATUR	1902
YAVATMAL	1912
JALNA	2456
BEED	2525

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	DHULE	235	863	0	1972	4	971
2	RAIGAD	55	185	21	629	2	481
3	NANDED	30	3672	4	4106	9	1284
4	AKOLA	30	522	6	2903	3	980
5	NANDURBAR	1	83	13	1052	25	1030
6	PALGHAR	30	424	5	1700	1	600
7	GADCHIROLI	3	518	18	1711	13	1312
8	YAVATMAL	8	690	13	3945	12	1912
9	LATUR	0	1455	16	3852	6	1902
10	BEED	0	2212	16	5313	0	2525
11	NAGPUR	10	474	4	904	1	296
12	BHANDARA	5	642	3	1043	3	383
13	SOLAPUR	0	700	5	1475	4	708
14	THANE	7	227	0	361	2	216
15	AURANGABAD	3	2884	4	3635	1	1410
16	CHANDRAPUR	0	2594	3	2066	4	1161
17	WARDHA	6	342	1	1215	0	426
18	WASHIM	2	354	3	1389	1	821
19	AMRAVATI	1	838	3	2774	1	981
20	BULDHANA	3	398	0	2162	2	1588
21	JALGAON	0	628	2	2202	2	1298
22	GONDIA	0	840	1	1085	2	506
23	AHMEDNAGAR	0	407	0	2133	2	1324
24	HINGOLI	2	1851	0	3076	0	906
25	NASHIK	0	632	0	1319	2	888
26	PUNE	1	271	1	980	0	626
27	SINDHUDURG	0	13	0	67	2	62
28	RATNAGIRI	0	44	1	167	0	154
29	SATARA	1	155	0	399	0	275
30	JALNA	0	1180	0	3456	0	2456
31	KOLHAPUR	0	337	0	995	0	364
32	OSMANABAD	0	1680	0	3372	0	1264
33	PARBHANI	0	901	0	2468	0	865
34	SANGLI	0	181	0	838	0	390
	Total	433	29197	143	66764	104	32365

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेला घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेला घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2026	1812	3022	1339	49
AKOLA	3977	3562	3582	877	586
AMRAVATI	6608	5641	7221	1440	996
AURANGABAD	2315	2274	4923	1017	382
BEED	2057	1866	6673	1605	408
BHANDARA	6031	5311	4948	745	2110
BULDHANA	2302	2167	4003	827	671
CHANDRAPUR	2525	1946	3518	683	279
DHULE	4315	4109	5994	2132	1501
GADCHIROLI	3542	2507	2331	1181	843
GONDIA	2011	1980	3094	1020	152
HINGOLI	749	672	2552	445	93
JALGAON	7348	6656	11324	1968	621
JALNA	1217	1075	3153	774	257
KOLHAPUR	1561	755	2393	276	90
LATUR	759	732	2710	426	53
NAGPUR	3150	2376	2585	458	586
NANDED	9555	9167	14835	1907	342
NANDURBAR	11037	10052	7038	4598	5009
NASHIK	5994	3596	4871	2083	1521
OSMANABAD	646	581	1237	439	6
PALGHAR	758	659	1380	542	363
PARBHANI	786	737	4044	492	78
PUNE	2039	1744	1942	478	425
RAIGAD	710	240	472	220	160
RATNAGIRI	97	47	349	93	44
SANGLI	2731	2324	3486	511	119
SATARA	556	393	889	197	137
SINDHUDURG	118	90	207	69	24
SOLAPUR	4845	4632	5013	1234	488
THANE	194	188	577	149	89
WARDHA	991	811	943	212	226
WASHIM	1116	866	2658	386	99
YAVATMAL	5568	4352	7200	1803	1606
