



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २६.०४.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१०५०५	३४	१०३८२९६	६१७	०	०	०
राज्य योजना	५५६८१०	६४५	४०३४०९	३४२	०	०	०
एकूण	१९६७३१५	६७९	१४४१७०५	९५९	०	०	०

PMAY-G Completion Progress Bar

73.6%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

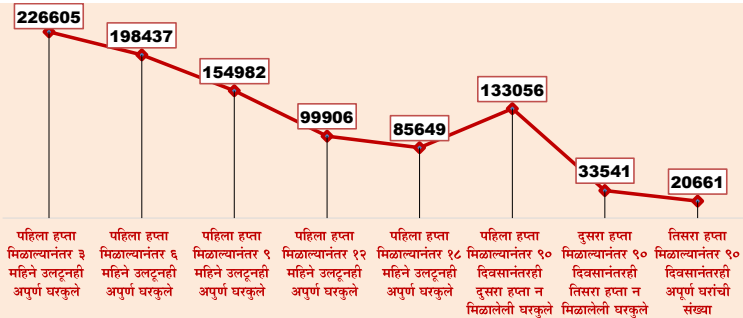

Abhiyan Achievement Day 157

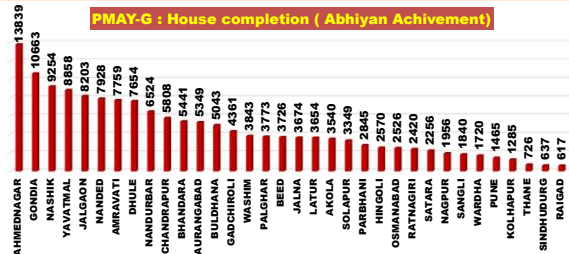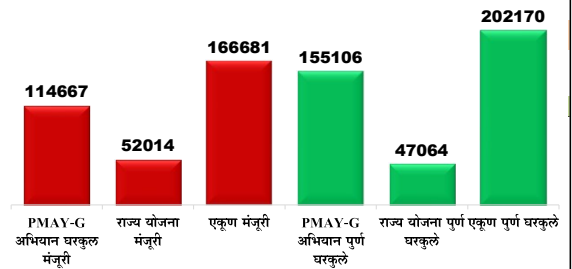


State Schemes: House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण
४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	25.04.2023	26.04.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	275027	274561	274561	9	466
2	AURANGABAD DIV.	238035	237361	237283	9	752
3	NAGPUR DIV.	292074	291455	291444	9	630
4	NASHIK DIV.	414823	413758	413758	3	1065
5	KONKAN DIV.	69817	69634	69637	3	180
6	PUNE DIV.	124697	123825	123822	1	875
Total		1414473	1410594	1410505	34	3968

Sr. No.	District	Target (PWL+Awaas Plus)	25.04.2023	26.04.2023	Daily_Achievement	Remaining
1	AMRAVATI	95714	95470	95479	9	235
2	BHANDARA	65071	65041	65049	8	22
3	LATUR	20679	20475	20480	5	199
4	OSMANABAD	14506	14404	14408	4	98
5	PALGHAR	35344	35185	35188	3	156
6	NASHIK	89730	89678	89680	2	50
7	GONDIA	96493	96144	96145	1	348
8	JALGAON	79748	79444	79445	1	303
9	SATARA	15347	15345	15346	1	1
10	AKOLA	48792	48778	48778	0	14
11	BEED	35310	35253	35253	0	57
12	CHANDRAPUR	43122	42999	42999	0	123
13	DHULE	64989	64917	64917	0	72
14	HINGOLI	18109	18083	18083	0	26
15	JALNA	24039	24029	24029	0	10
16	KOLHAPUR	17685	17685	17685	0	0
17	NANDED	69533	69460	69460	0	73
18	NANDURBAR	119564	118959	118959	0	605
19	PARBHANI	19094	19059	19059	0	35
20	PUNE	20543	20528	20528	0	15
21	RAIGAD	9831	9822	9822	0	9
22	RATNAGIRI	9895	9886	9886	0	9
23	SANGLI	21889	21746	21746	0	143
24	SINDHUDURG	5142	5142	5142	0	0
25	THANE	9605	9599	9599	0	6
26	YAVATMAL	65355	65235	65235	0	120
27	BULDHANA	44765	44716	44715	-1	50
28	WARDHA	18633	18606	18605	-1	28
29	GADCHIROLI	31702	31619	31617	-2	85
30	AHMEDNAGAR	60792	60760	60757	-3	35
31	SOLAPUR	49233	48521	48517	-4	716
32	WASHIM	20401	20362	20354	-8	47
33	NAGPUR	37053	37046	37029	-17	24
34	AURANGABAD	36765	36598	36511	-87	254
Total		1414473	1410594	1410505	34	3968

Remaining Sanction RANK


KOLHAPUR	0
SINDHUDURG	0
SATARA	1
THANE	6
RAIGAD	9
RATNAGIRI	9
JALNA	10
AKOLA	14
PUNE	15
BHANDARA	22
NAGPUR	24
HINGOLI	26
WARDHA	28
AHMEDNAGAR	35
PARBHANI	35
WASHIM	47
BULDHANA	50
NASHIK	50
BEED	57
DHULE	72
NANDED	73
GADCHIROLI	85
OSMANABAD	98
YAVATMAL	120
CHANDRAPUR	123
SANGLI	143
PALGHAR	156
LATUR	199
AMRAVATI	235
AURANGABAD	254
JALGAON	303
GONDIA	348
NANDURBAR	605
SOLAPUR	716

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	44	83	30
10	NANDED	362	277	85	362	242	120	35
11	BEED	212	101	111	212	72	140	29
12	SANGLI	431	143	288	430	141	289	2
13	PARBHANI	332	15	317	331	13	318	2
14	SATARA	1309	598	711	1304	628	676	-30
15	NASHIK	1824	1475	349	1803	927	876	548
16	HINGOLI	1713	787	926	1713	466	1247	321
17	JALNA	1413	165	1248	1381	85	1296	80
18	CHANDRAPUR	2791	1463	1328	2770	1302	1468	161
19	WARDHA	2819	1284	1535	2803	1214	1589	70
20	NAGPUR	5134	3397	1737	5038	3422	1616	-25
21	GONDIA	2450	2450	0	2450	765	1685	1685
22	PUNE	2925	992	1933	2924	885	2039	107
23	LATUR	2299	68	2231	2299	66	2233	2
24	OSMANABAD	2470	104	2366	2470	56	2414	48
25	YAVATMAL	3437	1119	2318	3612	1181	2431	-62
26	BHANDARA	5825	3230	2595	5782	3233	2549	-3
27	WASHIM	3477	865	2612	3447	850	2597	15
28	AURANGABAD	3328	1779	1549	3290	288	3002	1491
29	AKOLA	7074	3842	3232	7074	3844	3230	-2
30	JALGAON	22872	21026	1846	22962	19036	3926	1990
31	AHMEDNAGAR	7762	4828	2934	7756	3621	4135	1207
32	SOLAPUR	7960	2595	5365	7317	1188	6129	1407
33	BULDHANA	15085	8586	6499	15228	7097	8131	1489
34	AMRAVATI	21560	11238	10322	21559	11331	10228	-93
Total		127734	73244	54490	127187	62710	64477	10749

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	25.04.2023	26.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK DIV.	413758	328827	328988	161	84770	290	2119
2	AURANGABAD DIV.	237283	139706	139833	127	97450	206	2436
3	NAGPUR DIV.	291444	237954	238077	123	53367	191	1334
4	AMRAVATI DIV.	274561	186115	186200	85	88361	185	2209
5	PUNE DIV.	123822	87553	87617	64	36205	65	905
6	KONKAN DIV.	69637	57524	57581	57	12056	52	301
Total		1410505	1037679	1038296	617	372209	988	9305

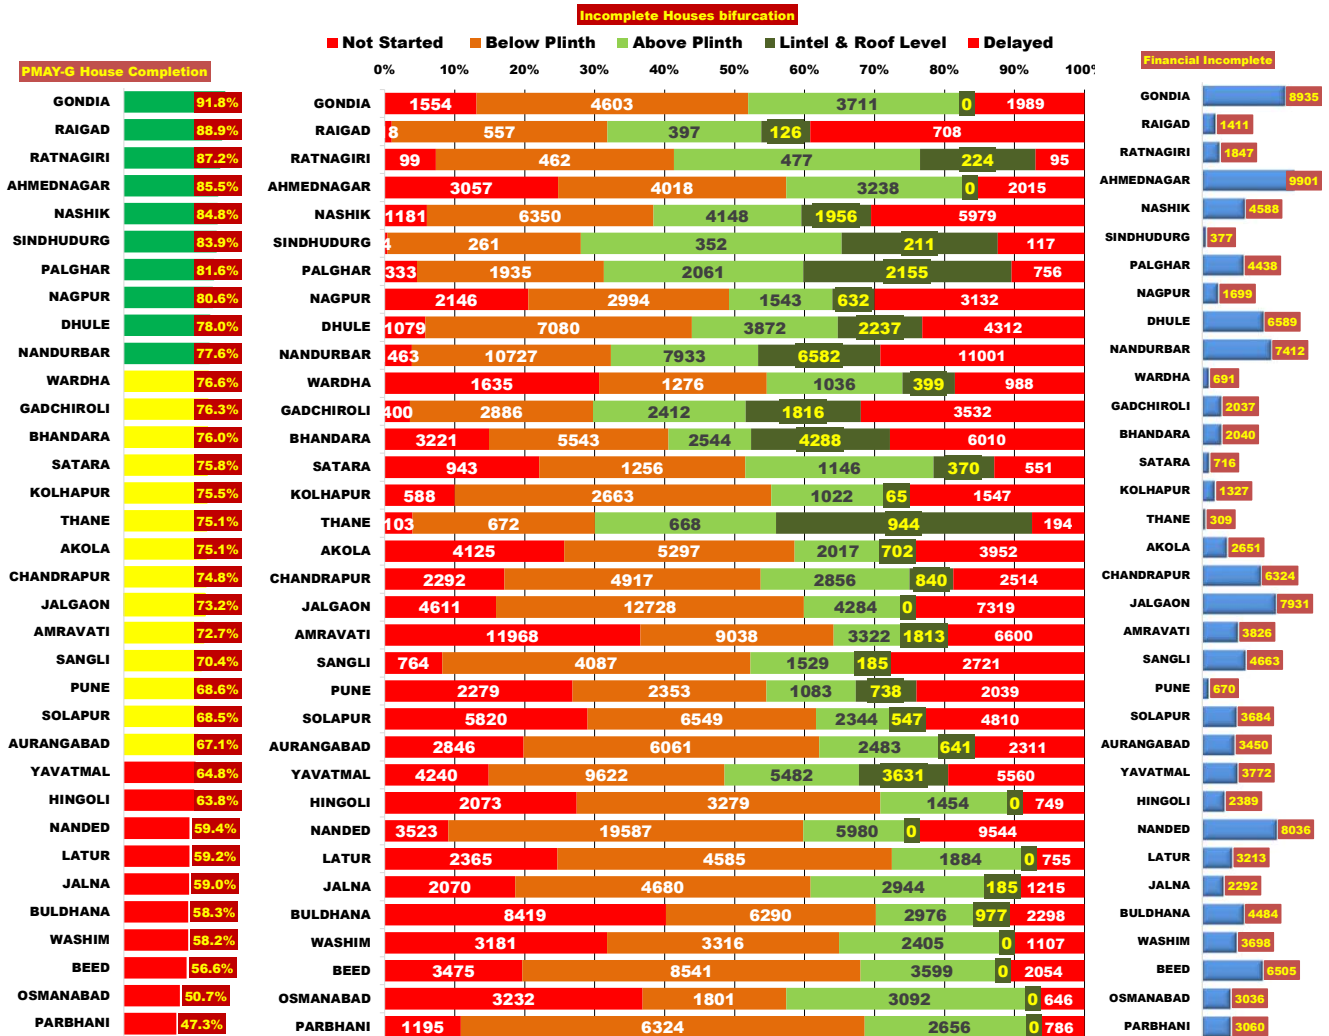

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	25.04.2023	26.04.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDURBAR	118959	92173	92254	81	26705	42	668
2	LATUR	20480	12067	12128	61	8352	23	209
3	AKOLA	48778	36588	36637	49	12141	23	304
4	GONDIA	96145	88201	88241	40	7904	68	198
5	CHANDRAPUR	42999	32112	32147	35	10852	37	271
6	AHMEDNAGAR	60757	51889	51919	30	8838	88	221
7	NASHIK	89680	76018	76045	27	13635	59	341
8	NANDED	69460	41213	41238	25	28222	50	706
9	PALGHAR	35188	28679	28704	25	6484	24	162
10	SANGLI	21746	15283	15307	24	6439	12	161
11	GADCHIROLI	31617	24111	24128	17	7489	28	187
12	JALGAON	79445	58104	58121	17	21324	52	533
13	YAVATMAL	65235	42249	42266	17	22969	56	574
14	RATNAGIRI	9886	8609	8624	15	1262	15	32
15	NAGPUR	37029	29835	29849	14	7180	12	180
16	SATARA	15346	11617	11631	14	3715	14	93
17	THANE	9599	7198	7212	14	2387	5	60
18	AURANGABAD	36511	24468	24481	13	12030	34	301
19	BEED	35253	19941	19954	13	15299	24	382
20	KOLHAPUR	17685	13334	13347	13	4338	8	108
21	SOLAPUR	48517	33244	33257	13	15260	21	382
22	WASHIM	20354	11837	11849	12	8505	24	213
23	BHANDARA	65049	49442	49453	11	15596	35	390
24	BULDHANA	44715	26057	26064	7	18651	32	466
25	DHULE	64917	50643	50649	6	14268	49	357
26	JALNA	24029	14174	14180	6	9849	23	246
27	WARDHA	18605	14253	14259	6	4346	11	109
28	OSMANABAD	14408	7302	7306	4	7102	16	178
29	HINGOLI	18083	11525	11528	3	6555	16	164
30	PARBHANI	19059	9016	9018	2	10041	18	251
31	RAIGAD	9822	8725	8727	2	1095	4	27
32	SINDHUDURG	5142	4313	4314	1	828	4	21
33	AMRAVATI	95479	69384	69384	0	26095	49	652
34	PUNE	20528	14075	14075	0	6453	9	161
Total		1410505	1037679	1038296	617	372209	988	9305

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	25.04.2023	26.04.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	200269	165594	165936	350	34333
2	AMRAVATI DIV.	109705	93734	93832	98	15873
3	NAGPUR DIV.	118430	92219	92310	98	26120
4	KONKAN DIV.	34744	31068	31153	85	3591
5	NASHIK DIV.	141552	110569	110582	13	30970
6	PUNE DIV.	65859	62996	62997	1	2862
Total		670559	556180	556810	645	113749


Sr. No.	District	Target	25.04.2023	26.04.2023	Daily_Achievement	Remaining
1	NANDED	26760	20953	21126	173	5634
2	BEED	26878	25156	25293	137	1585
3	WASHIM	11503	10057	10151	94	1352
4	CHANDRAPUR	40285	26227	26304	77	13981
5	PALGHAR	11792	11002	11049	47	743
6	RAIGAD	7418	6302	6336	34	1082
7	LATUR	28004	26198	26221	23	1783
8	NAGPUR	16291	11165	11185	20	5106
9	HINGOLI	27298	15546	15563	17	11735
10	DHULE	21790	18070	18081	11	3709
11	AMRAVATI	23224	19812	19816	4	3408
12	THANE	6264	4965	4969	4	1295
13	NASHIK	32035	22848	22850	2	9185
14	GADCHIROLI	16834	15207	15208	1	1626
15	SANGLI	8732	8603	8604	1	128
16	AHMEDNAGAR	35298	32974	32974	0	2324
17	AKOLA	23681	17765	17765	0	5916
18	BHANDARA	17612	15558	15558	0	2054
19	BULDHANA	21616	19987	19987	0	1629
20	JALGAON	25851	22540	22540	0	3311
21	JALNA	20551	19228	19228	0	1323
22	KOLHAPUR	13090	12528	12528	0	562
23	NANDURBAR	26578	14137	14137	0	12441
24	OSMANABAD	24853	17039	17039	0	7814
25	PARBHANI	19784	17632	17632	0	2152
26	PUNE	14672	12773	12773	0	1899
27	RATNAGIRI	7129	6691	6691	0	438
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2108	2108	0	33
30	SOLAPUR	18718	18445	18445	0	273
31	WARDHA	13147	11218	11218	0	1929
32	YAVATMAL	29681	26113	26113	0	3568
33	GONDIA	14261	12844	12837	-7	1424
34	AURANGABAD	26141	23842	23834	-8	2307
Total		670559	556180	556810	645	113749

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	273
RATNAGIRI	438
KOLHAPUR	562
PALGHAR	743
RAIGAD	1082
THANE	1295
JALNA	1323
WASHIM	1352
GONDIA	1424
BEED	1585
GADCHIROLI	1626
BULDHANA	1629
LATUR	1783
PUNE	1899
WARDHA	1929
BHANDARA	2054
PARBHANI	2152
AURANGABAD	2307
AHMEDNAGAR	2324
JALGAON	3311
AMRAVATI	3408
YAVATMAL	3568
DHULE	3709
NAGPUR	5106
NANDED	5634
AKOLA	5916
OSMANABAD	7814
NASHIK	9185
HINGOLI	11735
NANDURBAR	12441
CHANDRAPUR	13981

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	25.04.2023	26.04.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	165936	104107	104248	141	61688	90	1542
2	AMRAVATI DIV.	93832	64826	64898	72	28934	55	723
3	KONKAN DIV.	31153	23691	23740	49	7413	15	185
4	NAGPUR DIV.	92310	69451	69484	33	22826	44	571
5	NASHIK DIV.	110582	89003	89028	25	21554	70	539
6	PUNE DIV.	62997	51989	52011	22	10986	25	275
Total		556810	403067	403409	342	153401	300	3835

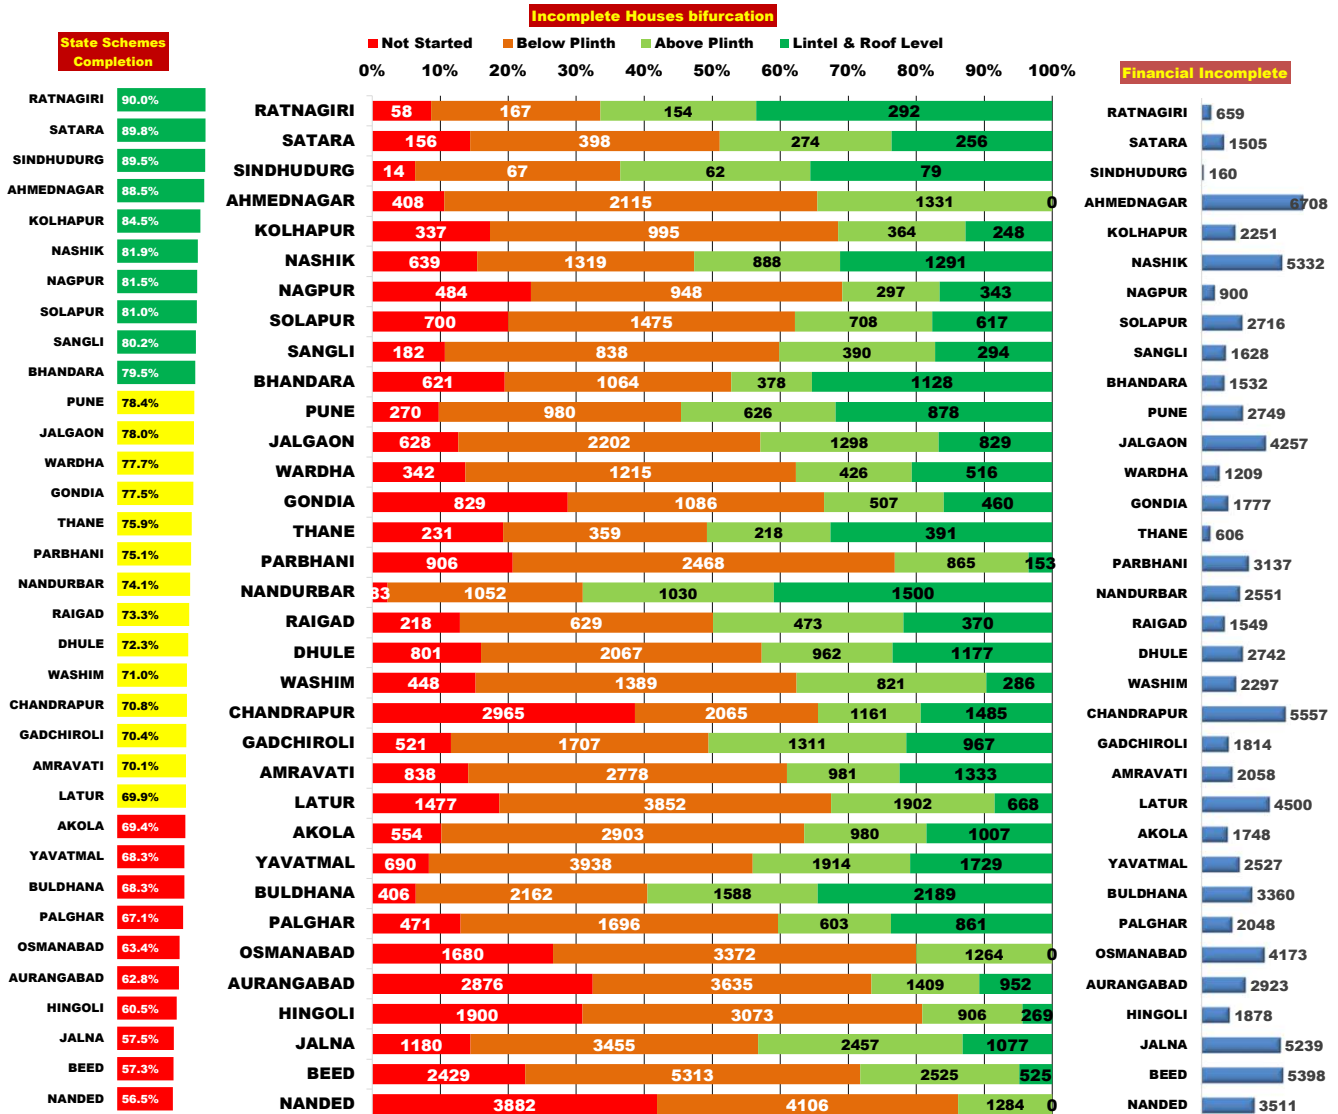

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	25.04.2023	26.04.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	LATUR	26221	18265	18322	57	7899	13	197
2	AKOLA	17765	12275	12321	46	5444	9	136
3	AURANGABAD	23834	14943	14962	19	8872	9	222
4	RAIGAD	6336	4627	4646	19	1690	3	42
5	HINGOLI	15563	9398	9415	17	6148	6	154
6	BEED	25293	14485	14501	16	10792	14	270
7	CHANDRAPUR	26304	18612	18628	16	7676	13	192
8	JALNA	19228	11044	11059	15	8169	25	204
9	THANE	4969	3756	3770	14	1199	2	30
10	BULDHANA	19987	13629	13642	13	6345	17	159
11	RATNAGIRI	6691	6007	6020	13	671	3	17
12	WASHIM	10151	7196	7207	11	2944	8	74
13	NANDED	21126	11933	11943	10	9183	9	230
14	AHMEDNAGAR	32974	29179	29186	7	3788	29	95
15	NANDURBAR	14137	10465	10472	7	3665	6	92
16	OSMANABAD	17039	10799	10806	7	6233	10	156
17	SANGLI	8604	6894	6900	6	1704	4	43
18	SOLAPUR	18445	14939	14945	6	3500	7	88
19	WARDHA	11218	8713	8719	6	2499	7	62
20	KOLHAPUR	12528	10579	10584	5	1944	3	49
21	NASHIK	22850	18708	18713	5	4137	13	103
22	GONDIA	12837	9951	9955	4	2882	8	72
23	SATARA	10647	9559	9563	4	1084	6	27
24	DHULE	18081	13071	13074	3	5007	10	125
25	GADCHIROLI	15208	10699	10702	3	4506	9	113
26	JALGAON	22540	17580	17583	3	4957	12	124
27	NAGPUR	11185	9110	9113	3	2072	4	52
28	PALGHAR	11049	7415	7418	3	3631	6	91
29	YAVATMAL	26113	17840	17842	2	8271	13	207
30	BHANDARA	15558	12366	12367	1	3191	4	80
31	PUNE	12773	10018	10019	1	2754	6	69
32	AMRAVATI	19816	13886	13886	0	5930	9	148
33	PARBHANI	17632	13240	13240	0	4392	4	110
34	SINDHUDURG	2108	1886	1886	0	222	1	6
Total		556810	403067	403409	342	153401	300	3835

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	11391	0	40903	0	23475
2	AMRAVATI DIV.	0	31867	0	33563	0	16202
3	AURANGABAD DIV.	0	20748	0	54858	0	24092
4	NAGPUR DIV.	0	11035	0	22219	0	14102
5	KONKAN DIV.	0	554	0	3887	0	3955
6	PUNE DIV.	0	10268	0	16908	0	7124
	Total	0	85863	0	172338	0	88950

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	15
RATNAGIRI	99
THANE	103
PALGHAR	333
GADCHIROLI	375
KOLHAPUR	588
SANGLI	638
SATARA	943
DHULE	1079
NASHIK	1181
PARBHANI	1195
NANDURBAR	1463
GONDIA	1554
WARDHA	1635
NAGPUR	2011
JALNA	2040
HINGOLI	2073
CHANDRAPUR	2239
PUNE	2279
LATUR	2365
AURANGABAD	2845
AHMEDNAGAR	3057
WASHIM	3178
BHANDARA	3221
OSMANABAD	3232
BEED	3475
NANDED	3523
AKOLA	4125
YAVATMAL	4234
JALGAON	4611
SOLAPUR	5820
BULDHANA	8408
AMRAVATI	11922

PMAY-G 2nd Ins Pending

SINDHUDURG	261
RATNAGIRI	462
RAIGAD	557
THANE	672
SATARA	1256
WARDHA	1276
OSMANABAD	1801
PALGHAR	1935
PUNE	2353
KOLHAPUR	2663
GADCHIROLI	2886
NAGPUR	2994
HINGOLI	3279
WASHIM	3316
AHMEDNAGAR	4018
SANGLI	4087
LATUR	4585
GONDIA	4603
JALNA	4680
CHANDRAPUR	4917
AKOLA	5297
BHANDARA	5543
AURANGABAD	6061
BULDHANA	6290
PARBHANI	6324
NASHIK	6350
SOLAPUR	6549
DHULE	7080
BEED	8541
AMRAVATI	9038
YAVATMAL	9622
NANDURBAR	10727
JALGAON	12728
NANDED	19587

PMAY-G 3rd Ins Pending

SINDHUDURG	352
RAIGAD	397
RATNAGIRI	477
THANE	668
KOLHAPUR	1022
WARDHA	1036
PUNE	1083
SATARA	1146
HINGOLI	1454
SANGLI	1529
NAGPUR	1543
LATUR	1884
AKOLA	2017
PALGHAR	2061
SOLAPUR	2344
WASHIM	2405
GADCHIROLI	2412
AURANGABAD	2483
BHANDARA	2544
PARBHANI	2656
CHANDRAPUR	2856
JALNA	2944
BULDHANA	2976
OSMANABAD	3092
AHMEDNAGAR	3238
AMRAVATI	3322
BEED	3599
GONDIA	3711
DHULE	3872
NASHIK	4148
JALGAON	4284
YAVATMAL	5482
NANDED	5980
NANDURBAR	7933

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3057	0	4018	0	3238
2	AKOLA	0	4125	0	5297	0	2017
3	AMRAVATI	0	11922	0	9038	0	3322
4	AURANGABAD	0	2845	0	6061	0	2483
5	BEED	0	3475	0	8541	0	3599
6	BHANDARA	0	3221	0	5543	0	2544
7	BULDHANA	0	8408	0	6290	0	2976
8	CHANDRAPUR	0	2239	0	4917	0	2856
9	DHULE	0	1079	0	7080	0	3872
10	GADCHIROLI	0	375	0	2886	0	2412
11	GONDIA	0	1554	0	4603	0	3711
12	HINGOLI	0	2073	0	3279	0	1454
13	JALGAON	0	4611	0	12728	0	4284
14	JALNA	0	2040	0	4680	0	2944
15	KOLHAPUR	0	588	0	2663	0	1022
16	LATUR	0	2365	0	4585	0	1884
17	NAGPUR	0	2011	0	2994	0	1543
18	NANDED	0	3523	0	19587	0	5980
19	NANDURBAR	0	1463	0	10727	0	7933
20	NASHIK	0	1181	0	6350	0	4148
21	OSMANABAD	0	3232	0	1801	0	3092
22	PALGHAR	0	333	0	1935	0	2061
23	PARBHANI	0	1195	0	6324	0	2656
24	PUNE	0	2279	0	2353	0	1083
25	RAIGAD	0	15	0	557	0	397
26	RATNAGIRI	0	99	0	462	0	477
27	SANGLI	0	638	0	4087	0	1529
28	SINDHUDURG	0	4	0	261	0	352
29	SOLAPUR	0	5820	0	6549	0	2344
30	THANE	0	103	0	672	0	668
31	WARDHA	0	1635	0	1276	0	1036
32	WASHIM	0	3178	0	3316	0	2405
33	YAVATMAL	0	4234	0	9622	0	5482
34	SATARA	-3	943	0	1256	0	1146
	Total	0	85863	0	172338	0	88950

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2559	0	8755	0	5509
2	AMRAVATI DIV.	0	2936	0	13170	0	6284
3	AURANGABAD DIV.	0	16330	0	29274	0	12612
4	NAGPUR DIV.	0	5762	0	8085	0	4080
5	KONKAN DIV.	0	992	0	2918	0	1510
6	PUNE DIV.	0	1645	0	4686	0	2362
Total		0	30224	0	66888	0	32357

State Schemes 1st Ins Pending

SINDHUDURG	14
RATNAGIRI	58
NANDURBAR	83
SATARA	156
SANGLI	182
RAIGAD	218
THANE	231
PUNE	270
KOLHAPUR	337
WARDHA	342
BULDHANA	406
AHMEDNAGAR	408
WASHIM	448
PALGHAR	471
NAGPUR	484
GADCHIROLI	521
AKOLA	554
BHANDARA	621
JALGAON	628
NASHIK	639
YAVATMAL	690
SOLAPUR	700
DHULE	801
GONDIA	829
AMRAVATI	838
PARBHANI	906
JALNA	1180
LATUR	1477
OSMANABAD	1680
HINGOLI	1900
BEED	2429
AURANGABAD	2876
CHANDRAPUR	2965
NANDED	3882

State Schemes 2nd Ins Pending

SINDHUDURG	67
RATNAGIRI	167
THANE	359
SATARA	398
RAIGAD	629
SANGLI	838
NAGPUR	948
PUNE	980
KOLHAPUR	995
NANDURBAR	1052
BHANDARA	1064
GONDIA	1086
WARDHA	1215
NASHIK	1319
WASHIM	1389
SOLAPUR	1475
PALGHAR	1696
GADCHIROLI	1707
CHANDRAPUR	2065
DHULE	2067
AHMEDNAGAR	2115
BULDHANA	2162
JALGAON	2202
PARBHANI	2468
AMRAVATI	2778
AKOLA	2903
HINGOLI	3073
OSMANABAD	3372
JALNA	3455
AURANGABAD	3635
LATUR	3852
YAVATMAL	3938
NANDED	4106
BEED	5313

State Schemes 3rd Ins Pending

SINDHUDURG	62
RATNAGIRI	154
THANE	218
SATARA	274
NAGPUR	297
KOLHAPUR	364
BHANDARA	378
SANGLI	390
WARDHA	426
RAIGAD	473
GONDIA	507
PALGHAR	603
PUNE	626
SOLAPUR	708
WASHIM	821
PARBHANI	865
NASHIK	888
HINGOLI	906
DHULE	962
AKOLA	980
AMRAVATI	981
NANDURBAR	1030
CHANDRAPUR	1161
OSMANABAD	1264
NANDED	1284
JALGAON	1298
GADCHIROLI	1311
AHMEDNAGAR	1331
AURANGABAD	1409
BULDHANA	1588
LATUR	1902
YAVATMAL	1914
JALNA	2457
BEED	2525

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	408	0	2115	0	1331
2	AKOLA	0	554	0	2903	0	980
3	AMRAVATI	0	838	0	2778	0	981
4	AURANGABAD	0	2876	0	3635	0	1409
5	BEED	0	2429	0	5313	0	2525
6	BHANDARA	0	621	0	1064	0	378
7	BULDHANA	0	406	0	2162	0	1588
8	CHANDRAPUR	0	2965	0	2065	0	1161
9	DHULE	0	801	0	2067	0	962
10	GADCHIROLI	0	521	0	1707	0	1311
11	GONDIA	0	829	0	1086	0	507
12	HINGOLI	0	1900	0	3073	0	906
13	JALGAON	0	628	0	2202	0	1298
14	JALNA	0	1180	0	3455	0	2457
15	KOLHAPUR	0	337	0	995	0	364
16	LATUR	0	1477	0	3852	0	1902
17	NAGPUR	0	484	0	948	0	297
18	NANDED	0	3882	0	4106	0	1284
19	NANDURBAR	0	83	0	1052	0	1030
20	NASHIK	0	639	0	1319	0	888
21	OSMANABAD	0	1680	0	3372	0	1264
22	PALGHAR	0	471	0	1696	0	603
23	PARBHANI	0	906	0	2468	0	865
24	PUNE	0	270	0	980	0	626
25	RAIGAD	0	218	0	629	0	473
26	RATNAGIRI	0	58	0	167	0	154
27	SANGLI	0	182	0	838	0	390
28	SINDHUDURG	0	14	0	67	0	62
29	SOLAPUR	0	700	0	1475	0	708
30	THANE	0	231	0	359	0	218
31	WARDHA	0	342	0	1215	0	426
32	WASHIM	0	448	0	1389	0	821
33	YAVATMAL	0	690	0	3938	0	1914
34	SATARA	-1	156	0	398	0	274
	Total	0	30224	0	66888	0	32357

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले

■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2015	1804	3129	1386	48
AKOLA	3952	3543	3625	897	586
AMRAVATI	6600	5633	7274	1463	1013
AURANGABAD	2311	2270	4982	1056	394
BEED	2054	1863	6762	1638	417
BHANDARA	6010	5292	4984	772	2139
BULDHANA	2298	2163	4105	866	693
CHANDRAPUR	2514	1938	3615	699	285
DHULE	4312	4107	6027	2165	1509
GADCHIROLI	3532	2499	2360	1216	860
GONDIA	1989	1958	3268	1052	152
HINGOLI	749	672	2609	452	97
JALGAON	7319	6630	11405	2025	628
JALNA	1215	1074	3191	787	262
KOLHAPUR	1547	752	2410	281	91
LATUR	755	729	2764	445	47
NAGPUR	3132	2363	2606	468	587
NANDED	9544	9156	14864	1945	348
NANDURBAR	11001	10019	7152	4662	5025
NASHIK	5979	3587	4921	2099	1523
OSMANABAD	646	581	1237	440	6
PALGHAR	756	657	1417	679	379
PARBHANI	786	737	4291	534	80
PUNE	2039	1744	1956	483	435
RAIGAD	708	240	487	224	160
RATNAGIRI	95	46	354	120	49
SANGLI	2721	2316	3517	529	124
SATARA	551	389	906	215	140
SINDHUDURG	117	89	221	72	24
SOLAPUR	4810	4597	5102	1257	493
THANE	194	188	621	161	125
WARDHA	988	809	961	217	229
WASHIM	1107	858	2661	389	93
YAVATMAL	5560	4346	7272	1847	1620
