



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०२.०६.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०८६९४	०	१०६७०७४	८६४	०	०	०
राज्य योजना	५७३९०६	१५६५	४१२५८०	४२०	०	०	-१
एकूण	१९८२६००	१५६५	१४७९६५४	१२८४	०	०	-१

PMAY-G Completion Progress Bar

75.7%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

71.9%

State Schemes: Incomplete Houses bifurcation

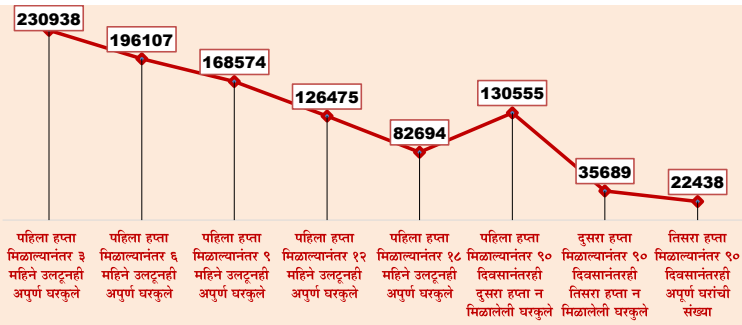


Abhiyan Achievement Day 194

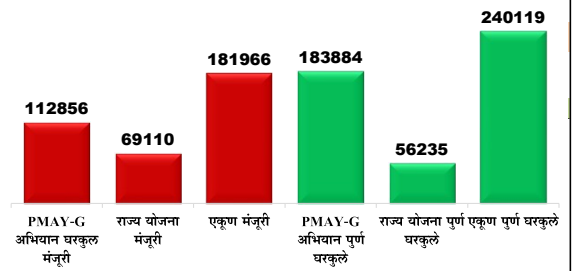

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	01.06.2023	02.06.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414866	413487	413485	0	1381
2	AMRAVATI DIV.	274734	274201	274186	0	548
3	AURANGABAD DIV.	237996	237285	237285	0	711
4	NAGPUR DIV.	291888	291202	291202	0	686
5	KONKAN DIV.	69871	69611	69611	0	260
6	PUNE DIV.	124056	123012	122925	0	1131
Total		1413411	1408798	1408694	0	4717

Sr. No.	District	Target (PWL+Awaas Plus)	01.06.2023	02.06.2023	Daily_Achievement	Remaining
1	AKOLA	48792	48778	48778	0	14
2	AMRAVATI	95496	95242	95242	0	254
3	AURANGABAD	36740	36514	36514	0	226
4	BEED	35310	35253	35253	0	57
5	BHANDARA	64976	64914	64914	0	62
6	BULDHANA	44741	44696	44696	0	45
7	CHANDRAPUR	43094	42958	42958	0	136
8	DHULE	65009	64917	64917	0	92
9	GADCHIROLI	31707	31615	31615	0	92
10	GONDIA	96493	96138	96138	0	355
11	HINGOLI	18109	18083	18083	0	26
12	JALGAON	79662	79180	79180	0	482
13	JALNA	24038	24023	24023	0	15
14	KOLHAPUR	17636	17585	17585	0	51
15	LATUR	20679	20493	20493	0	186
16	NAGPUR	36985	36970	36970	0	15
17	NANDED	69533	69463	69463	0	70
18	NANDURBAR	119664	118958	118958	0	706
19	NASHIK	89748	89683	89683	0	65
20	OSMANABAD	14499	14394	14394	0	105
21	PALGHAR	35415	35188	35188	0	227
22	PARBHANI	19088	19062	19062	0	26
23	PUNE	20367	20292	20292	0	75
24	RAIGAD	9830	9820	9820	0	10
25	RATNAGIRI	9888	9871	9871	0	17
26	SANGLI	21778	21606	21606	0	172
27	SINDHUDURG	5133	5133	5133	0	0
28	SOLAPUR	49081	48380	48380	0	701
29	THANE	9605	9599	9599	0	6
30	WARDHA	18633	18607	18607	0	26
31	WASHIM	20384	20355	20355	0	29
32	AHMEDNAGAR	60783	60749	60747	-2	36
33	YAVATMAL	65321	65130	65115	-15	206
34	SATARA	15194	15149	15062	-87	132
Total		1413411	1408798	1408694	0	4717

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	29
AHMEDNAGAR	36
BULDHANA	45
KOLHAPUR	51
BEED	57
BHANDARA	62
NASHIK	65
NANDED	70
PUNE	75
DHULE	92
GADCHIROLI	92
OSMANABAD	105
SATARA	132
CHANDRAPUR	136
SANGLI	172
LATUR	186
YAVATMAL	206
AURANGABAD	226
PALGHAR	227
AMRAVATI	254
GONDIA	355
JALGAON	482
SOLAPUR	701
NANDURBAR	706

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1161	630	531	29
16	NASHIK	1802	1300	502	1803	1081	722	219
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1676	1127	2829	1349	1480	327
21	NAGPUR	5088	3624	1464	5020	3460	1560	164
22	LATUR	2299	1121	1178	2310	477	1833	644
23	PUNE	2924	1602	1322	2781	880	1901	722
24	JALGAON	22928	20121	2807	22868	20935	1933	-814
25	YAVATMAL	3612	1450	2162	3663	1290	2373	160
26	BHANDARA	5675	3660	2015	5666	3266	2400	394
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3436	865	2571	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7753	4452	3301	-269
31	AKOLA	7072	3935	3137	7367	3942	3425	-7
32	SOLAPUR	7297	3684	3613	7223	1408	5815	2276
33	BULDHANA	15191	8938	6253	15601	7989	7612	949
34	AMRAVATI	21529	12817	8712	21539	11392	10147	1425
	Total	127022	78556	48466	127251	69409	57842	10504

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.06.2023	02.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237285	146583	146897	314	90388	203	30129
2	NASHIK DIV.	413485	334092	334292	200	79193	262	26398
3	NAGPUR DIV.	291202	244126	244258	132	46944	186	15648
4	AMRAVATI DIV.	274186	192514	192620	106	81566	183	27189
5	KONKAN DIV.	69611	59412	59477	65	10134	52	3378
6	PUNE DIV.	122925	89483	89530	47	33395	62	11132
Total		1408694	1066210	1067074	864	341620	948	113873

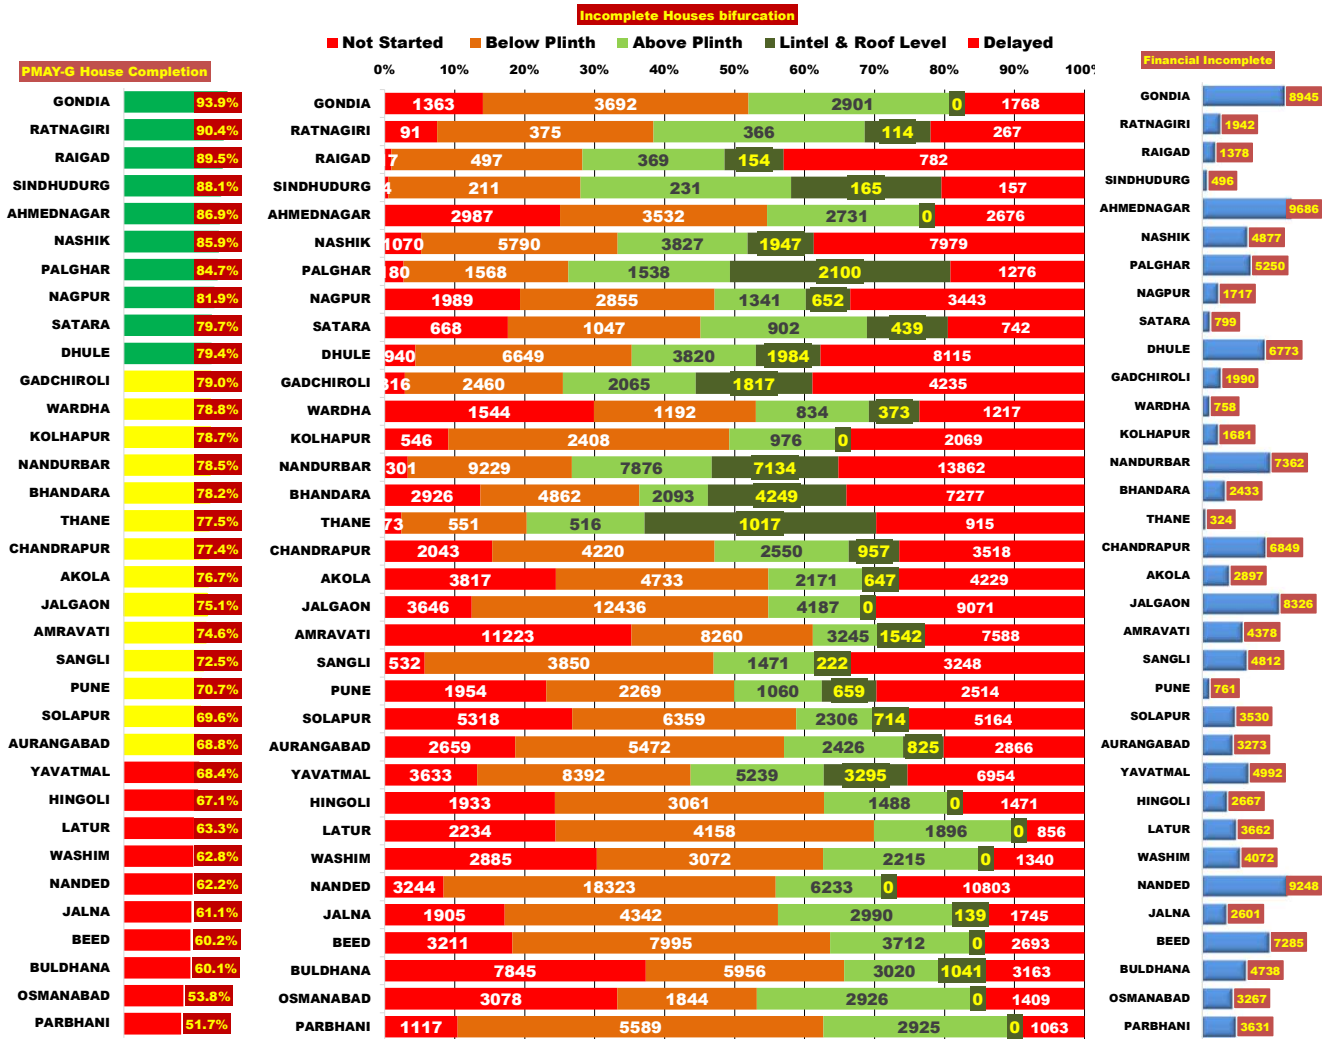

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.06.2023	02.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	69463	42971	43187	216	26276	51	8759
2	NASHIK	89683	76943	77049	106	12634	53	4211
3	GADCHIROLI	31615	24930	24980	50	6635	27	2212
4	YAVATMAL	65115	44514	44563	49	20552	58	6851
5	PALGHAR	35188	29757	29802	45	5386	25	1795
6	JALGAON	79180	59448	59485	37	19695	49	6565
7	AHMEDNAGAR	60747	52782	52816	34	7931	76	2644
8	PARBHANI	19062	9817	9851	34	9211	19	3070
9	AURANGABAD	36514	25104	25133	29	11381	31	3794
10	BHANDARA	64914	50760	50784	24	14130	35	4710
11	GONDIA	96138	90298	90321	23	5817	66	1939
12	BULDHANA	44696	26825	26844	19	17852	30	5951
13	CHANDRAPUR	42958	33222	33241	19	9717	36	3239
14	KOLHAPUR	17585	13817	13834	17	3751	9	1250
15	AMRAVATI	95242	71002	71018	16	24224	48	8075
16	AKOLA	48778	37395	37410	15	11368	22	3789
17	BEED	35253	21207	21221	14	14032	26	4677
18	NAGPUR	36970	30254	30268	14	6702	12	2234
19	NANDURBAR	118958	93404	93418	14	25540	40	8513
20	SOLAPUR	48380	33670	33683	13	14697	19	4899
21	JALNA	24023	14666	14677	11	9346	22	3115
22	RATNAGIRI	9871	8914	8925	11	946	14	315
23	DHULE	64917	51515	51524	9	13393	44	4464
24	LATUR	20493	12958	12966	8	7527	23	2509
25	SATARA	15062	11999	12006	7	3056	14	1019
26	THANE	9599	7435	7442	7	2157	5	719
27	WASHIM	20355	12778	12785	7	7570	25	2523
28	PUNE	20292	14345	14350	5	5942	9	1981
29	SANGLI	21606	15652	15657	5	5949	11	1983
30	HINGOLI	18083	12123	12125	2	5958	16	1986
31	RAIGAD	9820	8784	8786	2	1034	3	345
32	WARDHA	18607	14662	14664	2	3943	11	1314
33	OSMANABAD	14394	7737	7737	0	6657	15	2219
34	SINDHUDURG	5133	4522	4522	0	611	4	204
Total		1408694	1066210	1067074	864	341620	948	113873

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	01.06.2023	02.06.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	200327	170724	171500	776	28827
2	NASHIK DIV.	141552	113156	113621	465	27931
3	AMRAVATI DIV.	110155	95636	95894	258	14261
4	NAGPUR DIV.	118430	97453	97517	64	20913
5	KONKAN DIV.	34744	31985	31987	2	2757
6	PUNE DIV.	65859	63387	63387	0	2472
Total		671067	572341	573906	1565	97161


Sr. No.	District	Target	01.06.2023	02.06.2023	Daily_Achievement	Remaining
1	AURANGABAD	26141	24847	25360	513	781
2	JALGAON	25851	23522	23803	281	2048
3	HINGOLI	27298	17416	17679	263	9619
4	DHULE	21790	18088	18272	184	3518
5	YAVATMAL	30045	27126	27280	154	2765
6	BULDHANA	21702	20220	20324	104	1378
7	CHANDRAPUR	40285	30305	30352	47	9933
8	WARDHA	13147	11255	11264	9	1883
9	GONDIA	14261	13487	13495	8	766
10	RAIGAD	7418	6695	6697	2	721
11	AHMEDNAGAR	35298	34499	34499	0	799
12	AKOLA	23681	17832	17832	0	5849
13	AMRAVATI	23224	19907	19907	0	3317
14	BEED	26878	26109	26109	0	769
15	BHANDARA	17612	15606	15606	0	2006
16	GADCHIROLI	16834	15344	15344	0	1490
17	JALNA	20609	19339	19339	0	1270
18	KOLHAPUR	13090	12889	12889	0	201
19	LATUR	28004	26341	26341	0	1663
20	NAGPUR	16291	11456	11456	0	4835
21	NANDED	26760	21897	21897	0	4863
22	NANDURBAR	26578	14141	14141	0	12437
23	NASHIK	32035	22906	22906	0	9129
24	OSMANABAD	24853	17116	17116	0	7737
25	PALGHAR	11792	11509	11509	0	283
26	PARBHANI	19784	17659	17659	0	2125
27	PUNE	14672	12765	12765	0	1907
28	RATNAGIRI	7129	6690	6690	0	439
29	SANGLI	8732	8604	8604	0	128
30	SATARA	10647	10647	10647	0	0
31	SINDHUDURG	2141	2108	2108	0	33
32	SOLAPUR	18718	18482	18482	0	236
33	THANE	6264	4983	4983	0	1281
34	WASHIM	11503	10551	10551	0	952
Total		671067	572341	573906	1565	97161

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	236
PALGHAR	283
RATNAGIRI	439
RAIGAD	721
GONDIA	766
BEED	769
AURANGABAD	781
AHMEDNAGAR	799
WASHIM	952
JALNA	1270
THANE	1281
BULDHANA	1378
GADCHIROLI	1490
LATUR	1663
WARDHA	1883
PUNE	1907
BHANDARA	2006
JALGAON	2048
PARBHANI	2125
YAVATMAL	2765
AMRAVATI	3317
DHULE	3518
NAGPUR	4835
NANDED	4863
AKOLA	5849
OSMANABAD	7737
NASHIK	9129
HINGOLI	9619
CHANDRAPUR	9933
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.06.2023	02.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	171500	106985	107147	162	64353	88	21451
2	AMRAVATI DIV.	95894	66954	67049	95	28845	56	9615
3	NASHIK DIV.	113621	90267	90326	59	23295	63	7765
4	KONKAN DIV.	31987	24302	24350	48	7637	15	2546
5	NAGPUR DIV.	97517	71108	71149	41	26368	44	8789
6	PUNE DIV.	63387	52544	52559	15	10828	23	3609
Total		573906	412160	412580	420	161326	290	53775

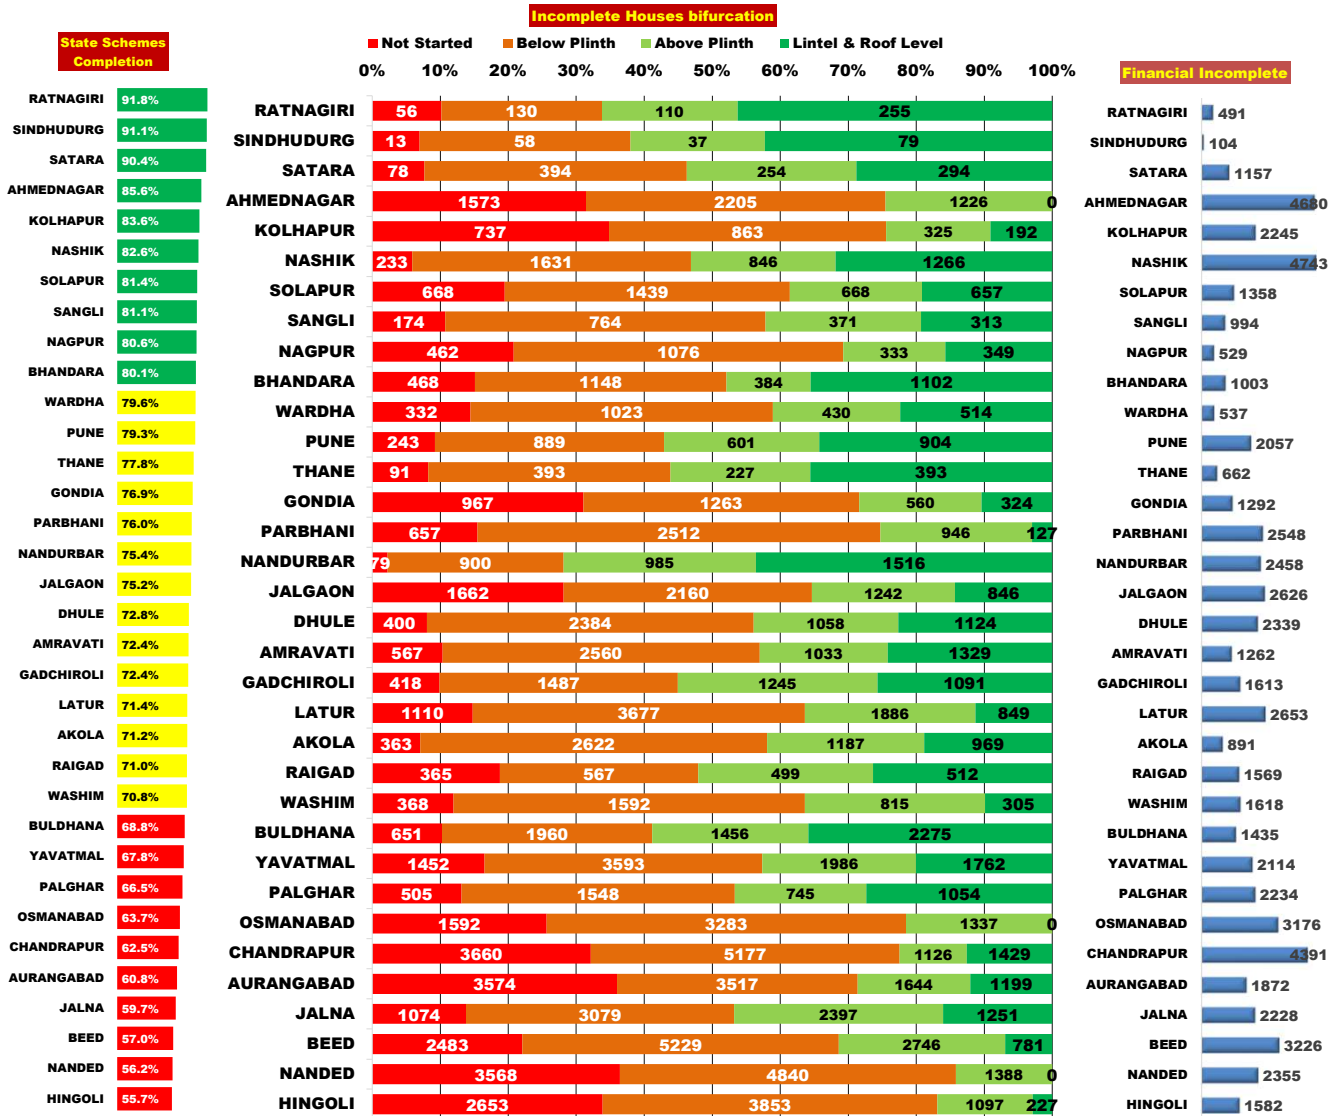

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.06.2023	02.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	YAVATMAL	27280	18425	18487	62	8793	14	2931
2	JALNA	19339	11489	11538	49	7801	23	2600
3	NANDED	21897	12269	12317	48	9580	9	3193
4	AURANGABAD	25360	15399	15426	27	9934	10	3311
5	JALGAON	23803	17869	17893	24	5910	11	1970
6	PALGHAR	11509	7633	7657	24	3852	6	1284
7	GADCHIROLI	15344	11080	11103	23	4241	9	1414
8	LATUR	26341	18796	18819	23	7522	13	2507
9	NASHIK	22906	18915	18930	15	3976	11	1325
10	BULDHANA	20324	13968	13982	14	6342	15	2114
11	THANE	4983	3865	3879	14	1104	2	368
12	CHANDRAPUR	30352	18950	18960	10	11392	12	3797
13	AKOLA	17832	12682	12691	9	5141	9	1714
14	BEED	26109	14861	14870	9	11239	13	3746
15	KOLHAPUR	12889	10763	10772	9	2117	4	706
16	NANDURBAR	14141	10653	10661	8	3480	6	1160
17	RAIGAD	6697	4746	4754	8	1943	3	648
18	AMRAVATI	19907	14411	14418	7	5489	10	1830
19	AHMEDNAGAR	34499	29530	29536	6	4963	25	1654
20	DHULE	18272	13300	13306	6	4966	9	1655
21	NAGPUR	11456	9230	9236	6	2220	4	740
22	HINGOLI	17679	9845	9849	4	7830	7	2610
23	SOLAPUR	18482	15046	15050	4	3432	6	1144
24	WASHIM	10551	7468	7471	3	3080	8	1027
25	PARBHANI	17659	13415	13417	2	4242	4	1414
26	RATNAGIRI	6690	6137	6139	2	551	3	184
27	BHANDARA	15606	12503	12504	1	3102	4	1034
28	GONDIA	13495	10380	10381	1	3114	9	1038
29	PUNE	12765	10127	10128	1	2637	5	879
30	SATARA	10647	9626	9627	1	1020	5	340
31	OSMANABAD	17116	10911	10911	0	6205	9	2068
32	SANGLI	8604	6982	6982	0	1622	3	541
33	SINDHUDURG	2108	1921	1921	0	187	1	62
34	WARDHA	11264	8965	8965	0	2299	7	766
Total		573906	412160	412580	420	161326	290	53775

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	9944	0	37636	0	22441
2	AMRAVATI DIV.	0	29337	0	30413	0	15890
3	AURANGABAD DIV.	0	19350	0	50784	0	24596
4	NAGPUR DIV.	0	9970	0	19281	0	11784
5	KONKAN DIV.	0	362	0	3202	0	3020
6	PUNE DIV.	0	8892	0	15933	0	6715
	Total	0	77855	0	157249	0	84446

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	14
THANE	73
RATNAGIRI	91
PALGHAR	180
GADCHIROLI	293
SANGLI	406
KOLHAPUR	546
SATARA	668
DHULE	940
NASHIK	1070
PARBHANI	1117
NANDURBAR	1301
GONDIA	1363
WARDHA	1544
NAGPUR	1854
JALNA	1875
HINGOLI	1933
PUNE	1954
CHANDRAPUR	1990
LATUR	2234
AURANGABAD	2658
WASHIM	2882
BHANDARA	2926
AHMEDNAGAR	2987
OSMANABAD	3078
BEED	3211
NANDED	3244
YAVATMAL	3626
JALGAON	3646
AKOLA	3817
SOLAPUR	5318
BULDHANA	7835
AMRAVATI	11177

PMAY-G 2nd Ins Pending

SINDHUDURG	211
RATNAGIRI	375
RAIGAD	497
THANE	551
SATARA	1047
WARDHA	1192
PALGHAR	1568
OSMANABAD	1844
PUNE	2269
KOLHAPUR	2408
GADCHIROLI	2460
NAGPUR	2855
HINGOLI	3061
WASHIM	3072
AHMEDNAGAR	3532
GONDIA	3692
SANGLI	3850
LATUR	4158
CHANDRAPUR	4220
JALNA	4342
AKOLA	4733
BHANDARA	4862
AURANGABAD	5472
PARBHANI	5589
NASHIK	5790
BULDHANA	5956
SOLAPUR	6359
DHULE	6649
BEED	7995
AMRAVATI	8260
YAVATMAL	8392
NANDURBAR	9229
JALGAON	12436
NANDED	18323

PMAY-G 3rd Ins Pending

SINDHUDURG	231
RATNAGIRI	366
RAIGAD	369
THANE	516
WARDHA	834
SATARA	902
KOLHAPUR	976
PUNE	1060
NAGPUR	1341
SANGLI	1471
HINGOLI	1488
PALGHAR	1538
LATUR	1896
GADCHIROLI	2065
BHANDARA	2093
AKOLA	2171
WASHIM	2215
SOLAPUR	2306
AURANGABAD	2426
CHANDRAPUR	2550
AHMEDNAGAR	2731
GONDIA	2901
PARBHANI	2925
OSMANABAD	2926
JALNA	2990
BULDHANA	3020
AMRAVATI	3245
BEED	3712
DHULE	3820
NASHIK	3827
JALGAON	4187
YAVATMAL	5239
NANDED	6233
NANDURBAR	7876

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	2987	0	3532	0	2731
2	AKOLA	0	3817	0	4733	0	2171
3	AMRAVATI	0	11177	0	8260	0	3245
4	AURANGABAD	0	2658	0	5472	0	2426
5	BEED	0	3211	0	7995	0	3712
6	BHANDARA	0	2926	0	4862	0	2093
7	BULDHANA	0	7835	0	5956	0	3020
8	CHANDRAPUR	0	1990	0	4220	0	2550
9	DHULE	0	940	0	6649	0	3820
10	GADCHIROLI	0	293	0	2460	0	2065
11	GONDIA	0	1363	0	3692	0	2901
12	HINGOLI	0	1933	0	3061	0	1488
13	JALGAON	0	3646	0	12436	0	4187
14	JALNA	0	1875	0	4342	0	2990
15	KOLHAPUR	0	546	0	2408	0	976
16	LATUR	0	2234	0	4158	0	1896
17	NAGPUR	0	1854	0	2855	0	1341
18	NANDED	0	3244	0	18323	0	6233
19	NANDURBAR	0	1301	0	9229	0	7876
20	NASHIK	0	1070	0	5790	0	3827
21	OSMANABAD	0	3078	0	1844	0	2926
22	PALGHAR	0	180	0	1568	0	1538
23	PARBHANI	0	1117	0	5589	0	2925
24	PUNE	0	1954	0	2269	0	1060
25	RAIGAD	0	14	0	497	0	369
26	RATNAGIRI	0	91	0	375	0	366
27	SANGLI	0	406	0	3850	0	1471
28	SATARA	0	668	0	1047	0	902
29	SINDHUDURG	0	4	0	211	0	231
30	SOLAPUR	0	5318	0	6359	0	2306
31	THANE	0	73	0	551	0	516
32	WARDHA	0	1544	0	1192	0	834
33	WASHIM	0	2882	0	3072	0	2215
34	YAVATMAL	0	3626	0	8392	0	5239
	Total	0	77855	0	157249	0	84446

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	3947	0	9280	0	5357
2	AMRAVATI DIV.	0	3401	0	12327	0	6477
3	AURANGABAD DIV.	0	16711	0	29990	0	13441
4	NAGPUR DIV.	0	6307	0	11174	0	4078
5	KONKAN DIV.	0	1030	0	2696	-1	1618
6	PUNE DIV.	0	1900	0	4349	0	2219
Total		0	33296	0	69816	-1	33190

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	56
SATARA	78
NANDURBAR	79
THANE	91
SANGLI	174
NASHIK	233
PUNE	243
WARDHA	332
AKOLA	363
RAIGAD	365
WASHIM	368
DHULE	400
GADCHIROLI	418
NAGPUR	462
BHANDARA	468
PALGHAR	505
AMRAVATI	567
BULDHANA	651
PARBHANI	657
SOLAPUR	668
KOLHAPUR	737
GONDIA	967
JALNA	1074
LATUR	1110
YAVATMAL	1452
AHMEDNAGAR	1573
OSMANABAD	1592
JALGAON	1662
BEED	2483
HINGOLI	2653
NANDED	3568
AURANGABAD	3574
CHANDRAPUR	3660

State Schemes 2nd Ins Pending

SINDHUDURG	58
RATNAGIRI	130
THANE	393
SATARA	394
RAIGAD	567
SANGLI	764
KOLHAPUR	863
PUNE	889
NANDURBAR	900
WARDHA	1023
NAGPUR	1076
BHANDARA	1148
GONDIA	1263
SOLAPUR	1439
GADCHIROLI	1487
PALGHAR	1548
WASHIM	1592
NASHIK	1631
BULDHANA	1960
JALGAON	2160
AHMEDNAGAR	2205
DHULE	2384
PARBHANI	2512
AMRAVATI	2560
AKOLA	2622
JALNA	3079
OSMANABAD	3283
AURANGABAD	3517
YAVATMAL	3593
LATUR	3677
HINGOLI	3853
NANDED	4840
CHANDRAPUR	5177
BEED	5229

State Schemes 3rd Ins Pending

SINDHUDURG	37
RATNAGIRI	110
THANE	227
SATARA	254
KOLHAPUR	325
NAGPUR	333
SANGLI	371
BHANDARA	384
WARDHA	430
RAIGAD	499
GONDIA	560
PUNE	601
SOLAPUR	668
PALGHAR	745
WASHIM	815
NASHIK	846
PARBHANI	946
NANDURBAR	985
AMRAVATI	1033
DHULE	1058
HINGOLI	1097
CHANDRAPUR	1126
AKOLA	1187
AHMEDNAGAR	1226
JALGAON	1242
GADCHIROLI	1245
OSMANABAD	1337
NANDED	1388
BULDHANA	1456
AURANGABAD	1644
LATUR	1886
YAVATMAL	1986
JALNA	2397
BEED	2746

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	1573	0	2205	0	1226
2	AKOLA	0	363	0	2622	0	1187
3	AMRAVATI	0	567	0	2560	0	1033
4	AURANGABAD	0	3574	0	3517	0	1644
5	BEED	0	2483	0	5229	0	2746
6	BHANDARA	0	468	0	1148	0	384
7	BULDHANA	0	651	0	1960	0	1456
8	CHANDRAPUR	0	3660	0	5177	0	1126
9	DHULE	0	400	0	2384	0	1058
10	GADCHIROLI	0	418	0	1487	0	1245
11	GONDIA	0	967	0	1263	0	560
12	HINGOLI	0	2653	0	3853	0	1097
13	JALGAON	0	1662	0	2160	0	1242
14	JALNA	0	1074	0	3079	0	2397
15	KOLHAPUR	0	737	0	863	0	325
16	LATUR	0	1110	0	3677	0	1886
17	NAGPUR	0	462	0	1076	0	333
18	NANDED	0	3568	0	4840	0	1388
19	NANDURBAR	0	79	0	900	0	985
20	NASHIK	0	233	0	1631	0	846
21	OSMANABAD	0	1592	0	3283	0	1337
22	PALGHAR	0	505	0	1548	-1	745
23	PARBHANI	0	657	0	2512	0	946
24	PUNE	0	243	0	889	0	601
25	RAIGAD	0	365	0	567	0	499
26	RATNAGIRI	0	56	0	130	0	110
27	SANGLI	0	174	0	764	0	371
28	SATARA	0	78	0	394	0	254
29	SINDHUDURG	0	13	0	58	0	37
30	SOLAPUR	0	668	0	1439	0	668
31	THANE	0	91	0	393	0	227
32	WARDHA	0	332	0	1023	0	430
33	WASHIM	0	368	0	1592	0	815
34	YAVATMAL	0	1452	0	3593	0	1986
	Total	0	33296	0	69816	0	33190

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

जिल्हा	पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले	दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले	तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या
AHMEDNAGAR	2676	1675	3174	1696	40
AKOLA	4229	3378	3424	853	554
AMRAVATI	7588	5370	6887	1491	1032
AURANGABAD	2866	2216	4846	1136	493
BEED	2693	1798	6825	1735	436
BHANDARA	7277	4989	4467	800	2295
BULDHANA	3163	2113	4288	935	755
CHANDRAPUR	3518	1936	3408	781	316
DHULE	8115	4021	5780	2364	1631
GADCHIROLI	4235	2367	2209	1188	935
GONDIA	1768	1636	3040	1029	128
HINGOLI	1471	650	2654	514	104
JALGAON	9071	6472	11044	2186	650
JALNA	1745	1063	3345	906	341
KOLHAPUR	2069	708	2289	313	87
LATUR	856	696	2883	507	42
NAGPUR	3443	2274	2541	440	589
NANDED	10803	8918	14801	2134	382
NANDURBAR	13862	9875	7480	4733	5289
NASHIK	7979	3521	4866	2099	1533
OSMANABAD	1409	576	1222	450	6
PALGHAR	1276	624	1233	727	664
PARBHANI	1063	719	4770	708	127
PUNE	2514	1688	1937	547	480
RAIGAD	782	236	468	252	168
RATNAGIRI	267	39	336	154	80
SANGLI	3248	2228	3346	599	174
SATARA	742	352	835	264	176
SINDHUDURG	157	78	195	71	35
SOLAPUR	5164	4515	5131	1251	558
THANE	915	187	509	191	351
WARDHA	1217	765	920	222	215
WASHIM	1340	794	2413	471	52
YAVATMAL	6954	4217	6989	1942	1720
