



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०३.०६.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०८५७४	०	१०६८१९३	१११९	४६२	२३५८	३२०९
राज्य योजना	५७४४५३	५४८	४१३१५२	५७२	०	०	०
एकूण	१९८३०२७	५४८	१४८१३४५	१६९१	४६२	२३५८	३२०९

PMAY-G Completion Progress Bar

75.8%



PMAY-G: Incomplete Houses bifurcation

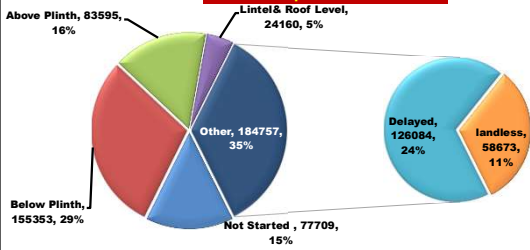



State Schemes Progress Bar

71.9%


State Schemes: Incomplete Houses bifurcation

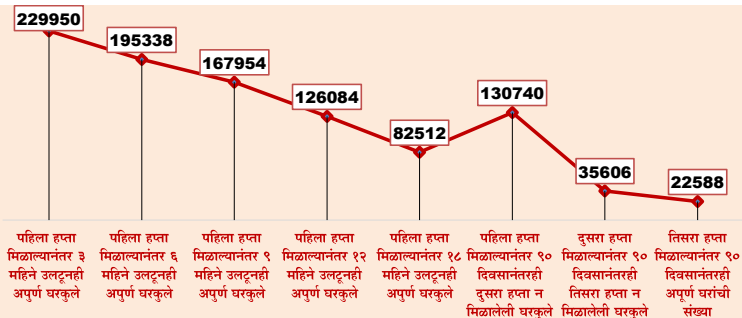

Abhiyan Achievement Day 195

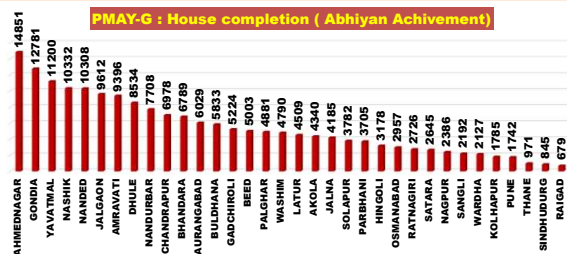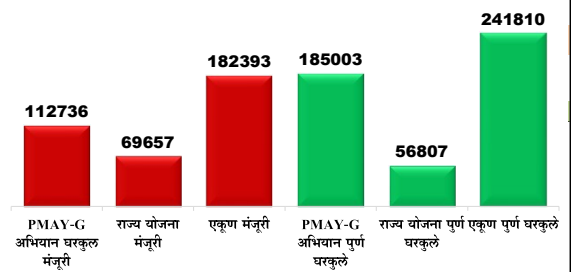

State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.



PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	02.06.2023	03.06.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414866	413485	413464	0	1402
2	AMRAVATI DIV.	274730	274186	274145	0	585
3	AURANGABAD DIV.	237996	237285	237285	0	711
4	NAGPUR DIV.	291859	291202	291172	0	687
5	KONKAN DIV.	69871	69611	69611	0	260
6	PUNE DIV.	124036	122925	122897	0	1139
Total		1413358	1408694	1408574	0	4784

Sr. No.	District	Target (PWL+Awaas Plus)	02.06.2023	03.06.2023	Daily_Achievement	Remaining
1	AKOLA	48792	48778	48778	0	14
2	AURANGABAD	36740	36514	36514	0	226
3	BEED	35310	35253	35253	0	57
4	BHANDARA	64976	64914	64914	0	62
5	BULDHANA	44741	44696	44696	0	45
6	CHANDRAPUR	43094	42958	42958	0	136
7	DHULE	65009	64917	64917	0	92
8	GADCHIROLI	31707	31615	31615	0	92
9	HINGOLI	18109	18083	18083	0	26
10	JALNA	24038	24023	24023	0	15
11	KOLHAPUR	17636	17585	17585	0	51
12	LATUR	20679	20493	20493	0	186
13	NANDED	69533	69463	69463	0	70
14	NANDURBAR	119664	118958	118958	0	706
15	NASHIK	89748	89683	89683	0	65
16	OSMANABAD	14499	14394	14394	0	105
17	PALGHAR	35415	35188	35188	0	227
18	PARBHANI	19088	19062	19062	0	26
19	PUNE	20367	20292	20292	0	75
20	RAIGAD	9830	9820	9820	0	10
21	RATNAGIRI	9888	9871	9871	0	17
22	SANGLI	21778	21606	21606	0	172
23	SINDHUDURG	5133	5133	5133	0	0
24	SOLAPUR	49081	48380	48380	0	701
25	THANE	9605	9599	9599	0	6
26	WARDHA	18633	18607	18607	0	26
27	WASHIM	20384	20355	20355	0	29
28	GONDIA	96493	96138	96137	-1	356
29	JALGAON	79662	79180	79176	-4	486
30	AHMEDNAGAR	60783	60747	60730	-17	53
31	YAVATMAL	65320	65115	65096	-19	224
32	AMRAVATI	95493	95242	95220	-22	273
33	SATARA	15174	15062	15034	-28	140
34	NAGPUR	36956	36970	36941	-29	15
Total		1413358	1408694	1408574	0	4784

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	29
BULDHANA	45
KOLHAPUR	51
AHMEDNAGAR	53
BEED	57
BHANDARA	62
NASHIK	65
NANDED	70
PUNE	75
DHULE	92
GADCHIROLI	92
OSMANABAD	105
CHANDRAPUR	136
SATARA	140
SANGLI	172
LATUR	186
YAVATMAL	224
AURANGABAD	226
PALGHAR	227
AMRAVATI	273
GONDIA	356
JALGAON	486
SOLAPUR	701
NANDURBAR	706

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1127	630	497	29
16	NASHIK	1802	1300	502	1803	1147	656	153
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1499	1304	2829	1395	1434	104
21	NAGPUR	5088	3642	1446	4997	3459	1538	183
22	LATUR	2299	1121	1178	2310	477	1833	644
23	PUNE	2924	1599	1325	2781	880	1901	719
24	JALGAON	22928	20121	2807	22868	20935	1933	-814
25	YAVATMAL	3612	1450	2162	3661	1290	2371	160
26	BHANDARA	5675	3660	2015	5666	3266	2400	394
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3436	865	2571	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7745	4451	3294	-268
31	AKOLA	7072	3935	3137	7373	3942	3431	-7
32	SOLAPUR	7297	3684	3613	7223	1408	5815	2276
33	BULDHANA	15191	8938	6253	15601	7989	7612	949
34	AMRAVATI	21529	12817	8712	21522	11389	10133	1428
	Total	127022	78394	48628	127173	69516	57657	10234

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.06.2023	03.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237285	146897	147435	538	89850	204	44925
2	NASHIK DIV.	413464	334292	334551	259	78913	262	39457
3	NAGPUR DIV.	291172	244258	244413	155	46759	186	23380
4	AMRAVATI DIV.	274145	192620	192716	96	81429	182	40715
5	PUNE DIV.	122897	89530	89568	38	33329	62	16665
6	KONKAN DIV.	69611	59477	59510	33	10101	52	5051
Total		1408574	1067074	1068193	1119	340381	949	170191

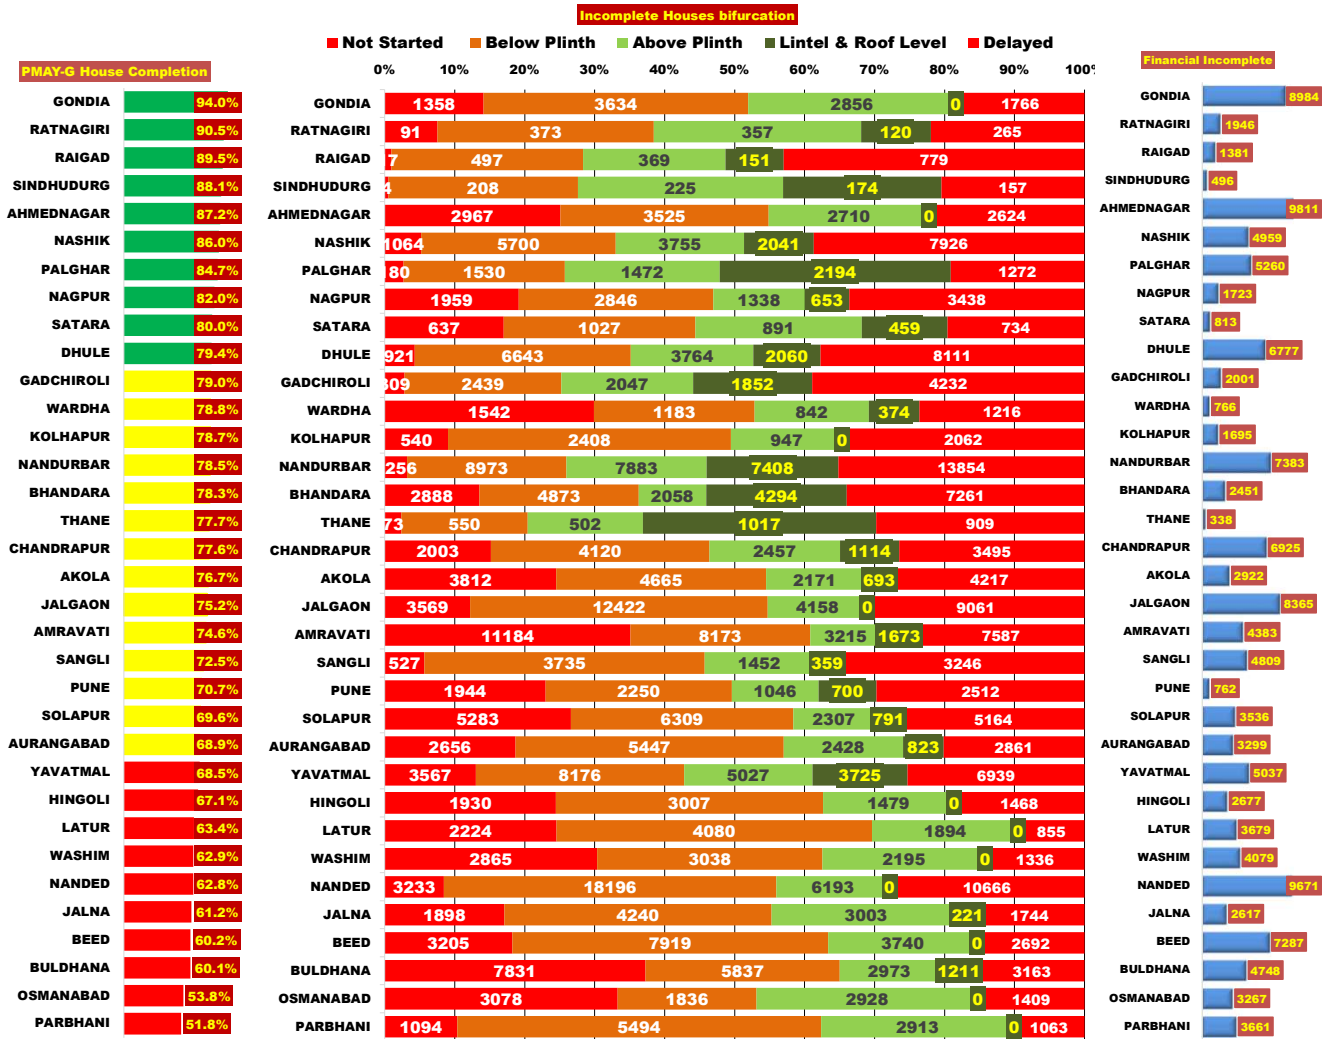

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.06.2023	03.06.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	69463	43187	43618	431	25845	53	12923
2	AHMEDNAGAR	60730	52816	52931	115	7799	76	3900
3	CHANDRAPUR	42958	33241	33317	76	9641	36	4821
4	NASHIK	89683	77049	77123	74	12560	53	6280
5	JALGAON	79176	59485	59530	45	19646	49	9823
6	YAVATMAL	65096	44563	44608	45	20488	57	10244
7	GONDIA	96137	90321	90359	38	5778	66	2889
8	AURANGABAD	36514	25133	25161	28	11353	31	5677
9	AKOLA	48778	37410	37437	27	11341	22	5671
10	PARBHANI	19062	9851	9878	27	9184	19	4592
11	NANDURBAR	118958	93418	93438	20	25520	40	12760
12	BHANDARA	64914	50784	50801	17	14113	35	7057
13	LATUR	20493	12966	12983	17	7510	23	3755
14	THANE	9599	7442	7457	15	2142	5	1071
15	JALNA	24023	14677	14691	14	9332	21	4666
16	SATARA	15034	12006	12020	14	3014	14	1507
17	KOLHAPUR	17585	13834	13847	13	3738	9	1869
18	GADCHIROLI	31615	24980	24991	11	6624	27	3312
19	HINGOLI	18083	12125	12136	11	5947	16	2974
20	NAGPUR	36941	30268	30279	11	6662	12	3331
21	WASHIM	20355	12785	12796	11	7559	25	3780
22	BEED	35253	21221	21231	10	14022	26	7011
23	BULDHANA	44696	26844	26854	10	17842	30	8921
24	PALGHAR	35188	29802	29812	10	5376	25	2688
25	SOLAPUR	48380	33683	33690	7	14690	19	7345
26	DHULE	64917	51524	51529	5	13388	44	6694
27	RATNAGIRI	9871	8925	8930	5	941	14	471
28	AMRAVATI	95220	71018	71021	3	24199	48	12100
29	RAIGAD	9820	8786	8789	3	1031	3	516
30	PUNE	20292	14350	14352	2	5940	9	2970
31	SANGLI	21606	15657	15659	2	5947	11	2974
32	WARDHA	18607	14664	14666	2	3941	11	1971
33	OSMANABAD	14394	7737	7737	0	6657	15	3329
34	SINDHUDURG	5133	4522	4522	0	611	4	306
Total		1408574	1067074	1068193	1119	340381	949	170191

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	02.06.2023	03.06.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	97517	97780	263	20650
2	NASHIK DIV.	141552	113621	113854	233	27698
3	AURANGABAD DIV.	200327	171500	171531	32	28796
4	AMRAVATI DIV.	110155	95894	95913	19	14242
5	KONKAN DIV.	34744	31987	31988	1	2756
6	PUNE DIV.	65859	63387	63387	0	2472
Total		671067	573906	574453	548	96614


Sr. No.	District	Target	02.06.2023	03.06.2023	Daily_Achievement	Remaining
1	JALGAON	25851	23803	24036	233	1815
2	CHANDRAPUR	40285	30352	30506	154	9779
3	NAGPUR	16291	11456	11562	106	4729
4	NANDED	26760	21897	21922	25	4838
5	BULDHANA	21702	20324	20343	19	1359
6	JALNA	20609	19339	19346	7	1263
7	GADCHIROLI	16834	15344	15347	3	1487
8	RAIGAD	7418	6697	6698	1	720
9	AHMEDNAGAR	35298	34499	34499	0	799
10	AKOLA	23681	17832	17832	0	5849
11	AMRAVATI	23224	19907	19907	0	3317
12	AURANGABAD	26141	25360	25360	0	781
13	BHANDARA	17612	15606	15606	0	2006
14	DHULE	21790	18272	18272	0	3518
15	GONDIA	14261	13495	13495	0	766
16	HINGOLI	27298	17679	17679	0	9619
17	KOLHAPUR	13090	12889	12889	0	201
18	LATUR	28004	26341	26341	0	1663
19	NANDURBAR	26578	14141	14141	0	12437
20	NASHIK	32035	22906	22906	0	9129
21	OSMANABAD	24853	17116	17116	0	7737
22	PALGHAR	11792	11509	11509	0	283
23	PARBHANI	19784	17659	17659	0	2125
24	PUNE	14672	12765	12765	0	1907
25	RATNAGIRI	7129	6690	6690	0	439
26	SANGLI	8732	8604	8604	0	128
27	SATARA	10647	10647	10647	0	0
28	SINDHUDURG	2141	2108	2108	0	33
29	SOLAPUR	18718	18482	18482	0	236
30	THANE	6264	4983	4983	0	1281
31	WARDHA	13147	11264	11264	0	1883
32	WASHIM	11503	10551	10551	0	952
33	YAVATMAL	30045	27280	27280	0	2765
34	BEED	26878	26109	26108	-1	770
Total		671067	573906	574453	548	96614

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	236
PALGHAR	283
RATNAGIRI	439
RAIGAD	720
GONDIA	766
BEED	770
AURANGABAD	781
AHMEDNAGAR	799
WASHIM	952
JALNA	1263
THANE	1281
BULDHANA	1359
GADCHIROLI	1487
LATUR	1663
JALGAON	1815
WARDHA	1883
PUNE	1907
BHANDARA	2006
PARBHANI	2125
YAVATMAL	2765
AMRAVATI	3317
DHULE	3518
NAGPUR	4729
NANDED	4838
AKOLA	5849
OSMANABAD	7737
NASHIK	9129
HINGOLI	9619
CHANDRAPUR	9779
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.06.2023	03.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	171531	107147	107321	174	64210	88	32105
2	AMRAVATI DIV.	95913	67049	67206	157	28707	56	14354
3	NAGPUR DIV.	97780	71149	71297	148	26483	45	13242
4	NASHIK DIV.	113854	90326	90371	45	23483	63	11742
5	KONKAN DIV.	31988	24350	24377	27	7611	15	3806
6	PUNE DIV.	63387	52559	52580	21	10807	23	5404
Total		574453	412580	413152	572	161301	291	80651

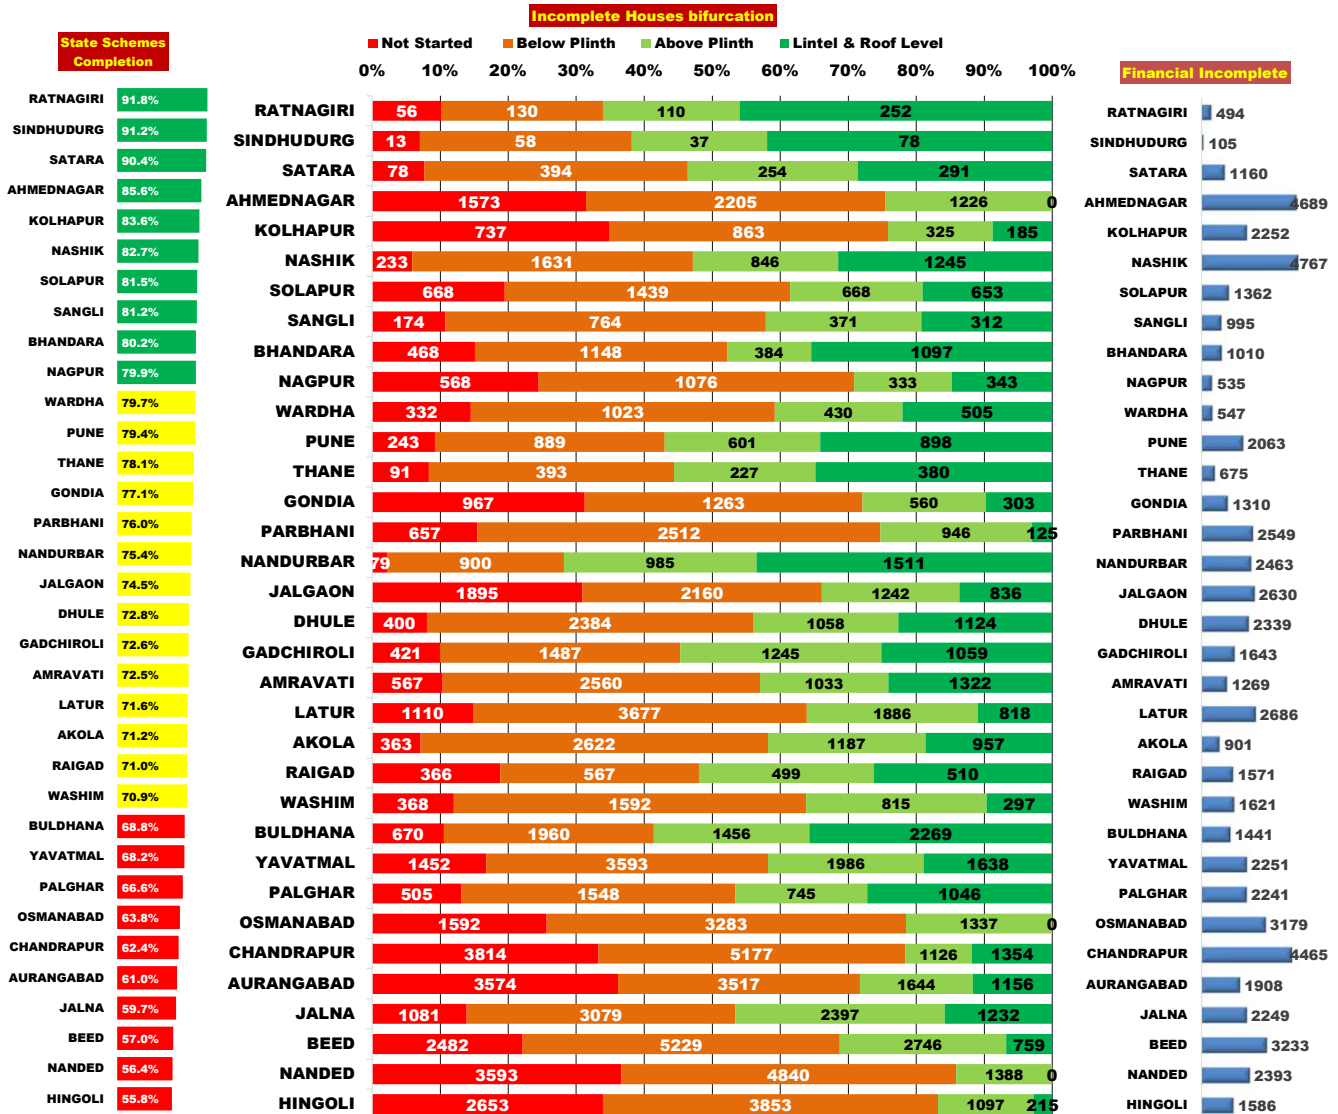

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.06.2023	03.06.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	YAVATMAL	27280	18487	18611	124	8669	14	4335
2	CHANDRAPUR	30506	18960	19035	75	11471	12	5736
3	AURANGABAD	25360	15426	15469	43	9891	10	4946
4	NANDED	21922	12317	12359	42	9563	9	4782
5	GADCHIROLI	15347	11103	11135	32	4212	9	2106
6	LATUR	26341	18819	18850	31	7491	13	3746
7	BEED	26108	14870	14892	22	11216	13	5608
8	GONDIA	13495	10381	10402	21	3093	9	1547
9	NASHIK	22906	18930	18951	21	3955	11	1978
10	JALNA	19346	11538	11557	19	7789	23	3895
11	THANE	4983	3879	3892	13	1091	2	546
12	AKOLA	17832	12691	12703	12	5129	9	2565
13	HINGOLI	17679	9849	9861	12	7818	7	3909
14	JALGAON	24036	17893	17903	10	6133	11	3067
15	AHMEDNAGAR	34499	29536	29545	9	4954	25	2477
16	WARDHA	11264	8965	8974	9	2290	7	1145
17	PALGHAR	11509	7657	7665	8	3844	6	1922
18	WASHIM	10551	7471	7479	8	3072	8	1536
19	AMRAVATI	19907	14418	14425	7	5482	10	2741
20	KOLHAPUR	12889	10772	10779	7	2110	4	1055
21	BULDHANA	20343	13982	13988	6	6355	15	3178
22	NAGPUR	11562	9236	9242	6	2320	4	1160
23	PUNE	12765	10128	10134	6	2631	5	1316
24	BHANDARA	15606	12504	12509	5	3097	4	1549
25	NANDURBAR	14141	10661	10666	5	3475	6	1738
26	SOLAPUR	18482	15050	15054	4	3428	6	1714
27	OSMANABAD	17116	10911	10914	3	6202	9	3101
28	RATNAGIRI	6690	6139	6142	3	548	3	274
29	SATARA	10647	9627	9630	3	1017	5	509
30	PARBHANI	17659	13417	13419	2	4240	4	2120
31	RAIGAD	6698	4754	4756	2	1942	3	971
32	SANGLI	8604	6982	6983	1	1621	3	811
33	SINDHUDURG	2108	1921	1922	1	186	1	93
34	DHULE	18272	13306	13306	0	4966	9	2483
Total		574453	412580	413152	572	161301	291	80651

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AMRAVATI DIV.	103	29193	627	29889	936	15581
2	NASHIK DIV.	146	9777	519	37263	690	22270
3	AURANGABAD DIV.	63	19287	628	50219	646	24578
4	NAGPUR DIV.	91	9849	277	19095	463	11598
5	PUNE DIV.	59	8805	263	15729	335	6643
6	KONKAN DIV.	0	362	44	3158	139	2925
Total		462	77273	2358	155353	3209	83595

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	14
THANE	73
RATNAGIRI	91
PALGHAR	180
GADCHIROLI	286
SANGLI	401
KOLHAPUR	540
SATARA	637
DHULE	921
NASHIK	1064
PARBHANI	1094
NANDURBAR	1256
GONDIA	1358
WARDHA	1542
NAGPUR	1825
JALNA	1868
HINGOLI	1930
PUNE	1944
CHANDRAPUR	1950
LATUR	2224
AURANGABAD	2655
WASHIM	2862
BHANDARA	2888
AHMEDNAGAR	2967
OSMANABAD	3078
BEED	3205
NANDED	3233
YAVATMAL	3560
JALGAON	3569
AKOLA	3812
SOLAPUR	5283
BULDHANA	7821
AMRAVATI	11138

PMAY-G 2nd Ins Pending

SINDHUDURG	208
RATNAGIRI	373
RAIGAD	497
THANE	550
SATARA	1027
WARDHA	1183
PALGHAR	1530
OSMANABAD	1836
PUNE	2250
KOLHAPUR	2408
GADCHIROLI	2439
NAGPUR	2846
HINGOLI	3007
WASHIM	3038
AHMEDNAGAR	3525
GONDIA	3634
SANGLI	3735
LATUR	4080
CHANDRAPUR	4120
JALNA	4240
AKOLA	4665
BHANDARA	4873
AURANGABAD	5447
PARBHANI	5494
NASHIK	5700
BULDHANA	5837
SOLAPUR	6309
DHULE	6643
BEED	7919
AMRAVATI	8173
YAVATMAL	8176
NANDURBAR	8973
JALGAON	12422
NANDED	18196

PMAY-G 3rd Ins Pending

SINDHUDURG	225
RATNAGIRI	357
RAIGAD	369
THANE	502
WARDHA	842
SATARA	891
KOLHAPUR	947
PUNE	1046
NAGPUR	1338
SANGLI	1452
PALGHAR	1472
HINGOLI	1479
LATUR	1894
GADCHIROLI	2047
BHANDARA	2058
AKOLA	2171
WASHIM	2195
SOLAPUR	2307
AURANGABAD	2428
CHANDRAPUR	2457
AHMEDNAGAR	2710
GONDIA	2856
PARBHANI	2913
OSMANABAD	2928
BULDHANA	2973
JALNA	3003
AMRAVATI	3215
BEED	3740
NASHIK	3755
DHULE	3764
JALGAON	4158
YAVATMAL	5027
NANDED	6193
NANDURBAR	7883

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	YAVATMAL	47	3560	263	8176	475	5027
2	NANDURBAR	45	1256	301	8973	294	7883
3	CHANDRAPUR	40	1950	140	4120	233	2457
4	BULDHANA	14	7821	133	5837	180	2973
5	NANDED	11	3233	138	18196	178	6193
6	JALGAON	73	3569	87	12422	116	4158
7	PARBHANI	23	1094	118	5494	130	2913
8	NASHIK	6	1064	96	5700	168	3755
9	SANGLI	5	401	120	3735	139	1452
10	AMRAVATI	17	11138	104	8173	134	3215
11	JALNA	7	1868	109	4240	96	3003
12	SOLAPUR	35	5283	85	6309	84	2307
13	LATUR	10	2224	88	4080	90	1894
14	GONDIA	4	1358	62	3634	107	2856
15	AKOLA	5	3812	73	4665	73	2171
16	WASHIM	20	2862	54	3038	74	2195
17	BEED	6	3205	82	7919	54	3740
18	PALGHAR	0	180	38	1530	104	1472
19	BHANDARA	38	2888	27	4873	62	2058
20	HINGOLI	3	1930	57	3007	66	1479
21	DHULE	19	921	25	6643	81	3764
22	PUNE	10	1944	29	2250	43	1046
23	GADCHIROLI	7	286	28	2439	46	2047
24	SATARA	3	637	23	1027	34	891
25	AURANGABAD	3	2655	28	5447	26	2428
26	KOLHAPUR	6	540	6	2408	35	947
27	AHMEDNAGAR	3	2967	10	3525	31	2710
28	NAGPUR	0	1825	9	2846	12	1338
29	THANE	0	73	1	550	15	502
30	WARDHA	2	1542	11	1183	3	842
31	OSMANABAD	0	3078	8	1836	6	2928
32	RATNAGIRI	0	91	2	373	11	357
33	SINDHUDURG	0	4	3	208	9	225
34	RAIGAD	0	14	0	497	0	369
	Total	462	77273	2358	155353	3209	83595

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	4180	0	9280	0	5357
2	AMRAVATI DIV.	0	3420	0	12327	0	6477
3	AURANGABAD DIV.	0	16742	0	29990	0	13441
4	NAGPUR DIV.	0	6570	0	11174	0	4078
5	KONKAN DIV.	0	1031	0	2696	0	1618
6	PUNE DIV.	0	1900	0	4349	0	2219
Total		0	33843	0	69816	0	33190

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	56
SATARA	78
NANDURBAR	79
THANE	91
SANGLI	174
NASHIK	233
PUNE	243
WARDHA	332
AKOLA	363
RAIGAD	366
WASHIM	368
DHULE	400
GADCHIROLI	421
BHANDARA	468
PALGHAR	505
AMRAVATI	567
NAGPUR	568
PARBHANI	657
SOLAPUR	668
BULDHANA	670
KOLHAPUR	737
GONDIA	967
JALNA	1081
LATUR	1110
YAVATMAL	1452
AHMEDNAGAR	1573
OSMANABAD	1592
JALGAON	1895
BEED	2482
HINGOLI	2653
AURANGABAD	3574
NANDED	3593
CHANDRAPUR	3814

State Schemes 2nd Ins Pending

SINDHUDURG	58
RATNAGIRI	130
THANE	393
SATARA	394
RAIGAD	567
SANGLI	764
KOLHAPUR	863
PUNE	889
NANDURBAR	900
WARDHA	1023
NAGPUR	1076
BHANDARA	1148
GONDIA	1263
SOLAPUR	1439
GADCHIROLI	1487
PALGHAR	1548
WASHIM	1592
NASHIK	1631
BULDHANA	1960
JALGAON	2160
AHMEDNAGAR	2205
DHULE	2384
PARBHANI	2512
AMRAVATI	2560
AKOLA	2622
JALNA	3079
OSMANABAD	3283
AURANGABAD	3517
YAVATMAL	3593
LATUR	3677
HINGOLI	3853
NANDED	4840
CHANDRAPUR	5177
BEED	5229

State Schemes 3rd Ins Pending

SINDHUDURG	37
RATNAGIRI	110
THANE	227
SATARA	254
KOLHAPUR	325
NAGPUR	333
SANGLI	371
BHANDARA	384
WARDHA	430
RAIGAD	499
GONDIA	560
PUNE	601
SOLAPUR	668
PALGHAR	745
WASHIM	815
NASHIK	846
PARBHANI	946
NANDURBAR	985
AMRAVATI	1033
DHULE	1058
HINGOLI	1097
CHANDRAPUR	1126
AKOLA	1187
AHMEDNAGAR	1226
JALGAON	1242
GADCHIROLI	1245
OSMANABAD	1337
NANDED	1388
BULDHANA	1456
AURANGABAD	1644
LATUR	1886
YAVATMAL	1986
JALNA	2397
BEED	2746

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	1573	0	2205	0	1226
2	AKOLA	0	363	0	2622	0	1187
3	AMRAVATI	0	567	0	2560	0	1033
4	AURANGABAD	0	3574	0	3517	0	1644
5	BEED	0	2482	0	5229	0	2746
6	BHANDARA	0	468	0	1148	0	384
7	BULDHANA	0	670	0	1960	0	1456
8	CHANDRAPUR	0	3814	0	5177	0	1126
9	DHULE	0	400	0	2384	0	1058
10	GADCHIROLI	0	421	0	1487	0	1245
11	GONDIA	0	967	0	1263	0	560
12	HINGOLI	0	2653	0	3853	0	1097
13	JALGAON	0	1895	0	2160	0	1242
14	JALNA	0	1081	0	3079	0	2397
15	KOLHAPUR	0	737	0	863	0	325
16	LATUR	0	1110	0	3677	0	1886
17	NAGPUR	0	568	0	1076	0	333
18	NANDED	0	3593	0	4840	0	1388
19	NANDURBAR	0	79	0	900	0	985
20	NASHIK	0	233	0	1631	0	846
21	OSMANABAD	0	1592	0	3283	0	1337
22	PALGHAR	0	505	0	1548	0	745
23	PARBHANI	0	657	0	2512	0	946
24	PUNE	0	243	0	889	0	601
25	RAIGAD	0	366	0	567	0	499
26	RATNAGIRI	0	56	0	130	0	110
27	SANGLI	0	174	0	764	0	371
28	SATARA	0	78	0	394	0	254
29	SINDHUDURG	0	13	0	58	0	37
30	SOLAPUR	0	668	0	1439	0	668
31	THANE	0	91	0	393	0	227
32	WARDHA	0	332	0	1023	0	430
33	WASHIM	0	368	0	1592	0	815
34	YAVATMAL	0	1452	0	3593	0	1986
	Total	0	33843	0	69816	0	33190

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
 ■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

जिल्हा	पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले	दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले	तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या
AHMEDNAGAR	2624	1658	3173	1695	38
AKOLA	4217	3371	3450	854	555
AMRAVATI	7587	5369	6890	1492	1041
AURANGABAD	2861	2212	4832	1138	492
BEED	2692	1797	6759	1724	436
BHANDARA	7261	4977	4456	802	2327
BULDHANA	3163	2113	4246	908	760
CHANDRAPUR	3495	1929	3398	781	314
DHULE	8111	4020	5780	2364	1629
GADCHIROLI	4232	2366	2204	1187	964
GONDIA	1766	1635	3026	1036	131
HINGOLI	1468	649	2651	512	105
JALGAON	9061	6470	11021	2165	643
JALNA	1744	1062	3343	915	345
KOLHAPUR	2062	708	2288	315	88
LATUR	855	695	2860	497	42
NAGPUR	3438	2273	2539	440	586
NANDED	10666	8818	14814	2125	366
NANDURBAR	13854	9870	7973	4767	5313
NASHIK	7926	3516	4843	2091	1527
OSMANABAD	1409	576	1217	453	6
PALGHAR	1272	622	1267	742	727
PARBHANI	1063	719	4692	678	126
PUNE	2512	1687	1932	548	489
RAIGAD	779	235	468	252	169
RATNAGIRI	265	39	337	149	81
SANGLI	3246	2227	3326	590	178
SATARA	734	351	820	265	175
SINHDURG	157	78	195	71	35
SOLAPUR	5164	4515	5117	1242	561
THANE	909	187	509	197	344
WARDHA	1216	765	918	223	218
WASHIM	1336	791	2448	482	54
YAVATMAL	6939	4212	6948	1906	1723
