



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०२.०३.२०२३

प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी व पूर्ण घरकुले
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी व पूर्ण घरकुले



योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१५२७८	११	१७६०३५	३४३२	०	०	०
राज्य योजना	५३४९८८	२७९	३८६१०२	७६२	०	०	०
एकूण	१९५०२६६	२९०	१३६२१३७	४१९४	०	०	०

PMAY-G Completion Progress Bar


69.0%

State Schemes Progress Bar

72.2%

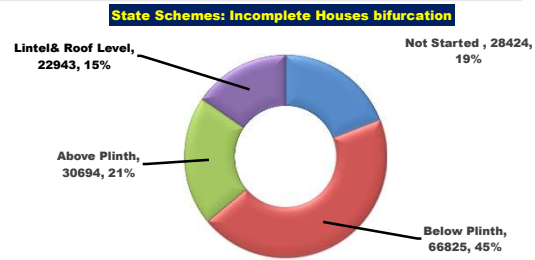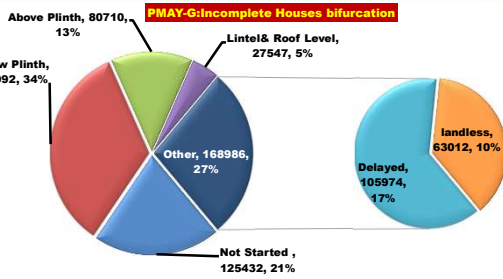


Delayed Houses bifurcation

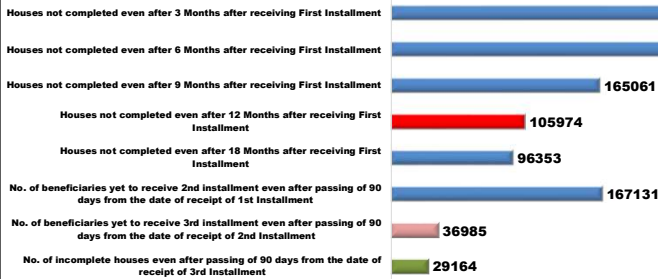


Abhiyan Achievement


Day 102

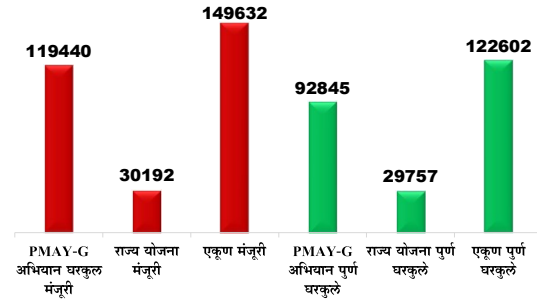

PMAY-G : House completion (Abhiyan Achievement)

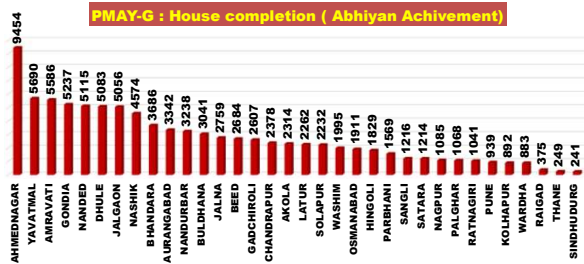

State Schemes : House completion (Abhiyan Achievement)

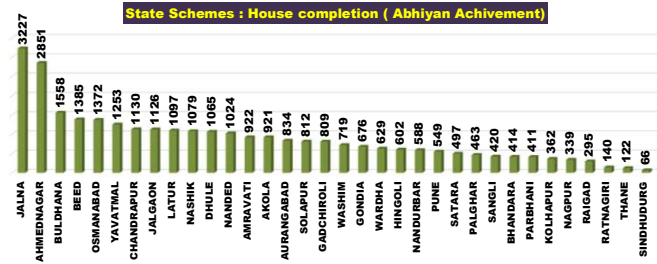


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	01.03.2023	02.03.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414760	414025	414032	11	728
2	AMRAVATI DIV.	274989	274639	274639	0	350
3	AURANGABAD DIV.	238469	238173	238168	0	301
4	NAGPUR DIV.	292587	292040	292030	0	557
5	KONKAN DIV.	69688	69663	69663	0	25
6	PUNE DIV.	127186	127064	126746	0	440
	Total	1417679	1415604	1415278	11	2401

PMAY-G Remaining Sanction

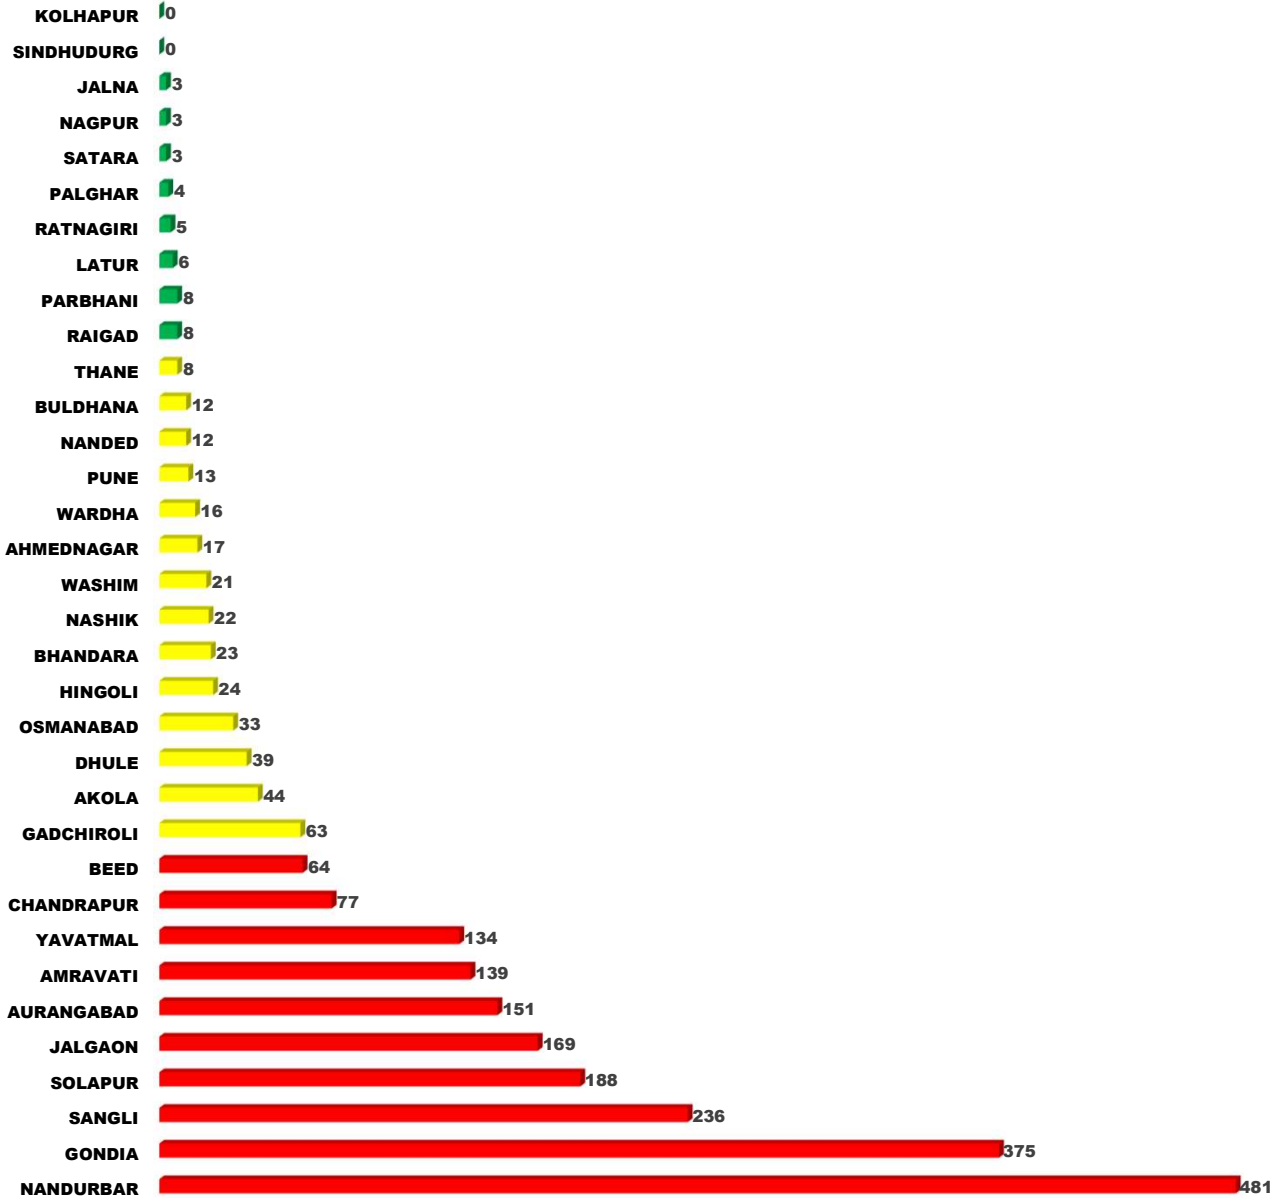


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	01.03.2023	02.03.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60814	60786	60797	11	17
2	AKOLA	48794	48750	48750	0	44
3	AMRAVATI	95646	95507	95507	0	139
4	AURANGABAD	36905	36754	36754	0	151
5	BEED	35334	35270	35270	0	64
6	BHANDARA	65136	65113	65113	0	23
7	BULDHANA	44742	44730	44730	0	12
8	DHULE	64916	64877	64877	0	39
9	GADCHIROLI	31639	31576	31576	0	63
10	HINGOLI	18107	18083	18083	0	24
11	JALNA	24047	24044	24044	0	3
12	KOLHAPUR	17795	17795	17795	0	0
13	LATUR	20799	20793	20793	0	6
14	NAGPUR	37331	37328	37328	0	3
15	NANDURBAR	119349	118868	118868	0	481
16	OSMANABAD	14583	14550	14550	0	33
17	PALGHAR	35152	35148	35148	0	4
18	PARBHANI	19106	19098	19098	0	8
19	RAIGAD	9847	9839	9839	0	8
20	RATNAGIRI	9927	9922	9922	0	5
21	SINDHUDURG	5156	5156	5156	0	0
22	THANE	9606	9598	9598	0	8
23	WARDHA	18671	18655	18655	0	16
24	WASHIM	20416	20395	20395	0	21
25	YAVATMAL	65391	65257	65257	0	134
26	JALGAON	79891	79723	79722	-1	169
27	SATARA	15568	15567	15565	-2	3
28	GONDIA	96474	96102	96099	-3	375
29	NASHIK	89790	89771	89768	-3	22
30	NANDED	69588	69581	69576	-5	12
31	CHANDRAPUR	43336	43266	43259	-7	77
32	SOLAPUR	50379	50215	50191	-24	188
33	PUNE	21144	21167	21131	-36	13
34	SANGLI	22300	22320	22064	-256	236
Total		1417679	1415604	1415278	11	2401

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.03.2023	02.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI DIV.	274639	174775	175783	1008	98856	183	3409
2	NASHIK DIV.	414032	310060	310919	859	103113	269	3556
3	NAGPUR DIV.	292030	223365	224004	639	68026	156	2346
4	PUNE DIV.	126746	83455	83915	460	42831	64	1477
5	KONKAN DIV.	69663	52085	52382	297	17281	29	596
6	AURANGABAD DIV.	238168	128863	129032	169	109136	211	3763
Total		1415278	972603	976035	3432	439243	910	15146

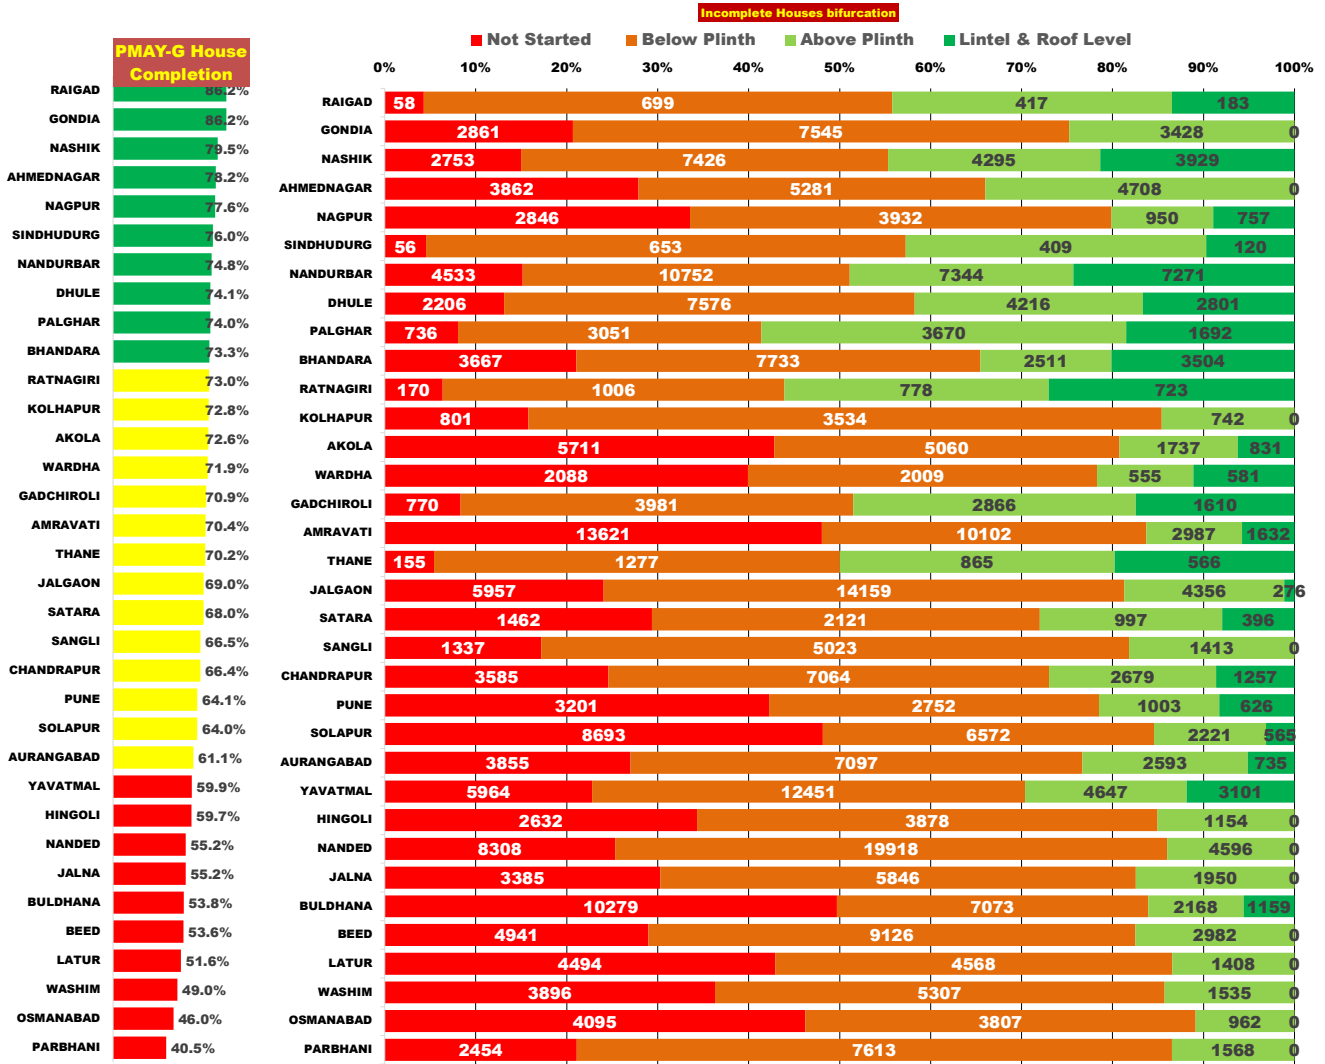


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.03.2023	02.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI	95507	66885	67211	326	28296	55	976
2	GONDIA	96099	82545	82815	270	13284	51	458
3	AHMEDNAGAR	60797	47305	47534	229	13263	93	457
4	YAVATMAL	65257	38875	39098	223	26159	56	902
5	PUNE	21131	13333	13549	216	7582	9	261
6	NASHIK	89768	71172	71365	193	18403	45	635
7	PALGHAR	35148	25810	25999	189	9149	10	315
8	AKOLA	48750	35224	35411	187	13339	23	460
9	JALGAON	79722	54791	54974	183	24748	50	853
10	NANDURBAR	118868	88812	88968	156	29900	32	1031
11	BULDHANA	44730	23916	24062	146	20668	30	713
12	WASHIM	20395	9875	10001	126	10394	20	358
13	CHANDRAPUR	43259	28593	28717	124	14542	23	501
14	DHULE	64877	47980	48078	98	16799	50	579
15	KOLHAPUR	17795	12857	12954	97	4841	9	167
16	SOLAPUR	50191	32053	32140	87	18051	22	622
17	NAGPUR	37328	28906	28978	72	8350	11	288
18	GADCHIROLI	31576	22308	22374	66	9202	26	317
19	RATNAGIRI	9922	7184	7245	61	2677	10	92
20	BHANDARA	65113	47640	47698	58	17415	36	601
21	WARDHA	18655	13373	13422	49	5233	9	180
22	AURANGABAD	36754	22429	22474	45	14280	33	492
23	SATARA	15565	10556	10589	33	4976	12	172
24	SINDHUDURG	5156	3885	3918	33	1238	2	43
25	JALNA	24044	13238	13265	27	10779	27	372
26	SANGLI	22064	14656	14683	27	7381	12	255
27	NANDED	69576	38399	38425	26	31151	50	1074
28	PARBHANI	19098	7718	7742	24	11356	15	392
29	OSMANABAD	14550	6677	6691	14	7859	19	271
30	BEED	35270	18899	18912	13	16358	26	564
31	HINGOLI	18083	10775	10787	12	7296	18	252
32	RAIGAD	9839	8476	8485	9	1354	4	47
33	LATUR	20793	10728	10736	8	10057	22	347
34	THANE	9598	6730	6735	5	2863	2	99
Total		1415278	972603	976035	3432	439243	910	15146

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	01.03.2023	02.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	157251	157448	197	41883
2	AMRAVATI DIV.	109702	90648	90690	52	19012
3	KONKAN DIV.	34729	28980	29002	22	5727
4	NAGPUR DIV.	116255	86616	86621	5	29634
5	NASHIK DIV.	141360	108326	108329	3	33031
6	PUNE DIV.	65334	62898	62898	0	2436
	Total	666711	534719	534988	279	131723

State Scheme Remaining Sanction

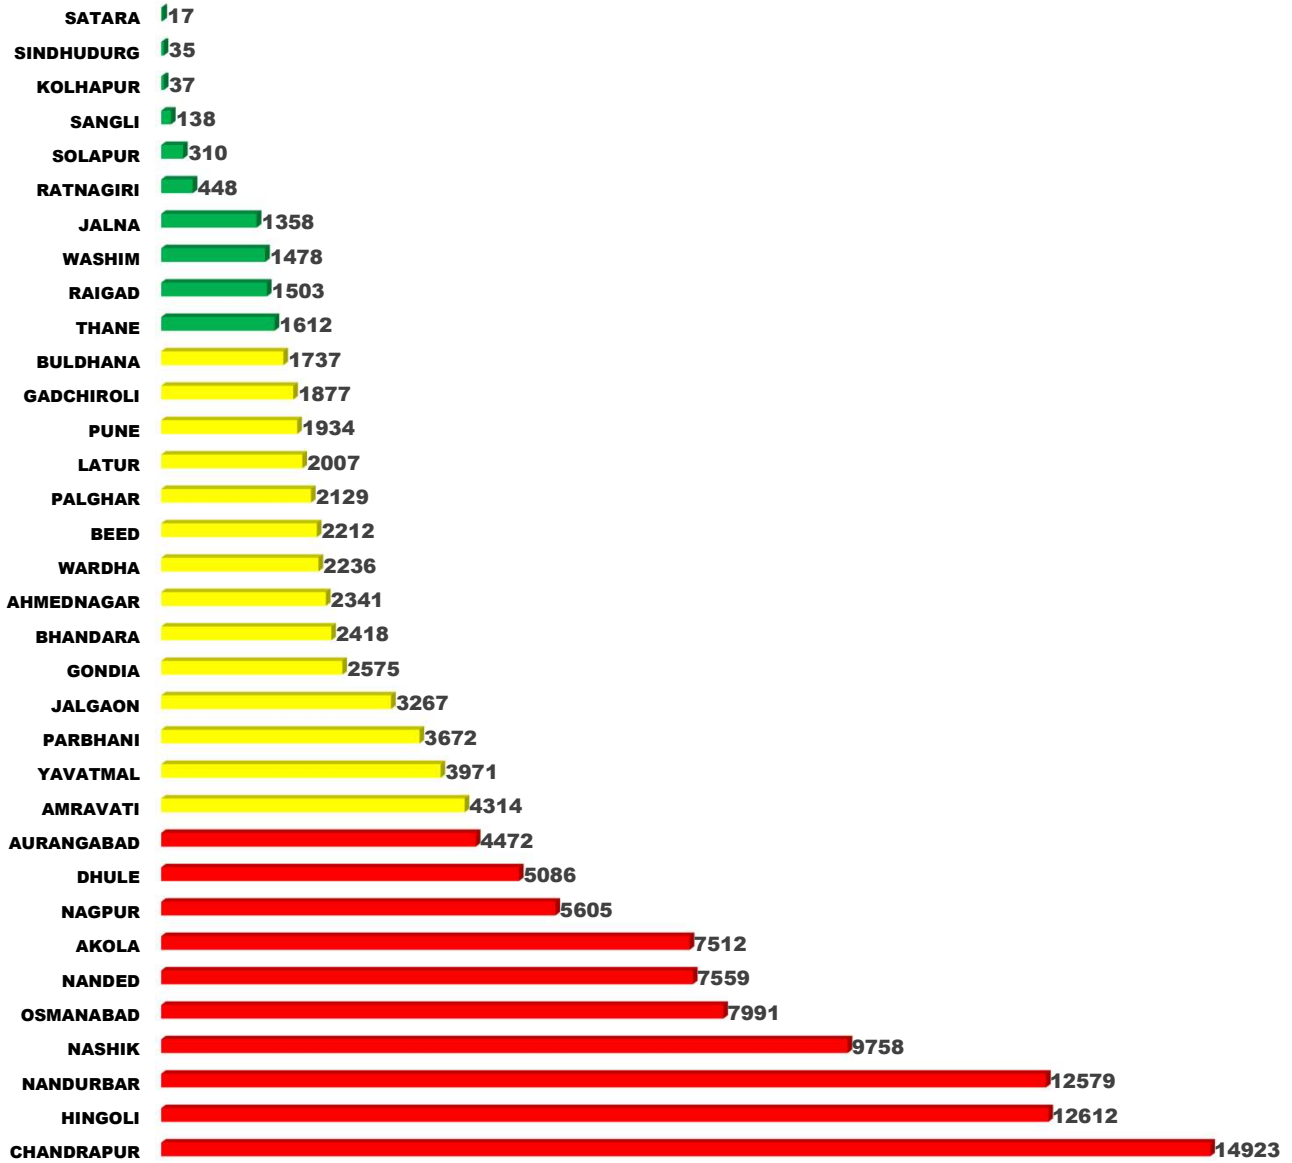


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	01.03.2023	02.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19016	19201	185	7559
2	YAVATMAL	29681	25658	25710	52	3971
3	RAIGAD	7406	5881	5903	22	1503
4	LATUR	27171	25155	25164	9	2007
5	CHANDRAPUR	38147	23220	23224	4	14923
6	PARBHANI	19784	16109	16112	3	3672
7	AHMEDNAGAR	35298	32955	32957	2	2341
8	GADCHIROLI	16834	14956	14957	1	1877
9	NANDURBAR	26578	13998	13999	1	12579
10	AKOLA	23681	16169	16169	0	7512
11	AURANGABAD	26141	21669	21669	0	4472
12	BEED	26878	24666	24666	0	2212
13	BHANDARA	17590	15172	15172	0	2418
14	BULDHANA	21616	19879	19879	0	1737
15	DHULE	21790	16704	16704	0	5086
16	GONDIA	14246	11671	11671	0	2575
17	HINGOLI	27298	14686	14686	0	12612
18	JALGAON	25659	22392	22392	0	3267
19	JALNA	20446	19088	19088	0	1358
20	KOLHAPUR	12565	12528	12528	0	37
21	NAGPUR	16291	10686	10686	0	5605
22	NASHIK	32035	22277	22277	0	9758
23	OSMANABAD	24853	16862	16862	0	7991
24	PALGHAR	11792	9663	9663	0	2129
25	PUNE	14672	12738	12738	0	1934
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8594	8594	0	138
28	SATARA	10647	10630	10630	0	17
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18408	18408	0	310
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	10911	10911	0	2236
33	WASHIM	11500	10022	10022	0	1478
34	AMRAVATI	23224	18920	18910	-10	4314
Total		666711	534719	534988	279	131723

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.03.2023	02.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI DIV.	90690	61374	61571	197	29119	53	1004
2	NASHIK DIV.	108329	84571	84766	195	23563	66	813
3	NAGPUR DIV.	86621	66416	66542	126	20079	39	692
4	PUNE DIV.	62898	50615	50705	90	12193	26	420
5	KONKAN DIV.	29002	22375	22460	85	6542	11	226
6	AURANGABAD DIV.	157448	99989	100058	69	57390	98	1979
Total		534988	385340	386102	762	148886	292	5134

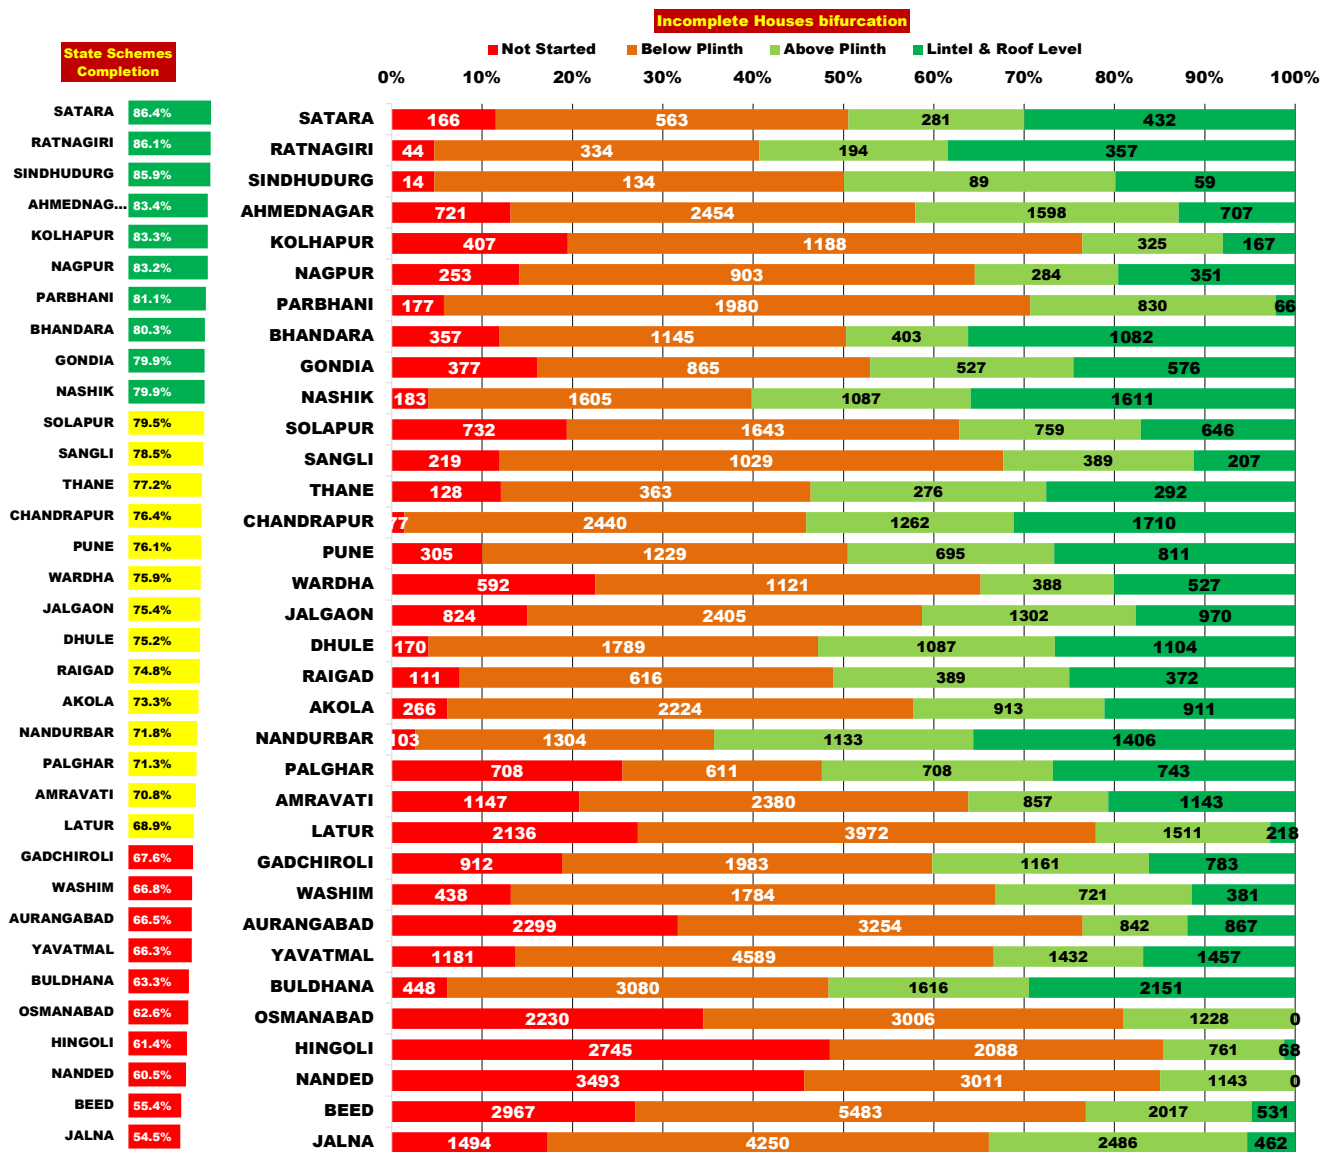

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.03.2023	02.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32957	27419	27477	58	5480	28	189
2	AKOLA	16169	11797	11855	58	4314	9	149
3	PALGHAR	9663	6837	6893	56	2770	5	96
4	PUNE	12738	9650	9698	48	3040	5	105
5	YAVATMAL	25710	17004	17051	47	8659	12	299
6	WASHIM	10022	6652	6698	46	3324	7	115
7	JALGAON	22392	16848	16891	43	5501	11	190
8	NASHIK	22277	17750	17791	41	4486	11	155
9	GONDIA	11671	9291	9326	35	2345	7	81
10	DHULE	16704	12522	12554	32	4150	10	143
11	GADCHIROLI	14957	10090	10118	28	4839	8	167
12	BULDHANA	19879	12559	12584	25	7295	15	252
13	AMRAVATI	18910	13362	13383	21	5527	9	191
14	CHANDRAPUR	23224	17714	17735	21	5489	11	189
15	NANDURBAR	13999	10032	10053	21	3946	6	136
16	KOLHAPUR	12528	10423	10441	18	2087	4	72
17	WARDHA	10911	8266	8283	17	2628	6	91
18	JALNA	19088	10380	10396	16	8692	32	300
19	RAIGAD	5903	4399	4415	16	1488	3	51
20	NAGPUR	10686	8880	8895	15	1791	3	62
21	AURANGABAD	21669	14394	14407	13	7262	8	250
22	SOLAPUR	18408	14616	14628	12	3780	8	130
23	BHANDARA	15172	12175	12185	10	2987	4	103
24	NANDED	19201	11604	11613	9	7588	10	262
25	RATNAGIRI	6678	5740	5749	9	929	1	32
26	SATARA	10630	9179	9188	9	1442	5	50
27	HINGOLI	14686	9016	9024	8	5662	6	195
28	PARBHANI	16112	13051	13059	8	3053	4	105
29	OSMANABAD	16862	10558	10564	6	6298	13	217
30	BEED	24666	13663	13668	5	10998	14	379
31	LATUR	25164	17323	17327	4	7837	11	270
32	SINDHUDURG	2106	1806	1810	4	296	1	10
33	SANGLI	8594	6747	6750	3	1844	4	64
34	THANE	4652	3593	3593	0	1059	1	37
	Total	534988	385340	386102	762	148886	292	5134

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19311	0	45194	0	24919
2	AMRAVATI DIV.	0	39407	0	39993	0	13074
3	AURANGABAD DIV.	0	34129	0	61853	0	17213
4	NAGPUR DIV.	0	15614	0	32264	0	12989
5	KONKAN DIV.	0	1172	0	6686	0	6139
6	PUNE DIV.	0	15361	0	20002	0	6376
	Total	0	124994	0	205992	0	80710

PMAY-G 1st Ins Pending

RAIGAD	55
SINDHUDURG	56
THANE	155
RATNAGIRI	170
PALGHAR	736
GADCHIROLI	745
KOLHAPUR	801
SANGLI	1204
SATARA	1462
WARDHA	2088
DHULE	2206
PARBHANI	2454
HINGOLI	2632
NAGPUR	2711
NASHIK	2753
GONDIA	2861
PUNE	3201
JALNA	3355
CHANDRAPUR	3542
BHANDARA	3667
AURANGABAD	3855
AHMEDNAGAR	3862
WASHIM	3893
OSMANABAD	4095
LATUR	4494
NANDURBAR	4533
BEED	4941
AKOLA	5711
JALGAON	5957
YAVATMAL	5960
NANDED	8303
SOLAPUR	8693
BULDHANA	10268
AMRAVATI	13575

PMAY-G 2nd Ins Pending

SINDHUDURG	653
RAIGAD	699
RATNAGIRI	1006
THANE	1277
WARDHA	2009
SATARA	2121
PUNE	2752
PALGHAR	3051
KOLHAPUR	3534
OSMANABAD	3807
HINGOLI	3878
NAGPUR	3932
GADCHIROLI	3981
LATUR	4568
SANGLI	5023
AKOLA	5060
AHMEDNAGAR	5281
WASHIM	5307
JALNA	5846
SOLAPUR	6572
CHANDRAPUR	7064
BULDHANA	7073
AURANGABAD	7097
NASHIK	7426
GONDIA	7545
DHULE	7576
PARBHANI	7613
BHANDARA	7733
BEED	9126
AMRAVATI	10102
NANDURBAR	10752
YAVATMAL	12451
JALGAON	14159
NANDED	19918

PMAY-G 3rd Ins Pending

SINDHUDURG	409
RAIGAD	417
WARDHA	555
KOLHAPUR	742
RATNAGIRI	778
THANE	865
NAGPUR	950
OSMANABAD	962
SATARA	997
PUNE	1003
HINGOLI	1154
LATUR	1408
SANGLI	1413
WASHIM	1535
PARBHANI	1568
AKOLA	1737
JALNA	1950
BULDHANA	2168
SOLAPUR	2221
BHANDARA	2511
AURANGABAD	2593
CHANDRAPUR	2679
GADCHIROLI	2866
BEED	2982
AMRAVATI	2987
GONDIA	3428
PALGHAR	3670
DHULE	4216
NASHIK	4295
JALGAON	4356
NANDED	4596
YAVATMAL	4647
AHMEDNAGAR	4708
NANDURBAR	7344

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3862	0	5281	0	4708
2	AKOLA	0	5711	0	5060	0	1737
3	AMRAVATI	0	13575	0	10102	0	2987
4	AURANGABAD	0	3855	0	7097	0	2593
5	BEED	0	4941	0	9126	0	2982
6	BHANDARA	0	3667	0	7733	0	2511
7	BULDHANA	0	10268	0	7073	0	2168
8	CHANDRAPUR	0	3542	0	7064	0	2679
9	DHULE	0	2206	0	7576	0	4216
10	GADCHIROLI	0	745	0	3981	0	2866
11	GONDIA	0	2861	0	7545	0	3428
12	HINGOLI	0	2632	0	3878	0	1154
13	JALGAON	0	5957	0	14159	0	4356
14	JALNA	0	3355	0	5846	0	1950
15	KOLHAPUR	0	801	0	3534	0	742
16	LATUR	0	4494	0	4568	0	1408
17	NAGPUR	0	2711	0	3932	0	950
18	NANDED	0	8303	0	19918	0	4596
19	NANDURBAR	0	4533	0	10752	0	7344
20	NASHIK	0	2753	0	7426	0	4295
21	OSMANABAD	0	4095	0	3807	0	962
22	PALGHAR	0	736	0	3051	0	3670
23	PARBHANI	0	2454	0	7613	0	1568
24	PUNE	0	3201	0	2752	0	1003
25	RAIGAD	0	55	0	699	0	417
26	RATNAGIRI	0	170	0	1006	0	778
27	SANGLI	0	1204	0	5023	0	1413
28	SINDHUDURG	0	56	0	653	0	409
29	SOLAPUR	0	8693	0	6572	0	2221
30	THANE	0	155	0	1277	0	865
31	WARDHA	0	2088	0	2009	0	555
32	WASHIM	0	3893	0	5307	0	1535
33	YAVATMAL	0	5960	0	12451	0	4647
34	SATARA	-7	1462	0	2121	0	997
	Total	0	124994	0	205992	0	80710

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	NASHIK DIV.	0	2001	0	9557	0	6207
2	AMRAVATI DIV.	0	3480	0	14057	0	5539
3	AURANGABAD DIV.	0	17541	0	27044	0	10818
4	NAGPUR DIV.	0	2568	0	8457	0	4025
5	KONKAN DIV.	0	1005	0	2058	0	1656
6	PUNE DIV.	0	1829	0	5652	0	2449
	Total	0	28424	0	66825	0	30694

State Schemes 1st Ins Pending

SINDHUDURG	14
RATNAGIRI	44
CHANDRAPUR	77
NANDURBAR	103
RAIGAD	111
THANE	128
SATARA	166
DHULE	170
PARBHANI	177
NASHIK	183
SANGLI	219
NAGPUR	253
AKOLA	266
PUNE	305
BHANDARA	357
GONDIA	377
KOLHAPUR	407
WASHIM	438
BULDHANA	448
WARDHA	592
PALGHAR	708
AHMEDNAGAR	721
SOLAPUR	732
JALGAON	824
GADCHIROLI	912
AMRAVATI	1147
YAVATMAL	1181
JALNA	1494
LATUR	2136
OSMANABAD	2230
AURANGABAD	2299
HINGOLI	2745
BEED	2967
NANDED	3493

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	334
THANE	363
SATARA	563
PALGHAR	611
RAIGAD	616
GONDIA	865
NAGPUR	903
SANGLI	1029
WARDHA	1121
BHANDARA	1145
KOLHAPUR	1188
PUNE	1229
NANDURBAR	1304
NASHIK	1605
SOLAPUR	1643
WASHIM	1784
DHULE	1789
PARBHANI	1980
GADCHIROLI	1983
HINGOLI	2088
AKOLA	2224
AMRAVATI	2380
JALGAON	2405
CHANDRAPUR	2440
AHMEDNAGAR	2454
OSMANABAD	3006
NANDED	3011
BULDHANA	3080
AURANGABAD	3254
LATUR	3972
JALNA	4250
YAVATMAL	4589
BEED	5483

State Schemes 3rd Ins Pending

SINDHUDURG	89
RATNAGIRI	194
THANE	276
SATARA	281
NAGPUR	284
KOLHAPUR	325
WARDHA	388
RAIGAD	389
SANGLI	389
BHANDARA	403
GONDIA	527
PUNE	695
PALGHAR	708
WASHIM	721
SOLAPUR	759
HINGOLI	761
PARBHANI	830
AURANGABAD	842
AMRAVATI	857
AKOLA	913
NASHIK	1087
DHULE	1087
NANDURBAR	1133
NANDED	1143
GADCHIROLI	1161
OSMANABAD	1228
CHANDRAPUR	1262
JALGAON	1302
YAVATMAL	1432
LATUR	1511
AHMEDNAGAR	1598
BULDHANA	1616
BEED	2017
JALNA	2486

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	721	0	2454	0	1598
2	AKOLA	0	266	0	2224	0	913
3	AMRAVATI	0	1147	0	2380	0	857
4	AURANGABAD	0	2299	0	3254	0	842
5	BEED	0	2967	0	5483	0	2017
6	BHANDARA	0	357	0	1145	0	403
7	BULDHANA	0	448	0	3080	0	1616
8	CHANDRAPUR	0	77	0	2440	0	1262
9	DHULE	0	170	0	1789	0	1087
10	GADCHIROLI	0	912	0	1983	0	1161
11	GONDIA	0	377	0	865	0	527
12	HINGOLI	0	2745	0	2088	0	761
13	JALGAON	0	824	0	2405	0	1302
14	JALNA	0	1494	0	4250	0	2486
15	KOLHAPUR	0	407	0	1188	0	325
16	LATUR	0	2136	0	3972	0	1511
17	NAGPUR	0	253	0	903	0	284
18	NANDED	0	3493	0	3011	0	1143
19	NANDURBAR	0	103	0	1304	0	1133
20	NASHIK	0	183	0	1605	0	1087
21	OSMANABAD	0	2230	0	3006	0	1228
22	PALGHAR	0	708	0	611	0	708
23	PARBHANI	0	177	0	1980	0	830
24	PUNE	0	305	0	1229	0	695
25	RAIGAD	0	111	0	616	0	389
26	RATNAGIRI	0	44	0	334	0	194
27	SANGLI	0	219	0	1029	0	389
28	SINDHUDURG	0	14	0	134	0	89
29	SOLAPUR	0	732	0	1643	0	759
30	THANE	0	128	0	363	0	276
31	WARDHA	0	592	0	1121	0	388
32	WASHIM	0	438	0	1784	0	721
33	YAVATMAL	0	1181	0	4589	0	1432
34	SATARA	-4	166	0	563	0	281
	Total	0	28424	0	66825	0	30694
