



# अमृत महा आवास अभियान २०२२-२३

## दैनिक प्रगती अहवाल : ०३.०३.२०२३

### प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी व पूर्ण घरकुले राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी व पूर्ण घरकुले


योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१५०५५	७७	९८११५०	५११५	०	०	०
राज्य योजना	५३५३७२	४११	३८७०२४	९२२	१८५०	१५५३	१२८३
एकूण	१९५०४२७	४८८	१३६८१७४	६०३७	१८५०	१५५३	१२८३

PMAY-G Completion Progress Bar


69.3%

State Schemes Progress Bar


72.3%

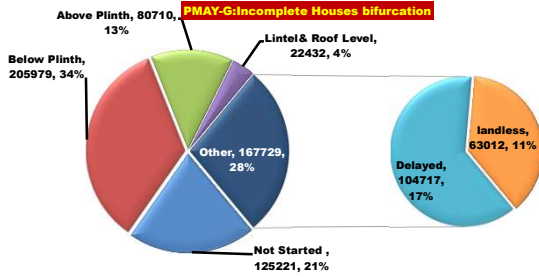

State Schemes: Incomplete Houses bifurcation




Delayed Houses bifurcation

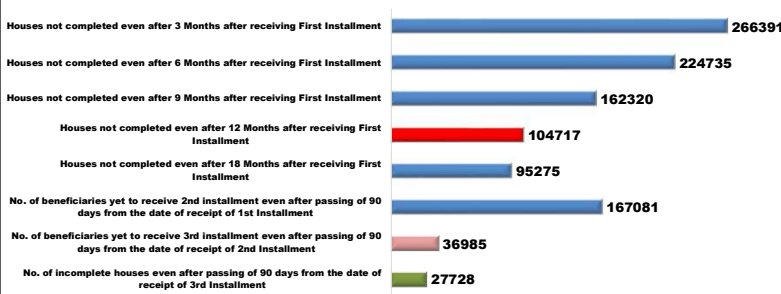


Abhiyan Achievement


Day 103

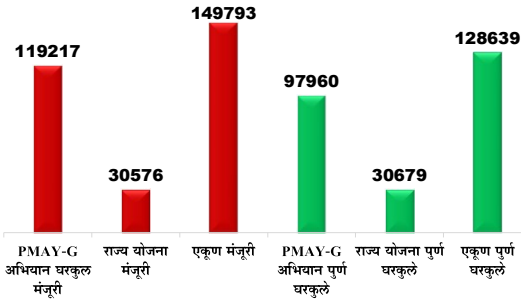

PMAY-G : House completion ( Abhiyan Achievement)

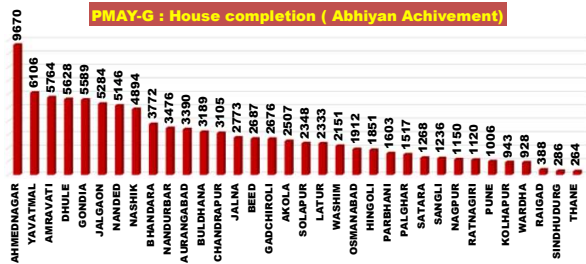

State Schemes : House completion ( Abhiyan Achievement)

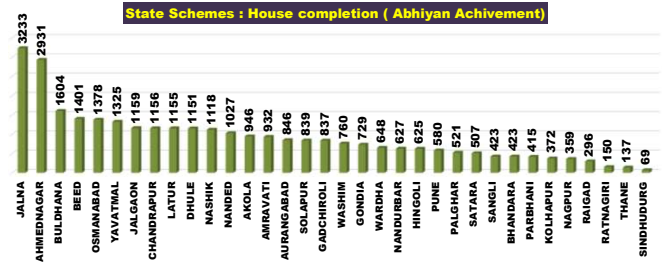


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


**PMAY-G Delayed Houses TOP 10 Dist.**




**PMAY-G Delayed Houses Bottom 10 Dist.**




**PMAY-G Completion TOP 10 Dist.**




**PMAY-G Completion Bottom 10 Dist.**




**PMAY-G Daily Completion Top 10 Dist.**




**PMAY-G Daily Completion Bottom 10 Dist.**




**PMAY-G : Current Pace of Completion Per Day (Abhiyan)**




**PMAY-G Required Pace of Completion Per Day**




**State Schemes Sanction TOP 10 Dist.**




**State Schemes Sanction Bottom 10 Dist.**




**State Schemes Completion TOP 10 Dist.**




**State Schemes Completion Bottom 10 Dist.**




**State Schemes Daily Completion Top 10 Dist.**




**State Schemes Daily Completion Bottom 10 Dist.**



**State Schemes : Current Pace of Completion Per Day (Abhiyan)**




**State Schemes Required Pace of Completion Per Day**



**PMAY-G Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Remaining 2nd Installments Bottom 10 Dist.**



**PMAY-G Remaining 3rd Installments Bottom 10 Dist.**



**State Schemes Remaining 1st Installments Bottom 10 Dist.**



**State Schemes Remaining 2nd Installments Bottom 10 Dist.**




**State Schemes Remaining 3rd Installments Bottom 10 Dist.**



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	02.03.2023	03.03.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	274989	274639	274663	32	326
2	PUNE DIV.	126829	126746	126544	17	285
3	AURANGABAD DIV.	238469	238168	238176	16	293
4	NAGPUR DIV.	292564	292030	292021	12	543
5	NASHIK DIV.	414743	414032	413989	0	754
6	KONKAN DIV.	69688	69663	69662	0	26
<b>Total</b>		<b>1417282</b>	<b>1415278</b>	<b>1415055</b>	<b>77</b>	<b>2227</b>

PMAY-G Remaining Sanction

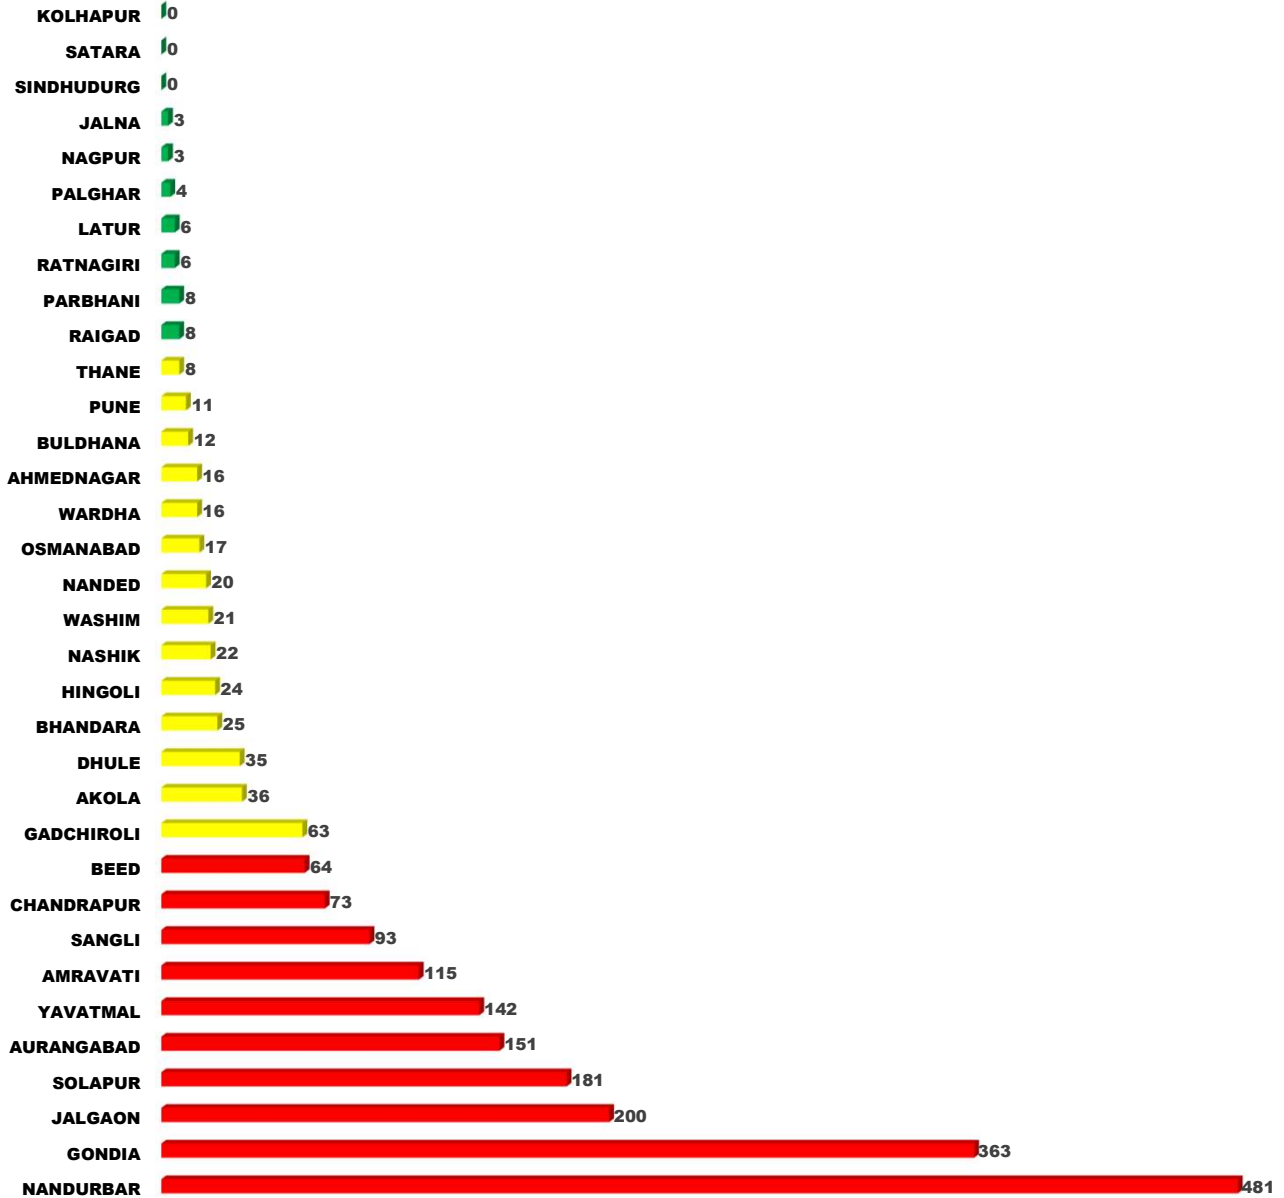


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	02.03.2023	03.03.2023	Daily_Achievement	Remaining
1	AMRAVATI	95646	95507	95531	24	115
2	SANGLI	22174	22064	22081	17	93
3	OSMANABAD	14583	14550	14566	16	17
4	GONDIA	96474	96099	96111	12	363
5	AKOLA	48794	48750	48758	8	36
6	AURANGABAD	36905	36754	36754	0	151
7	BEED	35334	35270	35270	0	64
8	BULDHANA	44742	44730	44730	0	12
9	DHULE	64912	64877	64877	0	35
10	GADCHIROLI	31639	31576	31576	0	63
11	HINGOLI	18107	18083	18083	0	24
12	JALNA	24047	24044	24044	0	3
13	LATUR	20799	20793	20793	0	6
14	NAGPUR	37331	37328	37328	0	3
15	NANDURBAR	119349	118868	118868	0	481
16	PALGHAR	35152	35148	35148	0	4
17	PARBHANI	19106	19098	19098	0	8
18	RAIGAD	9847	9839	9839	0	8
19	SATARA	15565	15565	15565	0	0
20	SINDHUDURG	5156	5156	5156	0	0
21	THANE	9606	9598	9598	0	8
22	WARDHA	18671	18655	18655	0	16
23	WASHIM	20416	20395	20395	0	21
24	NASHIK	89789	89768	89767	-1	22
25	RATNAGIRI	9927	9922	9921	-1	6
26	BHANDARA	65133	65113	65108	-5	25
27	NANDED	69588	69576	69568	-8	20
28	YAVATMAL	65391	65257	65249	-8	142
29	PUNE	21133	21131	21122	-9	11
30	AHMEDNAGAR	60802	60797	60786	-11	16
31	CHANDRAPUR	43316	43259	43243	-16	73
32	KOLHAPUR	17772	17795	17772	-23	0
33	JALGAON	79891	79722	79691	-31	200
34	SOLAPUR	50185	50191	50004	-187	181
<b>Total</b>		<b>1417282</b>	<b>1415278</b>	<b>1415055</b>	<b>77</b>	<b>2227</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.03.2023	03.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	<b>NASHIK DIV.</b>	<b>413989</b>	<b>310919</b>	<b>312466</b>	<b>1547</b>	<b>101523</b>	<b>281</b>	<b>3626</b>
2	<b>NAGPUR DIV.</b>	<b>292021</b>	<b>224004</b>	<b>225348</b>	<b>1344</b>	<b>66673</b>	<b>167</b>	<b>2381</b>
3	<b>AMRAVATI DIV.</b>	<b>274663</b>	<b>175783</b>	<b>176874</b>	<b>1091</b>	<b>97789</b>	<b>191</b>	<b>3492</b>
4	<b>KONKAN DIV.</b>	<b>69662</b>	<b>52382</b>	<b>52983</b>	<b>601</b>	<b>16679</b>	<b>35</b>	<b>596</b>
5	<b>PUNE DIV.</b>	<b>126544</b>	<b>83915</b>	<b>84223</b>	<b>308</b>	<b>42321</b>	<b>66</b>	<b>1511</b>
6	<b>AURANGABAD DIV.</b>	<b>238176</b>	<b>129032</b>	<b>129256</b>	<b>224</b>	<b>108920</b>	<b>211</b>	<b>3890</b>
<b>Total</b>		<b>1415055</b>	<b>976035</b>	<b>981150</b>	<b>5115</b>	<b>433905</b>	<b>951</b>	<b>15497</b>

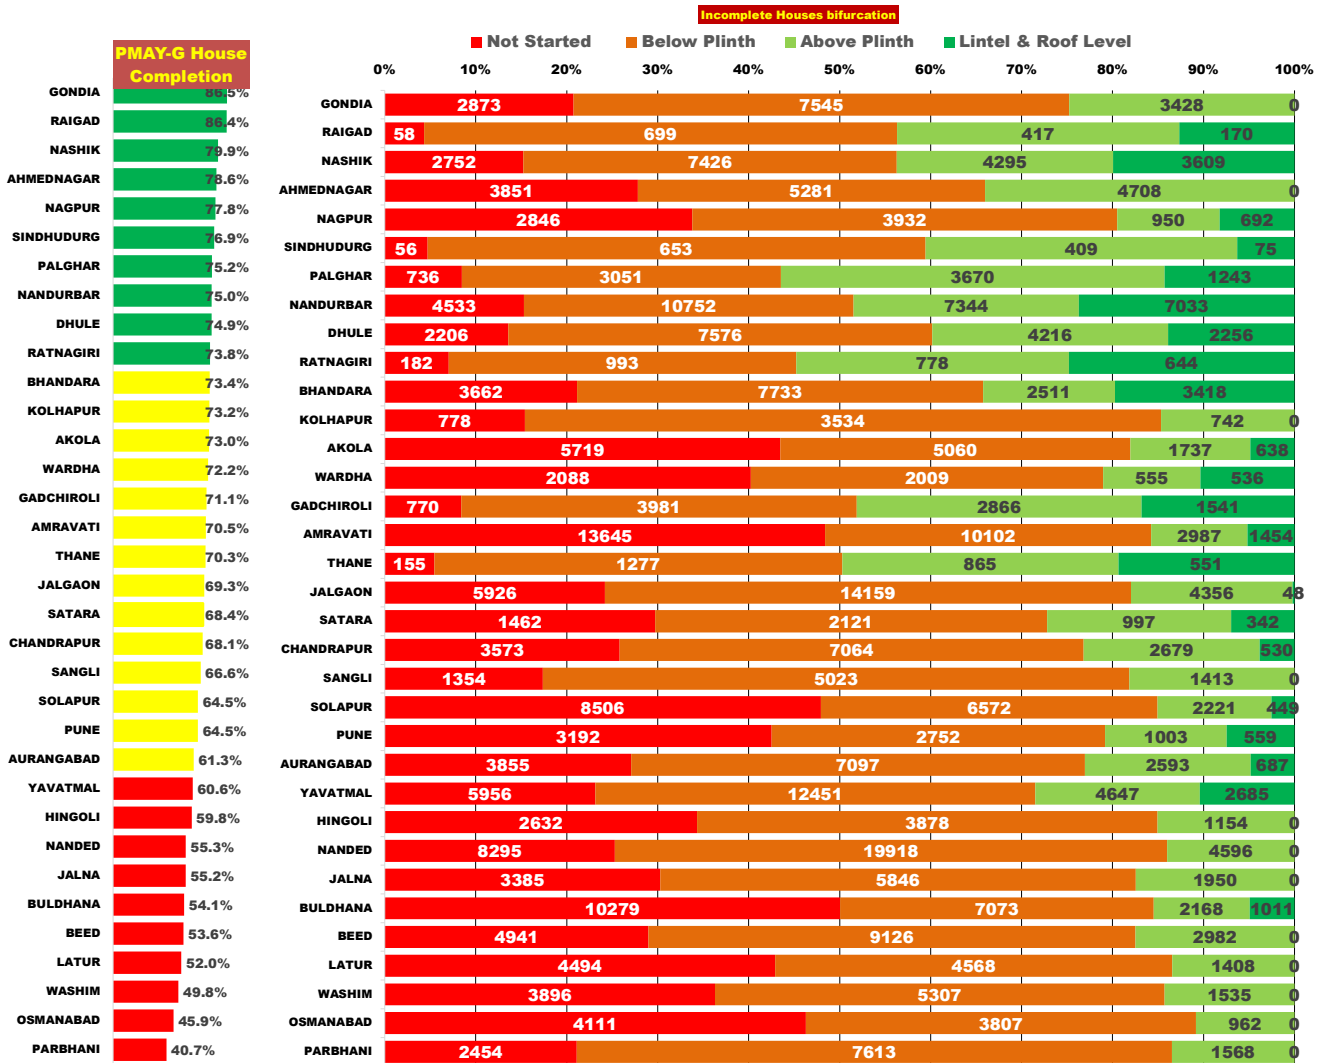


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.03.2023	03.03.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	CHANDRAPUR	43243	28717	29444	727	13799	30	493
2	DHULE	64877	48078	48623	545	16254	55	581
3	PALGHAR	35148	25999	26448	449	8700	15	311
4	YAVATMAL	65249	39098	39514	416	25735	59	919
5	GONDIA	96111	82815	83167	352	12944	54	462
6	NASHIK	89767	71365	71685	320	18082	48	646
7	NANDURBAR	118868	88968	89206	238	29662	34	1059
8	JALGAON	79691	54974	55202	228	24489	51	875
9	AHMEDNAGAR	60786	47534	47750	216	13036	94	466
10	AKOLA	48758	35411	35604	193	13154	24	470
11	AMRAVATI	95531	67211	67389	178	28142	56	1005
12	WASHIM	20395	10001	10157	156	10238	21	366
13	BULDHANA	44730	24062	24210	148	20520	31	733
14	SOLAPUR	50004	32140	32256	116	17748	23	634
15	BHANDARA	65108	47698	47784	86	17324	37	619
16	RATNAGIRI	9921	7245	7324	79	2597	11	93
17	LATUR	20793	10736	10807	71	9986	23	357
18	GADCHIROLI	31576	22374	22443	69	9133	26	326
19	PUNE	21122	13549	13616	67	7506	10	268
20	NAGPUR	37328	28978	29043	65	8285	11	296
21	SATARA	15565	10589	10643	54	4922	12	176
22	KOLHAPUR	17772	12954	13005	51	4767	9	170
23	AURANGABAD	36754	22474	22522	48	14232	33	508
24	SINDHUDURG	5156	3918	3963	45	1193	3	43
25	WARDHA	18655	13422	13467	45	5188	9	185
26	PARBHANI	19098	7742	7776	34	11322	16	404
27	NANDED	69568	38425	38456	31	31112	50	1111
28	HINGOLI	18083	10787	10809	22	7274	18	260
29	SANGLI	22081	14683	14703	20	7378	12	264
30	THANE	9598	6735	6750	15	2848	3	102
31	JALNA	24044	13265	13279	14	10765	27	384
32	RAIGAD	9839	8485	8498	13	1341	4	48
33	BEED	35270	18912	18915	3	16355	26	584
34	OSMANABAD	14566	6691	6692	1	7874	19	281
Total		1415055	976035	981150	5115	433905	951	15497

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	02.03.2023	03.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	157448	157732	284	41599
2	AMRAVATI DIV.	109702	90690	90760	70	18942
3	KONKAN DIV.	34729	29002	29056	54	5673
4	PUNE DIV.	65334	62898	62900	2	2434
5	NAGPUR DIV.	116255	86621	86622	1	29633
6	NASHIK DIV.	141360	108329	108302	0	33058
	<b>Total</b>	<b>666711</b>	<b>534988</b>	<b>535372</b>	<b>411</b>	<b>131339</b>

State Scheme Remaining Sanction

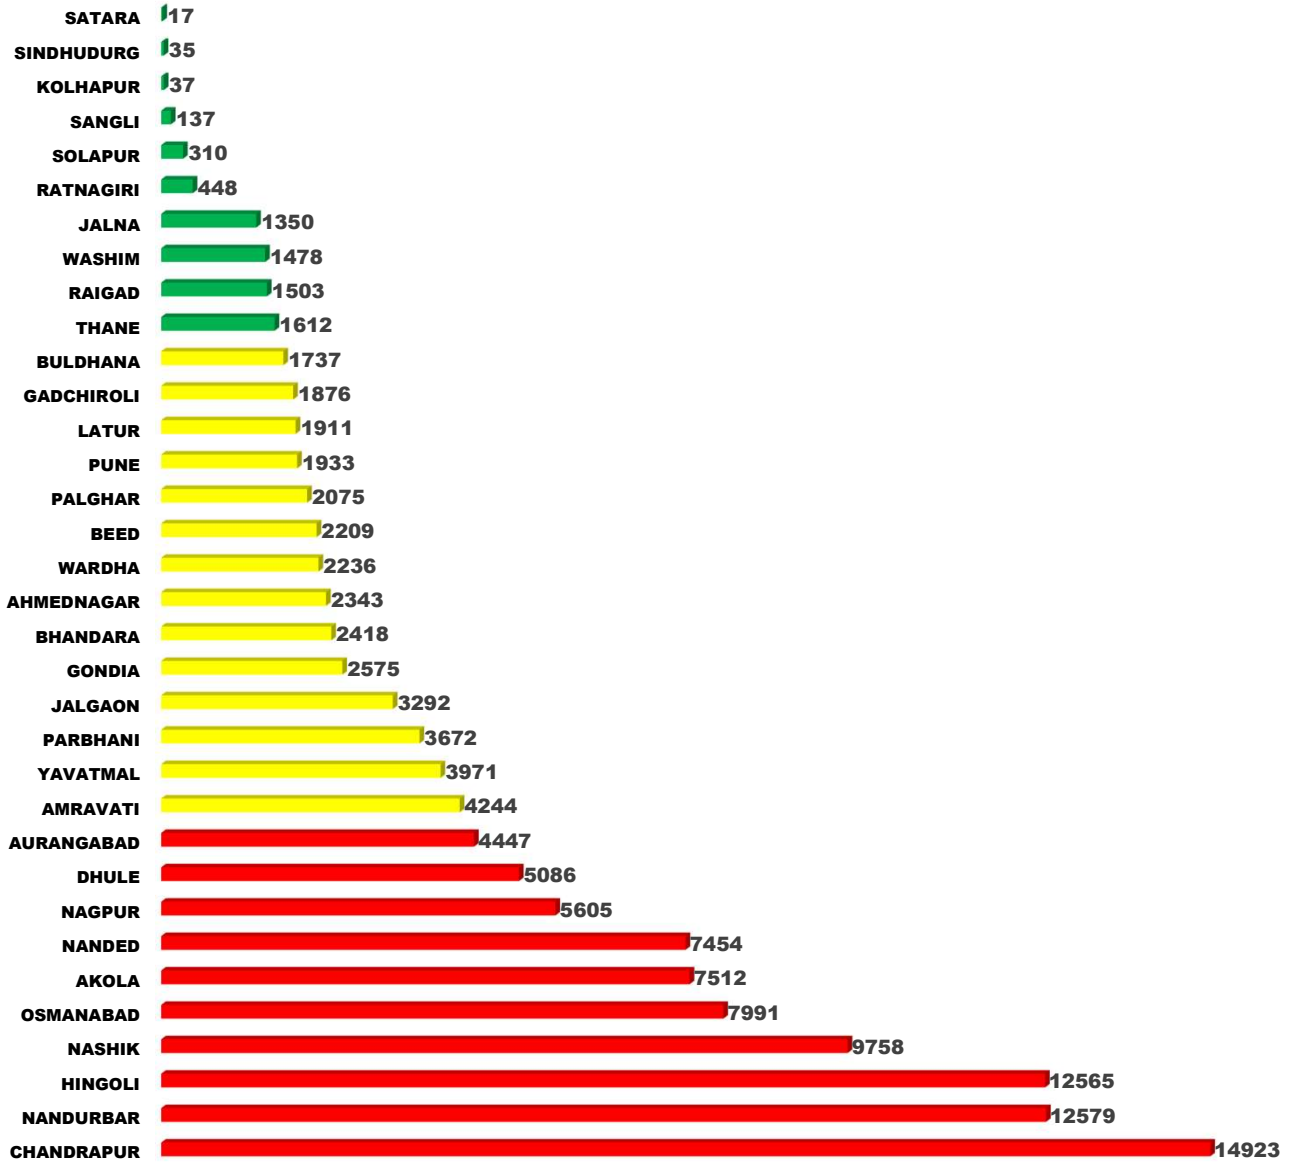


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	02.03.2023	03.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19201	19306	105	7454
2	LATUR	27171	25164	25260	96	1911
3	AMRAVATI	23224	18910	18980	70	4244
4	PALGHAR	11792	9663	9717	54	2075
5	HINGOLI	27298	14686	14733	47	12565
6	AURANGABAD	26141	21669	21694	25	4447
7	JALNA	20446	19088	19096	8	1350
8	BEED	26878	24666	24669	3	2209
9	GADCHIROLI	16834	14957	14958	1	1876
10	PUNE	14672	12738	12739	1	1933
11	SANGLI	8732	8594	8595	1	137
12	AKOLA	23681	16169	16169	0	7512
13	BHANDARA	17590	15172	15172	0	2418
14	BULDHANA	21616	19879	19879	0	1737
15	CHANDRAPUR	38147	23224	23224	0	14923
16	DHULE	21790	16704	16704	0	5086
17	GONDIA	14246	11671	11671	0	2575
18	KOLHAPUR	12565	12528	12528	0	37
19	NAGPUR	16291	10686	10686	0	5605
20	NANDURBAR	26578	13999	13999	0	12579
21	NASHIK	32035	22277	22277	0	9758
22	OSMANABAD	24853	16862	16862	0	7991
23	PARBHANI	19784	16112	16112	0	3672
24	RAIGAD	7406	5903	5903	0	1503
25	RATNAGIRI	7126	6678	6678	0	448
26	SATARA	10647	10630	10630	0	17
27	SINDHUDURG	2141	2106	2106	0	35
28	SOLAPUR	18718	18408	18408	0	310
29	THANE	6264	4652	4652	0	1612
30	WARDHA	13147	10911	10911	0	2236
31	WASHIM	11500	10022	10022	0	1478
32	YAVATMAL	29681	25710	25710	0	3971
33	AHMEDNAGAR	35298	32957	32955	-2	2343
34	JALGAON	25659	22392	22367	-25	3292
<b>Total</b>		<b>666711</b>	<b>534988</b>	<b>535372</b>	<b>411</b>	<b>131339</b>



## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.03.2023	03.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	<b>NASHIK DIV.</b>	<b>108302</b>	<b>84766</b>	<b>85043</b>	<b>277</b>	<b>23259</b>	<b>68</b>	<b>831</b>
2	<b>AMRAVATI DIV.</b>	<b>90760</b>	<b>61571</b>	<b>61765</b>	<b>194</b>	<b>28995</b>	<b>54</b>	<b>1036</b>
3	<b>NAGPUR DIV.</b>	<b>86622</b>	<b>66542</b>	<b>66697</b>	<b>155</b>	<b>19925</b>	<b>40</b>	<b>712</b>
4	<b>AURANGABAD DIV.</b>	<b>157732</b>	<b>100058</b>	<b>100186</b>	<b>128</b>	<b>57546</b>	<b>98</b>	<b>2055</b>
5	<b>KONKAN DIV.</b>	<b>29056</b>	<b>22460</b>	<b>22547</b>	<b>87</b>	<b>6509</b>	<b>11</b>	<b>232</b>
6	<b>PUNE DIV.</b>	<b>62900</b>	<b>50705</b>	<b>50786</b>	<b>81</b>	<b>12114</b>	<b>26</b>	<b>433</b>
<b>Total</b>		<b>535372</b>	<b>386102</b>	<b>387024</b>	<b>922</b>	<b>148348</b>	<b>298</b>	<b>5298</b>

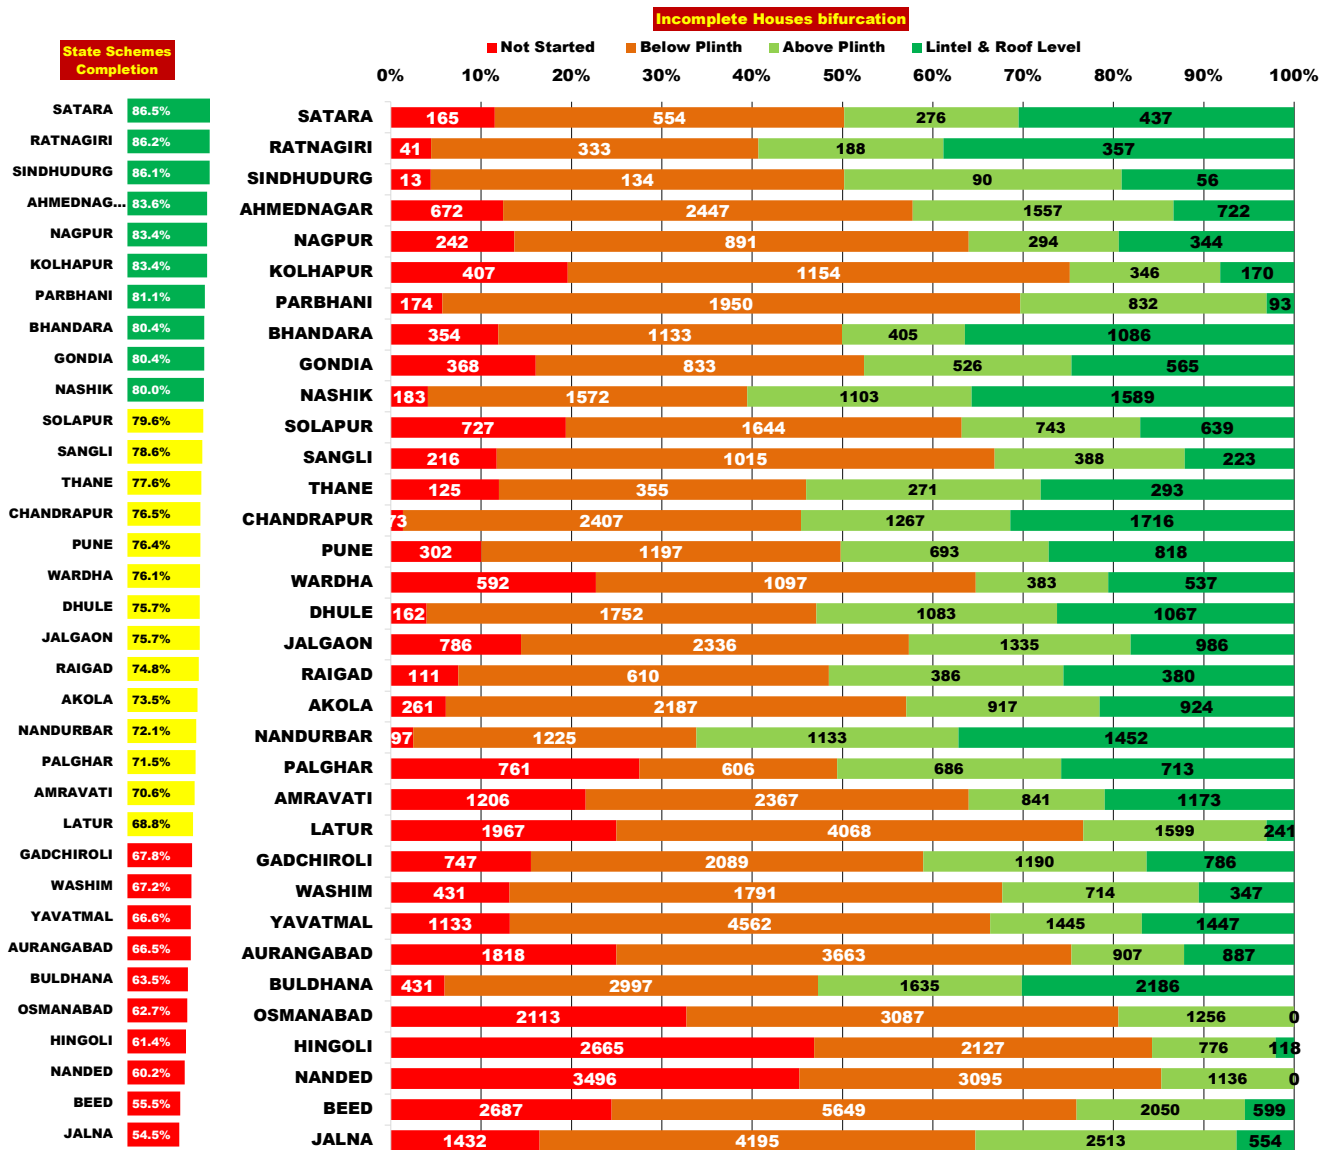

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.03.2023	03.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	DHULE	16704	12554	12640	86	4064	11	145
2	AHMEDNAGAR	32955	27477	27557	80	5398	28	193
3	YAVATMAL	25710	17051	17123	72	8587	13	307
4	LATUR	25260	17327	17385	58	7875	11	281
5	PALGHAR	9717	6893	6951	58	2766	5	99
6	GONDIA	11671	9326	9379	53	2292	7	82
7	BULDHANA	19879	12584	12630	46	7249	16	259
8	WASHIM	10022	6698	6739	41	3283	7	117
9	NANDURBAR	13999	10053	10092	39	3907	6	140
10	NASHIK	22277	17791	17830	39	4447	11	159
11	JALGAON	22367	16891	16924	33	5443	11	194
12	PUNE	12739	9698	9729	31	3010	6	108
13	GADCHIROLI	14958	10118	10146	28	4812	8	172
14	SOLAPUR	18408	14628	14655	27	3753	8	134
15	CHANDRAPUR	23224	17735	17761	26	5463	11	195
16	AKOLA	16169	11855	11880	25	4289	9	153
17	HINGOLI	14733	9024	9047	23	5686	6	203
18	NAGPUR	10686	8895	8915	20	1771	3	63
19	WARDHA	10911	8283	8302	19	2609	6	93
20	BEED	24669	13668	13684	16	10985	14	392
21	THANE	4652	3593	3608	15	1044	1	37
22	AURANGABAD	21694	14407	14419	12	7275	8	260
23	AMRAVATI	18980	13383	13393	10	5587	9	200
24	KOLHAPUR	12528	10441	10451	10	2077	4	74
25	RATNAGIRI	6678	5749	5759	10	919	1	33
26	SATARA	10630	9188	9198	10	1432	5	51
27	BHANDARA	15172	12185	12194	9	2978	4	106
28	JALNA	19096	10396	10402	6	8694	31	311
29	OSMANABAD	16862	10564	10570	6	6292	13	225
30	PARBHANI	16112	13059	13063	4	3049	4	109
31	NANDED	19306	11613	11616	3	7690	10	275
32	SANGLI	8595	6750	6753	3	1842	4	66
33	SINDHUDURG	2106	1810	1813	3	293	1	10
34	RAIGAD	5903	4415	4416	1	1487	3	53
	<b>Total</b>	<b>535372</b>	<b>386102</b>	<b>387024</b>	<b>922</b>	<b>148348</b>	<b>298</b>	<b>5298</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19268	0	45194	0	24919
2	AMRAVATI DIV.	0	39431	0	39993	0	13074
3	AURANGABAD DIV.	0	34137	0	61853	0	17213
4	NAGPUR DIV.	0	15605	0	32264	0	12989
5	KONKAN DIV.	0	1184	0	6673	0	6139
6	PUNE DIV.	0	15159	0	20002	0	6376
	<b>Total</b>	<b>0</b>	<b>124784</b>	<b>0</b>	<b>205979</b>	<b>0</b>	<b>80710</b>

PMAY-G 1st Ins Pending

RAIGAD	55
SINDHUDURG	56
THANE	155
RATNAGIRI	182
PALGHAR	736
GADCHIROLI	745
KOLHAPUR	778
SANGLI	1221
SATARA	1462
WARDHA	2088
DHULE	2206
PARBHANI	2454
HINGOLI	2632
NAGPUR	2711
NASHIK	2752
GONDIA	2873
PUNE	3192
JALNA	3355
CHANDRAPUR	3526
BHANDARA	3662
AHMEDNAGAR	3851
AURANGABAD	3855
WASHIM	3893
OSMANABAD	4111
LATUR	4494
NANDURBAR	4533
BEED	4941
AKOLA	5719
JALGAON	5926
YAVATMAL	5952
NANDED	8295
SOLAPUR	8506
BULDHANA	10268
AMRAVATI	13599

PMAY-G 2nd Ins Pending

SINDHUDURG	653
RAIGAD	699
RATNAGIRI	993
THANE	1277
WARDHA	2009
SATARA	2121
PUNE	2752
PALGHAR	3051
KOLHAPUR	3534
OSMANABAD	3807
HINGOLI	3878
NAGPUR	3932
GADCHIROLI	3981
LATUR	4568
SANGLI	5023
AKOLA	5060
AHMEDNAGAR	5281
WASHIM	5307
JALNA	5846
SOLAPUR	6572
CHANDRAPUR	7064
BULDHANA	7073
AURANGABAD	7097
NASHIK	7426
GONDIA	7545
DHULE	7576
PARBHANI	7613
BHANDARA	7733
BEED	9126
AMRAVATI	10102
NANDURBAR	10752
YAVATMAL	12451
JALGAON	14159
NANDED	19918

PMAY-G 3rd Ins Pending

SINDHUDURG	409
RAIGAD	417
WARDHA	555
KOLHAPUR	742
RATNAGIRI	778
THANE	865
NAGPUR	950
OSMANABAD	962
SATARA	997
PUNE	1003
HINGOLI	1154
LATUR	1408
SANGLI	1413
WASHIM	1535
PARBHANI	1568
AKOLA	1737
JALNA	1950
BULDHANA	2168
SOLAPUR	2221
BHANDARA	2511
AURANGABAD	2593
CHANDRAPUR	2679
GADCHIROLI	2866
BEED	2982
AMRAVATI	2987
GONDIA	3428
PALGHAR	3670
DHULE	4216
NASHIK	4295
JALGAON	4356
NANDED	4596
YAVATMAL	4647
AHMEDNAGAR	4708
NANDURBAR	7344

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3851	0	5281	0	4708
2	AKOLA	0	5719	0	5060	0	1737
3	AMRAVATI	0	13599	0	10102	0	2987
4	AURANGABAD	0	3855	0	7097	0	2593
5	BEED	0	4941	0	9126	0	2982
6	BHANDARA	0	3662	0	7733	0	2511
7	BULDHANA	0	10268	0	7073	0	2168
8	CHANDRAPUR	0	3526	0	7064	0	2679
9	DHULE	0	2206	0	7576	0	4216
10	GADCHIROLI	0	745	0	3981	0	2866
11	GONDIA	0	2873	0	7545	0	3428
12	HINGOLI	0	2632	0	3878	0	1154
13	JALGAON	0	5926	0	14159	0	4356
14	JALNA	0	3355	0	5846	0	1950
15	KOLHAPUR	0	778	0	3534	0	742
16	LATUR	0	4494	0	4568	0	1408
17	NAGPUR	0	2711	0	3932	0	950
18	NANDED	0	8295	0	19918	0	4596
19	NANDURBAR	0	4533	0	10752	0	7344
20	NASHIK	0	2752	0	7426	0	4295
21	OSMANABAD	0	4111	0	3807	0	962
22	PALGHAR	0	736	0	3051	0	3670
23	PARBHANI	0	2454	0	7613	0	1568
24	PUNE	0	3192	0	2752	0	1003
25	RAIGAD	0	55	0	699	0	417
26	SANGLI	0	1221	0	5023	0	1413
27	SATARA	0	1462	0	2121	0	997
28	SINDHUDURG	0	56	0	653	0	409
29	SOLAPUR	0	8506	0	6572	0	2221
30	THANE	0	155	0	1277	0	865
31	WARDHA	0	2088	0	2009	0	555
32	WASHIM	0	3893	0	5307	0	1535
33	YAVATMAL	0	5952	0	12451	0	4647
34	RATNAGIRI	-13	182	0	993	0	778
	<b>Total</b>	<b>0</b>	<b>124784</b>	<b>0</b>	<b>205979</b>	<b>0</b>	<b>80710</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AURANGABAD DIV.	1473	16352	683	27834	432	11069
2	NASHIK DIV.	74	1900	299	9332	295	6211
3	AMRAVATI DIV.	88	3462	241	13904	228	5552
4	NAGPUR DIV.	193	2376	200	8450	160	4065
5	PUNE DIV.	14	1817	102	5564	105	2446
6	KONKAN DIV.	8	1051	28	2038	63	1621
	<b>Total</b>	<b>1850</b>	<b>26958</b>	<b>1553</b>	<b>67122</b>	<b>1283</b>	<b>30964</b>

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	41
CHANDRAPUR	73
NANDURBAR	97
RAIGAD	111
THANE	125
DHULE	162
SATARA	165
PARBHANI	174
NASHIK	183
SANGLI	216
NAGPUR	242
AKOLA	261
PUNE	302
BHANDARA	354
GONDIA	368
KOLHAPUR	407
WASHIM	431
BULDHANA	431
WARDHA	592
AHMEDNAGAR	672
SOLAPUR	727
GADCHIROLI	747
PALGHAR	761
JALGAON	786
YAVATMAL	1133
AMRAVATI	1206
JALNA	1432
AURANGABAD	1818
LATUR	1967
OSMANABAD	2113
HINGOLI	2665
BEED	2687
NANDED	3496

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	333
THANE	355
SATARA	554
PALGHAR	606
RAIGAD	610
GONDIA	833
NAGPUR	891
SANGLI	1015
WARDHA	1097
BHANDARA	1133
KOLHAPUR	1154
PUNE	1197
NANDURBAR	1225
NASHIK	1572
SOLAPUR	1644
DHULE	1752
WASHIM	1791
PARBHANI	1950
GADCHIROLI	2089
HINGOLI	2127
AKOLA	2187
JALGAON	2336
AMRAVATI	2367
CHANDRAPUR	2407
AHMEDNAGAR	2447
BULDHANA	2997
OSMANABAD	3087
NANDED	3095
AURANGABAD	3663
LATUR	4068
JALNA	4195
YAVATMAL	4562
BEED	5649

State Schemes 3rd Ins Pending

SINDHUDURG	90
RATNAGIRI	188
THANE	271
SATARA	276
NAGPUR	294
KOLHAPUR	346
WARDHA	383
RAIGAD	386
SANGLI	388
BHANDARA	405
GONDIA	526
PALGHAR	686
PUNE	693
WASHIM	714
SOLAPUR	743
HINGOLI	776
PARBHANI	832
AMRAVATI	841
AURANGABAD	907
AKOLA	917
DHULE	1083
NASHIK	1103
NANDURBAR	1133
NANDED	1136
GADCHIROLI	1190
OSMANABAD	1256
CHANDRAPUR	1267
JALGAON	1335
YAVATMAL	1445
AHMEDNAGAR	1557
LATUR	1599
BULDHANA	1635
BEED	2050
JALNA	2513

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD	506	1818	97	3663	32	907
2	LATUR	265	1967	169	4068	81	1599
3	BEED	283	2687	117	5649	84	2050
4	JALNA	70	1432	125	4195	98	2513
5	HINGOLI	127	2665	88	2127	73	776
6	GADCHIROLI	166	747	60	2089	31	1190
7	BULDHANA	17	431	100	2997	81	1635
8	AHMEDNAGAR	47	672	54	2447	95	1557
9	YAVATMAL	48	1133	75	4562	62	1445
10	NANDURBAR	6	97	85	1225	85	1133
11	OSMANABAD	117	2113	36	3087	8	1256
12	NANDED	102	3496	18	3095	25	1136
13	JALGAON	13	786	82	2336	49	1335
14	DHULE	8	162	45	1752	49	1083
15	GONDIA	9	368	41	833	42	526
16	AKOLA	5	261	42	2187	38	917
17	PUNE	4	302	36	1197	38	693
18	AMRAVATI	11	1206	24	2367	40	841
19	CHANDRAPUR	4	73	37	2407	32	1267
20	PARBHANI	3	174	33	1950	31	832
21	WARDHA	0	592	24	1097	29	383
22	NASHIK	0	183	33	1572	17	1103
23	KOLHAPUR	0	407	34	1154	13	346
24	NAGPUR	11	242	23	891	13	294
25	SANGLI	4	216	18	1015	19	388
26	PALGHAR	1	761	6	606	28	686
27	BHANDARA	3	354	15	1133	13	405
28	THANE	3	125	11	355	16	271
29	SOLAPUR	5	727	4	1644	20	743
30	SATARA	1	165	10	554	15	276
31	RATNAGIRI	3	41	4	333	10	188
32	RAIGAD	0	111	6	610	9	386
33	WASHIM	7	431	0	1791	7	714
34	SINDHUDURG	1	13	1	134	0	90
	<b>Total</b>	<b>1850</b>	<b>26958</b>	<b>1553</b>	<b>67122</b>	<b>1283</b>	<b>30964</b>
