



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०५.०३.२०२३

प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण



योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१४५३९	२	९९०५२७	२८०३	०	०	०
राज्य योजना	५३६२१८	३५	३८८८३६	५५८	०	०	०
एकूण	१९५०७५७	३७	१३७९३६३	३३६१	०	०	०

PMAY-G Completion Progress Bar


70.0%

State Schemes Progress Bar

72.5%

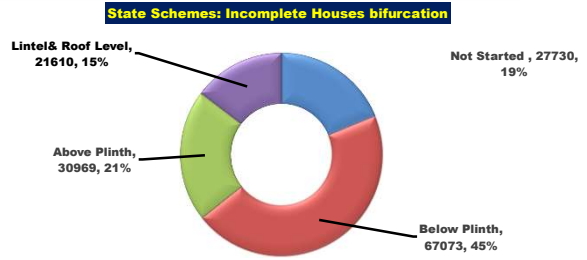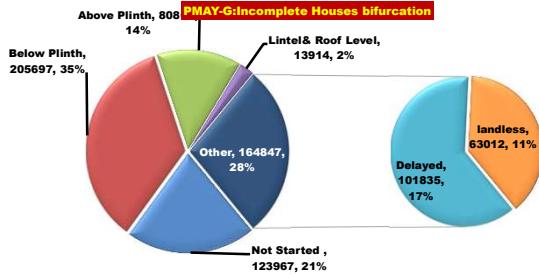


Delayed Houses bifurcation

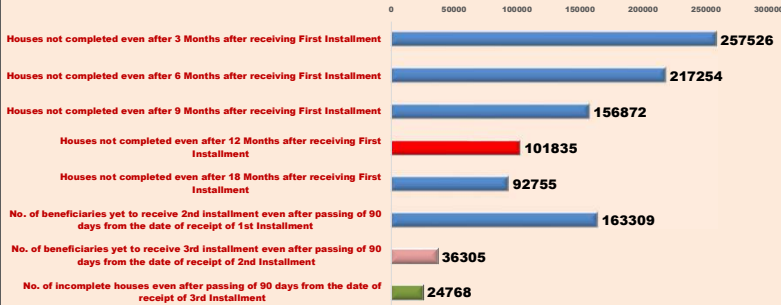


Abhiyan Achievement


Day 105

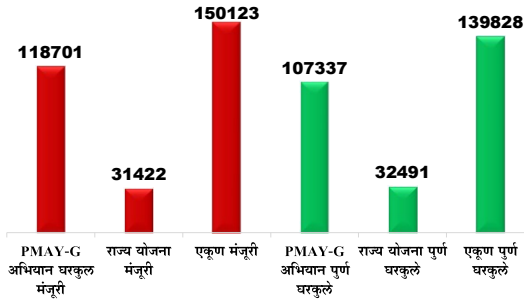

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	04.03.2023	05.03.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	292557	292010	291990	2	567
2	NASHIK DIV.	414686	413969	413911	0	775
3	AMRAVATI DIV.	274989	274674	274674	0	315
4	AURANGABAD DIV.	238381	238176	237915	0	466
5	KONKAN DIV.	69688	69661	69661	0	27
6	PUNE DIV.	126691	126475	126388	0	303
	Total	1416992	1414965	1414539	2	2453

PMAY-G Remaining Sanction

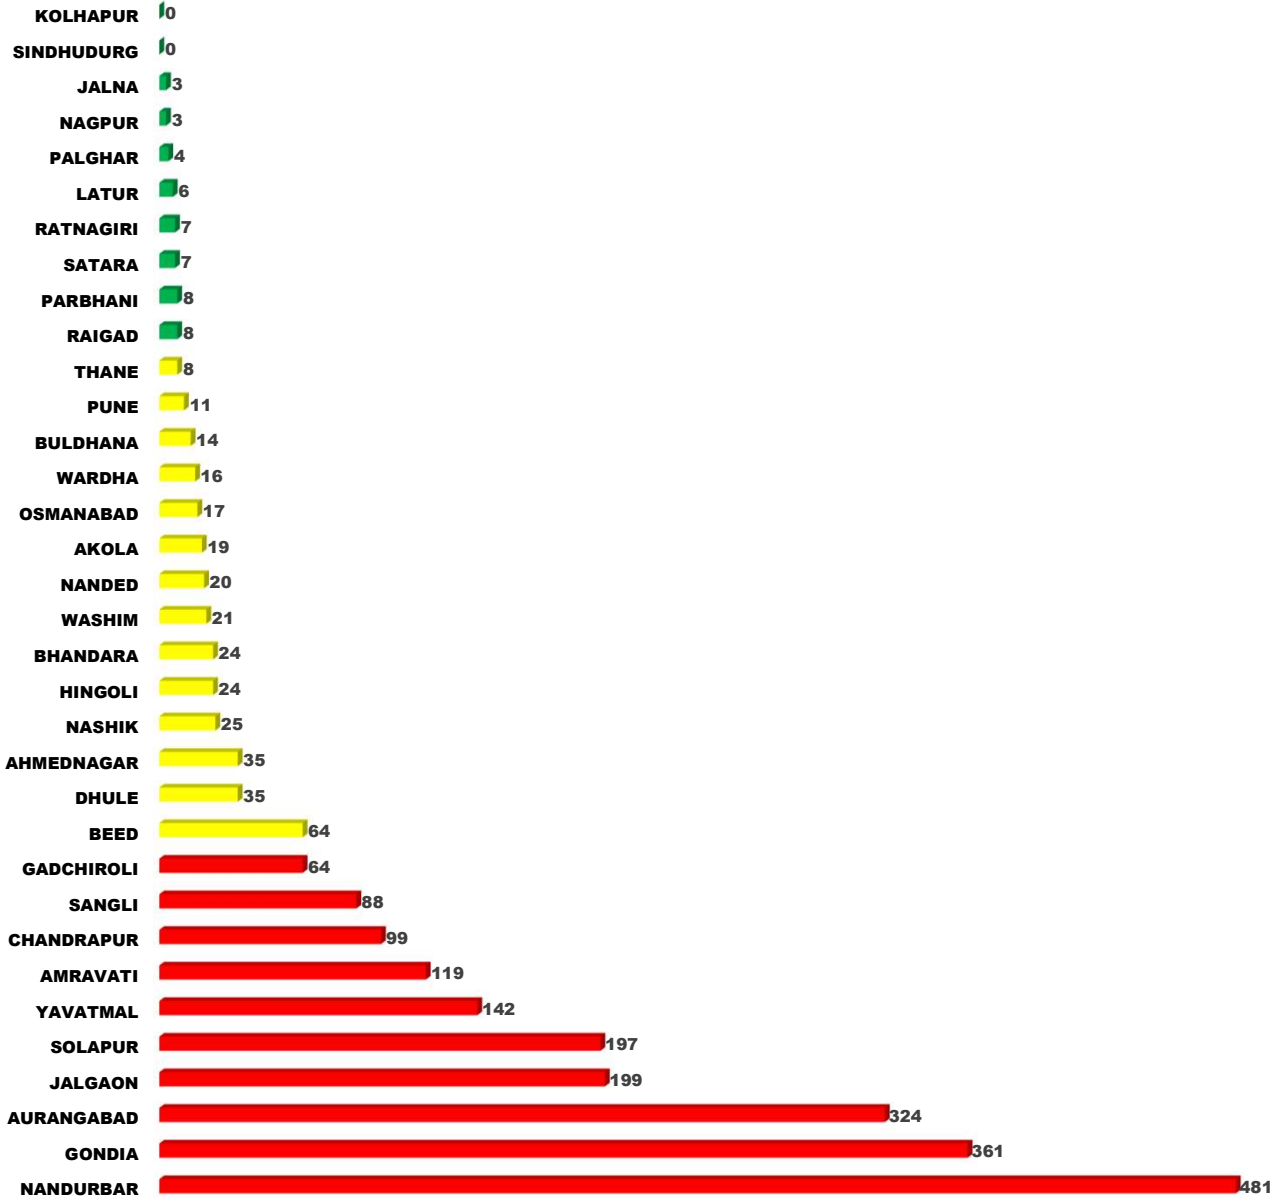


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	04.03.2023	05.03.2023	Daily_Achievement	Remaining
1	BHANDARA	65131	65106	65107	1	24
2	GONDIA	96474	96112	96113	1	361
3	AKOLA	48794	48775	48775	0	19
4	AMRAVATI	95646	95527	95527	0	119
5	BEED	35334	35270	35270	0	64
6	BULDHANA	44742	44728	44728	0	14
7	DHULE	64912	64877	64877	0	35
8	HINGOLI	18107	18083	18083	0	24
9	JALNA	24047	24044	24044	0	3
10	KOLHAPUR	17770	17770	17770	0	0
11	LATUR	20799	20793	20793	0	6
12	NAGPUR	37331	37328	37328	0	3
13	NANDED	69588	69568	69568	0	20
14	NANDURBAR	119349	118868	118868	0	481
15	NASHIK	89787	89762	89762	0	25
16	OSMANABAD	14583	14566	14566	0	17
17	PALGHAR	35152	35148	35148	0	4
18	PARBHANI	19106	19098	19098	0	8
19	RAIGAD	9847	9839	9839	0	8
20	RATNAGIRI	9927	9920	9920	0	7
21	SANGLI	22174	22086	22086	0	88
22	SINDHUDURG	5156	5156	5156	0	0
23	SOLAPUR	50165	49968	49968	0	197
24	THANE	9606	9598	9598	0	8
25	WARDHA	18671	18655	18655	0	16
26	WASHIM	20416	20395	20395	0	21
27	YAVATMAL	65391	65249	65249	0	142
28	GADCHIROLI	31639	31576	31575	-1	64
29	SATARA	15547	15545	15540	-5	7
30	CHANDRAPUR	43311	43233	43212	-21	99
31	AHMEDNAGAR	60802	60790	60767	-23	35
32	JALGAON	79836	79672	79637	-35	199
33	PUNE	21035	21106	21024	-82	11
34	AURANGABAD	36817	36754	36493	-261	324
Total		1416992	1414965	1414539	2	2453

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	04.03.2023	05.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NAGPUR DIV.	291990	227133	228114	981	63876	190	2457
2	NASHIK DIV.	413911	314492	315467	975	98444	304	3786
3	AMRAVATI DIV.	274674	178085	178440	355	96234	203	3701
4	AURANGABAD DIV.	237915	129704	129980	276	107935	214	4151
5	KONKAN DIV.	69661	53719	53840	121	15821	42	609
6	PUNE DIV.	126388	84591	84686	95	41702	69	1604
Total		1414539	987724	990527	2803	424012	1022	16308

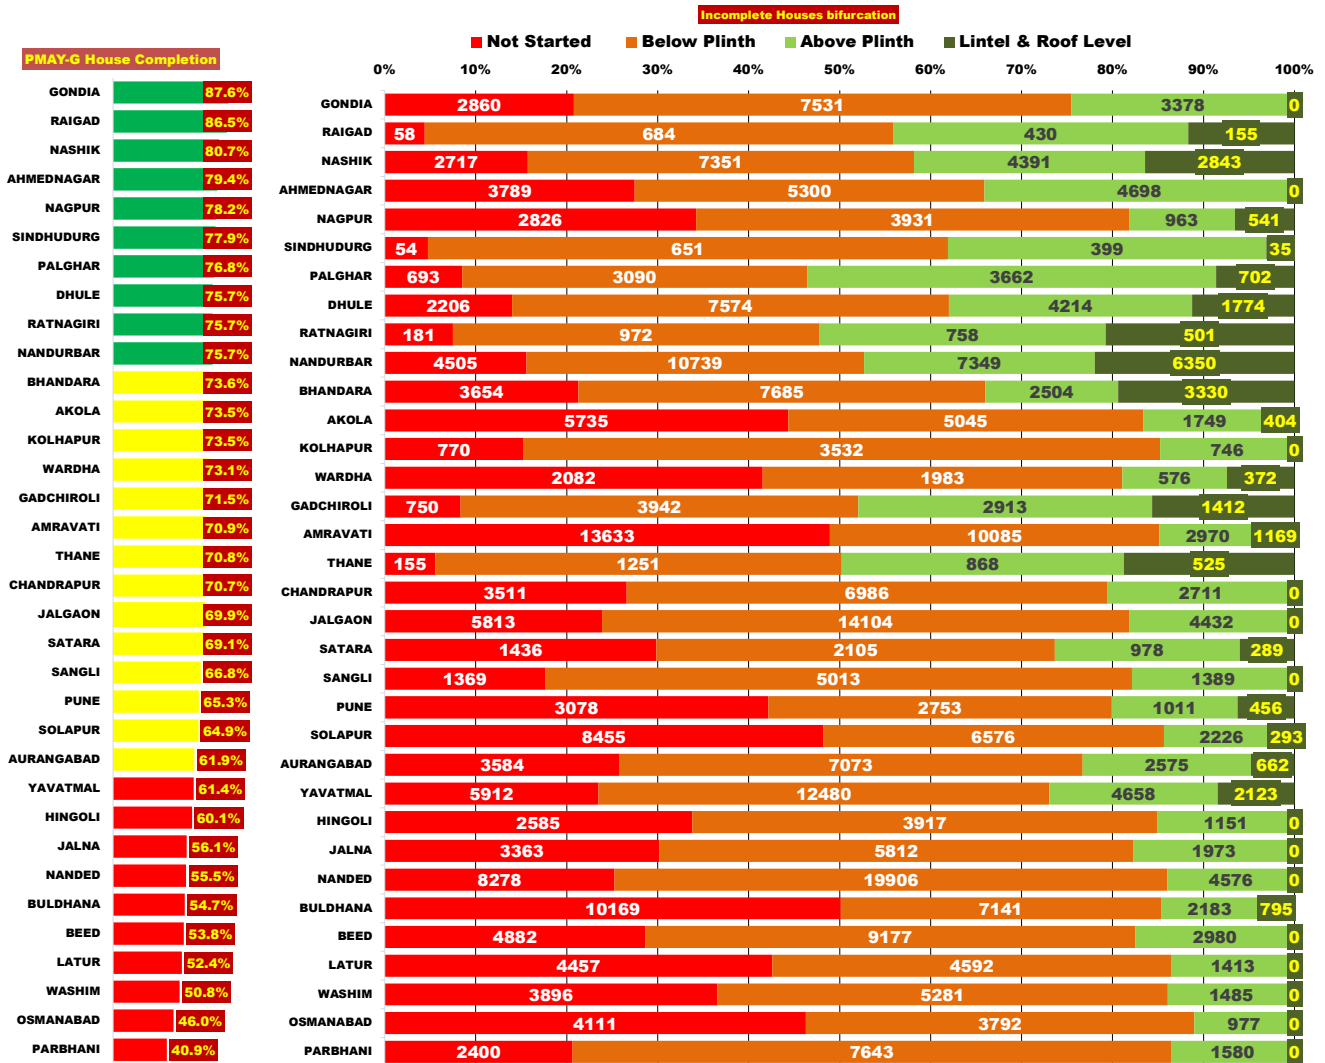


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	04.03.2023	05.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	GONDIA	96113	83627	84223	596	11890	63	457
2	NASHIK	89762	72151	72460	309	17302	54	665
3	AHMEDNAGAR	60767	48020	48279	259	12488	97	480
4	CHANDRAPUR	43212	30284	30530	246	12682	40	488
5	NANDURBAR	118868	89711	89925	214	28943	40	1113
6	AMRAVATI	95527	67586	67716	130	27811	58	1070
7	NANDED	69568	38530	38644	114	30924	51	1189
8	JALGAON	79637	55592	55694	102	23943	55	921
9	DHULE	64877	49018	49109	91	15768	58	606
10	NAGPUR	37328	29135	29202	67	8126	12	313
11	YAVATMAL	65249	40016	40080	64	25169	64	968
12	AKOLA	48775	35780	35842	62	12933	26	497
13	WASHIM	20395	10290	10351	61	10044	22	386
14	JALNA	24044	13436	13479	43	10565	28	406
15	RATNAGIRI	9920	7467	7508	41	2412	12	93
16	GADCHIROLI	31575	22543	22583	40	8992	27	346
17	BULDHANA	44728	24413	24451	38	20277	33	780
18	PUNE	21024	13695	13726	31	7298	11	281
19	SATARA	15540	10701	10732	31	4808	13	185
20	THANE	9598	6769	6799	30	2799	3	108
21	PARBHANI	19098	7790	7819	29	11279	16	434
22	SOLAPUR	49968	32389	32418	29	17550	24	675
23	PALGHAR	35148	26975	27001	26	8147	20	313
24	LATUR	20793	10861	10886	25	9907	23	381
25	WARDHA	18655	13619	13642	23	5013	11	193
26	BEED	35270	18964	18986	22	16284	26	626
27	HINGOLI	18083	10840	10860	20	7223	18	278
28	SINDHUDURG	5156	3998	4017	19	1139	3	44
29	AURANGABAD	36493	22586	22599	13	13894	33	534
30	OSMANABAD	14566	6697	6707	10	7859	18	302
31	BHANDARA	65107	47925	47934	9	17173	37	661
32	RAIGAD	9839	8510	8515	5	1324	4	51
33	KOLHAPUR	17770	13056	13058	2	4712	9	181
34	SANGLI	22086	14750	14752	2	7334	12	282
Total		1414539	987724	990527	2803	424012	1022	16308

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	04.03.2023	05.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	157936	157969	33	41362
2	NASHIK DIV.	141360	108308	108310	2	33050
3	KONKAN DIV.	34729	29558	29558	0	5171
4	PUNE DIV.	65334	62901	62901	0	2433
5	AMRAVATI DIV.	109702	90853	90853	0	18849
6	NAGPUR DIV.	116255	86627	86627	0	29628
Total		666711	536183	536218	35	130493

State Scheme Remaining Sanction

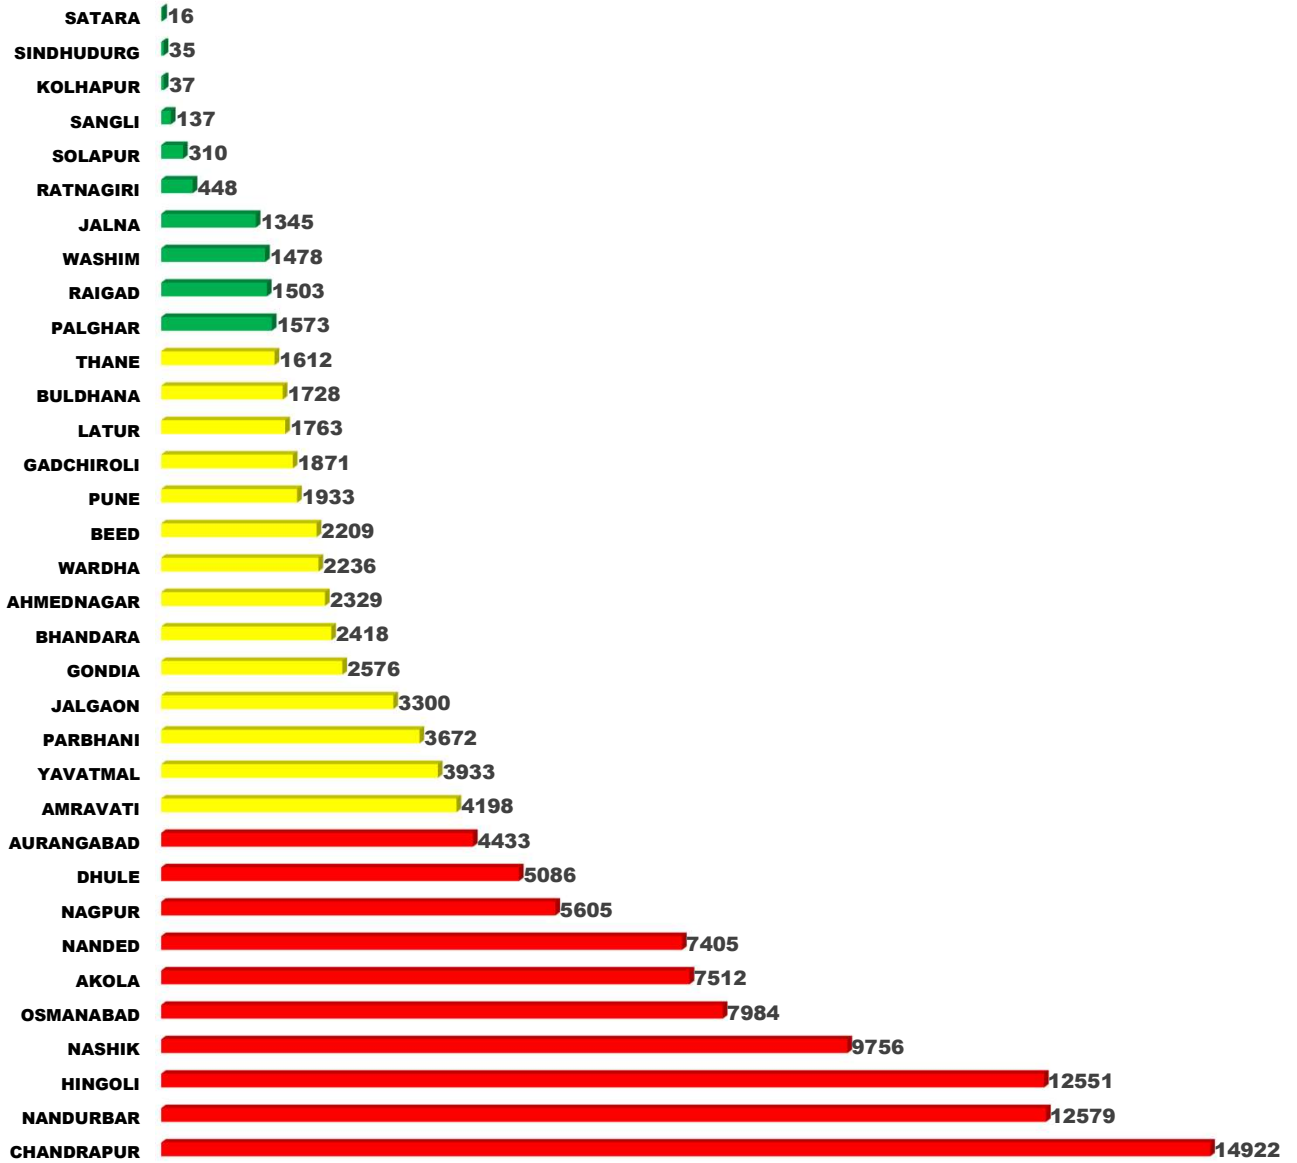


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	04.03.2023	05.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19336	19355	19	7405
2	AURANGABAD	26141	21694	21708	14	4433
3	AHMEDNAGAR	35298	32967	32969	2	2329
4	AKOLA	23681	16169	16169	0	7512
5	AMRAVATI	23224	19026	19026	0	4198
6	BEED	26878	24669	24669	0	2209
7	BHANDARA	17590	15172	15172	0	2418
8	BULDHANA	21616	19888	19888	0	1728
9	CHANDRAPUR	38147	23225	23225	0	14922
10	DHULE	21790	16704	16704	0	5086
11	GADCHIROLI	16834	14963	14963	0	1871
12	GONDIA	14246	11670	11670	0	2576
13	HINGOLI	27298	14747	14747	0	12551
14	JALGAON	25659	22359	22359	0	3300
15	JALNA	20446	19101	19101	0	1345
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	25408	25408	0	1763
18	NAGPUR	16291	10686	10686	0	5605
19	NANDURBAR	26578	13999	13999	0	12579
20	NASHIK	32035	22279	22279	0	9756
21	OSMANABAD	24853	16869	16869	0	7984
22	PALGHAR	11792	10219	10219	0	1573
23	PARBHANI	19784	16112	16112	0	3672
24	PUNE	14672	12739	12739	0	1933
25	RAIGAD	7406	5903	5903	0	1503
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10631	10631	0	16
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18408	18408	0	310
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	10911	10911	0	2236
33	WASHIM	11500	10022	10022	0	1478
34	YAVATMAL	29681	25748	25748	0	3933
Total		666711	536183	536218	35	130493

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	04.03.2023	05.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108310	85395	85594	199	22716	72	874
2	NAGPUR DIV.	86627	66909	67040	131	19587	43	753
3	AURANGABAD DIV.	157969	100412	100527	115	57442	99	2209
4	AMRAVATI DIV.	90853	61993	62046	53	28807	56	1108
5	PUNE DIV.	62901	50894	50928	34	11973	27	461
6	KONKAN DIV.	29558	22675	22701	26	6857	13	264
Total		536218	388278	388836	558	147382	309	5669

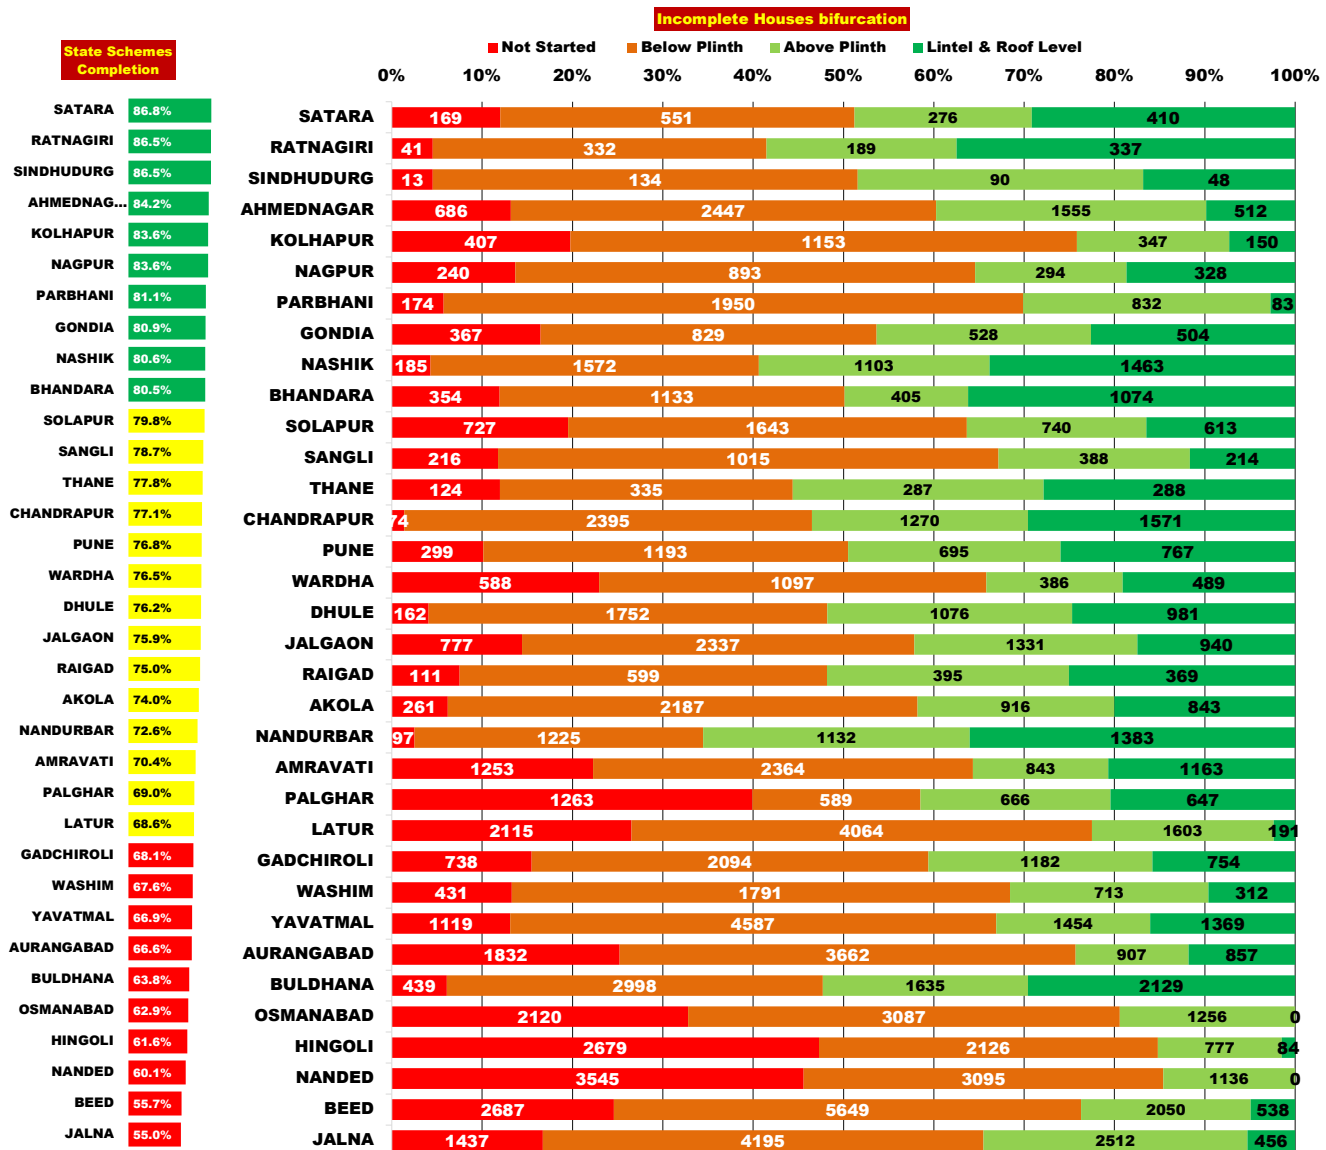

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	04.03.2023	05.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32969	27678	27769	91	5200	30	200
2	NASHIK	22279	17891	17956	65	4323	12	166
3	CHANDRAPUR	23225	17851	17915	64	5310	12	204
4	GONDIA	11670	9415	9442	27	2228	8	86
5	JALNA	19101	10474	10501	27	8600	32	331
6	BEED	24669	13721	13745	24	10924	14	420
7	PUNE	12739	9763	9785	22	2954	6	114
8	NANDURBAR	13999	10141	10162	21	3837	7	148
9	GADCHIROLI	14963	10175	10195	20	4768	8	183
10	HINGOLI	14747	9061	9081	20	5666	6	218
11	WARDHA	10911	8334	8351	17	2560	7	98
12	AKOLA	16169	11946	11962	16	4207	10	162
13	YAVATMAL	25748	17205	17219	14	8529	14	328
14	DHULE	16704	12720	12733	13	3971	12	153
15	BULDHANA	19888	12675	12687	12	7201	16	277
16	OSMANABAD	16869	10593	10604	11	6265	13	241
17	RAIGAD	5903	4418	4429	11	1474	3	57
18	AURANGABAD	21708	14440	14450	10	7258	8	279
19	NANDED	19355	11628	11638	10	7717	10	297
20	WASHIM	10022	6765	6775	10	3247	8	125
21	JALGAON	22359	16965	16974	9	5385	12	207
22	LATUR	25408	17426	17435	9	7973	11	307
23	PALGHAR	10219	7046	7054	8	3165	6	122
24	SATARA	10631	9218	9225	7	1406	5	54
25	PARBHANI	16112	13069	13073	4	3039	4	117
26	RATNAGIRI	6678	5775	5779	4	899	2	35
27	THANE	4652	3615	3618	3	1034	1	40
28	KOLHAPUR	12528	10469	10471	2	2057	4	79
29	NAGPUR	10686	8929	8931	2	1755	4	68
30	SOLAPUR	18408	14683	14685	2	3723	8	143
31	AMRAVATI	19026	13402	13403	1	5623	9	216
32	BHANDARA	15172	12205	12206	1	2966	4	114
33	SANGLI	8595	6761	6762	1	1833	4	71
34	SINDHUDURG	2106	1821	1821	0	285	1	11
Total		536218	388278	388836	558	147382	309	5669

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19030	0	45068	0	25084
2	AMRAVATI DIV.	0	39281	0	40032	0	13045
3	AURANGABAD DIV.	0	33630	0	61912	0	17225
4	NAGPUR DIV.	0	15481	0	32058	0	13045
5	KONKAN DIV.	0	1138	0	6648	0	6117
6	PUNE DIV.	0	14975	0	19979	0	6350
	Total	0	123535	0	205697	0	80866

PMAY-G 1st Ins Pending

SINDHUDURG	54
RAIGAD	55
THANE	155
RATNAGIRI	181
PALGHAR	693
GADCHIROLI	725
KOLHAPUR	770
SANGLI	1236
SATARA	1436
WARDHA	2082
DHULE	2206
PARBHANI	2400
HINGOLI	2585
NAGPUR	2691
NASHIK	2717
GONDIA	2860
PUNE	3078
JALNA	3333
CHANDRAPUR	3469
AURANGABAD	3584
BHANDARA	3654
AHMEDNAGAR	3789
WASHIM	3893
OSMANABAD	4111
LATUR	4457
NANDURBAR	4505
BEED	4882
AKOLA	5735
JALGAON	5813
YAVATMAL	5908
NANDED	8278
SOLAPUR	8455
BULDHANA	10158
AMRAVATI	13587

PMAY-G 2nd Ins Pending

SINDHUDURG	651
RAIGAD	684
RATNAGIRI	972
THANE	1251
WARDHA	1983
SATARA	2105
PUNE	2753
PALGHAR	3090
KOLHAPUR	3532
OSMANABAD	3792
HINGOLI	3917
NAGPUR	3931
GADCHIROLI	3942
LATUR	4592
SANGLI	5013
AKOLA	5045
WASHIM	5281
AHMEDNAGAR	5300
JALNA	5812
SOLAPUR	6576
CHANDRAPUR	6986
AURANGABAD	7073
BULDHANA	7141
NASHIK	7351
GONDIA	7531
DHULE	7574
PARBHANI	7643
BHANDARA	7685
BEED	9177
AMRAVATI	10085
NANDURBAR	10739
YAVATMAL	12480
JALGAON	14104
NANDED	19906

PMAY-G 3rd Ins Pending

SINDHUDURG	399
RAIGAD	430
WARDHA	576
KOLHAPUR	746
RATNAGIRI	758
THANE	868
NAGPUR	963
OSMANABAD	977
SATARA	978
PUNE	1011
HINGOLI	1151
SANGLI	1389
LATUR	1413
WASHIM	1485
PARBHANI	1580
AKOLA	1749
JALNA	1973
BULDHANA	2183
SOLAPUR	2226
BHANDARA	2504
AURANGABAD	2575
CHANDRAPUR	2711
GADCHIROLI	2913
AMRAVATI	2970
BEED	2980
GONDIA	3378
PALGHAR	3662
DHULE	4214
NASHIK	4391
JALGAON	4432
NANDED	4576
YAVATMAL	4658
AHMEDNAGAR	4698
NANDURBAR	7349

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3789	0	5300	0	4698
2	AKOLA	0	5735	0	5045	0	1749
3	AMRAVATI	0	13587	0	10085	0	2970
4	AURANGABAD	0	3584	0	7073	0	2575
5	BEED	0	4882	0	9177	0	2980
6	BHANDARA	0	3654	0	7685	0	2504
7	BULDHANA	0	10158	0	7141	0	2183
8	CHANDRAPUR	0	3469	0	6986	0	2711
9	DHULE	0	2206	0	7574	0	4214
10	GADCHIROLI	0	725	0	3942	0	2913
11	GONDIA	0	2860	0	7531	0	3378
12	HINGOLI	0	2585	0	3917	0	1151
13	JALGAON	0	5813	0	14104	0	4432
14	JALNA	0	3333	0	5812	0	1973
15	KOLHAPUR	0	770	0	3532	0	746
16	LATUR	0	4457	0	4592	0	1413
17	NAGPUR	0	2691	0	3931	0	963
18	NANDED	0	8278	0	19906	0	4576
19	NANDURBAR	0	4505	0	10739	0	7349
20	NASHIK	0	2717	0	7351	0	4391
21	OSMANABAD	0	4111	0	3792	0	977
22	PALGHAR	0	693	0	3090	0	3662
23	PARBHANI	0	2400	0	7643	0	1580
24	PUNE	0	3078	0	2753	0	1011
25	RAIGAD	0	55	0	684	0	430
26	RATNAGIRI	0	181	0	972	0	758
27	SANGLI	0	1236	0	5013	0	1389
28	SATARA	0	1436	0	2105	0	978
29	SINDHUDURG	0	54	0	651	0	399
30	SOLAPUR	0	8455	0	6576	0	2226
31	THANE	0	155	0	1251	0	868
32	WARDHA	0	2082	0	1983	0	576
33	WASHIM	0	3893	0	5281	0	1485
34	YAVATMAL	0	5908	0	12480	0	4658
	Total	0	123535	0	205697	0	80866

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	1907	0	9333	0	6197
2	AMRAVATI DIV.	0	3503	0	13927	0	5561
3	AURANGABAD DIV.	0	16589	0	27828	0	11073
4	NAGPUR DIV.	0	2361	0	8441	0	4065
5	KONKAN DIV.	0	1552	0	1989	0	1627
6	PUNE DIV.	0	1818	0	5555	0	2446
	Total	0	27730	0	67073	0	30969

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	41
CHANDRAPUR	74
NANDURBAR	97
RAIGAD	111
THANE	124
DHULE	162
SATARA	169
PARBHANI	174
NASHIK	185
SANGLI	216
NAGPUR	240
AKOLA	261
PUNE	299
BHANDARA	354
GONDIA	367
KOLHAPUR	407
WASHIM	431
BULDHANA	439
WARDHA	588
AHMEDNAGAR	686
SOLAPUR	727
GADCHIROLI	738
JALGAON	777
YAVATMAL	1119
AMRAVATI	1253
PALGHAR	1263
JALNA	1437
AURANGABAD	1832
LATUR	2115
OSMANABAD	2120
HINGOLI	2679
BEED	2687
NANDED	3545

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	332
THANE	335
SATARA	551
PALGHAR	589
RAIGAD	599
GONDIA	829
NAGPUR	893
SANGLI	1015
WARDHA	1097
BHANDARA	1133
KOLHAPUR	1153
PUNE	1193
NANDURBAR	1225
NASHIK	1572
SOLAPUR	1643
DHULE	1752
WASHIM	1791
PARBHANI	1950
GADCHIROLI	2094
HINGOLI	2126
AKOLA	2187
JALGAON	2337
AMRAVATI	2364
CHANDRAPUR	2395
AHMEDNAGAR	2447
BULDHANA	2998
OSMANABAD	3087
NANDED	3095
AURANGABAD	3662
LATUR	4064
JALNA	4195
YAVATMAL	4587
BEED	5649

State Schemes 3rd Ins Pending

SINDHUDURG	90
RATNAGIRI	189
SATARA	276
THANE	287
NAGPUR	294
KOLHAPUR	347
WARDHA	386
SANGLI	388
RAIGAD	395
BHANDARA	405
GONDIA	528
PALGHAR	666
PUNE	695
WASHIM	713
SOLAPUR	740
HINGOLI	777
PARBHANI	832
AMRAVATI	843
AURANGABAD	907
AKOLA	916
DHULE	1076
NASHIK	1103
NANDURBAR	1132
NANDED	1136
GADCHIROLI	1182
OSMANABAD	1256
CHANDRAPUR	1270
JALGAON	1331
YAVATMAL	1454
AHMEDNAGAR	1555
LATUR	1603
BULDHANA	1635
BEED	2050
JALNA	2512

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	686	0	2447	0	1555
2	AKOLA	0	261	0	2187	0	916
3	AMRAVATI	0	1253	0	2364	0	843
4	AURANGABAD	0	1832	0	3662	0	907
5	BEED	0	2687	0	5649	0	2050
6	BHANDARA	0	354	0	1133	0	405
7	BULDHANA	0	439	0	2998	0	1635
8	CHANDRAPUR	0	74	0	2395	0	1270
9	DHULE	0	162	0	1752	0	1076
10	GADCHIROLI	0	738	0	2094	0	1182
11	GONDIA	0	367	0	829	0	528
12	HINGOLI	0	2679	0	2126	0	777
13	JALGAON	0	777	0	2337	0	1331
14	JALNA	0	1437	0	4195	0	2512
15	KOLHAPUR	0	407	0	1153	0	347
16	LATUR	0	2115	0	4064	0	1603
17	NAGPUR	0	240	0	893	0	294
18	NANDED	0	3545	0	3095	0	1136
19	NANDURBAR	0	97	0	1225	0	1132
20	NASHIK	0	185	0	1572	0	1103
21	OSMANABAD	0	2120	0	3087	0	1256
22	PALGHAR	0	1263	0	589	0	666
23	PARBHANI	0	174	0	1950	0	832
24	PUNE	0	299	0	1193	0	695
25	RAIGAD	0	111	0	599	0	395
26	RATNAGIRI	0	41	0	332	0	189
27	SANGLI	0	216	0	1015	0	388
28	SATARA	0	169	0	551	0	276
29	SINDHUDURG	0	13	0	134	0	90
30	SOLAPUR	0	727	0	1643	0	740
31	THANE	0	124	0	335	0	287
32	WARDHA	0	588	0	1097	0	386
33	WASHIM	0	431	0	1791	0	713
34	YAVATMAL	0	1119	0	4587	0	1454
	Total	0	27730	0	67073	0	30969
