



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०६.०३.२०२३

प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण



योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१४५२७	४	९९२४४	१७१७	०	०	०
राज्य योजना	५३६४६३	२४५	३८९२४६	४१०	०	०	०
एकूण	१९५०९९०	२४९	१३८१४९०	२१२७	०	०	०

PMAY-G Completion Progress Bar


70.1%

State Schemes Progress Bar

72.6%

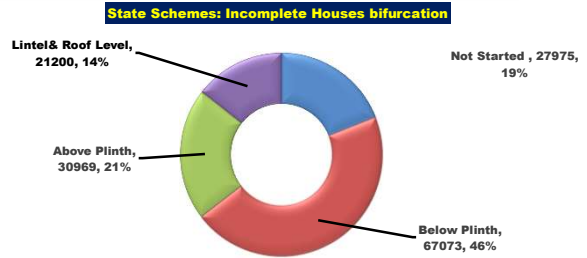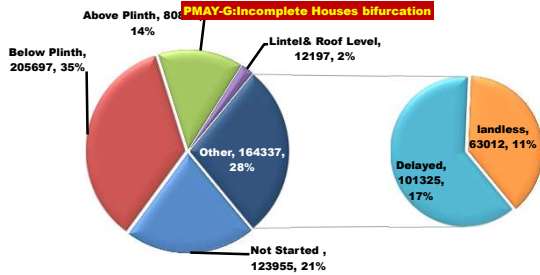


Delayed Houses Bifurcation

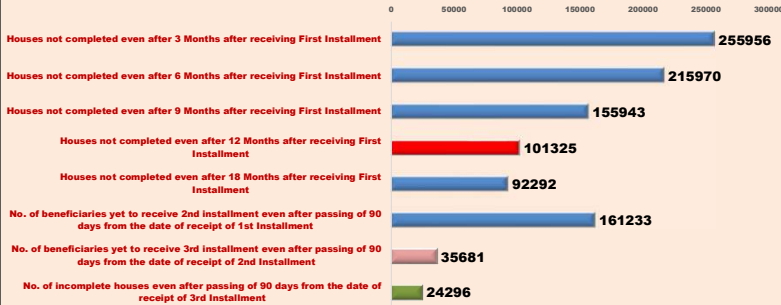


Abhiyan Achievement


Day 106

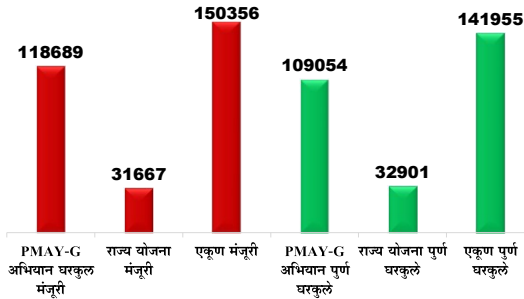

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	05.03.2023	06.03.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	292541	291990	291986	4	555
2	NASHIK DIV.	414686	413911	413906	0	780
3	AMRAVATI DIV.	274989	274674	274674	0	315
4	AURANGABAD DIV.	238371	237915	237912	0	459
5	KONKAN DIV.	69688	69661	69661	0	27
6	PUNE DIV.	126691	126388	126388	0	303
	Total	1416966	1414539	1414527	4	2439

PMAY-G Remaining Sanction

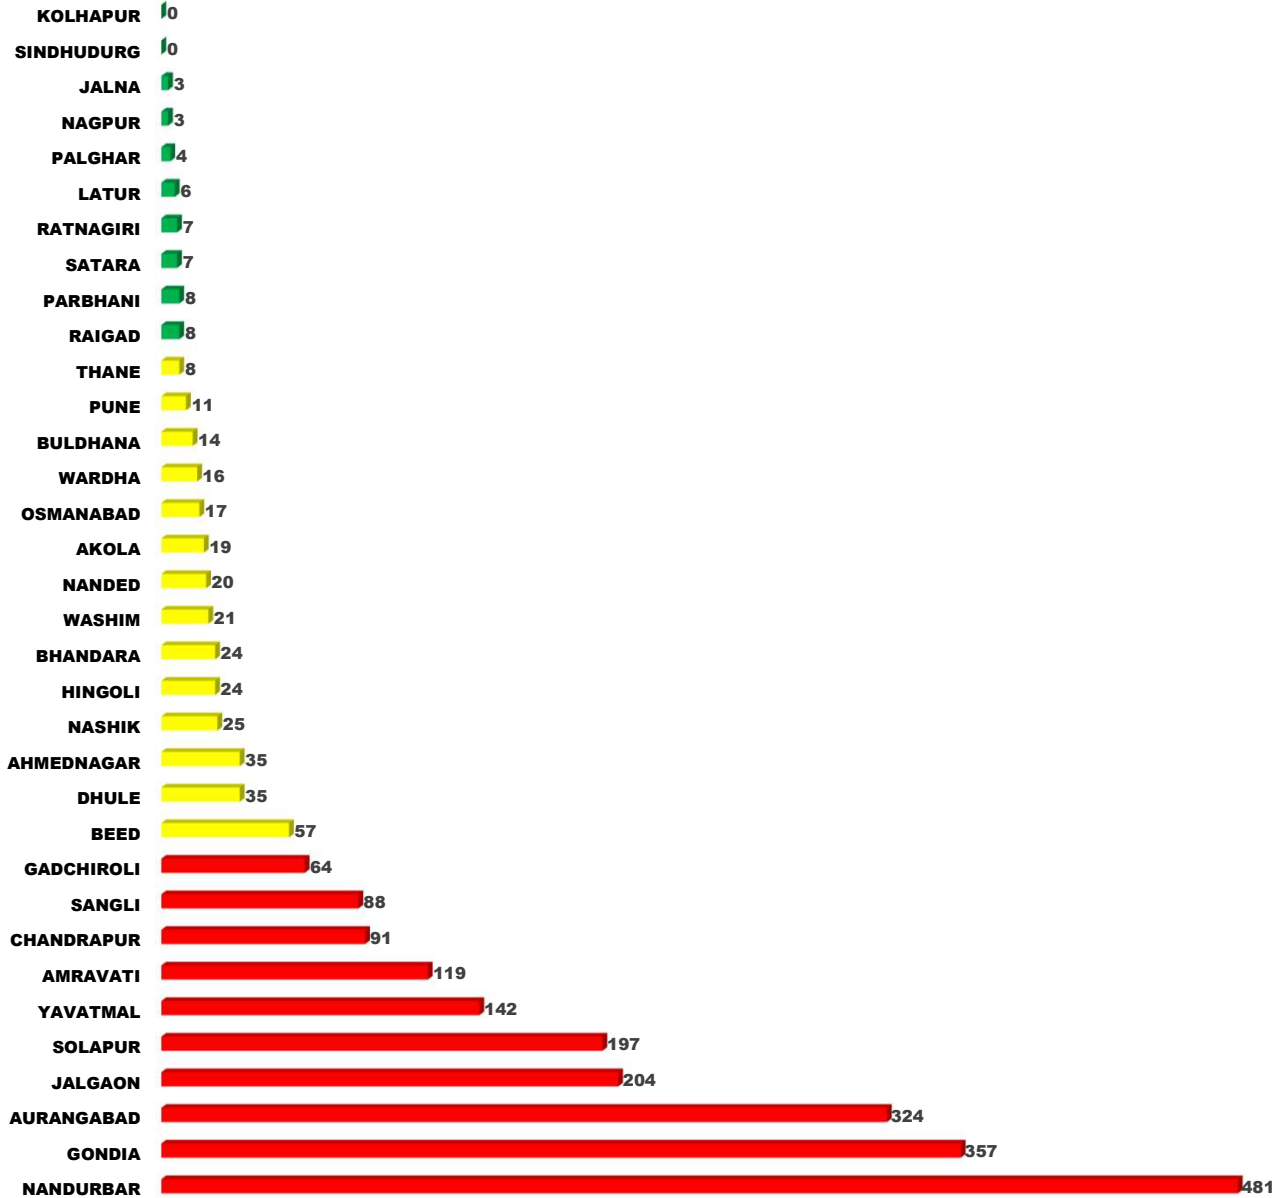


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	05.03.2023	06.03.2023	Daily_Achievement	Remaining
1	GONDIA	96474	96113	96117	4	357
2	AHMEDNAGAR	60802	60767	60767	0	35
3	AKOLA	48794	48775	48775	0	19
4	AMRAVATI	95646	95527	95527	0	119
5	AURANGABAD	36817	36493	36493	0	324
6	BHANDARA	65131	65107	65107	0	24
7	BULDHANA	44742	44728	44728	0	14
8	DHULE	64912	64877	64877	0	35
9	GADCHIROLI	31639	31575	31575	0	64
10	HINGOLI	18107	18083	18083	0	24
11	JALNA	24047	24044	24044	0	3
12	KOLHAPUR	17770	17770	17770	0	0
13	LATUR	20799	20793	20793	0	6
14	NAGPUR	37331	37328	37328	0	3
15	NANDED	69588	69568	69568	0	20
16	NANDURBAR	119349	118868	118868	0	481
17	NASHIK	89787	89762	89762	0	25
18	OSMANABAD	14583	14566	14566	0	17
19	PALGHAR	35152	35148	35148	0	4
20	PARBHANI	19106	19098	19098	0	8
21	PUNE	21035	21024	21024	0	11
22	RAIGAD	9847	9839	9839	0	8
23	RATNAGIRI	9927	9920	9920	0	7
24	SANGLI	22174	22086	22086	0	88
25	SATARA	15547	15540	15540	0	7
26	SINDHUDURG	5156	5156	5156	0	0
27	SOLAPUR	50165	49968	49968	0	197
28	THANE	9606	9598	9598	0	8
29	WARDHA	18671	18655	18655	0	16
30	WASHIM	20416	20395	20395	0	21
31	YAVATMAL	65391	65249	65249	0	142
32	BEED	35324	35270	35267	-3	57
33	JALGAON	79836	79637	79632	-5	204
34	CHANDRAPUR	43295	43212	43204	-8	91
Total		1416966	1414539	1414527	4	2439

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.03.2023	06.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NAGPUR DIV.	291986	228114	228753	639	63233	195	2529
2	NASHIK DIV.	413906	315467	315898	431	98008	306	3920
3	KONKAN DIV.	69661	53840	54084	244	15577	44	623
4	AURANGABAD DIV.	237912	129980	130184	204	107728	213	4309
5	AMRAVATI DIV.	274674	178440	178588	148	96086	202	3843
6	PUNE DIV.	126388	84686	84737	51	41651	69	1666
Total		1414527	990527	992244	1717	422283	1029	16891

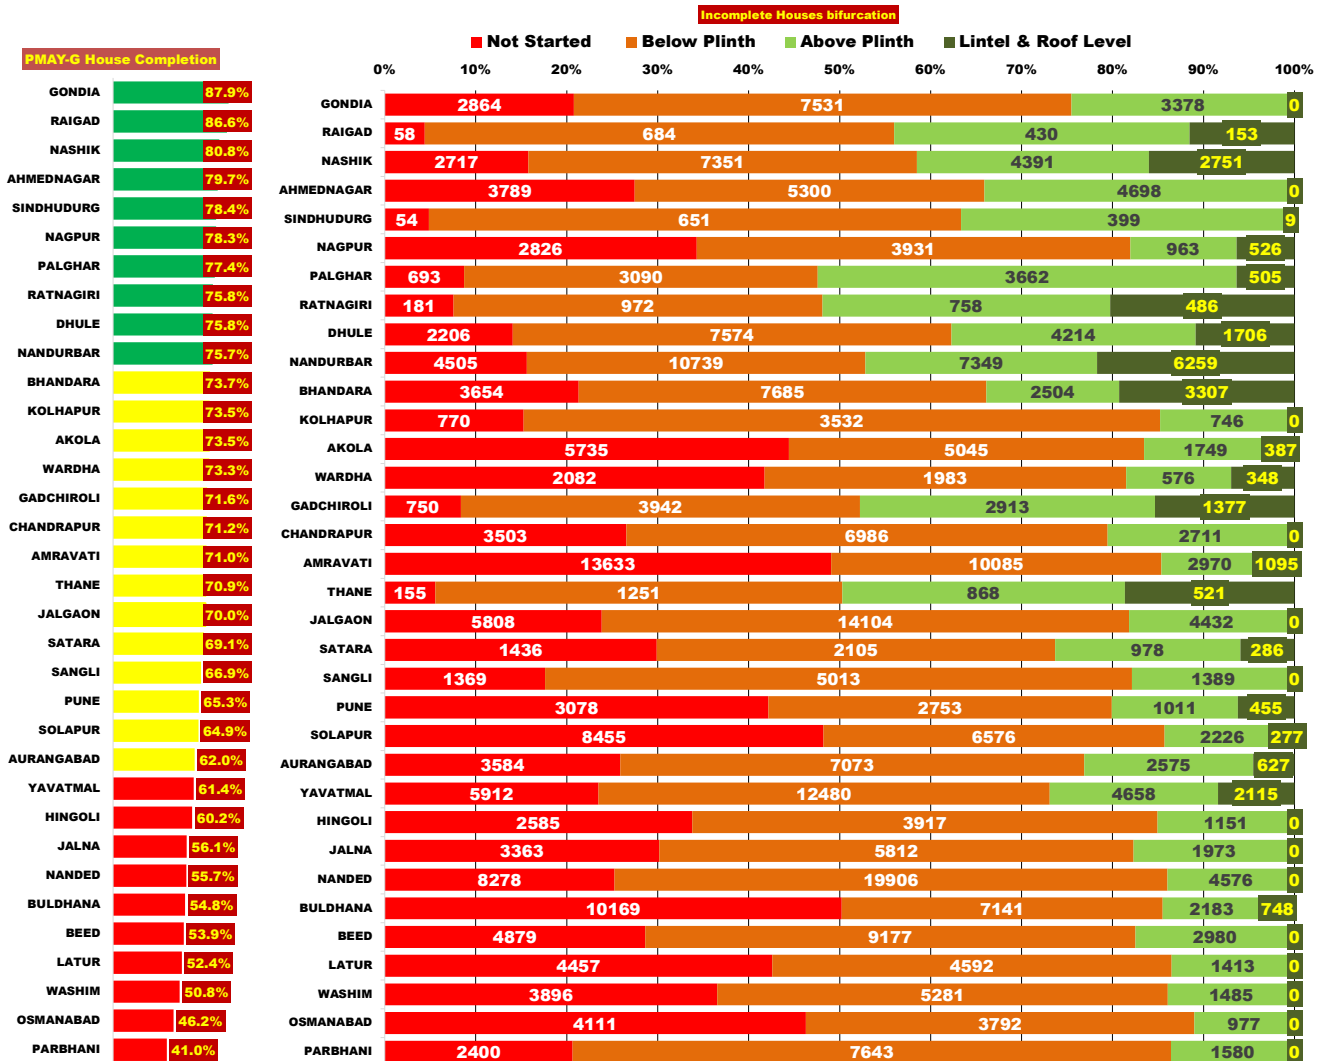


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.03.2023	06.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	GONDIA	96117	84223	84521	298	11596	66	464
2	CHANDRAPUR	43204	30530	30774	244	12430	42	497
3	PALGHAR	35148	27001	27198	197	7950	21	318
4	AHMEDNAGAR	60767	48279	48417	138	12350	98	494
5	NASHIK	89762	72460	72552	92	17210	54	688
6	NANDURBAR	118868	89925	90016	91	28852	40	1154
7	NANDED	69568	38644	38725	81	30843	51	1234
8	AMRAVATI	95527	67716	67790	74	27737	58	1109
9	DHULE	64877	49109	49177	68	15700	58	628
10	BULDHANA	44728	24451	24498	47	20230	33	809
11	JALGAON	79632	55694	55736	42	23896	55	956
12	AURANGABAD	36493	22599	22634	35	13859	33	554
13	GADCHIROLI	31575	22583	22618	35	8957	27	358
14	SINDHUDURG	5156	4017	4043	26	1113	3	45
15	WARDHA	18655	13642	13666	24	4989	11	200
16	BHANDARA	65107	47934	47957	23	17150	37	686
17	BEED	35267	18986	19007	21	16260	26	650
18	SANGLI	22086	14752	14773	21	7313	12	293
19	HINGOLI	18083	10860	10880	20	7203	18	288
20	AKOLA	48775	35842	35859	17	12916	26	517
21	OSMANABAD	14566	6707	6723	16	7843	18	314
22	SOLAPUR	49968	32418	32434	16	17534	24	701
23	NAGPUR	37328	29202	29217	15	8111	12	324
24	RATNAGIRI	9920	7508	7523	15	2397	12	96
25	LATUR	20793	10886	10900	14	9893	23	396
26	KOLHAPUR	17770	13058	13068	10	4702	9	188
27	JALNA	24044	13479	13488	9	10556	28	422
28	PARBHANI	19098	7819	7827	8	11271	16	451
29	YAVATMAL	65249	40080	40088	8	25161	63	1006
30	THANE	9598	6799	6803	4	2795	3	112
31	SATARA	15540	10732	10735	3	4805	13	192
32	RAIGAD	9839	8515	8517	2	1322	4	53
33	WASHIM	20395	10351	10353	2	10042	22	402
34	PUNE	21024	13726	13727	1	7297	11	292
Total		1414527	990527	992244	1717	422283	1029	16891

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	05.03.2023	06.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	157969	158214	245	41117
2	KONKAN DIV.	34729	29558	29558	0	5171
3	PUNE DIV.	65334	62901	62901	0	2433
4	NASHIK DIV.	141360	108310	108310	0	33050
5	AMRAVATI DIV.	109702	90853	90853	0	18849
6	NAGPUR DIV.	116255	86627	86627	0	29628
	Total	666711	536218	536463	245	130248

State Scheme Remaining Sanction

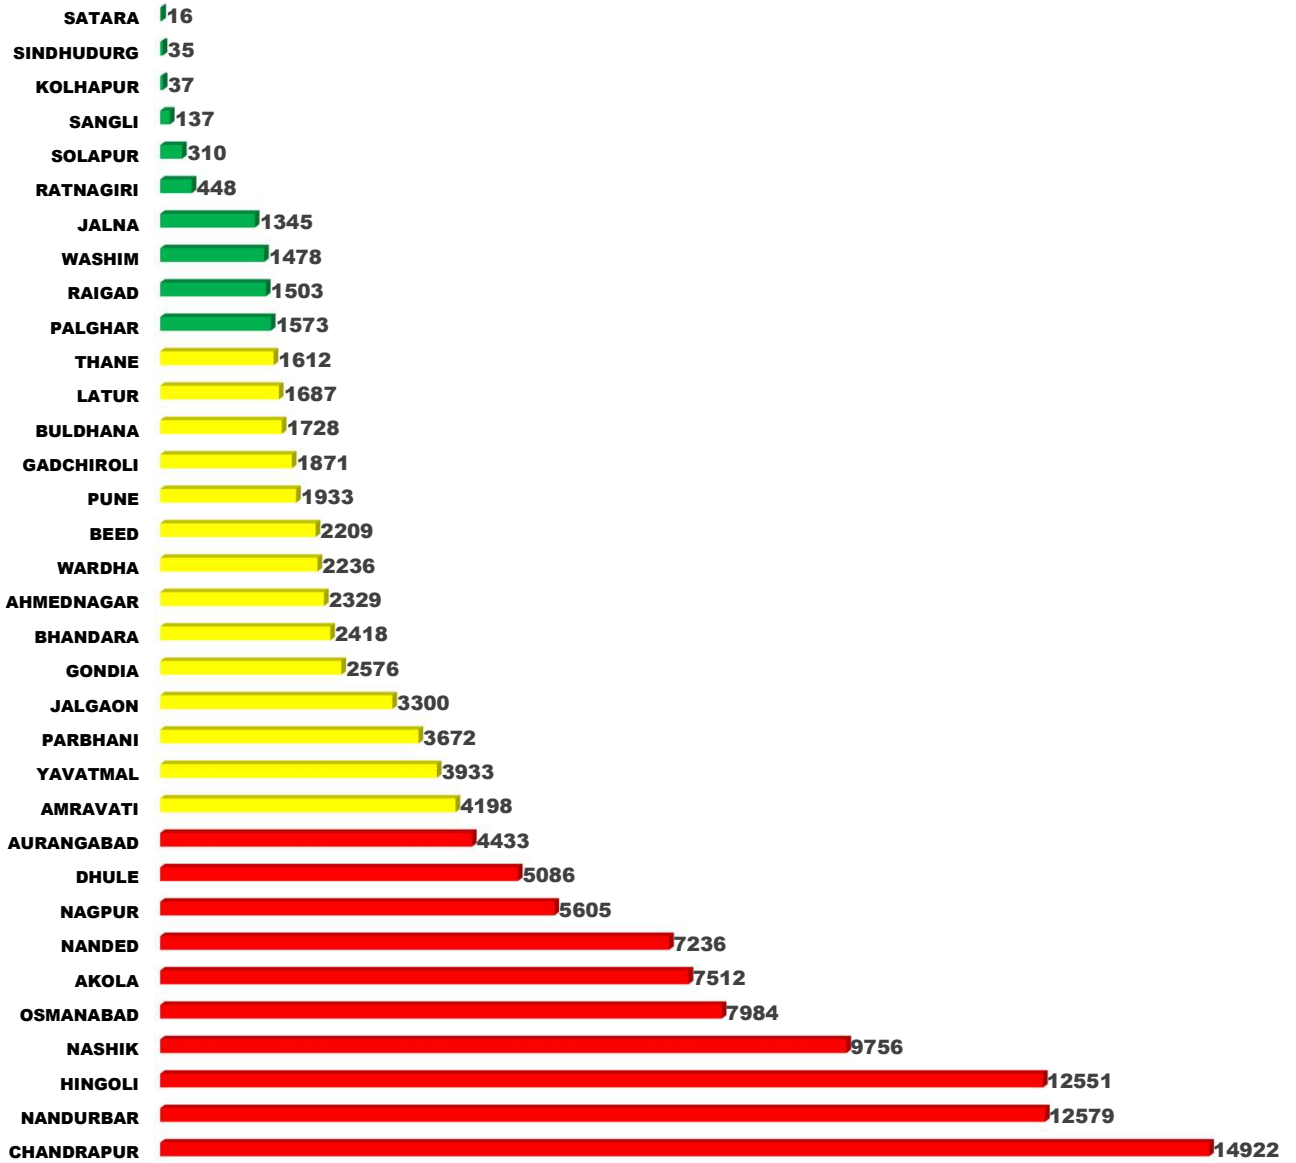


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	05.03.2023	06.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19355	19524	169	7236
2	LATUR	27171	25408	25484	76	1687
3	AHMEDNAGAR	35298	32969	32969	0	2329
4	AKOLA	23681	16169	16169	0	7512
5	AMRAVATI	23224	19026	19026	0	4198
6	AURANGABAD	26141	21708	21708	0	4433
7	BEED	26878	24669	24669	0	2209
8	BHANDARA	17590	15172	15172	0	2418
9	BULDHANA	21616	19888	19888	0	1728
10	CHANDRAPUR	38147	23225	23225	0	14922
11	DHULE	21790	16704	16704	0	5086
12	GADCHIROLI	16834	14963	14963	0	1871
13	GONDIA	14246	11670	11670	0	2576
14	HINGOLI	27298	14747	14747	0	12551
15	JALGAON	25659	22359	22359	0	3300
16	JALNA	20446	19101	19101	0	1345
17	KOLHAPUR	12565	12528	12528	0	37
18	NAGPUR	16291	10686	10686	0	5605
19	NANDURBAR	26578	13999	13999	0	12579
20	NASHIK	32035	22279	22279	0	9756
21	OSMANABAD	24853	16869	16869	0	7984
22	PALGHAR	11792	10219	10219	0	1573
23	PARBHANI	19784	16112	16112	0	3672
24	PUNE	14672	12739	12739	0	1933
25	RAIGAD	7406	5903	5903	0	1503
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10631	10631	0	16
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18408	18408	0	310
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	10911	10911	0	2236
33	WASHIM	11500	10022	10022	0	1478
34	YAVATMAL	29681	25748	25748	0	3933
Total		666711	536218	536463	245	130248

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.03.2023	06.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NAGPUR DIV.	86627	67040	67206	166	19421	44	777
2	NASHIK DIV.	108310	85594	85737	143	22573	72	903
3	AURANGABAD DIV.	158214	100527	100581	54	57633	99	2305
4	KONKAN DIV.	29558	22701	22725	24	6833	13	273
5	AMRAVATI DIV.	90853	62046	62059	13	28794	55	1152
6	PUNE DIV.	62901	50928	50938	10	11963	27	479
Total		536463	388836	389246	410	147217	310	5889

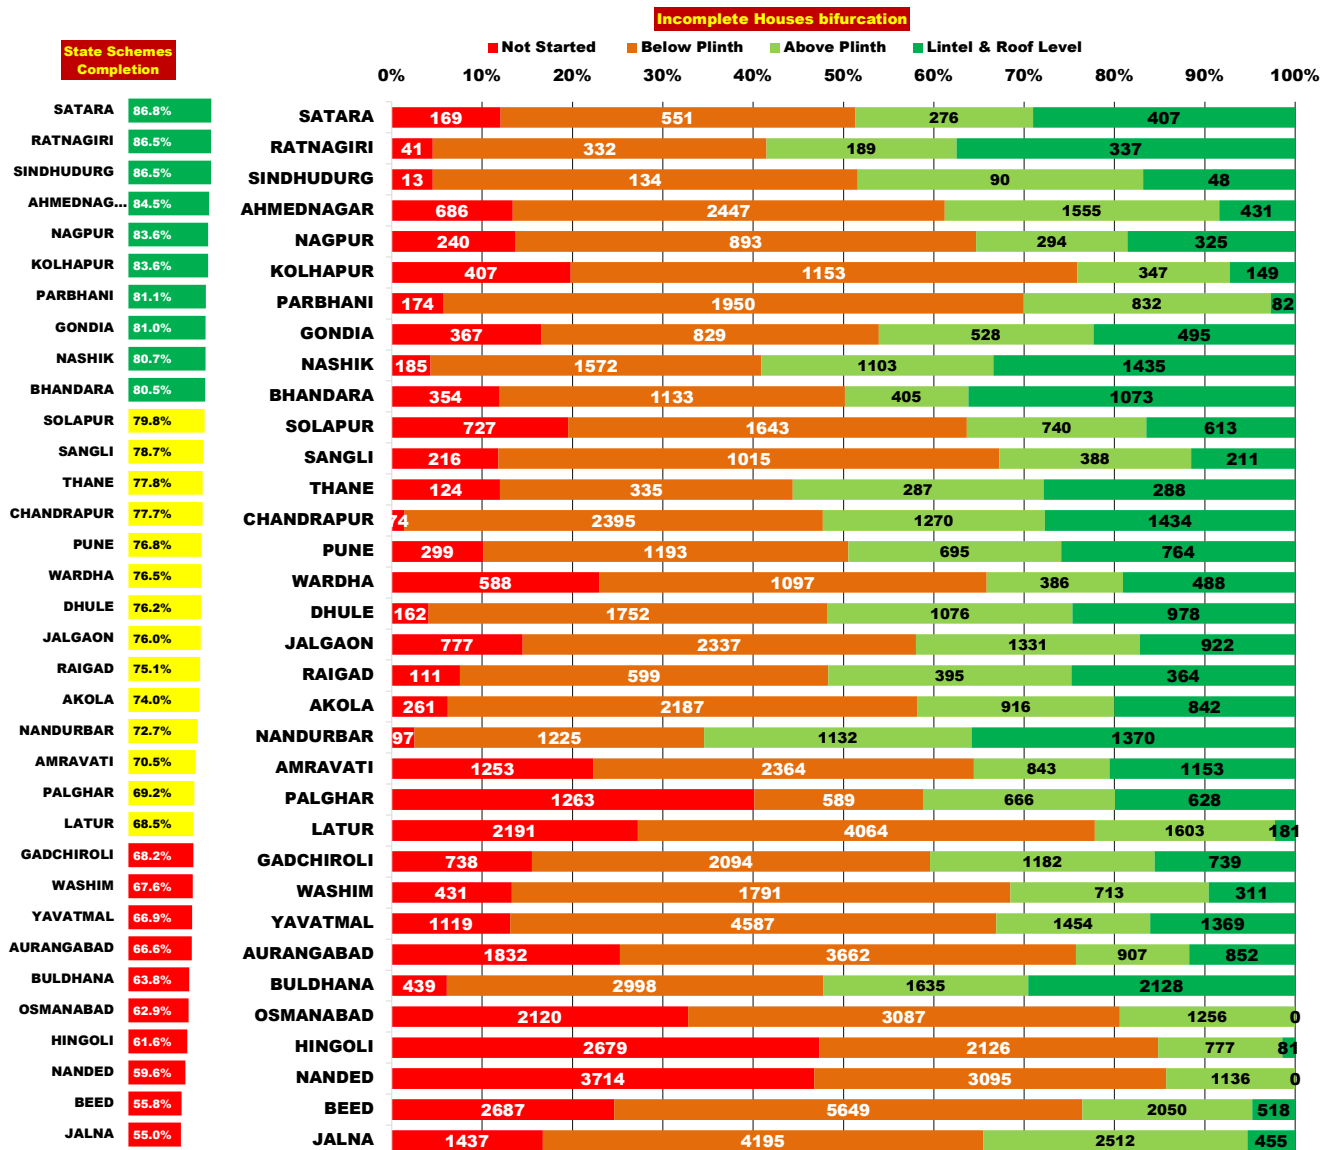

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.03.2023	06.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	CHANDRAPUR	23225	17915	18052	137	5173	14	207
2	AHMEDNAGAR	32969	27769	27850	81	5119	30	205
3	NASHIK	22279	17956	17984	28	4295	12	172
4	BEED	24669	13745	13765	20	10904	14	436
5	PALGHAR	10219	7054	7073	19	3146	6	126
6	JALGAON	22359	16974	16992	18	5367	12	215
7	GADCHIROLI	14963	10195	10210	15	4753	9	190
8	NANDURBAR	13999	10162	10175	13	3824	7	153
9	AMRAVATI	19026	13403	13413	10	5613	9	225
10	LATUR	25484	17435	17445	10	8039	11	322
11	OSMANABAD	16869	10604	10614	10	6255	13	250
12	GONDIA	11670	9442	9451	9	2219	8	89
13	AURANGABAD	21708	14450	14455	5	7253	8	290
14	RAIGAD	5903	4429	4434	5	1469	3	59
15	NANDED	19524	11638	11642	4	7882	10	315
16	DHULE	16704	12733	12736	3	3968	12	159
17	HINGOLI	14747	9081	9084	3	5663	6	227
18	NAGPUR	10686	8931	8934	3	1752	4	70
19	PUNE	12739	9785	9788	3	2951	6	118
20	SANGLI	8595	6762	6765	3	1830	4	73
21	SATARA	10631	9225	9228	3	1403	5	56
22	AKOLA	16169	11962	11963	1	4206	10	168
23	BHANDARA	15172	12206	12207	1	2965	4	119
24	BULDHANA	19888	12687	12688	1	7200	16	288
25	JALNA	19101	10501	10502	1	8599	31	344
26	KOLHAPUR	12528	10471	10472	1	2056	4	82
27	PARBHANI	16112	13073	13074	1	3038	4	122
28	WARDHA	10911	8351	8352	1	2559	7	102
29	WASHIM	10022	6775	6776	1	3246	8	130
30	RATNAGIRI	6678	5779	5779	0	899	2	36
31	SINDHUDURG	2106	1821	1821	0	285	1	11
32	SOLAPUR	18408	14685	14685	0	3723	8	149
33	THANE	4652	3618	3618	0	1034	1	41
34	YAVATMAL	25748	17219	17219	0	8529	13	341
Total		536463	388836	389246	410	147217	310	5889

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19025	0	45068	0	25084
2	AMRAVATI DIV.	0	39281	0	40032	0	13045
3	AURANGABAD DIV.	0	33627	0	61912	0	17225
4	NAGPUR DIV.	0	15477	0	32058	0	13045
5	KONKAN DIV.	0	1138	0	6648	0	6117
6	PUNE DIV.	0	14975	0	19979	0	6350
	Total	0	123523	0	205697	0	80866

PMAY-G 1st Ins Pending

SINDHUDURG	54
RAIGAD	55
THANE	155
RATNAGIRI	181
PALGHAR	693
GADCHIROLI	725
KOLHAPUR	770
SANGLI	1236
SATARA	1436
WARDHA	2082
DHULE	2206
PARBHANI	2400
HINGOLI	2585
NAGPUR	2691
NASHIK	2717
GONDIA	2864
PUNE	3078
JALNA	3333
CHANDRAPUR	3461
AURANGABAD	3584
BHANDARA	3654
AHMEDNAGAR	3789
WASHIM	3893
OSMANABAD	4111
LATUR	4457
NANDURBAR	4505
BEED	4879
AKOLA	5735
JALGAON	5808
YAVATMAL	5908
NANDED	8278
SOLAPUR	8455
BULDHANA	10158
AMRAVATI	13587

PMAY-G 2nd Ins Pending

SINDHUDURG	651
RAIGAD	684
RATNAGIRI	972
THANE	1251
WARDHA	1983
SATARA	2105
PUNE	2753
PALGHAR	3090
KOLHAPUR	3532
OSMANABAD	3792
HINGOLI	3917
NAGPUR	3931
GADCHIROLI	3942
LATUR	4592
SANGLI	5013
AKOLA	5045
WASHIM	5281
AHMEDNAGAR	5300
JALNA	5812
SOLAPUR	6576
CHANDRAPUR	6986
AURANGABAD	7073
BULDHANA	7141
NASHIK	7351
GONDIA	7531
DHULE	7574
PARBHANI	7643
BHANDARA	7685
BEED	9177
AMRAVATI	10085
NANDURBAR	10739
YAVATMAL	12480
JALGAON	14104
NANDED	19906

PMAY-G 3rd Ins Pending

SINDHUDURG	399
RAIGAD	430
WARDHA	576
KOLHAPUR	746
RATNAGIRI	758
THANE	868
NAGPUR	963
OSMANABAD	977
SATARA	978
PUNE	1011
HINGOLI	1151
SANGLI	1389
LATUR	1413
WASHIM	1485
PARBHANI	1580
AKOLA	1749
JALNA	1973
BULDHANA	2183
SOLAPUR	2226
BHANDARA	2504
AURANGABAD	2575
CHANDRAPUR	2711
GADCHIROLI	2913
AMRAVATI	2970
BEED	2980
GONDIA	3378
PALGHAR	3662
DHULE	4214
NASHIK	4391
JALGAON	4432
NANDED	4576
YAVATMAL	4658
AHMEDNAGAR	4698
NANDURBAR	7349

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3789	0	5300	0	4698
2	AKOLA	0	5735	0	5045	0	1749
3	AMRAVATI	0	13587	0	10085	0	2970
4	AURANGABAD	0	3584	0	7073	0	2575
5	BEED	0	4879	0	9177	0	2980
6	BHANDARA	0	3654	0	7685	0	2504
7	BULDHANA	0	10158	0	7141	0	2183
8	CHANDRAPUR	0	3461	0	6986	0	2711
9	DHULE	0	2206	0	7574	0	4214
10	GADCHIROLI	0	725	0	3942	0	2913
11	GONDIA	0	2864	0	7531	0	3378
12	HINGOLI	0	2585	0	3917	0	1151
13	JALGAON	0	5808	0	14104	0	4432
14	JALNA	0	3333	0	5812	0	1973
15	KOLHAPUR	0	770	0	3532	0	746
16	LATUR	0	4457	0	4592	0	1413
17	NAGPUR	0	2691	0	3931	0	963
18	NANDED	0	8278	0	19906	0	4576
19	NANDURBAR	0	4505	0	10739	0	7349
20	NASHIK	0	2717	0	7351	0	4391
21	OSMANABAD	0	4111	0	3792	0	977
22	PALGHAR	0	693	0	3090	0	3662
23	PARBHANI	0	2400	0	7643	0	1580
24	PUNE	0	3078	0	2753	0	1011
25	RAIGAD	0	55	0	684	0	430
26	RATNAGIRI	0	181	0	972	0	758
27	SANGLI	0	1236	0	5013	0	1389
28	SATARA	0	1436	0	2105	0	978
29	SINDHUDURG	0	54	0	651	0	399
30	SOLAPUR	0	8455	0	6576	0	2226
31	THANE	0	155	0	1251	0	868
32	WARDHA	0	2082	0	1983	0	576
33	WASHIM	0	3893	0	5281	0	1485
34	YAVATMAL	0	5908	0	12480	0	4658
	Total	0	123523	0	205697	0	80866

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	1907	0	9333	0	6197
2	AMRAVATI DIV.	0	3503	0	13927	0	5561
3	AURANGABAD DIV.	0	16834	0	27828	0	11073
4	NAGPUR DIV.	0	2361	0	8441	0	4065
5	KONKAN DIV.	0	1552	0	1989	0	1627
6	PUNE DIV.	0	1818	0	5555	0	2446
	Total	0	27975	0	67073	0	30969

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	41
CHANDRAPUR	74
NANDURBAR	97
RAIGAD	111
THANE	124
DHULE	162
SATARA	169
PARBHANI	174
NASHIK	185
SANGLI	216
NAGPUR	240
AKOLA	261
PUNE	299
BHANDARA	354
GONDIA	367
KOLHAPUR	407
WASHIM	431
BULDHANA	439
WARDHA	588
AHMEDNAGAR	686
SOLAPUR	727
GADCHIROLI	738
JALGAON	777
YAVATMAL	1119
AMRAVATI	1253
PALGHAR	1263
JALNA	1437
AURANGABAD	1832
OSMANABAD	2120
LATUR	2191
HINGOLI	2679
BEED	2687
NANDED	3714

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	332
THANE	335
SATARA	551
PALGHAR	589
RAIGAD	599
GONDIA	829
NAGPUR	893
SANGLI	1015
WARDHA	1097
BHANDARA	1133
KOLHAPUR	1153
PUNE	1193
NANDURBAR	1225
NASHIK	1572
SOLAPUR	1643
DHULE	1752
WASHIM	1791
PARBHANI	1950
GADCHIROLI	2094
HINGOLI	2126
AKOLA	2187
JALGAON	2337
AMRAVATI	2364
CHANDRAPUR	2395
AHMEDNAGAR	2447
BULDHANA	2998
OSMANABAD	3087
NANDED	3095
AURANGABAD	3662
LATUR	4064
JALNA	4195
YAVATMAL	4587
BEED	5649

State Schemes 3rd Ins Pending

SINDHUDURG	90
RATNAGIRI	189
SATARA	276
THANE	287
NAGPUR	294
KOLHAPUR	347
WARDHA	386
SANGLI	388
RAIGAD	395
BHANDARA	405
GONDIA	528
PALGHAR	666
PUNE	695
WASHIM	713
SOLAPUR	740
HINGOLI	777
PARBHANI	832
AMRAVATI	843
AURANGABAD	907
AKOLA	916
DHULE	1076
NASHIK	1103
NANDURBAR	1132
NANDED	1136
GADCHIROLI	1182
OSMANABAD	1256
CHANDRAPUR	1270
JALGAON	1331
YAVATMAL	1454
AHMEDNAGAR	1555
LATUR	1603
BULDHANA	1635
BEED	2050
JALNA	2512

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	686	0	2447	0	1555
2	AKOLA	0	261	0	2187	0	916
3	AMRAVATI	0	1253	0	2364	0	843
4	AURANGABAD	0	1832	0	3662	0	907
5	BEED	0	2687	0	5649	0	2050
6	BHANDARA	0	354	0	1133	0	405
7	BULDHANA	0	439	0	2998	0	1635
8	CHANDRAPUR	0	74	0	2395	0	1270
9	DHULE	0	162	0	1752	0	1076
10	GADCHIROLI	0	738	0	2094	0	1182
11	GONDIA	0	367	0	829	0	528
12	HINGOLI	0	2679	0	2126	0	777
13	JALGAON	0	777	0	2337	0	1331
14	JALNA	0	1437	0	4195	0	2512
15	KOLHAPUR	0	407	0	1153	0	347
16	LATUR	0	2191	0	4064	0	1603
17	NAGPUR	0	240	0	893	0	294
18	NANDED	0	3714	0	3095	0	1136
19	NANDURBAR	0	97	0	1225	0	1132
20	NASHIK	0	185	0	1572	0	1103
21	OSMANABAD	0	2120	0	3087	0	1256
22	PALGHAR	0	1263	0	589	0	666
23	PARBHANI	0	174	0	1950	0	832
24	PUNE	0	299	0	1193	0	695
25	RAIGAD	0	111	0	599	0	395
26	RATNAGIRI	0	41	0	332	0	189
27	SANGLI	0	216	0	1015	0	388
28	SATARA	0	169	0	551	0	276
29	SINDHUDURG	0	13	0	134	0	90
30	SOLAPUR	0	727	0	1643	0	740
31	THANE	0	124	0	335	0	287
32	WARDHA	0	588	0	1097	0	386
33	WASHIM	0	431	0	1791	0	713
34	YAVATMAL	0	1119	0	4587	0	1454
	Total	0	27975	0	67073	0	30969
