



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०७.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१४५७२	८९	९९३३९२	११४८	०	०	०
राज्य योजना	५३६८६५	४०३	३८९६३०	३८४	०	०	०
एकूण	१९५१४३७	४९२	१३८३०२२	१५३२	०	०	०

PMAY-G Completion Progress Bar

70.2%


PMAY-G: Incomplete Houses bifurcation

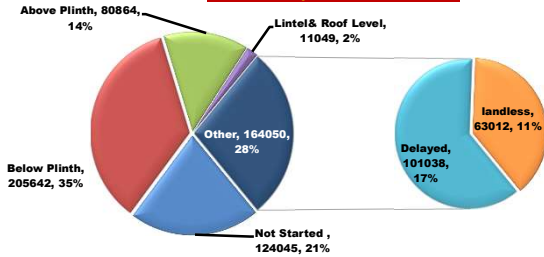


State Schemes Progress Bar

72.6%

State Schemes: Incomplete Houses bifurcation




Delayed Houses Bifurcation

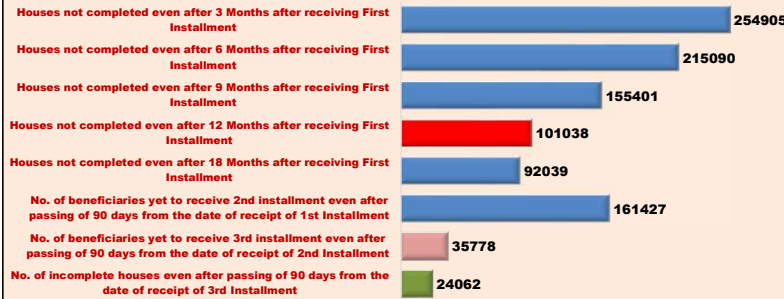


Abhiyan Achievement


Day 107

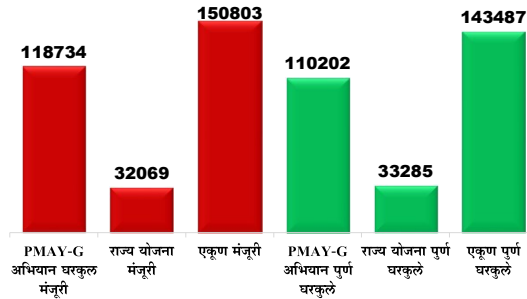

PMAY-G : House completion ( Abhiyan Achievement)

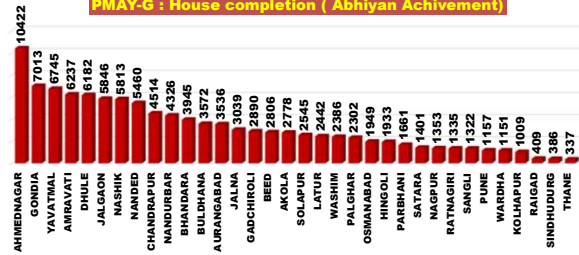

State Schemes : House completion ( Abhiyan Achievement)

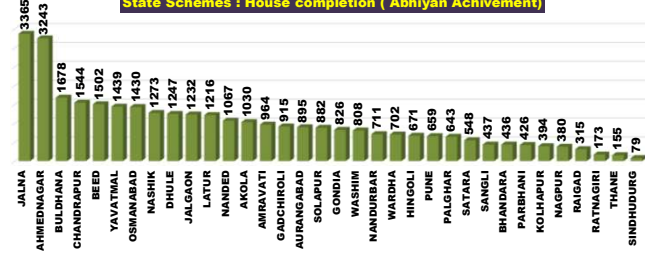


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	06.03.2023	07.03.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	238346	237912	237952	40	394
2	PUNE DIV.	126676	126388	126383	36	293
3	AMRAVATI DIV.	274989	274674	274682	8	307
4	NASHIK DIV.	414632	413906	413906	3	726
5	NAGPUR DIV.	292532	291986	291988	2	544
6	KONKAN DIV.	69687	69661	69661	0	26
<b>Total</b>		<b>1416862</b>	<b>1414527</b>	<b>1414572</b>	<b>89</b>	<b>2290</b>

PMAY-G Remaining Sanction

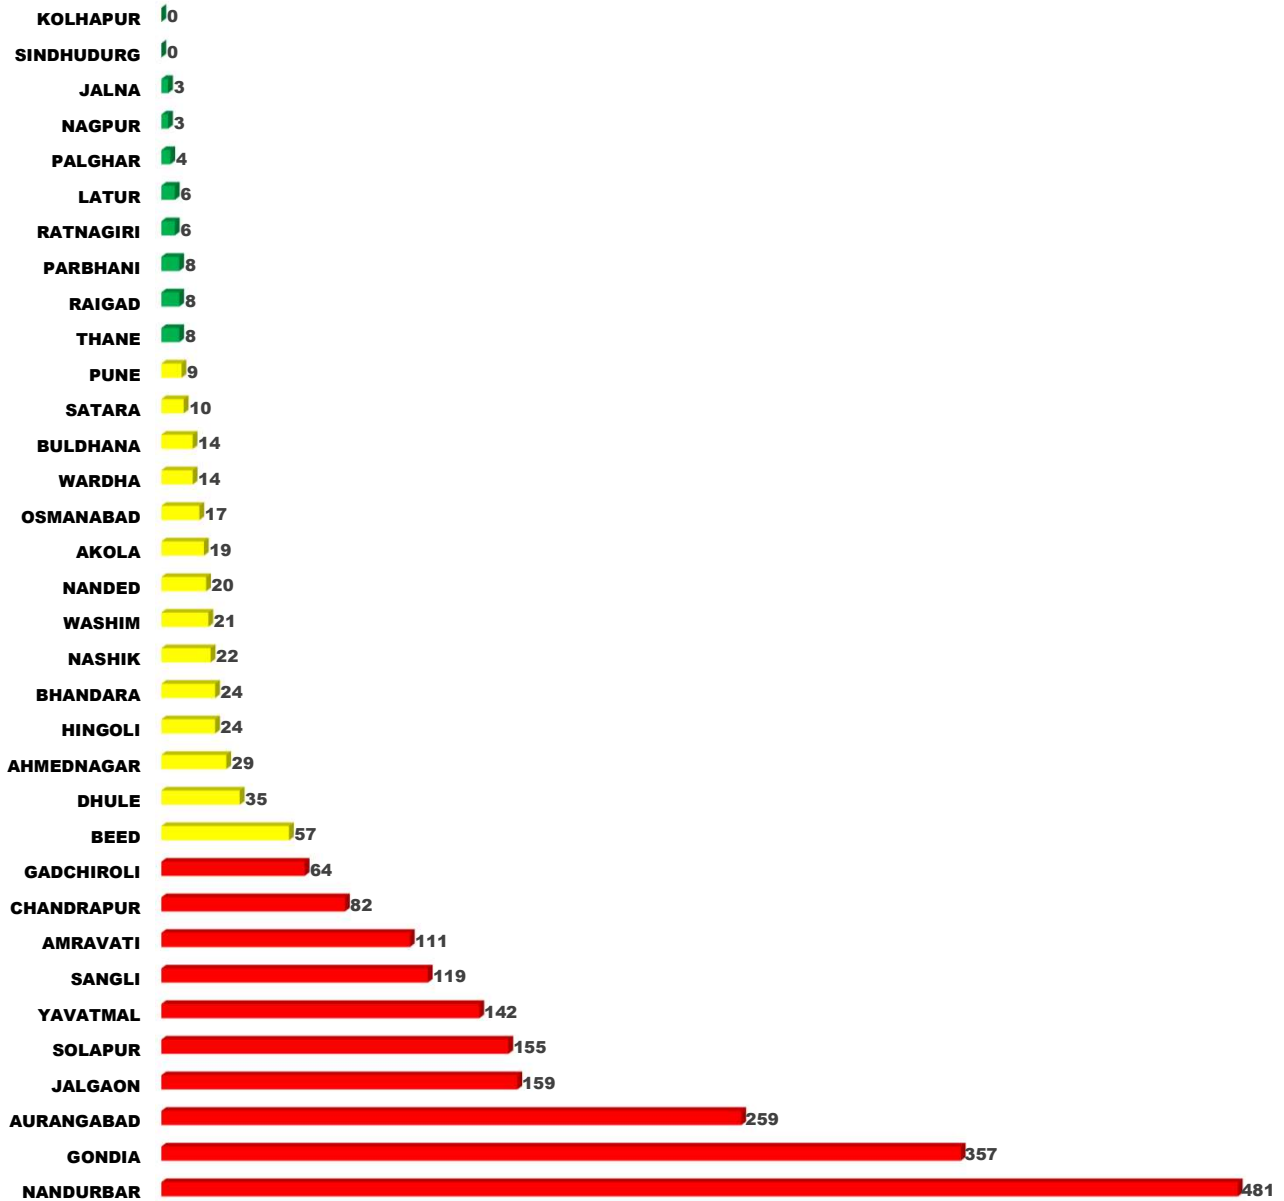


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	06.03.2023	07.03.2023	Daily_Achievement	Remaining
1	AURANGABAD	36792	36493	36533	40	259
2	SOLAPUR	50158	49968	50003	35	155
3	AMRAVATI	95646	95527	95535	8	111
4	NASHIK	89787	89762	89765	3	22
5	WARDHA	18671	18655	18657	2	14
6	PUNE	21034	21024	21025	1	9
7	AKOLA	48794	48775	48775	0	19
8	BEED	35324	35267	35267	0	57
9	BHANDARA	65131	65107	65107	0	24
10	BULDHANA	44742	44728	44728	0	14
11	CHANDRAPUR	43286	43204	43204	0	82
12	DHULE	64912	64877	64877	0	35
13	GADCHIROLI	31639	31575	31575	0	64
14	GONDIA	96474	96117	96117	0	357
15	HINGOLI	18107	18083	18083	0	24
16	JALGAON	79791	79632	79632	0	159
17	JALNA	24047	24044	24044	0	3
18	KOLHAPUR	17770	17770	17770	0	0
19	LATUR	20799	20793	20793	0	6
20	NAGPUR	37331	37328	37328	0	3
21	NANDED	69588	69568	69568	0	20
22	NANDURBAR	119349	118868	118868	0	481
23	OSMANABAD	14583	14566	14566	0	17
24	PALGHAR	35152	35148	35148	0	4
25	PARBHANI	19106	19098	19098	0	8
26	RAIGAD	9847	9839	9839	0	8
27	RATNAGIRI	9926	9920	9920	0	6
28	SINDHUDURG	5156	5156	5156	0	0
29	THANE	9606	9598	9598	0	8
30	WASHIM	20416	20395	20395	0	21
31	YAVATMAL	65391	65249	65249	0	142
32	AHMEDNAGAR	60793	60767	60764	-3	29
33	SATARA	15541	15540	15531	-9	10
34	SANGLI	22173	22086	22054	-32	119
<b>Total</b>		<b>1416862</b>	<b>1414527</b>	<b>1414572</b>	<b>89</b>	<b>2290</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	06.03.2023	07.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI DIV.	274682	178588	178875	287	95807	203	3992
2	NAGPUR DIV.	291988	228753	228994	241	62994	195	2625
3	NASHIK DIV.	413906	315898	316103	205	97803	305	4075
4	AURANGABAD DIV.	237952	130184	130387	203	107565	213	4482
5	PUNE DIV.	126383	84737	84856	119	41527	69	1730
6	KONKAN DIV.	69661	54084	54177	93	15484	45	645
<b>Total</b>		<b>1414572</b>	<b>992244</b>	<b>993392</b>	<b>1148</b>	<b>421180</b>	<b>1030</b>	<b>17549</b>

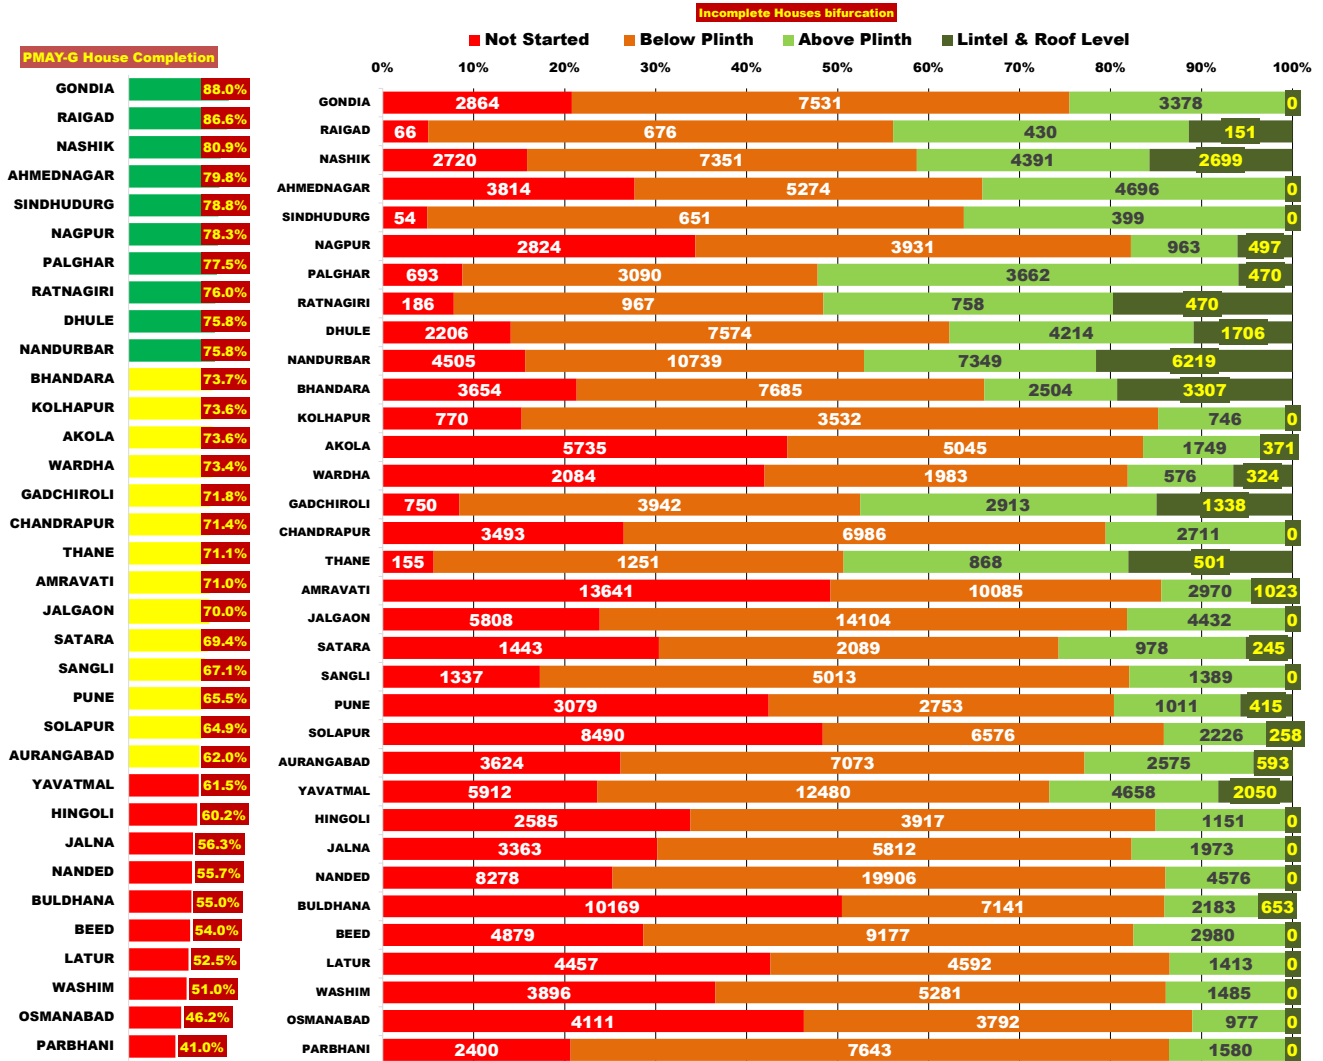


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	06.03.2023	07.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	BULDHANA	44728	24498	24593	95	20135	33	839
2	AHMEDNAGAR	60764	48417	48502	85	12262	97	511
3	CHANDRAPUR	43204	30774	30853	79	12351	42	515
4	AMRAVATI	95535	67790	67862	72	27673	58	1153
5	GONDIA	96117	84521	84591	70	11526	66	480
6	YAVATMAL	65249	40088	40153	65	25096	63	1046
7	JALNA	24044	13488	13545	57	10499	28	437
8	NASHIK	89765	72552	72604	52	17161	54	715
9	NANDED	69568	38725	38770	45	30798	51	1283
10	SATARA	15531	10735	10776	41	4755	13	198
11	NANDURBAR	118868	90016	90056	40	28812	40	1201
12	PUNE	21025	13727	13767	40	7258	11	302
13	GADCHIROLI	31575	22618	22657	39	8918	27	372
14	WASHIM	20395	10353	10392	39	10003	22	417
15	PALGHAR	35148	27198	27233	35	7915	22	330
16	AURANGABAD	36533	22634	22668	34	13865	33	578
17	NAGPUR	37328	29217	29246	29	8082	13	337
18	JALGAON	79632	55736	55764	28	23868	55	995
19	BEED	35267	19007	19034	27	16233	26	676
20	WARDHA	18657	13666	13690	24	4967	11	207
21	SINDHUDURG	5156	4043	4063	20	1093	4	46
22	THANE	9598	6803	6823	20	2775	3	116
23	SOLAPUR	50003	32434	32453	19	17550	24	731
24	AKOLA	48775	35859	35875	16	12900	26	538
25	LATUR	20793	10900	10916	16	9877	23	412
26	RATNAGIRI	9920	7523	7539	16	2381	12	99
27	SANGLI	22054	14773	14789	16	7265	12	303
28	HINGOLI	18083	10880	10891	11	7192	18	300
29	PARBHANI	19098	7827	7834	7	11264	16	469
30	OSMANABAD	14566	6723	6729	6	7837	18	327
31	KOLHAPUR	17770	13068	13071	3	4699	9	196
32	RAIGAD	9839	8517	8519	2	1320	4	55
33	BHANDARA	65107	47957	47957	0	17150	37	715
34	DHULE	64877	49177	49177	0	15700	58	654
Total		1414572	992244	993392	1148	421180	1030	17549

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	06.03.2023	07.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	158214	158506	292	40825
2	NASHIK DIV.	141360	108310	108404	94	32956
3	PUNE DIV.	65334	62901	62911	10	2423
4	NAGPUR DIV.	116255	86627	86632	5	29623
5	AMRAVATI DIV.	109702	90853	90854	2	18848
6	KONKAN DIV.	34729	29558	29558	0	5171
	<b>Total</b>	<b>666711</b>	<b>536463</b>	<b>536865</b>	<b>403</b>	<b>129846</b>

State Scheme Remaining Sanction

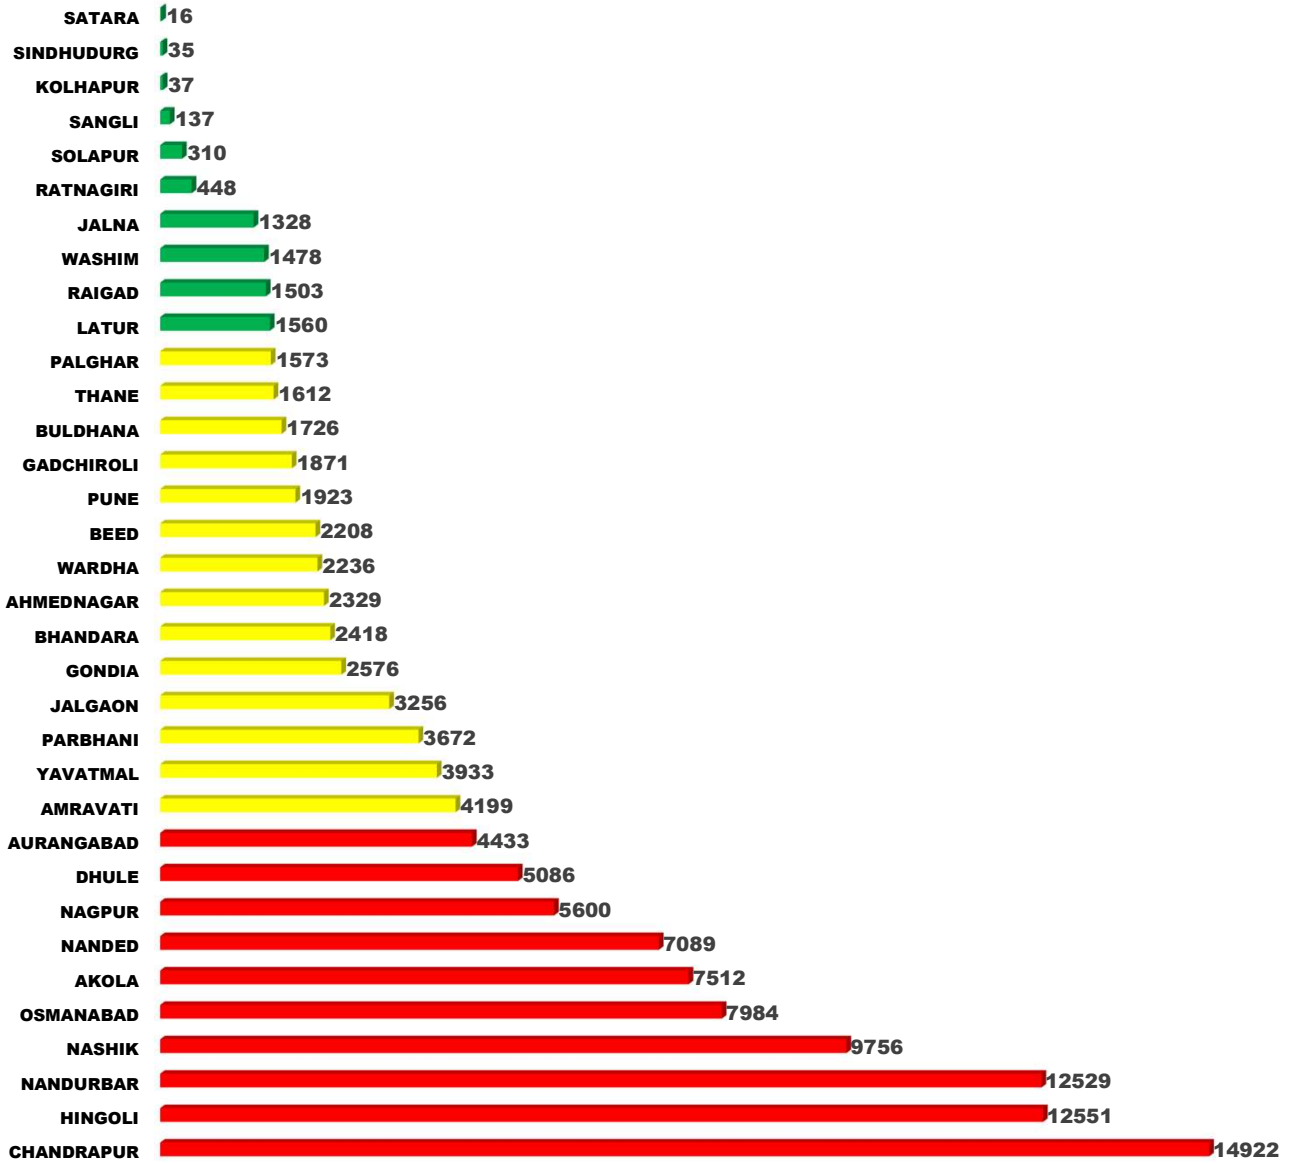


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	06.03.2023	07.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19524	19671	147	7089
2	LATUR	27171	25484	25611	127	1560
3	NANDURBAR	26578	13999	14049	50	12529
4	JALGAON	25659	22359	22403	44	3256
5	JALNA	20446	19101	19118	17	1328
6	PUNE	14672	12739	12749	10	1923
7	NAGPUR	16291	10686	10691	5	5600
8	BULDHANA	21616	19888	19890	2	1726
9	BEED	26878	24669	24670	1	2208
10	AHMEDNAGAR	35298	32969	32969	0	2329
11	AKOLA	23681	16169	16169	0	7512
12	AURANGABAD	26141	21708	21708	0	4433
13	BHANDARA	17590	15172	15172	0	2418
14	CHANDRAPUR	38147	23225	23225	0	14922
15	DHULE	21790	16704	16704	0	5086
16	GADCHIROLI	16834	14963	14963	0	1871
17	GONDIA	14246	11670	11670	0	2576
18	HINGOLI	27298	14747	14747	0	12551
19	KOLHAPUR	12565	12528	12528	0	37
20	NASHIK	32035	22279	22279	0	9756
21	OSMANABAD	24853	16869	16869	0	7984
22	PALGHAR	11792	10219	10219	0	1573
23	PARBHANI	19784	16112	16112	0	3672
24	RAIGAD	7406	5903	5903	0	1503
25	RATNAGIRI	7126	6678	6678	0	448
26	SANGLI	8732	8595	8595	0	137
27	SATARA	10647	10631	10631	0	16
28	SINDHUDURG	2141	2106	2106	0	35
29	SOLAPUR	18718	18408	18408	0	310
30	THANE	6264	4652	4652	0	1612
31	WARDHA	13147	10911	10911	0	2236
32	WASHIM	11500	10022	10022	0	1478
33	YAVATMAL	29681	25748	25748	0	3933
34	AMRAVATI	23224	19026	19025	-1	4199
<b>Total</b>		<b>666711</b>	<b>536463</b>	<b>536865</b>	<b>403</b>	<b>129846</b>



## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	06.03.2023	07.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	<b>NAGPUR DIV.</b>	<b>86632</b>	<b>67206</b>	<b>67348</b>	<b>142</b>	<b>19284</b>	<b>45</b>	<b>804</b>
2	<b>AURANGABAD DIV.</b>	<b>158506</b>	<b>100581</b>	<b>100678</b>	<b>97</b>	<b>57828</b>	<b>99</b>	<b>2410</b>
3	<b>AMRAVATI DIV.</b>	<b>90854</b>	<b>62059</b>	<b>62117</b>	<b>58</b>	<b>28737</b>	<b>55</b>	<b>1197</b>
4	<b>PUNE DIV.</b>	<b>62911</b>	<b>50938</b>	<b>50985</b>	<b>47</b>	<b>11926</b>	<b>27</b>	<b>497</b>
5	<b>NASHIK DIV.</b>	<b>108404</b>	<b>85737</b>	<b>85763</b>	<b>26</b>	<b>22641</b>	<b>72</b>	<b>943</b>
6	<b>KONKAN DIV.</b>	<b>29558</b>	<b>22725</b>	<b>22739</b>	<b>14</b>	<b>6819</b>	<b>13</b>	<b>284</b>
<b>Total</b>		<b>536865</b>	<b>389246</b>	<b>389630</b>	<b>384</b>	<b>147235</b>	<b>311</b>	<b>6135</b>

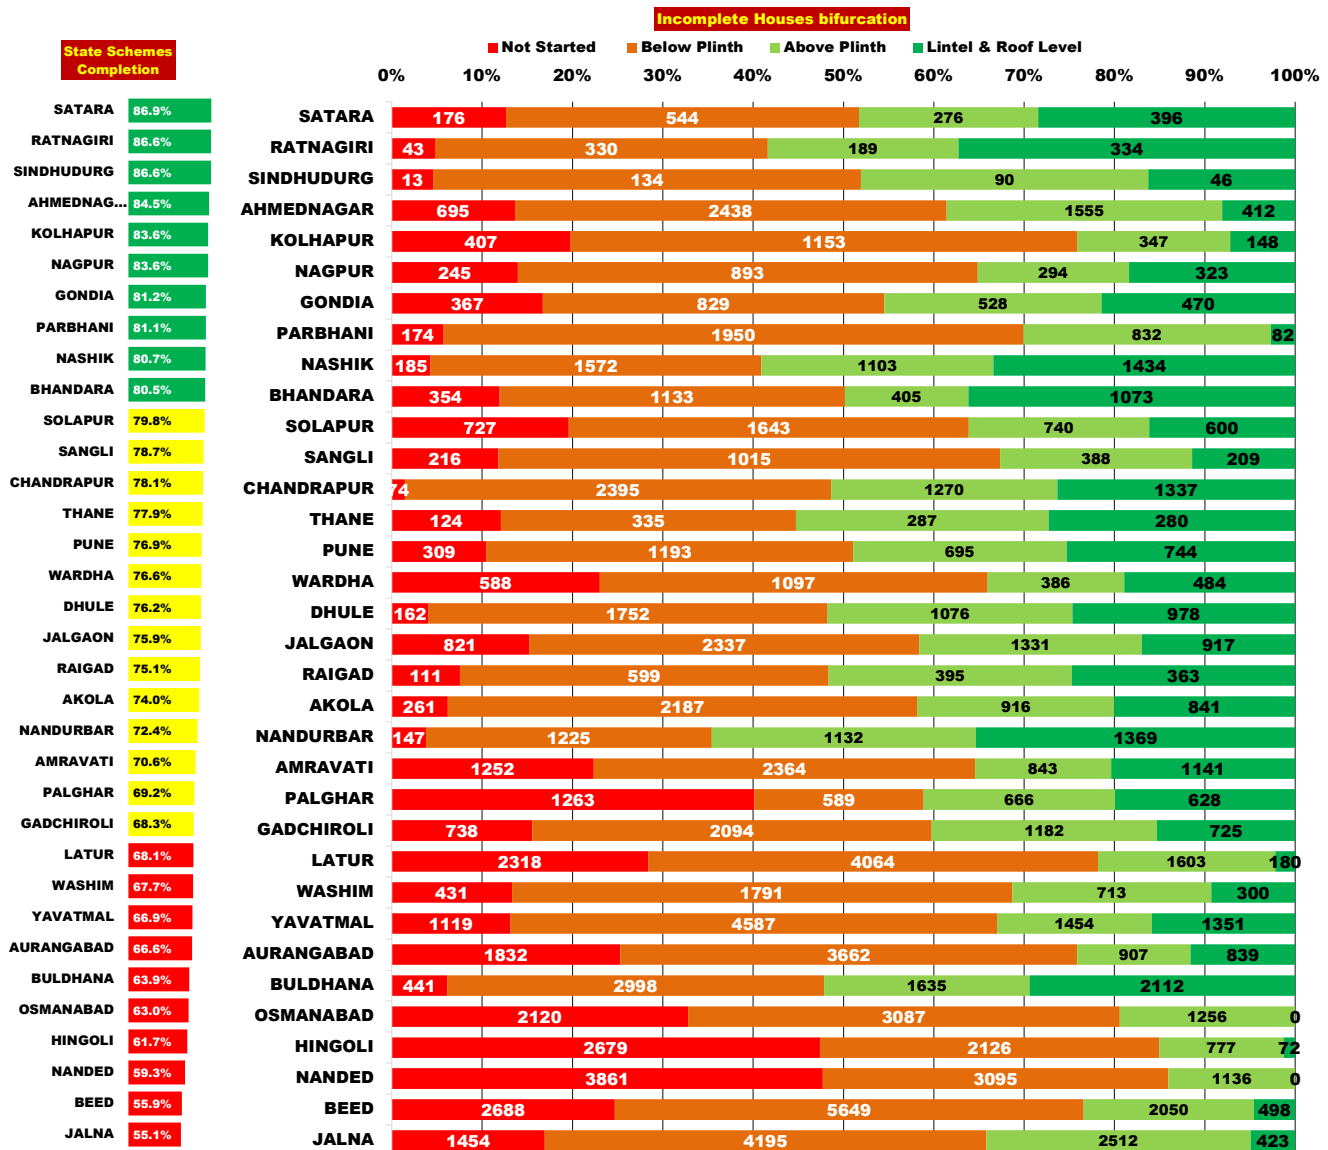

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	06.03.2023	07.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	CHANDRAPUR	23225	18052	18149	97	5076	14	212
2	JALNA	19118	10502	10534	32	8584	31	358
3	GONDIA	11670	9451	9476	25	2194	8	91
4	BEED	24670	13765	13785	20	10885	14	454
5	PUNE	12749	9788	9808	20	2941	6	123
6	AHMEDNAGAR	32969	27850	27869	19	5100	30	213
7	YAVATMAL	25748	17219	17237	18	8511	13	355
8	BULDHANA	19890	12688	12704	16	7186	16	299
9	GADCHIROLI	14963	10210	10224	14	4739	9	197
10	NANDED	19671	11642	11656	14	8015	10	334
11	AURANGABAD	21708	14455	14468	13	7240	8	302
12	SOLAPUR	18408	14685	14698	13	3710	8	155
13	AMRAVATI	19025	13413	13425	12	5600	9	233
14	SATARA	10631	9228	9239	11	1392	5	58
15	WASHIM	10022	6776	6787	11	3235	8	135
16	HINGOLI	14747	9084	9093	9	5654	6	236
17	OSMANABAD	16869	10614	10622	8	6247	13	260
18	THANE	4652	3618	3626	8	1026	1	43
19	JALGAON	22403	16992	16997	5	5406	12	225
20	WARDHA	10911	8352	8356	4	2555	7	106
21	RATNAGIRI	6678	5779	5782	3	896	2	37
22	NAGPUR	10691	8934	8936	2	1755	4	73
23	SANGLI	8595	6765	6767	2	1828	4	76
24	SINDHUDURG	2106	1821	1823	2	283	1	12
25	AKOLA	16169	11963	11964	1	4205	10	175
26	KOLHAPUR	12528	10472	10473	1	2055	4	86
27	LATUR	25611	17445	17446	1	8165	11	340
28	NANDURBAR	14049	10175	10176	1	3873	7	161
29	NASHIK	22279	17984	17985	1	4294	12	179
30	RAIGAD	5903	4434	4435	1	1468	3	61
31	BHANDARA	15172	12207	12207	0	2965	4	124
32	DHULE	16704	12736	12736	0	3968	12	165
33	PALGHAR	10219	7073	7073	0	3146	6	131
34	PARBHANI	16112	13074	13074	0	3038	4	127
<b>Total</b>		<b>536865</b>	<b>389246</b>	<b>389630</b>	<b>384</b>	<b>147235</b>	<b>311</b>	<b>6135</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19053	0	45042	0	25082
2	AMRAVATI DIV.	0	39289	0	40032	0	13045
3	AURANGABAD DIV.	0	33667	0	61912	0	17225
4	NAGPUR DIV.	0	15479	0	32058	0	13045
5	KONKAN DIV.	0	1151	0	6635	0	6117
6	PUNE DIV.	0	14986	0	19963	0	6350
	<b>Total</b>	<b>0</b>	<b>123625</b>	<b>0</b>	<b>205642</b>	<b>0</b>	<b>80864</b>

PMAY-G 1st Ins Pending

SINDHUDURG	54
RAIGAD	63
THANE	155
RATNAGIRI	186
PALGHAR	693
GADCHIROLI	725
KOLHAPUR	770
SANGLI	1204
SATARA	1443
WARDHA	2084
DHULE	2206
PARBHANI	2400
HINGOLI	2585
NAGPUR	2691
NASHIK	2720
GONDIA	2864
PUNE	3079
JALNA	3333
CHANDRAPUR	3461
AURANGABAD	3624
BHANDARA	3654
AHMEDNAGAR	3814
WASHIM	3893
OSMANABAD	4111
LATUR	4457
NANDURBAR	4505
BEED	4879
AKOLA	5735
JALGAON	5808
YAVATMAL	5908
NANDED	8278
SOLAPUR	8490
BULDHANA	10158
AMRAVATI	13595

PMAY-G 2nd Ins Pending

SINDHUDURG	651
RAIGAD	676
RATNAGIRI	967
THANE	1251
WARDHA	1983
SATARA	2089
PUNE	2753
PALGHAR	3090
KOLHAPUR	3532
OSMANABAD	3792
HINGOLI	3917
NAGPUR	3931
GADCHIROLI	3942
LATUR	4592
SANGLI	5013
AKOLA	5045
AHMEDNAGAR	5274
WASHIM	5281
JALNA	5812
SOLAPUR	6576
CHANDRAPUR	6986
AURANGABAD	7073
BULDHANA	7141
NASHIK	7351
GONDIA	7531
DHULE	7574
PARBHANI	7643
BHANDARA	7685
BEED	9177
AMRAVATI	10085
NANDURBAR	10739
YAVATMAL	12480
JALGAON	14104
NANDED	19906

PMAY-G 3rd Ins Pending

SINDHUDURG	399
RAIGAD	430
WARDHA	576
KOLHAPUR	746
RATNAGIRI	758
THANE	868
NAGPUR	963
OSMANABAD	977
SATARA	978
PUNE	1011
HINGOLI	1151
SANGLI	1389
LATUR	1413
WASHIM	1485
PARBHANI	1580
AKOLA	1749
JALNA	1973
BULDHANA	2183
SOLAPUR	2226
BHANDARA	2504
AURANGABAD	2575
CHANDRAPUR	2711
GADCHIROLI	2913
AMRAVATI	2970
BEED	2980
GONDIA	3378
PALGHAR	3662
DHULE	4214
NASHIK	4391
JALGAON	4432
NANDED	4576
YAVATMAL	4658
AHMEDNAGAR	4696
NANDURBAR	7349

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AKOLA	0	5735	0	5045	0	1749
2	AMRAVATI	0	13595	0	10085	0	2970
3	AURANGABAD	0	3624	0	7073	0	2575
4	BEED	0	4879	0	9177	0	2980
5	BHANDARA	0	3654	0	7685	0	2504
6	BULDHANA	0	10158	0	7141	0	2183
7	CHANDRAPUR	0	3461	0	6986	0	2711
8	DHULE	0	2206	0	7574	0	4214
9	GADCHIROLI	0	725	0	3942	0	2913
10	GONDIA	0	2864	0	7531	0	3378
11	HINGOLI	0	2585	0	3917	0	1151
12	JALGAON	0	5808	0	14104	0	4432
13	JALNA	0	3333	0	5812	0	1973
14	KOLHAPUR	0	770	0	3532	0	746
15	LATUR	0	4457	0	4592	0	1413
16	NAGPUR	0	2691	0	3931	0	963
17	NANDED	0	8278	0	19906	0	4576
18	NANDURBAR	0	4505	0	10739	0	7349
19	NASHIK	0	2720	0	7351	0	4391
20	OSMANABAD	0	4111	0	3792	0	977
21	PALGHAR	0	693	0	3090	0	3662
22	PARBHANI	0	2400	0	7643	0	1580
23	PUNE	0	3079	0	2753	0	1011
24	SANGLI	0	1204	0	5013	0	1389
25	SINDHUDURG	0	54	0	651	0	399
26	SOLAPUR	0	8490	0	6576	0	2226
27	THANE	0	155	0	1251	0	868
28	WARDHA	0	2084	0	1983	0	576
29	WASHIM	0	3893	0	5281	0	1485
30	YAVATMAL	0	5908	0	12480	0	4658
31	RATNAGIRI	-5	186	0	967	0	758
32	RAIGAD	-8	63	0	676	0	430
33	SATARA	-16	1443	0	2089	0	978
34	AHMEDNAGAR	-28	3814	-2	5274	0	4696
	<b>Total</b>	<b>0</b>	<b>123625</b>	<b>0</b>	<b>205642</b>	<b>0</b>	<b>80864</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2010	0	9324	0	6197
2	AMRAVATI DIV.	0	3504	0	13927	0	5561
3	AURANGABAD DIV.	0	17126	0	27828	0	11073
4	NAGPUR DIV.	0	2366	0	8441	0	4065
5	KONKAN DIV.	0	1554	0	1987	0	1627
6	PUNE DIV.	0	1835	0	5548	0	2446
	<b>Total</b>	<b>0</b>	<b>28395</b>	<b>0</b>	<b>67055</b>	<b>0</b>	<b>30969</b>

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	43
CHANDRAPUR	74
RAIGAD	111
THANE	124
NANDURBAR	147
DHULE	162
PARBHANI	174
SATARA	176
NASHIK	185
SANGLI	216
NAGPUR	245
AKOLA	261
PUNE	309
BHANDARA	354
GONDIA	367
KOLHAPUR	407
WASHIM	431
BULDHANA	441
WARDHA	588
AHMEDNAGAR	695
SOLAPUR	727
GADCHIROLI	738
JALGAON	821
YAVATMAL	1119
AMRAVATI	1252
PALGHAR	1263
JALNA	1454
AURANGABAD	1832
OSMANABAD	2120
LATUR	2318
HINGOLI	2679
BEED	2688
NANDED	3861

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	330
THANE	335
SATARA	544
PALGHAR	589
RAIGAD	599
GONDIA	829
NAGPUR	893
SANGLI	1015
WARDHA	1097
BHANDARA	1133
KOLHAPUR	1153
PUNE	1193
NANDURBAR	1225
NASHIK	1572
SOLAPUR	1643
DHULE	1752
WASHIM	1791
PARBHANI	1950
GADCHIROLI	2094
HINGOLI	2126
AKOLA	2187
JALGAON	2337
AMRAVATI	2364
CHANDRAPUR	2395
AHMEDNAGAR	2438
BULDHANA	2998
OSMANABAD	3087
NANDED	3095
AURANGABAD	3662
LATUR	4064
JALNA	4195
YAVATMAL	4587
BEED	5649

State Schemes 3rd Ins Pending

SINDHUDURG	90
RATNAGIRI	189
SATARA	276
THANE	287
NAGPUR	294
KOLHAPUR	347
WARDHA	386
SANGLI	388
RAIGAD	395
BHANDARA	405
GONDIA	528
PALGHAR	666
PUNE	695
WASHIM	713
SOLAPUR	740
HINGOLI	777
PARBHANI	832
AMRAVATI	843
AURANGABAD	907
AKOLA	916
DHULE	1076
NASHIK	1103
NANDURBAR	1132
NANDED	1136
GADCHIROLI	1182
OSMANABAD	1256
CHANDRAPUR	1270
JALGAON	1331
YAVATMAL	1454
AHMEDNAGAR	1555
LATUR	1603
BULDHANA	1635
BEED	2050
JALNA	2512

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	261	0	2187	0	916
2	AMRAVATI	0	1252	0	2364	0	843
3	AURANGABAD	0	1832	0	3662	0	907
4	BEED	0	2688	0	5649	0	2050
5	BHANDARA	0	354	0	1133	0	405
6	BULDHANA	0	441	0	2998	0	1635
7	CHANDRAPUR	0	74	0	2395	0	1270
8	DHULE	0	162	0	1752	0	1076
9	GADCHIROLI	0	738	0	2094	0	1182
10	GONDIA	0	367	0	829	0	528
11	HINGOLI	0	2679	0	2126	0	777
12	JALGAON	0	821	0	2337	0	1331
13	JALNA	0	1454	0	4195	0	2512
14	KOLHAPUR	0	407	0	1153	0	347
15	LATUR	0	2318	0	4064	0	1603
16	NAGPUR	0	245	0	893	0	294
17	NANDED	0	3861	0	3095	0	1136
18	NANDURBAR	0	147	0	1225	0	1132
19	NASHIK	0	185	0	1572	0	1103
20	OSMANABAD	0	2120	0	3087	0	1256
21	PALGHAR	0	1263	0	589	0	666
22	PARBHANI	0	174	0	1950	0	832
23	PUNE	0	309	0	1193	0	695
24	RAIGAD	0	111	0	599	0	395
25	SANGLI	0	216	0	1015	0	388
26	SINDHUDURG	0	13	0	134	0	90
27	SOLAPUR	0	727	0	1643	0	740
28	THANE	0	124	0	335	0	287
29	WARDHA	0	588	0	1097	0	386
30	WASHIM	0	431	0	1791	0	713
31	YAVATMAL	0	1119	0	4587	0	1454
32	RATNAGIRI	-2	43	0	330	0	189
33	SATARA	-7	176	0	544	0	276
34	AHMEDNAGAR	-9	695	0	2438	0	1555
	<b>Total</b>	<b>0</b>	<b>28395</b>	<b>0</b>	<b>67055</b>	<b>0</b>	<b>30969</b>
