



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०८.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१४५७३	१७	९९३५०३	१११	०	०	०
राज्य योजना	५३६९६८	१०३	३८९६६९	३९	०	०	०
एकूण	१९५१५४१	१२०	१३८३१७२	१५०	०	०	०

PMAY-G Completion Progress Bar

70.2%


PMAY-G: Incomplete Houses bifurcation

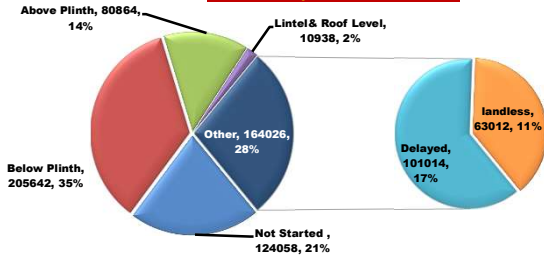


State Schemes Progress Bar

72.6%

State Schemes: Incomplete Houses bifurcation




Delayed Houses Bifurcation

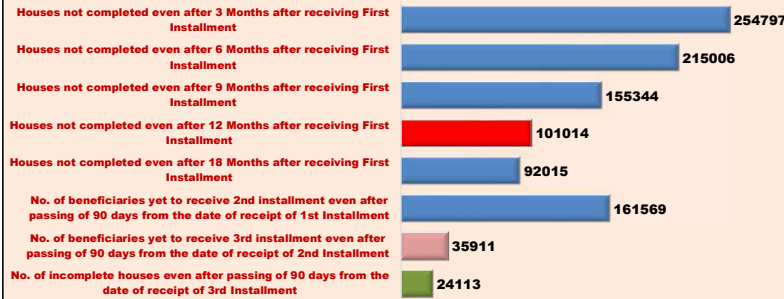


Abhiyan Achievement


Day 108

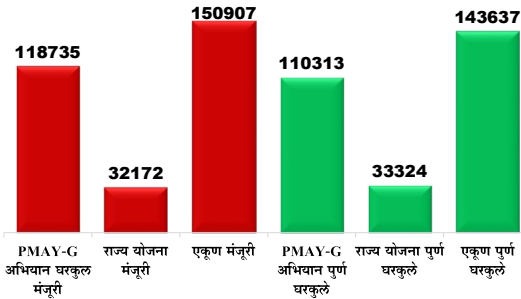

PMAY-G : House completion (Abhiyan Achievement)

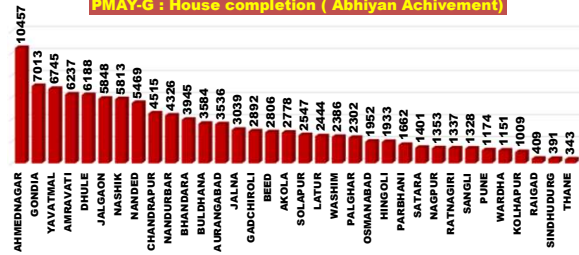

State Schemes : House completion (Abhiyan Achievement)

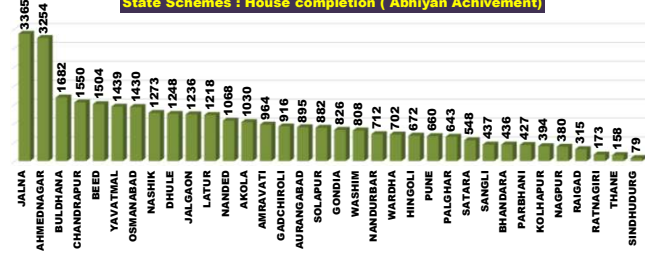


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.



State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	07.03.2023	08.03.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	238346	237952	237969	17	377
2	NASHIK DIV.	414632	413906	413906	0	726
3	AMRAVATI DIV.	274989	274682	274682	0	307
4	NAGPUR DIV.	292520	291988	291976	0	544
5	KONKAN DIV.	69687	69661	69661	0	26
6	PUNE DIV.	126664	126383	126379	0	285
	Total	1416838	1414572	1414573	17	2265

PMAY-G Remaining Sanction

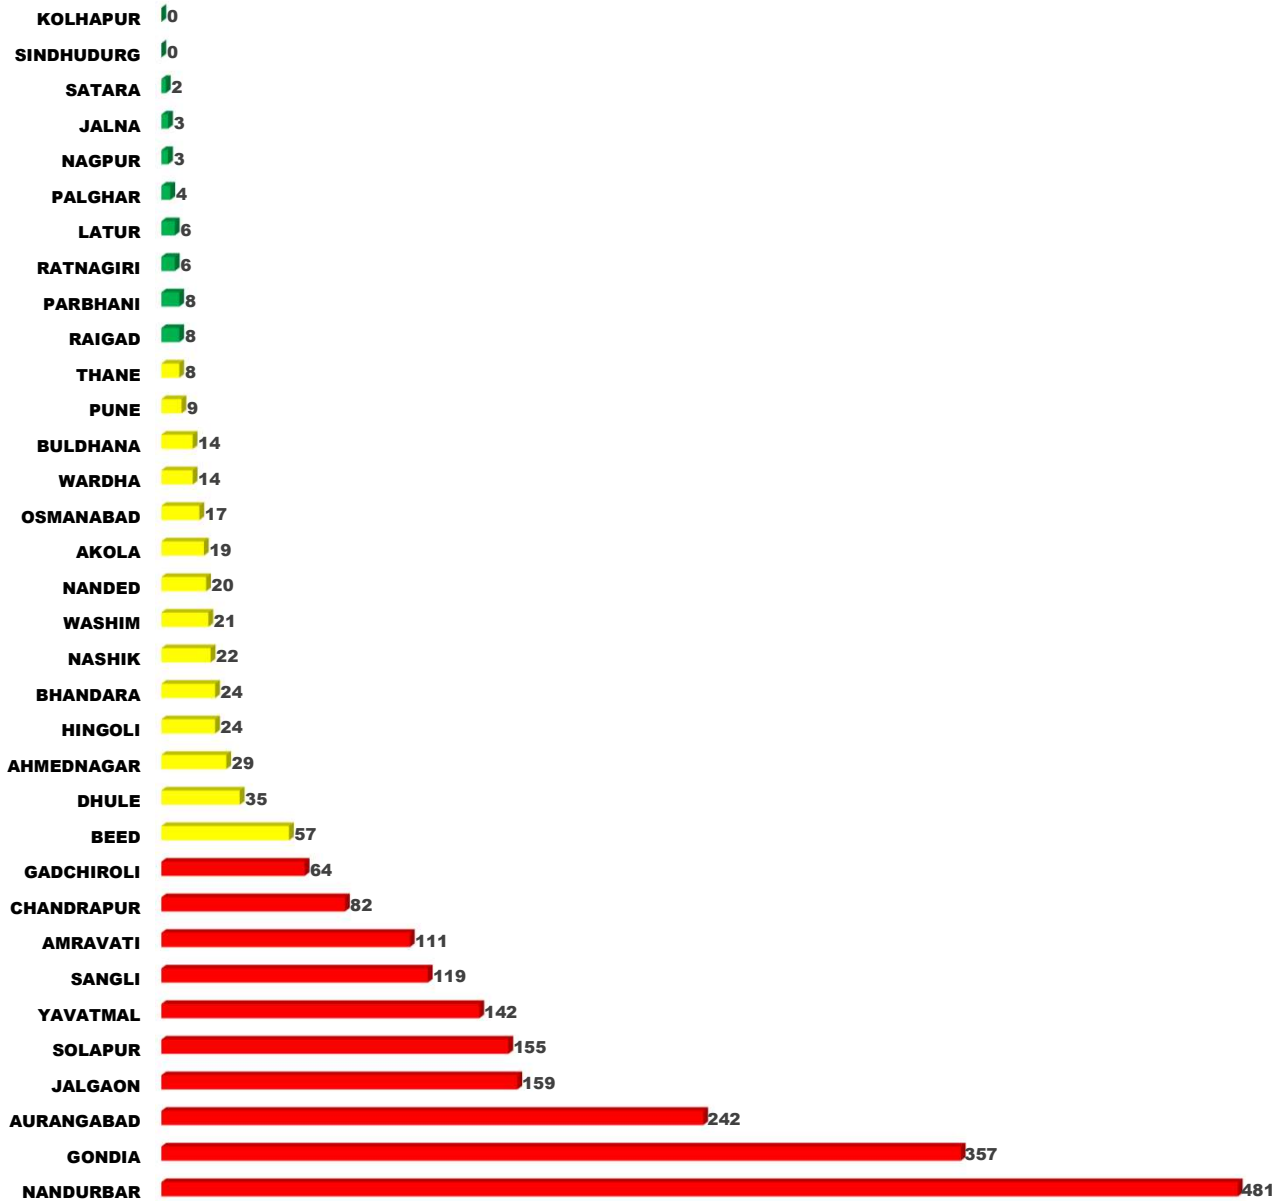


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	07.03.2023	08.03.2023	Daily_Achievement	Remaining
1	AURANGABAD	36792	36533	36550	17	242
2	AHMEDNAGAR	60793	60764	60764	0	29
3	AKOLA	48794	48775	48775	0	19
4	AMRAVATI	95646	95535	95535	0	111
5	BEED	35324	35267	35267	0	57
6	BHANDARA	65131	65107	65107	0	24
7	BULDHANA	44742	44728	44728	0	14
8	DHULE	64912	64877	64877	0	35
9	GADCHIROLI	31639	31575	31575	0	64
10	GONDIA	96474	96117	96117	0	357
11	HINGOLI	18107	18083	18083	0	24
12	JALGAON	79791	79632	79632	0	159
13	JALNA	24047	24044	24044	0	3
14	KOLHAPUR	17770	17770	17770	0	0
15	LATUR	20799	20793	20793	0	6
16	NANDED	69588	69568	69568	0	20
17	NANDURBAR	119349	118868	118868	0	481
18	NASHIK	89787	89765	89765	0	22
19	OSMANABAD	14583	14566	14566	0	17
20	PALGHAR	35152	35148	35148	0	4
21	PARBHANI	19106	19098	19098	0	8
22	PUNE	21034	21025	21025	0	9
23	RAIGAD	9847	9839	9839	0	8
24	RATNAGIRI	9926	9920	9920	0	6
25	SANGLI	22173	22054	22054	0	119
26	SINDHUDURG	5156	5156	5156	0	0
27	SOLAPUR	50158	50003	50003	0	155
28	THANE	9606	9598	9598	0	8
29	WARDHA	18671	18657	18657	0	14
30	WASHIM	20416	20395	20395	0	21
31	YAVATMAL	65391	65249	65249	0	142
32	NAGPUR	37329	37328	37326	-2	3
33	SATARA	15529	15531	15527	-4	2
34	CHANDRAPUR	43276	43204	43194	-10	82
Total		1416838	1414572	1414573	17	2265

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	07.03.2023	08.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413906	316103	316146	43	97760	302	4250
2	PUNE DIV.	126379	84856	84881	25	41498	69	1804
3	AURANGABAD DIV.	237969	130387	130402	15	107567	211	4677
4	KONKAN DIV.	69661	54177	54190	13	15471	44	673
5	AMRAVATI DIV.	274682	178875	178887	12	95795	201	4165
6	NAGPUR DIV.	291976	228994	228997	3	62979	193	2738
Total		1414573	993392	993503	111	421070	1021	18307

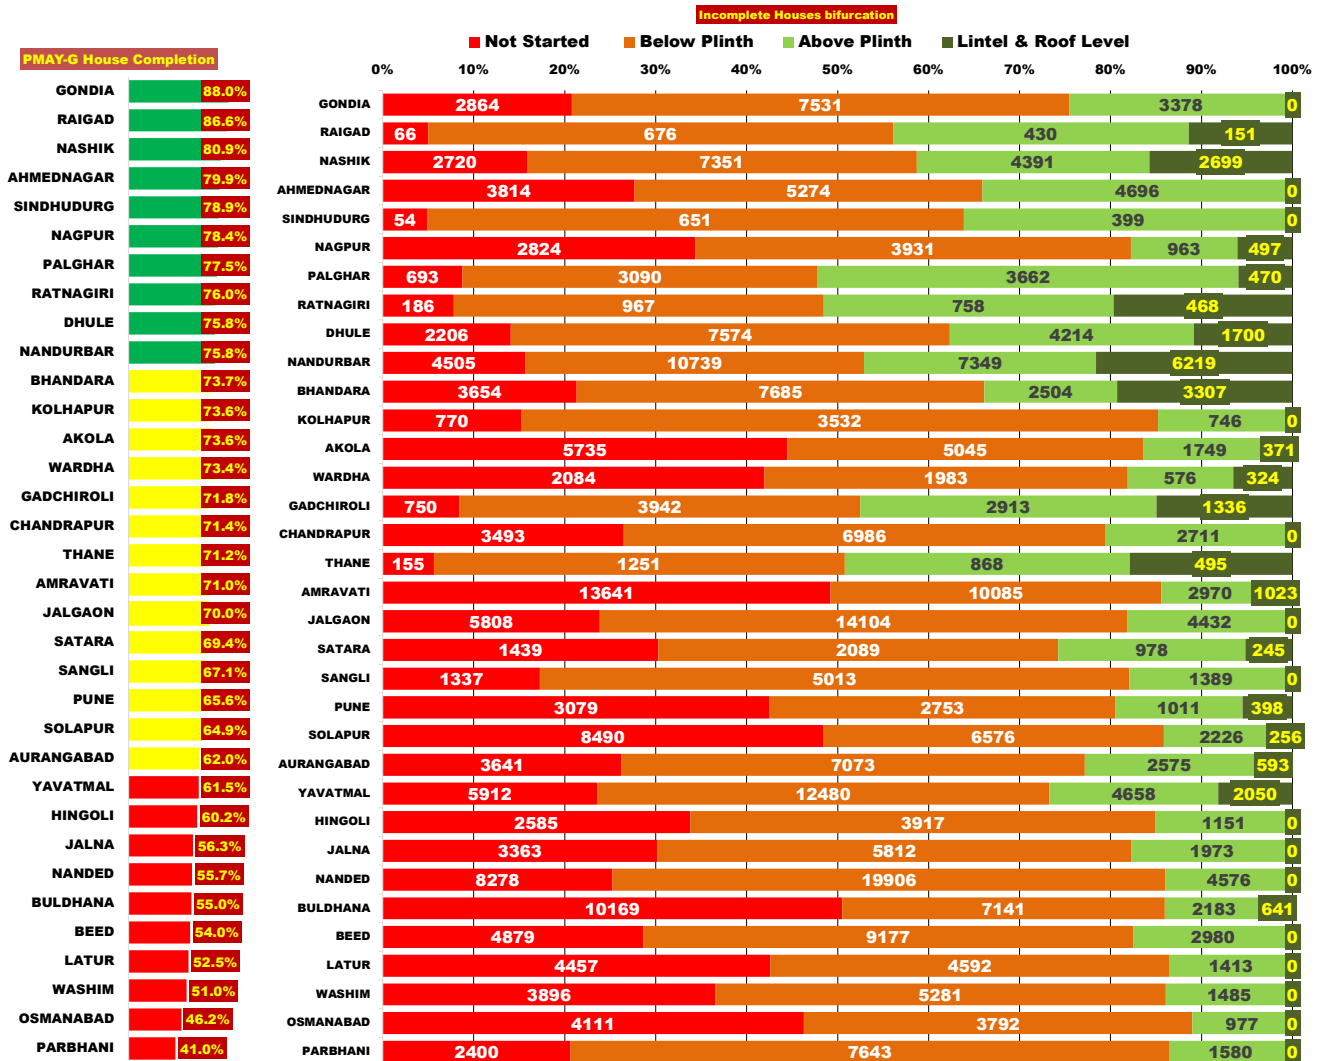


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	07.03.2023	08.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	60764	48502	48537	35	12227	97	532
2	PUNE	21025	13767	13784	17	7241	11	315
3	BULDHANA	44728	24593	24605	12	20123	33	875
4	NANDED	69568	38770	38779	9	30789	51	1339
5	DHULE	64877	49177	49183	6	15694	57	682
6	SANGLI	22054	14789	14795	6	7259	12	316
7	THANE	9598	6823	6829	6	2769	3	120
8	SINDHUDURG	5156	4063	4068	5	1088	4	47
9	OSMANABAD	14566	6729	6732	3	7834	18	341
10	GADCHIROLI	31575	22657	22659	2	8916	27	388
11	JALGAON	79632	55764	55766	2	23866	54	1038
12	LATUR	20793	10916	10918	2	9875	23	429
13	RATNAGIRI	9920	7539	7541	2	2379	12	103
14	SOLAPUR	50003	32453	32455	2	17548	24	763
15	CHANDRAPUR	43194	30853	30854	1	12340	42	537
16	PARBHANI	19098	7834	7835	1	11263	15	490
17	AKOLA	48775	35875	35875	0	12900	26	561
18	AMRAVATI	95535	67862	67862	0	27673	58	1203
19	AURANGABAD	36550	22668	22668	0	13882	33	604
20	BEED	35267	19034	19034	0	16233	26	706
21	BHANDARA	65107	47957	47957	0	17150	37	746
22	GONDIA	96117	84591	84591	0	11526	65	501
23	HINGOLI	18083	10891	10891	0	7192	18	313
24	JALNA	24044	13545	13545	0	10499	28	456
25	KOLHAPUR	17770	13071	13071	0	4699	9	204
26	NAGPUR	37326	29246	29246	0	8080	13	351
27	NANDURBAR	118868	90056	90056	0	28812	40	1253
28	NASHIK	89765	72604	72604	0	17161	54	746
29	PALGHAR	35148	27233	27233	0	7915	21	344
30	RAIGAD	9839	8519	8519	0	1320	4	57
31	SATARA	15527	10776	10776	0	4751	13	207
32	WARDHA	18657	13690	13690	0	4967	11	216
33	WASHIM	20395	10392	10392	0	10003	22	435
34	YAVATMAL	65249	40153	40153	0	25096	62	1091
Total		1414573	993392	993503	111	421070	1021	18307

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	07.03.2023	08.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	158506	158603	97	40728
2	NASHIK DIV.	141360	108404	108410	6	32950
3	KONKAN DIV.	34729	29558	29558	0	5171
4	PUNE DIV.	65334	62911	62911	0	2423
5	AMRAVATI DIV.	109702	90854	90854	0	18848
6	NAGPUR DIV.	116255	86632	86632	0	29623
	Total	666711	536865	536968	103	129743

State Scheme Remaining Sanction

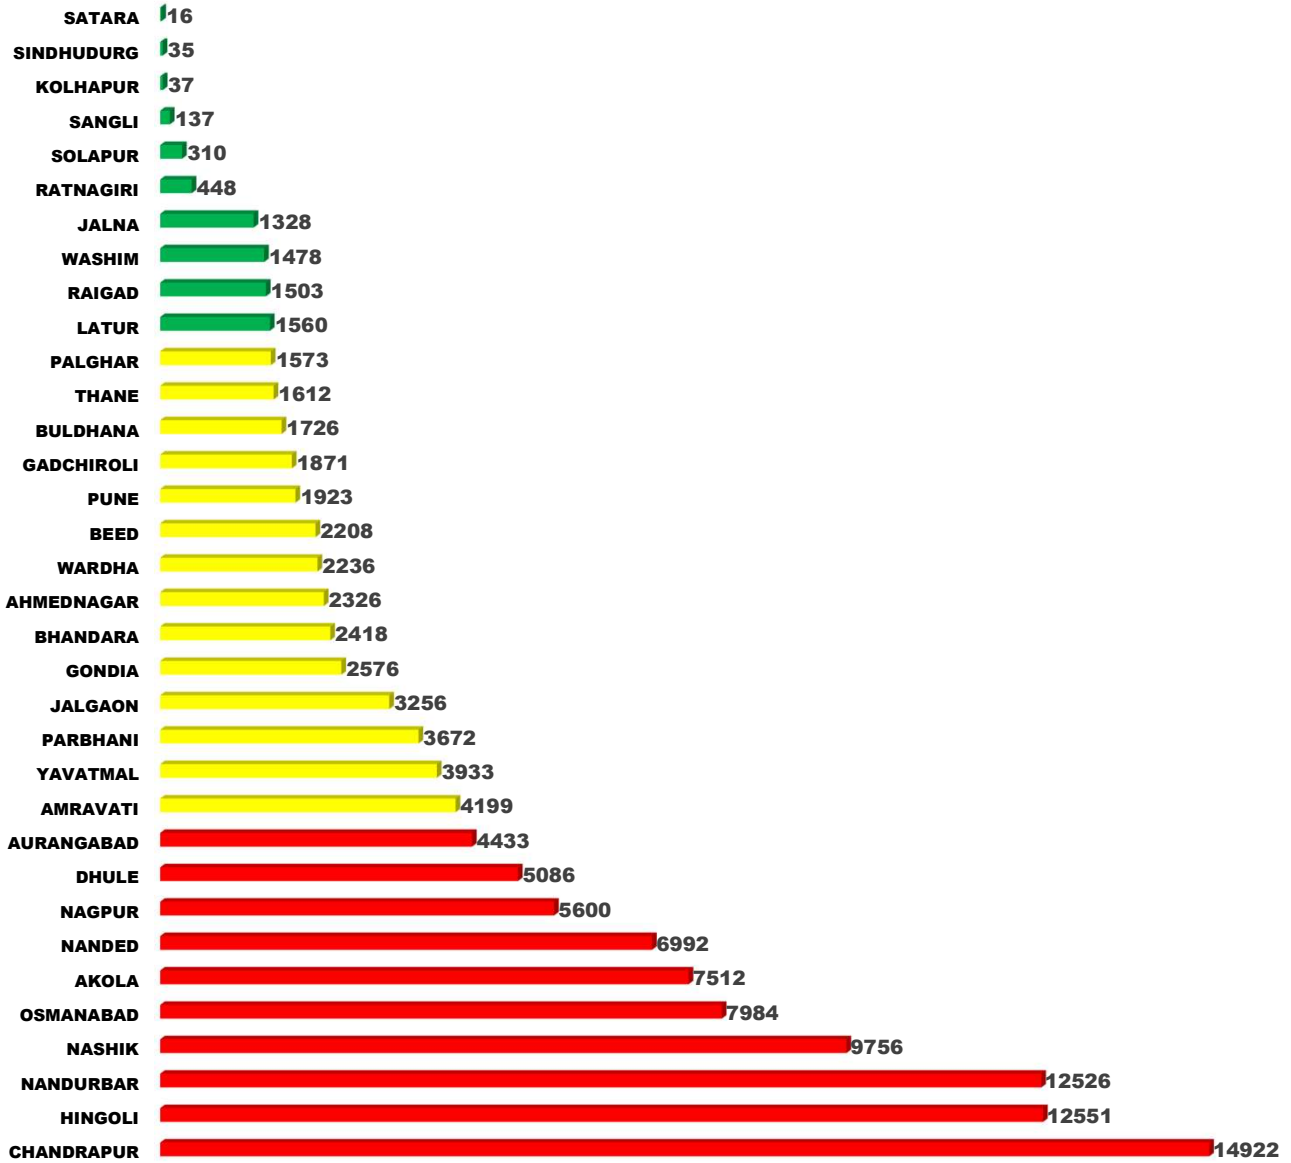


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	07.03.2023	08.03.2023	Daily_Achievement	Remaining
1	NANDED	26760	19671	19768	97	6992
2	AHMEDNAGAR	35298	32969	32972	3	2326
3	NANDURBAR	26578	14049	14052	3	12526
4	AKOLA	23681	16169	16169	0	7512
5	AMRAVATI	23224	19025	19025	0	4199
6	AURANGABAD	26141	21708	21708	0	4433
7	BEED	26878	24670	24670	0	2208
8	BHANDARA	17590	15172	15172	0	2418
9	BULDHANA	21616	19890	19890	0	1726
10	CHANDRAPUR	38147	23225	23225	0	14922
11	DHULE	21790	16704	16704	0	5086
12	GADCHIROLI	16834	14963	14963	0	1871
13	GONDIA	14246	11670	11670	0	2576
14	HINGOLI	27298	14747	14747	0	12551
15	JALGAON	25659	22403	22403	0	3256
16	JALNA	20446	19118	19118	0	1328
17	KOLHAPUR	12565	12528	12528	0	37
18	LATUR	27171	25611	25611	0	1560
19	NAGPUR	16291	10691	10691	0	5600
20	NASHIK	32035	22279	22279	0	9756
21	OSMANABAD	24853	16869	16869	0	7984
22	PALGHAR	11792	10219	10219	0	1573
23	PARBHANI	19784	16112	16112	0	3672
24	PUNE	14672	12749	12749	0	1923
25	RAIGAD	7406	5903	5903	0	1503
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10631	10631	0	16
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18408	18408	0	310
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	10911	10911	0	2236
33	WASHIM	11500	10022	10022	0	1478
34	YAVATMAL	29681	25748	25748	0	3933
Total		666711	536865	536968	103	129743

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	07.03.2023	08.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108410	85763	85780	17	22630	72	984
2	AURANGABAD DIV.	158603	100678	100685	7	57918	98	2518
3	NAGPUR DIV.	86632	67348	67355	7	19277	45	838
4	AMRAVATI DIV.	90854	62117	62121	4	28733	55	1249
5	KONKAN DIV.	29558	22739	22742	3	6816	13	296
6	PUNE DIV.	62911	50985	50986	1	11925	27	518
Total		536968	389630	389669	39	147299	309	6404

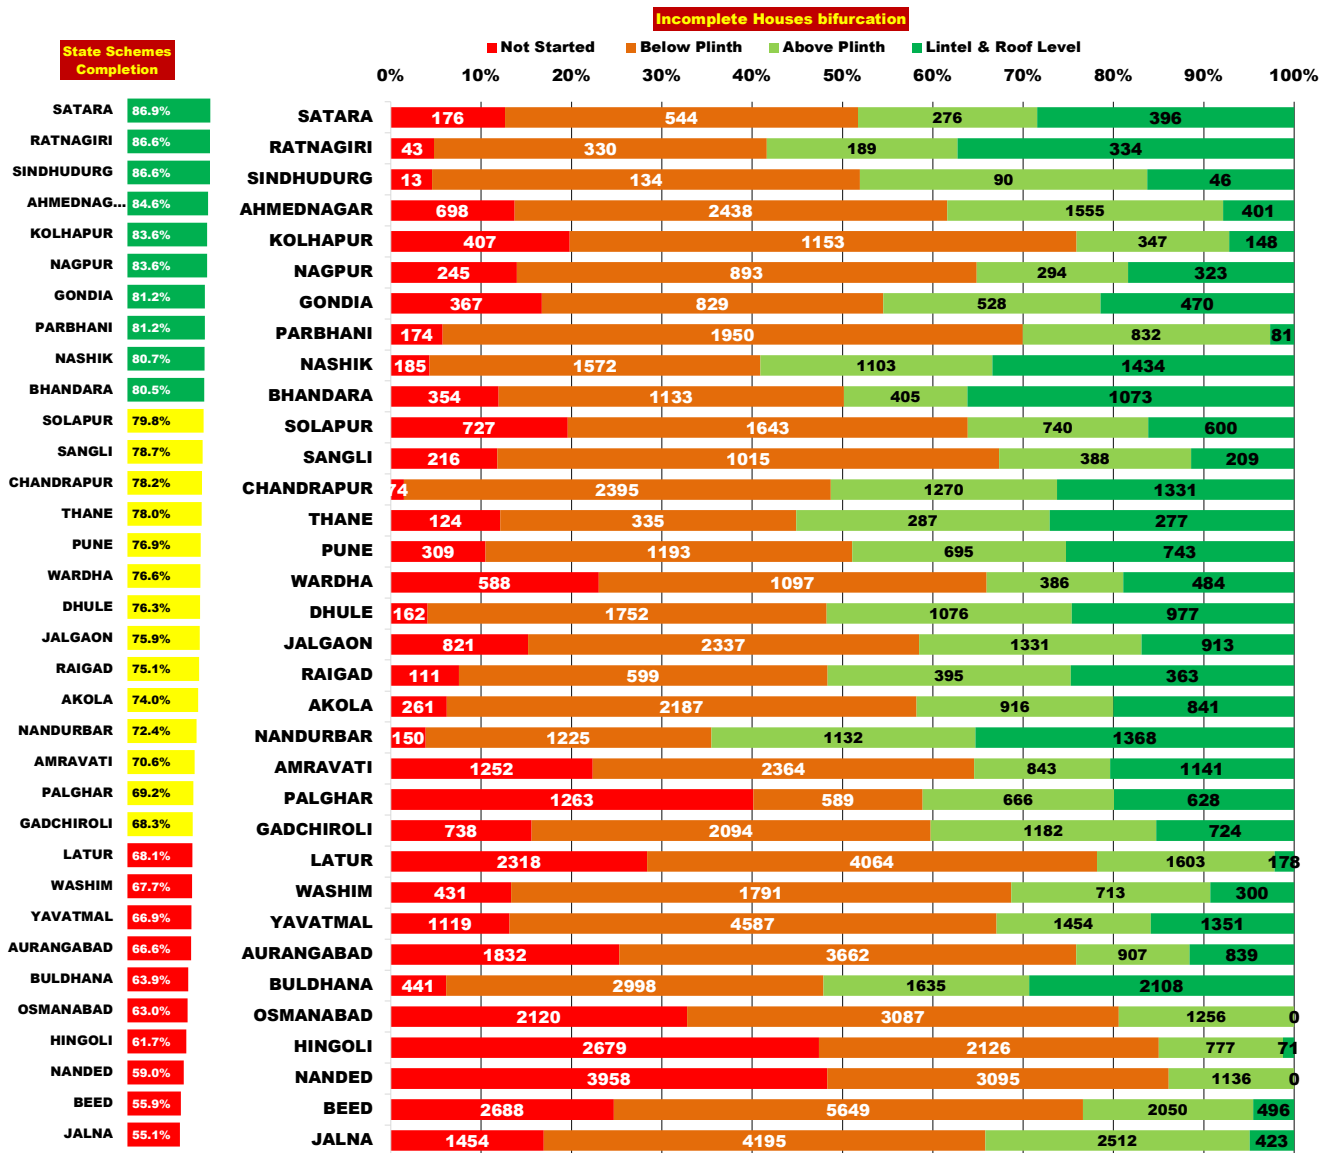

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	07.03.2023	08.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32972	27869	27880	11	5092	30	221
2	CHANDRAPUR	23225	18149	18155	6	5070	14	220
3	BULDHANA	19890	12704	12708	4	7182	16	312
4	JALGAON	22403	16997	17001	4	5402	11	235
5	THANE	4652	3626	3629	3	1023	1	44
6	BEED	24670	13785	13787	2	10883	14	473
7	LATUR	25611	17446	17448	2	8163	11	355
8	DHULE	16704	12736	12737	1	3967	12	172
9	GADCHIROLI	14963	10224	10225	1	4738	8	206
10	HINGOLI	14747	9093	9094	1	5653	6	246
11	NANDED	19768	11656	11657	1	8111	10	353
12	NANDURBAR	14052	10176	10177	1	3875	7	168
13	PARBHANI	16112	13074	13075	1	3037	4	132
14	PUNE	12749	9808	9809	1	2940	6	128
15	AKOLA	16169	11964	11964	0	4205	10	183
16	AMRAVATI	19025	13425	13425	0	5600	9	243
17	AURANGABAD	21708	14468	14468	0	7240	8	315
18	BHANDARA	15172	12207	12207	0	2965	4	129
19	GONDIA	11670	9476	9476	0	2194	8	95
20	JALNA	19118	10534	10534	0	8584	31	373
21	KOLHAPUR	12528	10473	10473	0	2055	4	89
22	NAGPUR	10691	8936	8936	0	1755	4	76
23	NASHIK	22279	17985	17985	0	4294	12	187
24	OSMANABAD	16869	10622	10622	0	6247	13	272
25	PALGHAR	10219	7073	7073	0	3146	6	137
26	RAIGAD	5903	4435	4435	0	1468	3	64
27	RATNAGIRI	6678	5782	5782	0	896	2	39
28	SANGLI	8595	6767	6767	0	1828	4	79
29	SATARA	10631	9239	9239	0	1392	5	61
30	SINDHUDURG	2106	1823	1823	0	283	1	12
31	SOLAPUR	18408	14698	14698	0	3710	8	161
32	WARDHA	10911	8356	8356	0	2555	7	111
33	WASHIM	10022	6787	6787	0	3235	7	141
34	YAVATMAL	25748	17237	17237	0	8511	13	370
	Total	536968	389630	389669	39	147299	309	6404

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	19053	0	45042	0	25082
2	AMRAVATI DIV.	0	39289	0	40032	0	13045
3	AURANGABAD DIV.	0	33684	0	61912	0	17225
4	NAGPUR DIV.	0	15467	0	32058	0	13045
5	KONKAN DIV.	0	1151	0	6635	0	6117
6	PUNE DIV.	0	14982	0	19963	0	6350
	Total	0	123626	0	205642	0	80864

PMAY-G 1st Ins Pending

SINDHUDURG	54
RAIGAD	63
THANE	155
RATNAGIRI	186
PALGHAR	693
GADCHIROLI	725
KOLHAPUR	770
SANGLI	1204
SATARA	1439
WARDHA	2084
DHULE	2206
PARBHANI	2400
HINGOLI	2585
NAGPUR	2689
NASHIK	2720
GONDIA	2864
PUNE	3079
JALNA	3333
CHANDRAPUR	3451
AURANGABAD	3641
BHANDARA	3654
AHMEDNAGAR	3814
WASHIM	3893
OSMANABAD	4111
LATUR	4457
NANDURBAR	4505
BEED	4879
AKOLA	5735
JALGAON	5808
YAVATMAL	5908
NANDED	8278
SOLAPUR	8490
BULDHANA	10158
AMRAVATI	13595

PMAY-G 2nd Ins Pending

SINDHUDURG	651
RAIGAD	676
RATNAGIRI	967
THANE	1251
WARDHA	1983
SATARA	2089
PUNE	2753
PALGHAR	3090
KOLHAPUR	3532
OSMANABAD	3792
HINGOLI	3917
NAGPUR	3931
GADCHIROLI	3942
LATUR	4592
SANGLI	5013
AKOLA	5045
AHMEDNAGAR	5274
WASHIM	5281
JALNA	5812
SOLAPUR	6576
CHANDRAPUR	6986
AURANGABAD	7073
BULDHANA	7141
NASHIK	7351
GONDIA	7531
DHULE	7574
PARBHANI	7643
BHANDARA	7685
BEED	9177
AMRAVATI	10085
NANDURBAR	10739
YAVATMAL	12480
JALGAON	14104
NANDED	19906

PMAY-G 3rd Ins Pending

SINDHUDURG	399
RAIGAD	430
WARDHA	576
KOLHAPUR	746
RATNAGIRI	758
THANE	868
NAGPUR	963
OSMANABAD	977
SATARA	978
PUNE	1011
HINGOLI	1151
SANGLI	1389
LATUR	1413
WASHIM	1485
PARBHANI	1580
AKOLA	1749
JALNA	1973
BULDHANA	2183
SOLAPUR	2226
BHANDARA	2504
AURANGABAD	2575
CHANDRAPUR	2711
GADCHIROLI	2913
AMRAVATI	2970
BEED	2980
GONDIA	3378
PALGHAR	3662
DHULE	4214
NASHIK	4391
JALGAON	4432
NANDED	4576
YAVATMAL	4658
AHMEDNAGAR	4696
NANDURBAR	7349

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3814	0	5274	0	4696
2	AKOLA	0	5735	0	5045	0	1749
3	AMRAVATI	0	13595	0	10085	0	2970
4	AURANGABAD	0	3641	0	7073	0	2575
5	BEED	0	4879	0	9177	0	2980
6	BHANDARA	0	3654	0	7685	0	2504
7	BULDHANA	0	10158	0	7141	0	2183
8	CHANDRAPUR	0	3451	0	6986	0	2711
9	DHULE	0	2206	0	7574	0	4214
10	GADCHIROLI	0	725	0	3942	0	2913
11	GONDIA	0	2864	0	7531	0	3378
12	HINGOLI	0	2585	0	3917	0	1151
13	JALGAON	0	5808	0	14104	0	4432
14	JALNA	0	3333	0	5812	0	1973
15	KOLHAPUR	0	770	0	3532	0	746
16	LATUR	0	4457	0	4592	0	1413
17	NAGPUR	0	2689	0	3931	0	963
18	NANDED	0	8278	0	19906	0	4576
19	NANDURBAR	0	4505	0	10739	0	7349
20	NASHIK	0	2720	0	7351	0	4391
21	OSMANABAD	0	4111	0	3792	0	977
22	PALGHAR	0	693	0	3090	0	3662
23	PARBHANI	0	2400	0	7643	0	1580
24	PUNE	0	3079	0	2753	0	1011
25	RAIGAD	0	63	0	676	0	430
26	RATNAGIRI	0	186	0	967	0	758
27	SANGLI	0	1204	0	5013	0	1389
28	SATARA	0	1439	0	2089	0	978
29	SINDHUDURG	0	54	0	651	0	399
30	SOLAPUR	0	8490	0	6576	0	2226
31	THANE	0	155	0	1251	0	868
32	WARDHA	0	2084	0	1983	0	576
33	WASHIM	0	3893	0	5281	0	1485
34	YAVATMAL	0	5908	0	12480	0	4658
	Total	0	123626	0	205642	0	80864

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	NASHIK DIV.	0	2016	0	9324	0	6197
2	AMRAVATI DIV.	0	3504	0	13927	0	5561
3	AURANGABAD DIV.	0	17223	0	27828	0	11073
4	NAGPUR DIV.	0	2366	0	8441	0	4065
5	KONKAN DIV.	0	1554	0	1987	0	1627
6	PUNE DIV.	0	1835	0	5548	0	2446
	Total	0	28498	0	67055	0	30969

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	43
CHANDRAPUR	74
RAIGAD	111
THANE	124
NANDURBAR	150
DHULE	162
PARBHANI	174
SATARA	176
NASHIK	185
SANGLI	216
NAGPUR	245
AKOLA	261
PUNE	309
BHANDARA	354
GONDIA	367
KOLHAPUR	407
WASHIM	431
BULDHANA	441
WARDHA	588
AHMEDNAGAR	698
SOLAPUR	727
GADCHIROLI	738
JALGAON	821
YAVATMAL	1119
AMRAVATI	1252
PALGHAR	1263
JALNA	1454
AURANGABAD	1832
OSMANABAD	2120
LATUR	2318
HINGOLI	2679
BEED	2688
NANDED	3958

State Schemes 2nd Ins Pending

SINDHUDURG	134
RATNAGIRI	330
THANE	335
SATARA	544
PALGHAR	589
RAIGAD	599
GONDIA	829
NAGPUR	893
SANGLI	1015
WARDHA	1097
BHANDARA	1133
KOLHAPUR	1153
PUNE	1193
NANDURBAR	1225
NASHIK	1572
SOLAPUR	1643
DHULE	1752
WASHIM	1791
PARBHANI	1950
GADCHIROLI	2094
HINGOLI	2126
AKOLA	2187
JALGAON	2337
AMRAVATI	2364
CHANDRAPUR	2395
AHMEDNAGAR	2438
BULDHANA	2998
OSMANABAD	3087
NANDED	3095
AURANGABAD	3662
LATUR	4064
JALNA	4195
YAVATMAL	4587
BEED	5649

State Schemes 3rd Ins Pending

SINDHUDURG	90
RATNAGIRI	189
SATARA	276
THANE	287
NAGPUR	294
KOLHAPUR	347
WARDHA	386
SANGLI	388
RAIGAD	395
BHANDARA	405
GONDIA	528
PALGHAR	666
PUNE	695
WASHIM	713
SOLAPUR	740
HINGOLI	777
PARBHANI	832
AMRAVATI	843
AURANGABAD	907
AKOLA	916
DHULE	1076
NASHIK	1103
NANDURBAR	1132
NANDED	1136
GADCHIROLI	1182
OSMANABAD	1256
CHANDRAPUR	1270
JALGAON	1331
YAVATMAL	1454
AHMEDNAGAR	1555
LATUR	1603
BULDHANA	1635
BEED	2050
JALNA	2512

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	698	0	2438	0	1555
2	AKOLA	0	261	0	2187	0	916
3	AMRAVATI	0	1252	0	2364	0	843
4	AURANGABAD	0	1832	0	3662	0	907
5	BEED	0	2688	0	5649	0	2050
6	BHANDARA	0	354	0	1133	0	405
7	BULDHANA	0	441	0	2998	0	1635
8	CHANDRAPUR	0	74	0	2395	0	1270
9	DHULE	0	162	0	1752	0	1076
10	GADCHIROLI	0	738	0	2094	0	1182
11	GONDIA	0	367	0	829	0	528
12	HINGOLI	0	2679	0	2126	0	777
13	JALGAON	0	821	0	2337	0	1331
14	JALNA	0	1454	0	4195	0	2512
15	KOLHAPUR	0	407	0	1153	0	347
16	LATUR	0	2318	0	4064	0	1603
17	NAGPUR	0	245	0	893	0	294
18	NANDED	0	3958	0	3095	0	1136
19	NANDURBAR	0	150	0	1225	0	1132
20	NASHIK	0	185	0	1572	0	1103
21	OSMANABAD	0	2120	0	3087	0	1256
22	PALGHAR	0	1263	0	589	0	666
23	PARBHANI	0	174	0	1950	0	832
24	PUNE	0	309	0	1193	0	695
25	RAIGAD	0	111	0	599	0	395
26	RATNAGIRI	0	43	0	330	0	189
27	SANGLI	0	216	0	1015	0	388
28	SATARA	0	176	0	544	0	276
29	SINDHUDURG	0	13	0	134	0	90
30	SOLAPUR	0	727	0	1643	0	740
31	THANE	0	124	0	335	0	287
32	WARDHA	0	588	0	1097	0	386
33	WASHIM	0	431	0	1791	0	713
34	YAVATMAL	0	1119	0	4587	0	1454
	Total	0	28498	0	67055	0	30969
