



# अमृत महा आवास अभियान २०२२-२३

## दैनिक प्रगती अहवाल : १२.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१३९८६	६	९९६९९७	७०४	५७५	८७५	९९९
राज्य योजना	५३९४२१	५०६	३९०९९५	२४९	२४८	३२३	२९९
एकूण	१९५३४०७	५१२	१३८७९९२	९५३	८२३	११९८	१२९८

PMAY-G Completion Progress Bar

70.5%



PMAY-G Incomplete Houses bifurcation

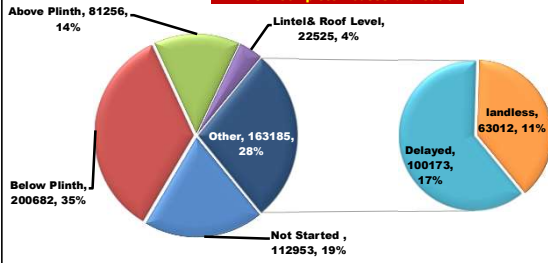


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

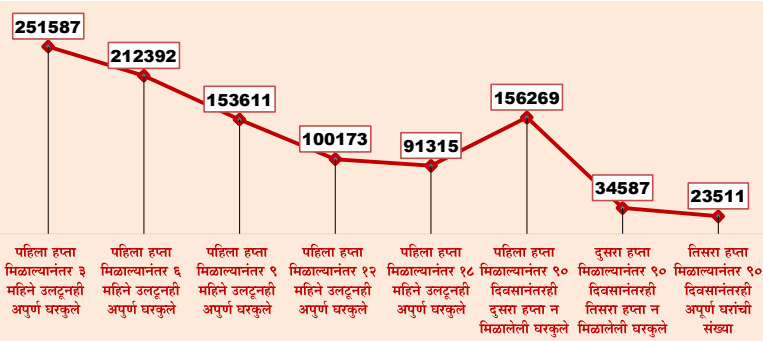


Abhiyan Achievement Day 112

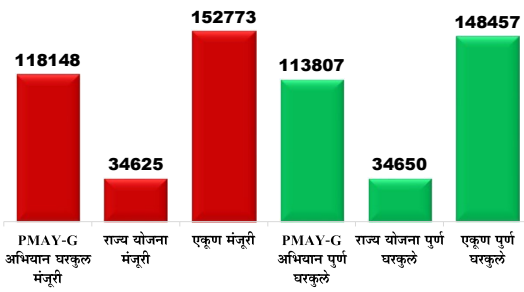

PMAY-G : House completion ( Abhiyan Achievement)

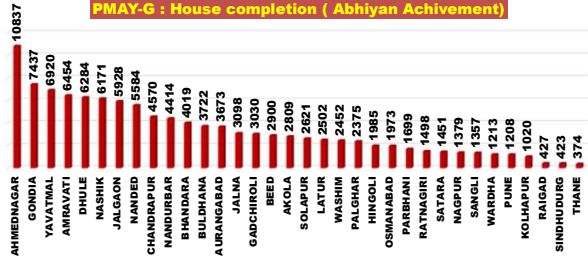

State Schemes : House completion ( Abhiyan Achievement)

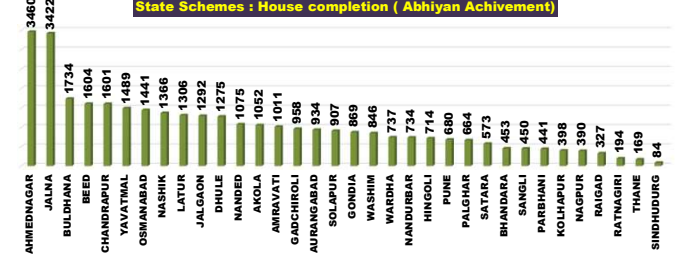


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.



PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	11.03.2023	12.03.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414565	413829	413831	2	734
2	AMRAVATI DIV.	274985	274674	274676	2	309
3	PUNE DIV.	126436	126223	126143	2	293
4	AURANGABAD DIV.	238306	237931	237858	0	448
5	NAGPUR DIV.	292387	291869	291826	0	561
6	KONKAN DIV.	69682	69652	69652	0	30
<b>Total</b>		<b>1416361</b>	<b>1414178</b>	<b>1413986</b>	<b>6</b>	<b>2375</b>

PMAY-G Remaining Sanction

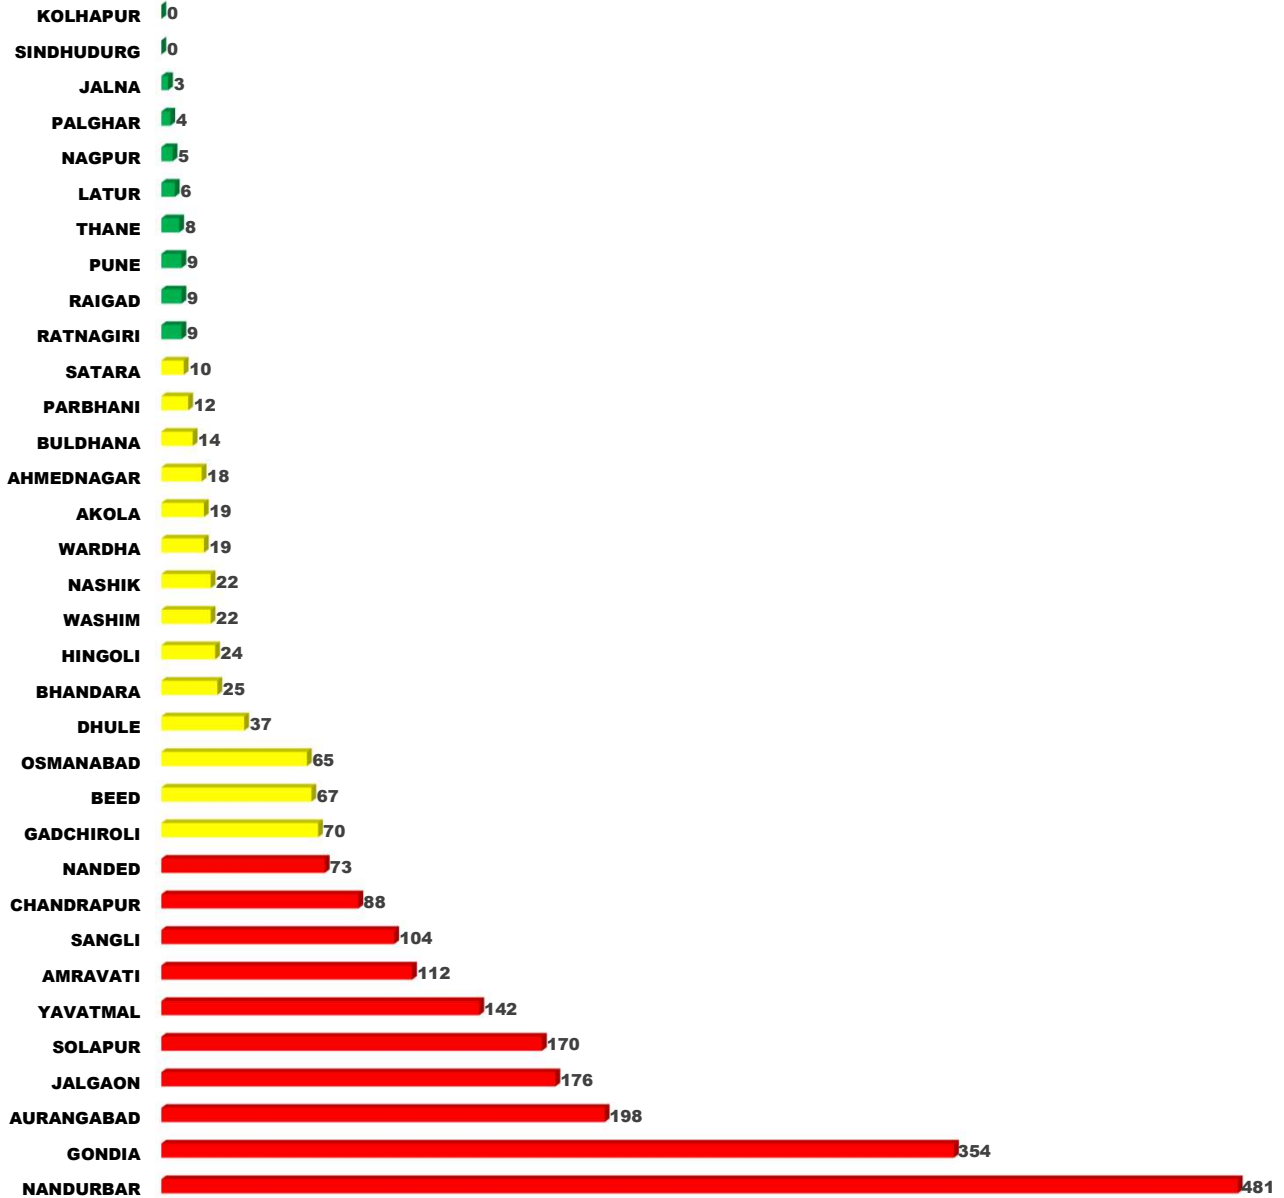


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	11.03.2023	12.03.2023	Daily_Achievement	Remaining
1	JALGAON	79767	79589	79591	2	176
2	SATARA	15514	15502	15504	2	10
3	WASHIM	20413	20389	20391	2	22
4	AHMEDNAGAR	60789	60771	60771	0	18
5	AKOLA	48794	48775	48775	0	19
6	AMRAVATI	95646	95534	95534	0	112
7	AURANGABAD	36792	36594	36594	0	198
8	BHANDARA	65128	65103	65103	0	25
9	BULDHANA	44742	44728	44728	0	14
10	CHANDRAPUR	43236	43148	43148	0	88
11	DHULE	64912	64875	64875	0	37
12	GADCHIROLI	31639	31569	31569	0	70
13	GONDIA	96470	96116	96116	0	354
14	HINGOLI	18107	18083	18083	0	24
15	JALNA	24047	24044	24044	0	3
16	KOLHAPUR	17770	17770	17770	0	0
17	LATUR	20799	20793	20793	0	6
18	NANDURBAR	119333	118852	118852	0	481
19	NASHIK	89764	89742	89742	0	22
20	PALGHAR	35152	35148	35148	0	4
21	PUNE	20989	20980	20980	0	9
22	RAIGAD	9844	9835	9835	0	9
23	RATNAGIRI	9924	9915	9915	0	9
24	SANGLI	22158	22054	22054	0	104
25	SINDHUDURG	5156	5156	5156	0	0
26	THANE	9606	9598	9598	0	8
27	YAVATMAL	65390	65248	65248	0	142
28	OSMANABAD	14565	14501	14500	-1	65
29	PARBHANI	19103	19094	19091	-3	12
30	WARDHA	18671	18657	18652	-5	19
31	BEED	35324	35270	35257	-13	67
32	NAGPUR	37243	37276	37238	-38	5
33	NANDED	69569	69552	69496	-56	73
34	SOLAPUR	50005	49917	49835	-82	170
<b>Total</b>		<b>1416361</b>	<b>1414178</b>	<b>1413986</b>	<b>6</b>	<b>2375</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	11.03.2023	12.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	<b>NASHIK DIV.</b>	<b>413831</b>	<b>316827</b>	<b>317148</b>	<b>321</b>	<b>96683</b>	<b>300</b>	<b>5089</b>
2	<b>AURANGABAD DIV.</b>	<b>237858</b>	<b>130857</b>	<b>130975</b>	<b>118</b>	<b>106883</b>	<b>209</b>	<b>5625</b>
3	<b>NAGPUR DIV.</b>	<b>291826</b>	<b>229664</b>	<b>229776</b>	<b>112</b>	<b>62050</b>	<b>193</b>	<b>3266</b>
4	<b>AMRAVATI DIV.</b>	<b>274676</b>	<b>179434</b>	<b>179514</b>	<b>80</b>	<b>95162</b>	<b>200</b>	<b>5009</b>
5	<b>KONKAN DIV.</b>	<b>69652</b>	<b>54464</b>	<b>54505</b>	<b>41</b>	<b>15147</b>	<b>46</b>	<b>797</b>
6	<b>PUNE DIV.</b>	<b>126143</b>	<b>85047</b>	<b>85079</b>	<b>32</b>	<b>41064</b>	<b>68</b>	<b>2161</b>
<b>Total</b>		<b>1413986</b>	<b>996293</b>	<b>996997</b>	<b>704</b>	<b>416989</b>	<b>1016</b>	<b>21947</b>

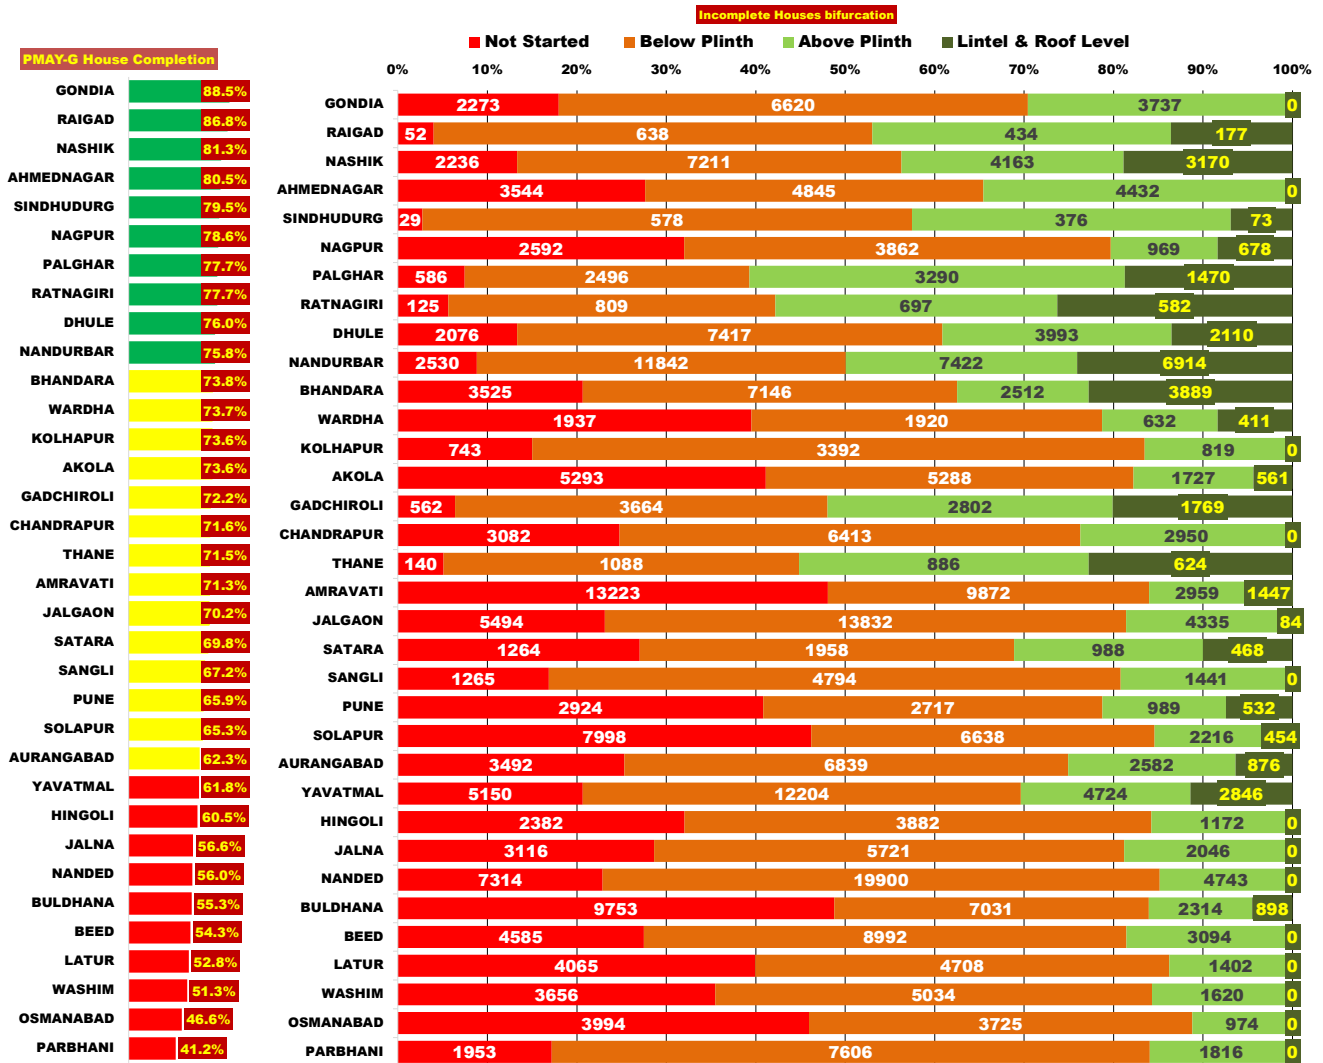


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	11.03.2023	12.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK	89742	72778	72962	184	16780	55	883
2	GONDIA	96116	84945	85015	70	11101	66	584
3	AHMEDNAGAR	60771	48856	48917	61	11854	97	624
4	AURANGABAD	36594	22757	22805	48	13789	33	726
5	NANDURBAR	118852	90112	90144	32	28708	39	1511
6	YAVATMAL	65248	40298	40328	30	24920	62	1312
7	DHULE	64875	49250	49279	29	15596	56	821
8	NANDED	69496	38866	38894	28	30602	50	1611
9	AMRAVATI	95534	68057	68079	22	27455	58	1445
10	GADCHIROLI	31569	22775	22797	22	8772	27	462
11	RATNAGIRI	9915	7682	7702	20	2213	13	116
12	SOLAPUR	49835	32512	32529	17	17306	23	911
13	BULDHANA	44728	24727	24743	16	19985	33	1052
14	WARDHA	18652	13736	13752	16	4900	11	258
15	JALGAON	79591	55831	55846	15	23745	53	1250
16	PALGHAR	35148	27292	27306	14	7842	21	413
17	BEED	35257	19115	19128	13	16129	26	849
18	WASHIM	20391	10446	10458	12	9933	22	523
19	HINGOLI	18083	10934	10943	9	7140	18	376
20	LATUR	20793	10967	10976	9	9817	22	517
21	SANGLI	22054	14816	14824	8	7230	12	381
22	SATARA	15504	10819	10826	7	4678	13	246
23	PARBHANI	19091	7866	7872	6	11219	15	590
24	THANE	9598	6854	6860	6	2738	3	144
25	JALNA	24044	13599	13604	5	10440	28	549
26	BHANDARA	65103	48027	48031	4	17072	36	899
27	RAIGAD	9835	8536	8537	1	1298	4	68
28	AKOLA	48775	35906	35906	0	12869	25	677
29	CHANDRAPUR	43148	30909	30909	0	12239	41	644
30	KOLHAPUR	17770	13082	13082	0	4688	9	247
31	NAGPUR	37238	29272	29272	0	7966	12	419
32	OSMANABAD	14500	6753	6753	0	7747	18	408
33	PUNE	20980	13818	13818	0	7162	11	377
34	SINDHUDURG	5156	4100	4100	0	1056	4	56
Total		1413986	996293	996997	704	416989	1016	21947

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	11.03.2023	12.03.2023	Daily Achievement	Remaining
1	AMRAVATI DIV.	109702	91592	91898	306	17804
2	AURANGABAD DIV.	199331	159147	159333	197	39998
3	PUNE DIV.	65334	62909	62912	3	2422
4	KONKAN DIV.	34729	29612	29612	0	5117
5	NASHIK DIV.	141360	108452	108452	0	32908
6	NAGPUR DIV.	116255	87214	87214	0	29041
<b>Total</b>		<b>666711</b>	<b>538926</b>	<b>539421</b>	<b>506</b>	<b>127290</b>

State Scheme Remaining Sanction

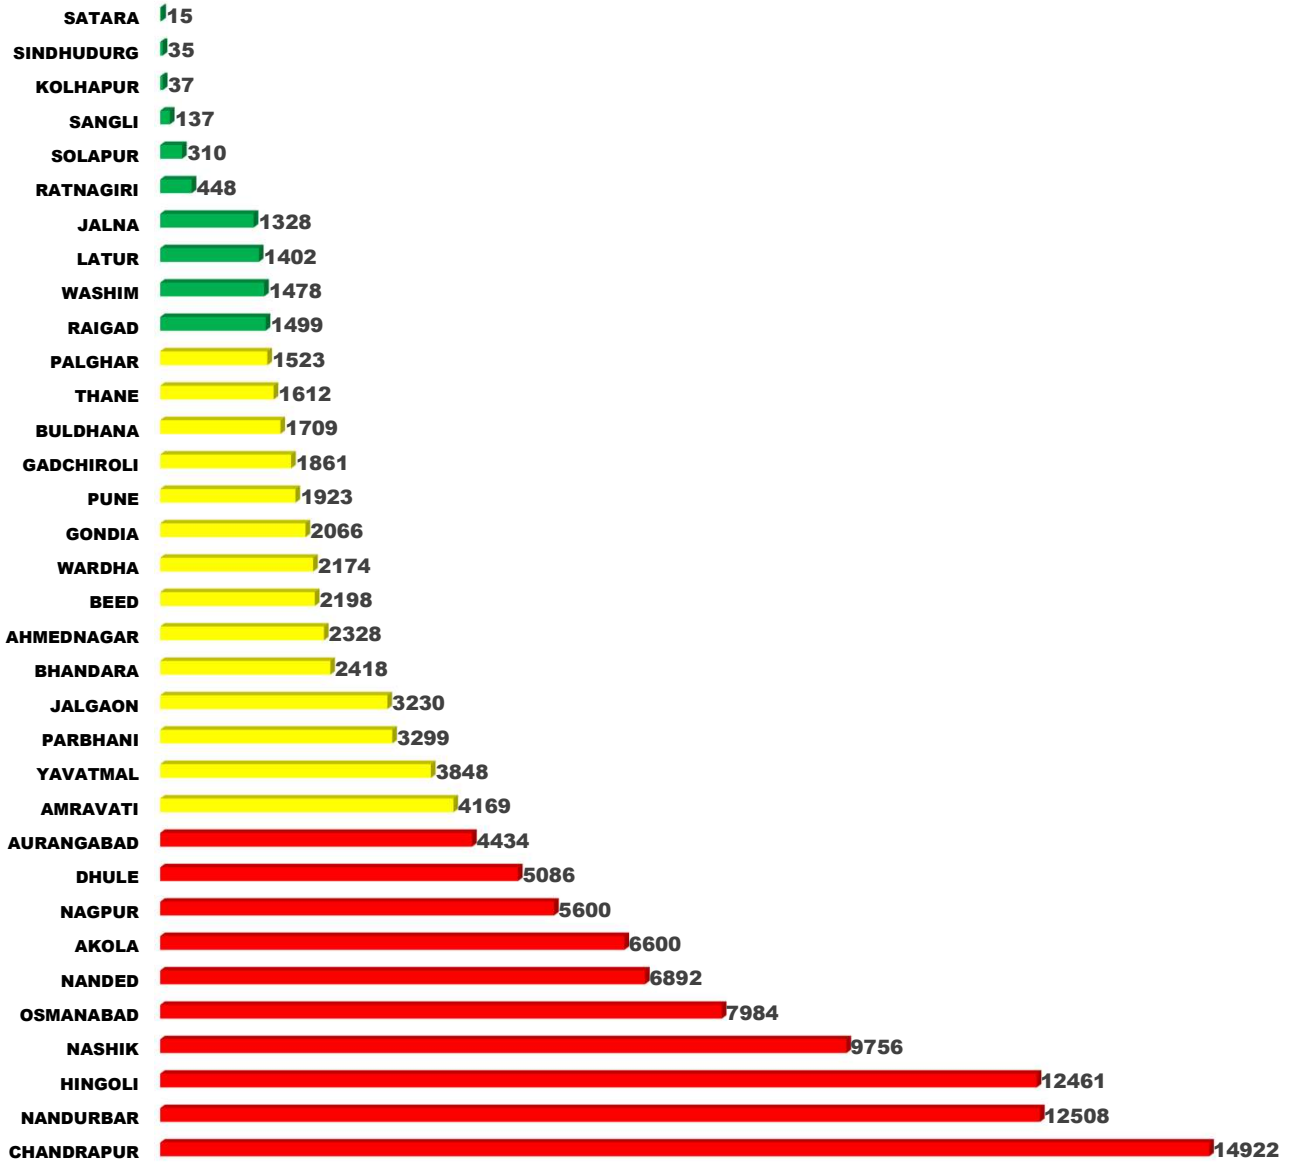


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	11.03.2023	12.03.2023	Daily_Achievement	Remaining
1	AKOLA	23681	16782	17081	299	6600
2	PARBHANI	19784	16288	16485	197	3299
3	AMRAVATI	23224	19048	19055	7	4169
4	SOLAPUR	18718	18405	18408	3	310
5	AHMEDNAGAR	35298	32970	32970	0	2328
6	BEED	26878	24680	24680	0	2198
7	BHANDARA	17590	15172	15172	0	2418
8	BULDHANA	21616	19907	19907	0	1709
9	CHANDRAPUR	38147	23225	23225	0	14922
10	DHULE	21790	16704	16704	0	5086
11	GADCHIROLI	16834	14973	14973	0	1861
12	GONDIA	14246	12180	12180	0	2066
13	HINGOLI	27298	14837	14837	0	12461
14	JALGAON	25659	22429	22429	0	3230
15	JALNA	20446	19118	19118	0	1328
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	25769	25769	0	1402
18	NAGPUR	16291	10691	10691	0	5600
19	NANDED	26760	19868	19868	0	6892
20	NANDURBAR	26578	14070	14070	0	12508
21	NASHIK	32035	22279	22279	0	9756
22	OSMANABAD	24853	16869	16869	0	7984
23	PALGHAR	11792	10269	10269	0	1523
24	PUNE	14672	12749	12749	0	1923
25	RAIGAD	7406	5907	5907	0	1499
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10632	10632	0	15
29	SINDHUDURG	2141	2106	2106	0	35
30	THANE	6264	4652	4652	0	1612
31	WARDHA	13147	10973	10973	0	2174
32	WASHIM	11500	10022	10022	0	1478
33	YAVATMAL	29681	25833	25833	0	3848
34	AURANGABAD	26141	21718	21707	-11	4434
<b>Total</b>		<b>666711</b>	<b>538926</b>	<b>539421</b>	<b>506</b>	<b>127290</b>



## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	11.03.2023	12.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	<b>NASHIK DIV.</b>	<b>108452</b>	<b>86089</b>	<b>86184</b>	<b>95</b>	<b>22268</b>	<b>73</b>	<b>1172</b>
2	<b>AURANGABAD DIV.</b>	<b>159333</b>	<b>100965</b>	<b>101043</b>	<b>78</b>	<b>58290</b>	<b>98</b>	<b>3068</b>
3	<b>AMRAVATI DIV.</b>	<b>91898</b>	<b>62294</b>	<b>62330</b>	<b>36</b>	<b>29568</b>	<b>55</b>	<b>1556</b>
4	<b>NAGPUR DIV.</b>	<b>87214</b>	<b>67528</b>	<b>67553</b>	<b>25</b>	<b>19661</b>	<b>45</b>	<b>1035</b>
5	<b>PUNE DIV.</b>	<b>62912</b>	<b>51063</b>	<b>51073</b>	<b>10</b>	<b>11839</b>	<b>27</b>	<b>623</b>
6	<b>KONKAN DIV.</b>	<b>29612</b>	<b>22807</b>	<b>22812</b>	<b>5</b>	<b>6800</b>	<b>13</b>	<b>358</b>
<b>Total</b>		<b>539421</b>	<b>390746</b>	<b>390995</b>	<b>249</b>	<b>148426</b>	<b>309</b>	<b>7812</b>

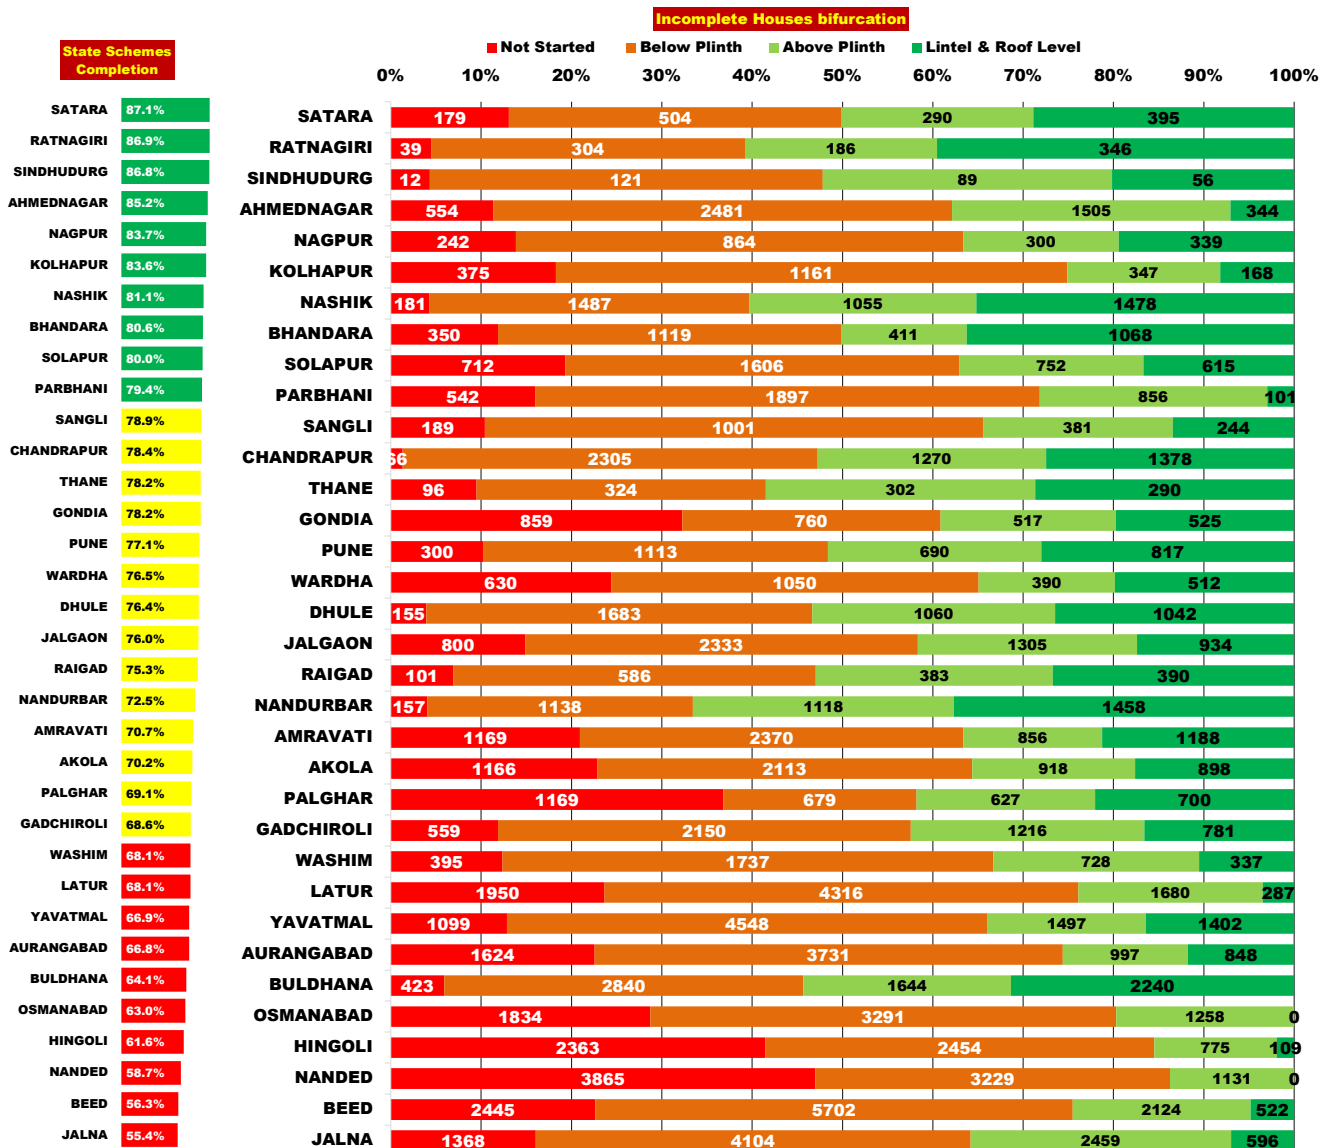

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	11.03.2023	12.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32970	28051	28086	35	4884	31	257
2	NASHIK	22279	18044	18078	34	4201	12	221
3	LATUR	25769	17511	17536	25	8233	12	433
4	AURANGABAD	21707	14486	14507	21	7200	8	379
5	JALGAON	22429	17040	17057	17	5372	12	283
6	WASHIM	10022	6811	6825	14	3197	8	168
7	BEED	24680	13874	13887	13	10793	14	568
8	BULDHANA	19907	12747	12760	13	7147	15	376
9	JALNA	19118	10583	10591	8	8527	31	449
10	HINGOLI	14837	9129	9136	7	5701	6	300
11	WARDHA	10973	8384	8391	7	2582	7	136
12	DHULE	16704	12758	12764	6	3940	11	207
13	GADCHIROLI	14973	10261	10267	6	4706	9	248
14	YAVATMAL	25833	17281	17287	6	8546	13	450
15	GONDIA	12180	9515	9519	4	2661	8	140
16	RATNAGIRI	6678	5799	5803	4	875	2	46
17	SANGLI	8595	6776	6780	4	1815	4	96
18	BHANDARA	15172	12221	12224	3	2948	4	155
19	NAGPUR	10691	8943	8946	3	1745	3	92
20	NANDURBAR	14070	10196	10199	3	3871	7	204
21	PARBHANI	16485	13086	13089	3	3396	4	179
22	PUNE	12749	9826	9829	3	2920	6	154
23	SOLAPUR	18408	14720	14723	3	3685	8	194
24	AKOLA	17081	11984	11986	2	5095	9	268
25	CHANDRAPUR	23225	18204	18206	2	5019	14	264
26	AMRAVATI	19055	13471	13472	1	5583	9	294
27	NANDED	19868	11663	11664	1	8204	10	432
28	PALGHAR	10269	7093	7094	1	3175	6	167
29	KOLHAPUR	12528	10477	10477	0	2051	4	108
30	OSMANABAD	16869	10633	10633	0	6236	13	328
31	RAIGAD	5907	4447	4447	0	1460	3	77
32	SATARA	10632	9264	9264	0	1368	5	72
33	SINDHUDURG	2106	1828	1828	0	278	1	15
34	THANE	4652	3640	3640	0	1012	2	53
	<b>Total</b>	<b>539421</b>	<b>390746</b>	<b>390995</b>	<b>249</b>	<b>148426</b>	<b>309</b>	<b>7812</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NAGPUR DIV.	91	13774	281	29625	215	13602
2	AURANGABAD DIV.	151	30871	247	61373	147	17829
3	AMRAVATI DIV.	251	37011	100	39429	163	13344
4	NASHIK DIV.	23	15880	84	45147	187	24345
5	KONKAN DIV.	4	929	98	5609	141	5683
6	PUNE DIV.	55	14061	65	19499	66	6453
	<b>Total</b>	<b>575</b>	<b>112526</b>	<b>875</b>	<b>200682</b>	<b>919</b>	<b>81256</b>

PMAY-G 1st Ins Pending

SINDHUDURG	29
RAIGAD	49
RATNAGIRI	125
THANE	140
GADCHIROLI	537
PALGHAR	586
KOLHAPUR	743
SANGLI	1132
SATARA	1264
WARDHA	1937
PARBHANI	1953
DHULE	2076
NASHIK	2236
GONDIA	2273
HINGOLI	2382
NAGPUR	2457
NANDURBAR	2530
PUNE	2924
CHANDRAPUR	3045
JALNA	3086
AURANGABAD	3492
BHANDARA	3525
AHMEDNAGAR	3544
WASHIM	3653
OSMANABAD	3994
LATUR	4065
BEED	4585
YAVATMAL	5146
AKOLA	5293
JALGAON	5494
NANDED	7314
SOLAPUR	7998
BULDHANA	9742
AMRAVATI	13177

PMAY-G 2nd Ins Pending

SINDHUDURG	578
RAIGAD	638
RATNAGIRI	809
THANE	1088
WARDHA	1920
SATARA	1958
PALGHAR	2496
PUNE	2717
KOLHAPUR	3392
GADCHIROLI	3664
OSMANABAD	3725
NAGPUR	3862
HINGOLI	3882
LATUR	4708
SANGLI	4794
AHMEDNAGAR	4845
WASHIM	5034
AKOLA	5288
JALNA	5721
CHANDRAPUR	6413
GONDIA	6620
SOLAPUR	6638
AURANGABAD	6839
BULDHANA	7031
BHANDARA	7146
NASHIK	7211
DHULE	7417
PARBHANI	7606
BEED	8992
AMRAVATI	9872
NANDURBAR	11842
YAVATMAL	12204
JALGAON	13832
NANDED	19900

PMAY-G 3rd Ins Pending

SINDHUDURG	376
RAIGAD	434
WARDHA	632
RATNAGIRI	697
KOLHAPUR	819
THANE	886
NAGPUR	969
OSMANABAD	974
SATARA	988
PUNE	989
HINGOLI	1172
LATUR	1402
SANGLI	1441
WASHIM	1620
AKOLA	1727
PARBHANI	1816
JALNA	2046
SOLAPUR	2216
BULDHANA	2314
BHANDARA	2512
AURANGABAD	2582
GADCHIROLI	2802
CHANDRAPUR	2950
AMRAVATI	2959
BEED	3094
PALGHAR	3290
GONDIA	3737
DHULE	3993
NASHIK	4163
JALGAON	4335
AHMEDNAGAR	4432
YAVATMAL	4724
NANDED	4743
NANDURBAR	7422

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	GONDIA	61	2273	130	6620	79	3737
2	NANDED	98	7314	93	19900	45	4743
3	CHANDRAPUR	13	3045	91	6413	82	2950
4	AKOLA	121	5293	4	5288	35	1727
5	PALGHAR	2	586	33	2496	96	3290
6	YAVATMAL	36	5146	32	12204	63	4724
7	NANDURBAR	0	2530	42	11842	82	7422
8	BEED	1	4585	83	8992	36	3094
9	AMRAVATI	39	13177	46	9872	34	2959
10	PARBHANI	7	1953	58	7606	34	1816
11	AHMEDNAGAR	5	3544	36	4845	41	4432
12	BULDHANA	47	9742	17	7031	16	2314
13	SOLAPUR	28	7998	14	6638	23	2216
14	THANE	0	140	61	1088	0	886
15	BHANDARA	0	3525	27	7146	30	2512
16	NASHIK	9	2236	4	7211	32	4163
17	PUNE	12	2924	16	2717	17	989
18	AURANGABAD	30	3492	2	6839	7	2582
19	SATARA	7	1264	18	1958	13	988
20	SANGLI	8	1132	16	4794	11	1441
21	WARDHA	4	1937	16	1920	14	632
22	JALNA	13	3086	4	5721	12	2046
23	GADCHIROLI	6	537	12	3664	8	2802
24	DHULE	4	2076	0	7417	21	3993
25	SINDHUDURG	0	29	0	578	24	376
26	WASHIM	8	3653	1	5034	15	1620
27	RATNAGIRI	2	125	0	809	21	697
28	JALGAON	5	5494	2	13832	11	4335
29	LATUR	2	4065	3	4708	9	1402
30	NAGPUR	7	2457	5	3862	2	969
31	HINGOLI	0	2382	4	3882	4	1172
32	RAIGAD	0	49	4	638	0	434
33	KOLHAPUR	0	743	1	3392	2	819
34	OSMANABAD	0	3994	0	3725	0	974
	<b>Total</b>	<b>575</b>	<b>112526</b>	<b>875</b>	<b>200682</b>	<b>919</b>	<b>81256</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD DIV.	127	15991	175	28724	81	11280
2	AMRAVATI DIV.	33	4252	85	13608	96	5643
3	NASHIK DIV.	20	1847	28	9122	75	6043
4	NAGPUR DIV.	30	2706	16	8248	28	4104
5	PUNE DIV.	27	1755	7	5385	11	2460
6	KONKAN DIV.	11	1417	12	2014	8	1587
<b>Total</b>		<b>248</b>	<b>27968</b>	<b>323</b>	<b>67101</b>	<b>299</b>	<b>31117</b>

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	39
CHANDRAPUR	66
THANE	96
RAIGAD	101
DHULE	155
NANDURBAR	157
SATARA	179
NASHIK	181
SANGLI	189
NAGPUR	242
PUNE	300
BHANDARA	350
KOLHAPUR	375
WASHIM	395
BULDHANA	423
PARBHANI	542
AHMEDNAGAR	554
GADCHIROLI	559
WARDHA	630
SOLAPUR	712
JALGAON	800
GONDIA	859
YAVATMAL	1099
AKOLA	1166
PALGHAR	1169
AMRAVATI	1169
JALNA	1368
AURANGABAD	1624
OSMANABAD	1834
LATUR	1950
HINGOLI	2363
BEED	2445
NANDED	3865

State Schemes 2nd Ins Pending

SINDHUDURG	121
RATNAGIRI	304
THANE	324
SATARA	504
RAIGAD	586
PALGHAR	679
GONDIA	760
NAGPUR	864
SANGLI	1001
WARDHA	1050
PUNE	1113
BHANDARA	1119
NANDURBAR	1138
KOLHAPUR	1161
NASHIK	1487
SOLAPUR	1606
DHULE	1683
WASHIM	1737
PARBHANI	1897
AKOLA	2113
GADCHIROLI	2150
CHANDRAPUR	2305
JALGAON	2333
AMRAVATI	2370
HINGOLI	2454
AHMEDNAGAR	2481
BULDHANA	2840
NANDED	3229
OSMANABAD	3291
AURANGABAD	3731
JALNA	4104
LATUR	4316
YAVATMAL	4548
BEED	5702

State Schemes 3rd Ins Pending

SINDHUDURG	89
RATNAGIRI	186
SATARA	290
NAGPUR	300
THANE	302
KOLHAPUR	347
SANGLI	381
RAIGAD	383
WARDHA	390
BHANDARA	411
GONDIA	517
PALGHAR	627
PUNE	690
WASHIM	728
SOLAPUR	752
HINGOLI	775
PARBHANI	856
AMRAVATI	856
AKOLA	918
AURANGABAD	997
NASHIK	1055
DHULE	1060
NANDURBAR	1118
NANDED	1131
GADCHIROLI	1216
OSMANABAD	1258
CHANDRAPUR	1270
JALGAON	1305
YAVATMAL	1497
AHMEDNAGAR	1505
BULDHANA	1644
LATUR	1680
BEED	2124
JALNA	2459

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AURANGABAD	32	1624	68	3731	17	997
2	JALNA	3	1368	37	4104	46	2459
3	BEED	26	2445	45	5702	8	2124
4	WASHIM	0	395	36	1737	39	728
5	BULDHANA	0	423	11	2840	33	1644
6	LATUR	21	1950	13	4316	8	1680
7	OSMANABAD	33	1834	7	3291	0	1258
8	AMRAVATI	28	1169	5	2370	6	856
9	GADCHIROLI	28	559	7	2150	3	1216
10	YAVATMAL	5	1099	17	4548	15	1497
11	KOLHAPUR	26	375	4	1161	1	347
12	NANDURBAR	7	157	10	1138	14	1118
13	AHMEDNAGAR	2	554	8	2481	20	1505
14	DHULE	0	155	1	1683	26	1060
15	NASHIK	2	181	4	1487	14	1055
16	AKOLA	0	1166	16	2113	3	918
17	JALGAON	9	800	5	2333	1	1305
18	THANE	9	96	2	324	4	302
19	GONDIA	0	859	4	760	10	517
20	NANDED	11	3865	2	3229	1	1131
21	RAIGAD	2	101	7	586	4	383
22	WARDHA	2	630	0	1050	10	390
23	PUNE	0	300	2	1113	4	690
24	CHANDRAPUR	0	66	2	2305	3	1270
25	PARBHANI	0	542	3	1897	1	856
26	SOLAPUR	0	712	0	1606	4	752
27	NAGPUR	0	242	2	864	1	300
28	RATNAGIRI	0	39	3	304	0	186
29	SATARA	0	179	1	504	2	290
30	BHANDARA	0	350	1	1119	1	411
31	HINGOLI	1	2363	0	2454	0	775
32	SANGLI	1	189	0	1001	0	381
33	PALGHAR	0	1169	0	679	0	627
34	SINDHUDURG	0	12	0	121	0	89
	<b>Total</b>	<b>248</b>	<b>27968</b>	<b>323</b>	<b>67101</b>	<b>299</b>	<b>31117</b>
