



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १४.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१३७०९	२९	९९८४९०	९५२	०	०	०
राज्य योजना	५४०८६५	७८६	३९१५०८	३७३	१	२	०
एकूण	१९५४५७४	८१५	१३८९९९८	१३२५	१	२	०

PMAY-G Completion Progress Bar

70.6%



PMAY-G Incomplete Houses bifurcation

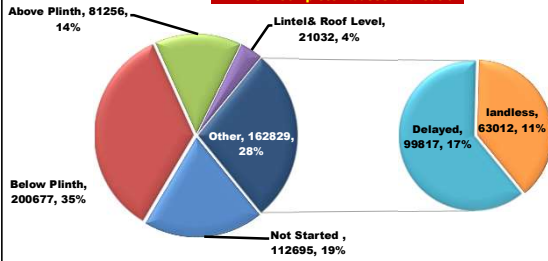


State Schemes Progress Bar

72.4%

State Schemes: Incomplete Houses bifurcation

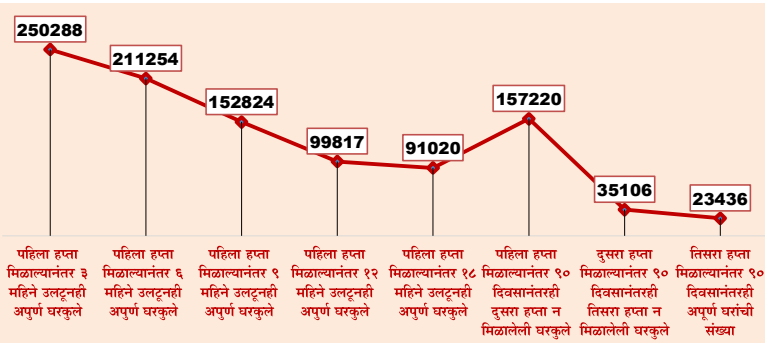


Abhiyan Achievement Day 114

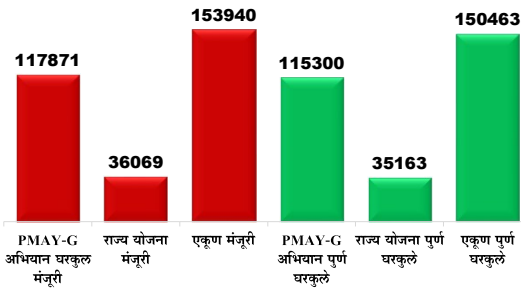

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	13.03.2023	14.03.2023	Daily_Achievement	Remaining
1	PUNE DIV.	126293	126053	126022	17	271
2	AURANGABAD DIV.	238296	237817	237825	8	471
3	NASHIK DIV.	414547	413823	413805	2	742
4	NAGPUR DIV.	292329	291804	291764	1	565
5	KONKAN DIV.	69657	69652	69620	1	37
6	AMRAVATI DIV.	274984	274676	274673	0	311
	Total	1416106	1413825	1413709	29	2397

PMAY-G Remaining Sanction

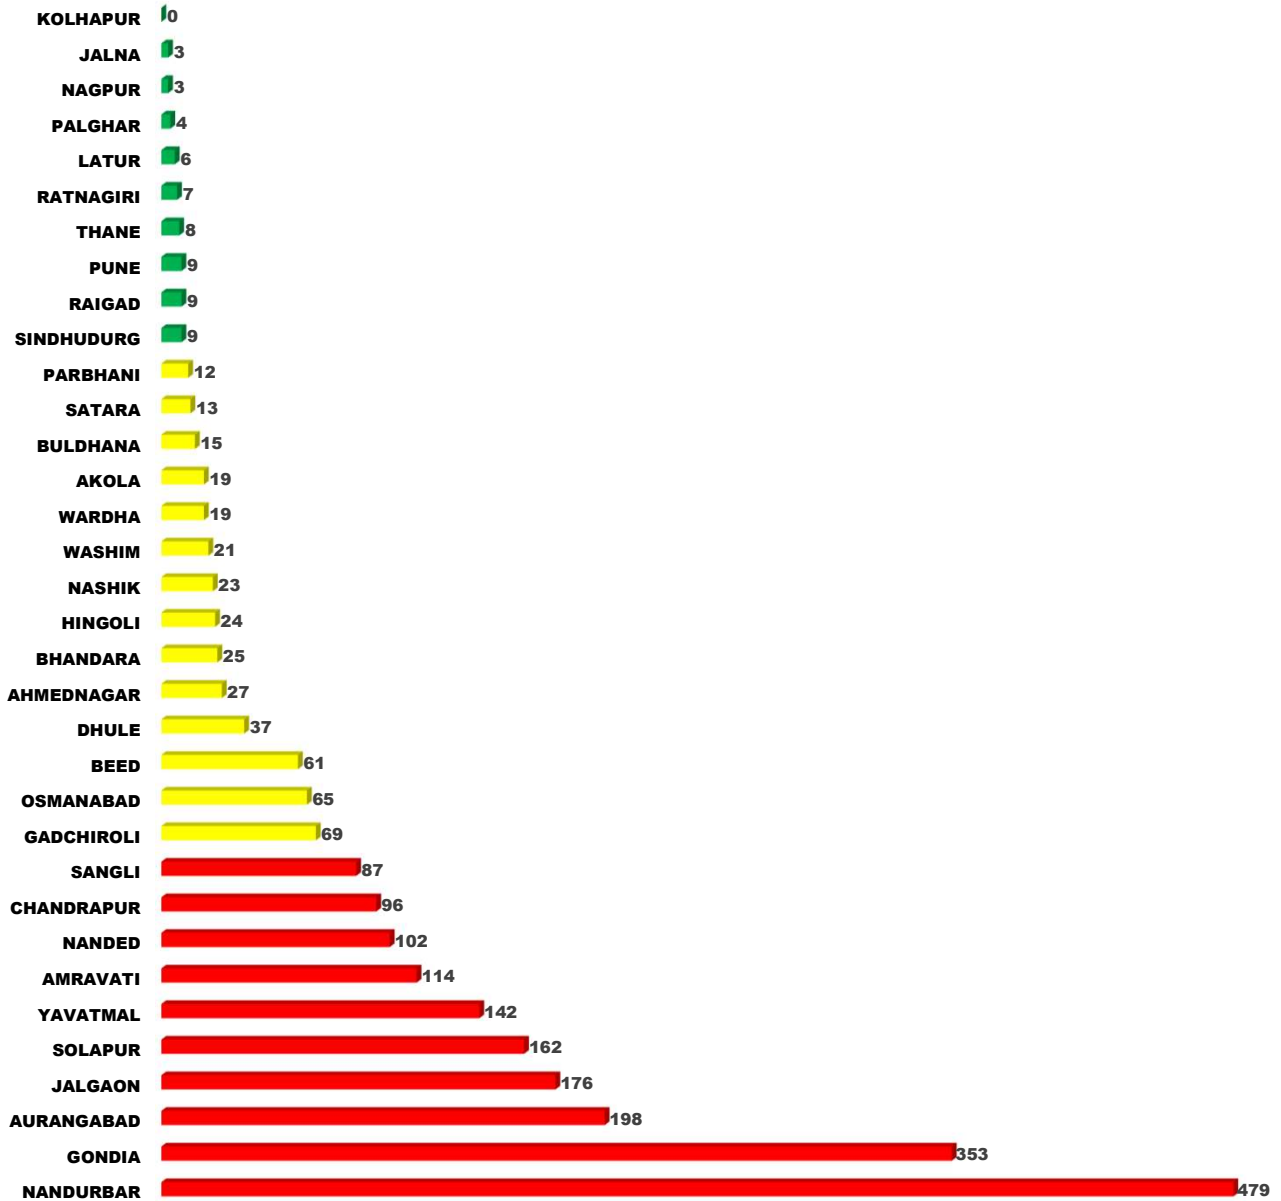


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	13.03.2023	14.03.2023	Daily_Achievement	Remaining
1	SANGLI	22158	22054	22071	17	87
2	NANDED	69565	69455	69463	8	102
3	NANDURBAR	119333	118852	118854	2	479
4	GONDIA	96470	96116	96117	1	353
5	RATNAGIRI	9923	9915	9916	1	7
6	AKOLA	48794	48775	48775	0	19
7	AURANGABAD	36792	36594	36594	0	198
8	BEED	35318	35257	35257	0	61
9	BHANDARA	65128	65103	65103	0	25
10	DHULE	64912	64875	64875	0	37
11	GADCHIROLI	31638	31569	31569	0	69
12	HINGOLI	18107	18083	18083	0	24
13	JALGAON	79767	79591	79591	0	176
14	JALNA	24047	24044	24044	0	3
15	KOLHAPUR	17770	17770	17770	0	0
16	LATUR	20799	20793	20793	0	6
17	NASHIK	89757	89734	89734	0	23
18	OSMANABAD	14565	14500	14500	0	65
19	PARBHANI	19103	19091	19091	0	12
20	RAIGAD	9844	9835	9835	0	9
21	THANE	9606	9598	9598	0	8
22	WARDHA	18671	18652	18652	0	19
23	WASHIM	20412	20391	20391	0	21
24	YAVATMAL	65390	65248	65248	0	142
25	BULDHANA	44742	44728	44727	-1	15
26	AMRAVATI	95646	95534	95532	-2	114
27	CHANDRAPUR	43220	43126	43124	-2	96
28	SOLAPUR	49902	49745	49740	-5	162
29	SINDHUDURG	5156	5156	5147	-9	9
30	PUNE	20979	20980	20970	-10	9
31	AHMEDNAGAR	60778	60771	60751	-20	27
32	PALGHAR	35128	35148	35124	-24	4
33	SATARA	15484	15504	15471	-33	13
34	NAGPUR	37202	37238	37199	-39	3
Total		1416106	1413825	1413709	29	2397

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	13.03.2023	14.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413805	317441	317845	404	95960	301	5645
2	AMRAVATI DIV.	274673	179564	179719	155	94954	198	5586
3	NAGPUR DIV.	291764	229825	229954	129	61810	191	3636
4	AURANGABAD DIV.	237825	131109	131235	126	106590	208	6270
5	KONKAN DIV.	69620	54518	54596	78	15024	46	884
6	PUNE DIV.	126022	85081	85141	60	40881	68	2405
Total		1413709	997538	998490	952	415219	1011	24425

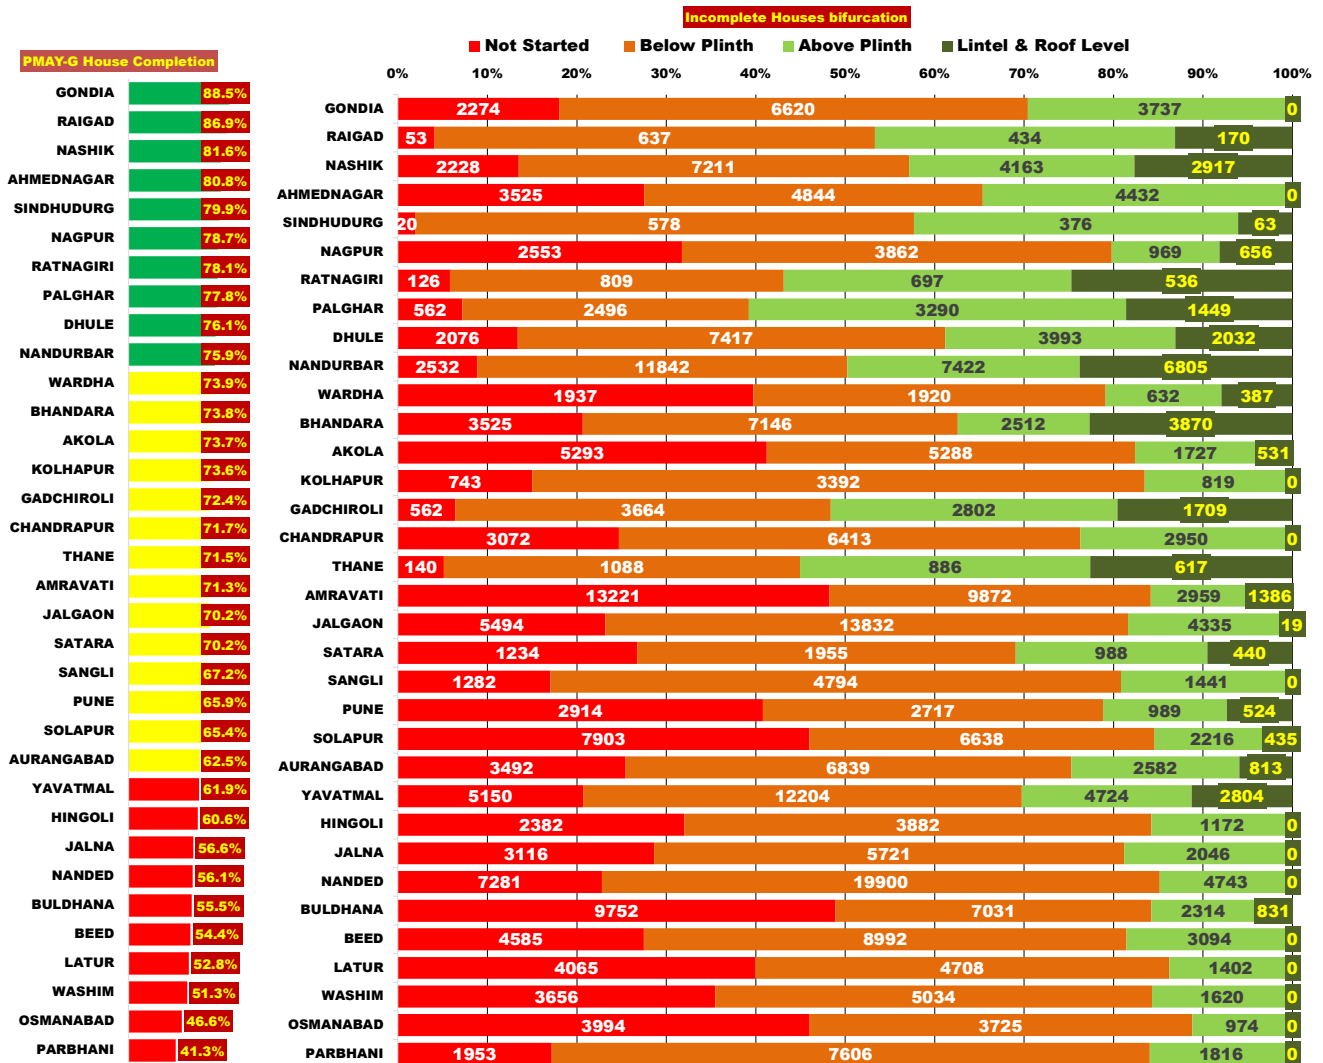


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	13.03.2023	14.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK	89734	73059	73215	156	16519	56	972
2	AHMEDNAGAR	60751	49018	49109	91	11642	97	685
3	NANDURBAR	118854	90178	90253	75	28601	40	1682
4	AMRAVATI	95532	68088	68140	52	27392	57	1611
5	GADCHIROLI	31569	22810	22857	47	8712	27	512
6	BULDHANA	44727	24767	24810	43	19917	33	1172
7	JALGAON	79591	55869	55911	42	23680	53	1393
8	DHULE	64875	49317	49357	40	15518	56	913
9	RATNAGIRI	9916	7709	7748	39	2168	14	128
10	YAVATMAL	65248	40332	40370	38	24878	61	1463
11	AURANGABAD	36594	22837	22868	31	13726	33	807
12	SATARA	15471	10826	10854	28	4617	13	272
13	GONDIA	96117	85040	85064	24	11053	66	650
14	NANDED	69463	38954	38978	24	30485	50	1793
15	NAGPUR	37199	29273	29294	21	7905	12	465
16	PALGHAR	35124	27306	27327	21	7797	21	459
17	AKOLA	48775	35916	35936	20	12839	25	755
18	SOLAPUR	49740	32529	32548	19	17192	23	1011
19	BHANDARA	65103	48032	48050	18	17053	35	1003
20	BEED	35257	19146	19163	17	16094	26	947
21	JALNA	24044	13604	13619	15	10425	27	613
22	PARBHANI	19091	7876	7891	15	11200	15	659
23	WARDHA	18652	13761	13776	15	4876	11	287
24	HINGOLI	18083	10956	10966	10	7117	18	419
25	LATUR	20793	10976	10986	10	9807	22	577
26	RAIGAD	9835	8537	8544	7	1291	4	76
27	SINDHUDURG	5147	4103	4110	7	1037	4	61
28	PUNE	20970	13820	13826	6	7144	11	420
29	KOLHAPUR	17770	13082	13087	5	4683	9	275
30	CHANDRAPUR	43124	30909	30913	4	12211	40	718
31	OSMANABAD	14500	6760	6764	4	7736	17	455
32	THANE	9598	6863	6867	4	2731	3	161
33	SANGLI	22071	14824	14826	2	7245	12	426
34	WASHIM	20391	10461	10463	2	9928	22	584
Total		1413709	997538	998490	952	415219	1011	24425

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	13.03.2023	14.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	159493	160129	636	39202
2	NAGPUR DIV.	116255	87214	87343	129	28912
3	AMRAVATI DIV.	109702	92397	92416	21	17286
4	KONKAN DIV.	34729	29612	29612	0	5117
5	PUNE DIV.	65334	62911	62911	0	2423
6	NASHIK DIV.	141360	108454	108454	0	32906
	Total	666711	540081	540865	786	125846

State Scheme Remaining Sanction

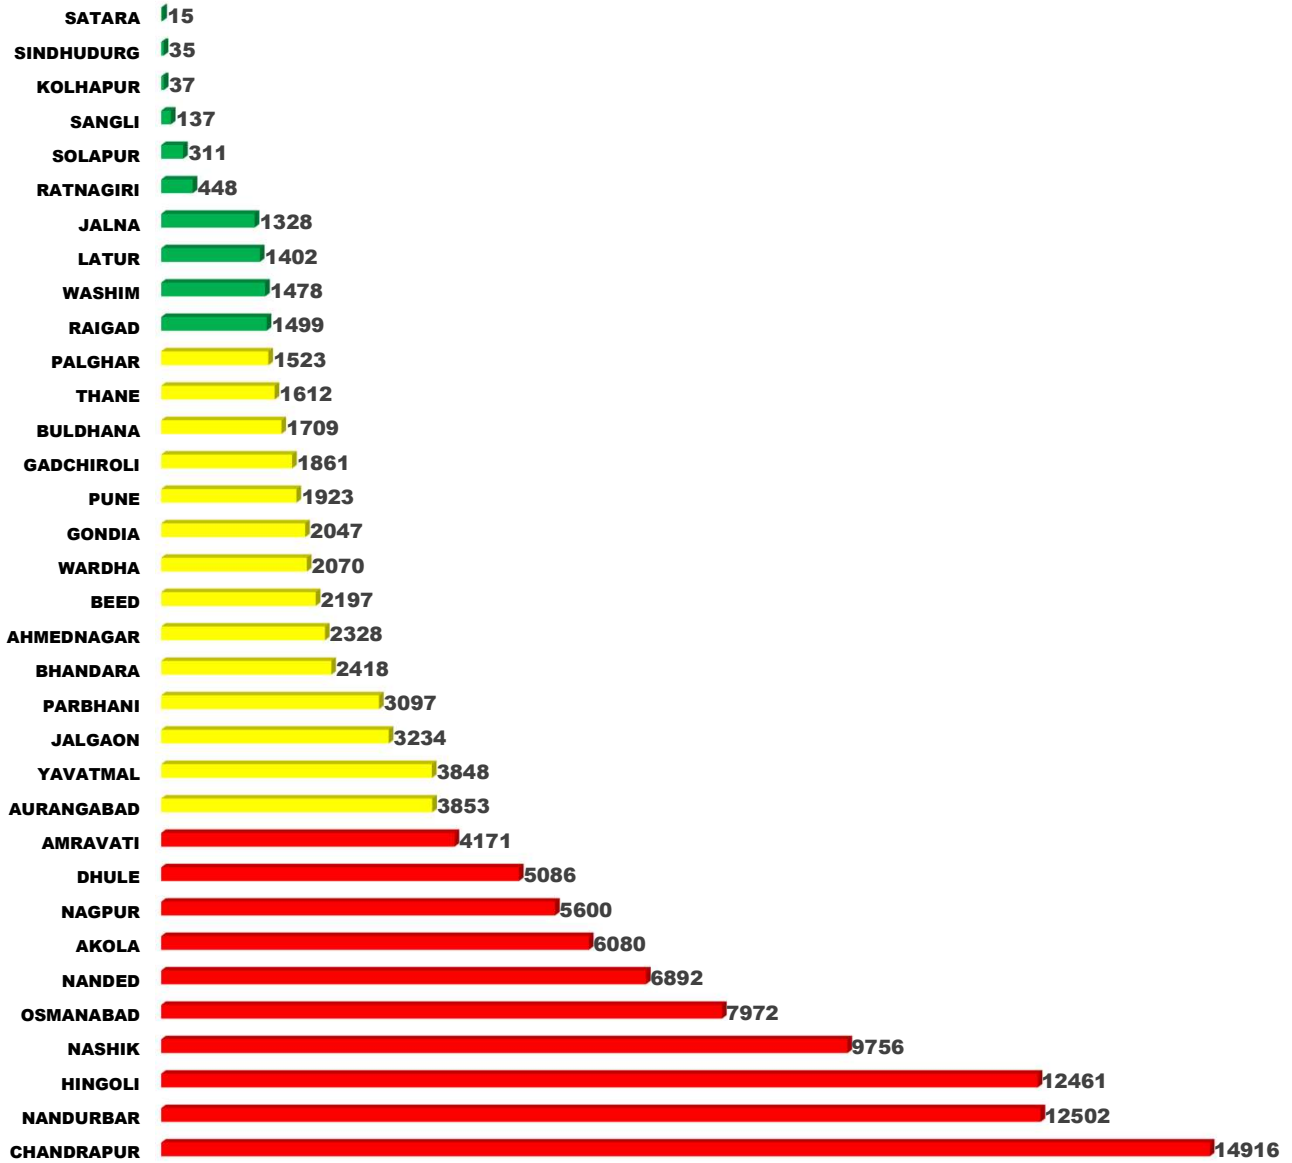


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	13.03.2023	14.03.2023	Daily_Achievement	Remaining
1	AURANGABAD	26141	21792	22288	496	3853
2	PARBHANI	19784	16548	16687	139	3097
3	WARDHA	13147	10973	11077	104	2070
4	AKOLA	23681	17580	17601	21	6080
5	GONDIA	14246	12180	12199	19	2047
6	CHANDRAPUR	38147	23225	23231	6	14916
7	BEED	26878	24680	24681	1	2197
8	AHMEDNAGAR	35298	32970	32970	0	2328
9	BHANDARA	17590	15172	15172	0	2418
10	BULDHANA	21616	19907	19907	0	1709
11	DHULE	21790	16704	16704	0	5086
12	GADCHIROLI	16834	14973	14973	0	1861
13	HINGOLI	27298	14837	14837	0	12461
14	JALGAON	25659	22425	22425	0	3234
15	JALNA	20446	19118	19118	0	1328
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	25769	25769	0	1402
18	NAGPUR	16291	10691	10691	0	5600
19	NANDED	26760	19868	19868	0	6892
20	NANDURBAR	26578	14076	14076	0	12502
21	NASHIK	32035	22279	22279	0	9756
22	OSMANABAD	24853	16881	16881	0	7972
23	PALGHAR	11792	10269	10269	0	1523
24	PUNE	14672	12749	12749	0	1923
25	RAIGAD	7406	5907	5907	0	1499
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10632	10632	0	15
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18407	18407	0	311
31	THANE	6264	4652	4652	0	1612
32	WASHIM	11500	10022	10022	0	1478
33	YAVATMAL	29681	25833	25833	0	3848
34	AMRAVATI	23224	19055	19053	-2	4171
Total		666711	540081	540865	786	125846

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	13.03.2023	14.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108454	86246	86376	130	22078	73	1299
2	AURANGABAD DIV.	160129	101081	101146	65	58983	97	3470
3	AMRAVATI DIV.	92416	62350	62409	59	30007	54	1765
4	NAGPUR DIV.	87343	67570	67627	57	19716	45	1160
5	PUNE DIV.	62911	51075	51111	36	11800	27	694
6	KONKAN DIV.	29612	22813	22839	26	6773	13	398
Total		540865	391135	391508	373	149357	308	8786

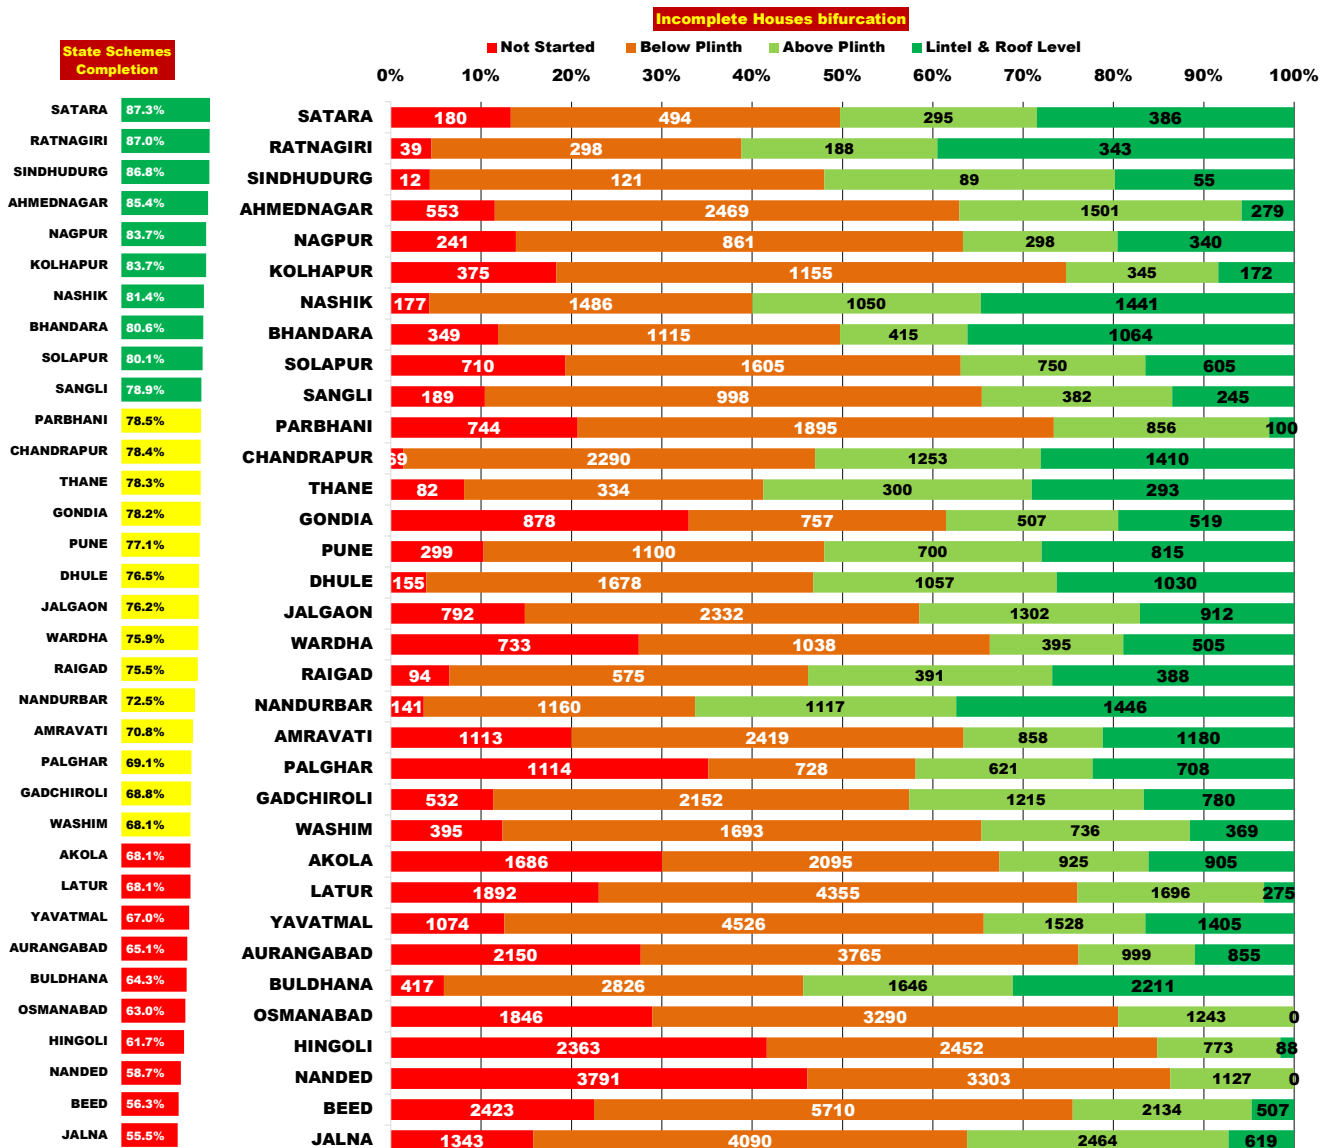

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	13.03.2023	14.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32970	28127	28168	41	4802	31	282
2	NASHIK	22279	18086	18125	39	4154	12	244
3	BULDHANA	19907	12774	12807	33	7100	16	418
4	JALGAON	22425	17061	17087	26	5338	12	314
5	GADCHIROLI	14973	10273	10294	21	4679	9	275
6	HINGOLI	14837	9140	9161	21	5676	6	334
7	GONDIA	12199	9522	9538	16	2661	8	157
8	BEED	24681	13892	13907	15	10774	14	634
9	SOLAPUR	18407	14723	14737	14	3670	8	216
10	SATARA	10632	9264	9277	13	1355	5	80
11	DHULE	16704	12772	12784	12	3920	11	231
12	NANDURBAR	14076	10200	10212	12	3864	7	227
13	RAIGAD	5907	4447	4459	12	1448	3	85
14	AMRAVATI	19053	13472	13483	11	5570	9	328
15	WARDHA	11077	8395	8406	11	2671	7	157
16	YAVATMAL	25833	17289	17300	11	8533	13	502
17	JALNA	19118	10592	10602	10	8516	30	501
18	LATUR	25769	17541	17551	10	8218	12	483
19	RATNAGIRI	6678	5803	5810	7	868	2	51
20	AKOLA	17601	11986	11990	4	5611	9	330
21	AURANGABAD	22288	14515	14519	4	7769	8	457
22	KOLHAPUR	12528	10477	10481	4	2047	4	120
23	PALGHAR	10269	7094	7098	4	3171	6	187
24	PUNE	12749	9831	9835	4	2914	6	171
25	BHANDARA	15172	12226	12229	3	2943	4	173
26	CHANDRAPUR	23231	18206	18209	3	5022	14	295
27	NAGPUR	10691	8948	8951	3	1740	3	102
28	NANDED	19868	11668	11671	3	8197	9	482
29	THANE	4652	3640	3643	3	1009	2	59
30	PARBHANI	16687	13090	13092	2	3595	4	211
31	SANGLI	8595	6780	6781	1	1814	4	107
32	OSMANABAD	16881	10643	10643	0	6238	13	367
33	SINDHUDURG	2106	1829	1829	0	277	1	16
34	WASHIM	10022	6829	6829	0	3193	7	188
	Total	540865	391135	391508	373	149357	308	8786

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	15855	0	45146	0	24345
2	AMRAVATI DIV.	0	37008	0	39429	0	13344
3	AURANGABAD DIV.	0	30838	0	61373	0	17829
4	NAGPUR DIV.	0	13712	0	29625	0	13602
5	KONKAN DIV.	0	898	0	5608	0	5683
6	PUNE DIV.	0	13943	0	19496	0	6453
	Total	0	112254	0	200677	0	81256

PMAY-G 1st Ins Pending

SINDHUDURG	20
RAIGAD	50
RATNAGIRI	126
THANE	140
GADCHIROLI	537
PALGHAR	562
KOLHAPUR	743
SANGLI	1149
SATARA	1234
WARDHA	1937
PARBHANI	1953
DHULE	2076
NASHIK	2228
GONDIA	2274
HINGOLI	2382
NAGPUR	2418
NANDURBAR	2532
PUNE	2914
CHANDRAPUR	3021
JALNA	3086
AURANGABAD	3492
AHMEDNAGAR	3525
BHANDARA	3525
WASHIM	3653
OSMANABAD	3994
LATUR	4065
BEED	4585
YAVATMAL	5146
AKOLA	5293
JALGAON	5494
NANDED	7281
SOLAPUR	7903
BULDHANA	9741
AMRAVATI	13175

PMAY-G 2nd Ins Pending

SINDHUDURG	578
RAIGAD	637
RATNAGIRI	809
THANE	1088
WARDHA	1920
SATARA	1955
PALGHAR	2496
PUNE	2717
KOLHAPUR	3392
GADCHIROLI	3664
OSMANABAD	3725
NAGPUR	3862
HINGOLI	3882
LATUR	4708
SANGLI	4794
AHMEDNAGAR	4844
WASHIM	5034
AKOLA	5288
JALNA	5721
CHANDRAPUR	6413
GONDIA	6620
SOLAPUR	6638
AURANGABAD	6839
BULDHANA	7031
BHANDARA	7146
NASHIK	7211
DHULE	7417
PARBHANI	7606
BEED	8992
AMRAVATI	9872
NANDURBAR	11842
YAVATMAL	12204
JALGAON	13832
NANDED	19900

PMAY-G 3rd Ins Pending

SINDHUDURG	376
RAIGAD	434
WARDHA	632
RATNAGIRI	697
KOLHAPUR	819
THANE	886
NAGPUR	969
OSMANABAD	974
SATARA	988
PUNE	989
HINGOLI	1172
LATUR	1402
SANGLI	1441
WASHIM	1620
AKOLA	1727
PARBHANI	1816
JALNA	2046
SOLAPUR	2216
BULDHANA	2314
BHANDARA	2512
AURANGABAD	2582
GADCHIROLI	2802
CHANDRAPUR	2950
AMRAVATI	2959
BEED	3094
PALGHAR	3290
GONDIA	3737
DHULE	3993
NASHIK	4163
JALGAON	4335
AHMEDNAGAR	4432
YAVATMAL	4724
NANDED	4743
NANDURBAR	7422

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	5293	0	5288	0	1727
2	AMRAVATI	0	13175	0	9872	0	2959
3	AURANGABAD	0	3492	0	6839	0	2582
4	BEED	0	4585	0	8992	0	3094
5	BHANDARA	0	3525	0	7146	0	2512
6	BULDHANA	0	9741	0	7031	0	2314
7	CHANDRAPUR	0	3021	0	6413	0	2950
8	DHULE	0	2076	0	7417	0	3993
9	GADCHIROLI	0	537	0	3664	0	2802
10	GONDIA	0	2274	0	6620	0	3737
11	HINGOLI	0	2382	0	3882	0	1172
12	JALGAON	0	5494	0	13832	0	4335
13	JALNA	0	3086	0	5721	0	2046
14	KOLHAPUR	0	743	0	3392	0	819
15	LATUR	0	4065	0	4708	0	1402
16	NAGPUR	0	2418	0	3862	0	969
17	NANDED	0	7281	0	19900	0	4743
18	NANDURBAR	0	2532	0	11842	0	7422
19	NASHIK	0	2228	0	7211	0	4163
20	OSMANABAD	0	3994	0	3725	0	974
21	PALGHAR	0	562	0	2496	0	3290
22	PARBHANI	0	1953	0	7606	0	1816
23	PUNE	0	2914	0	2717	0	989
24	RATNAGIRI	0	126	0	809	0	697
25	SANGLI	0	1149	0	4794	0	1441
26	SINDHUDURG	0	20	0	578	0	376
27	SOLAPUR	0	7903	0	6638	0	2216
28	THANE	0	140	0	1088	0	886
29	WARDHA	0	1937	0	1920	0	632
30	WASHIM	0	3653	0	5034	0	1620
31	YAVATMAL	0	5146	0	12204	0	4724
32	AHMEDNAGAR	-1	3525	0	4844	0	4432
33	RAIGAD	-1	50	0	637	0	434
34	SATARA	-1	1234	0	1955	0	988
	Total	0	112254	0	200677	0	81256

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	PUNE DIV.	0	1753	2	5352	0	2472
2	KONKAN DIV.	1	1341	0	2056	0	1589
3	NASHIK DIV.	0	1818	0	9125	0	6027
4	AMRAVATI DIV.	0	4685	0	13559	0	5693
5	AURANGABAD DIV.	0	16552	0	28860	0	11292
6	NAGPUR DIV.	0	2802	0	8213	0	4083
Total		1	28951	2	67165	0	31156

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	39
CHANDRAPUR	69
THANE	82
RAIGAD	94
NANDURBAR	141
DHULE	155
NASHIK	177
SATARA	180
SANGLI	189
NAGPUR	241
PUNE	299
BHANDARA	349
KOLHAPUR	375
WASHIM	395
BULDHANA	417
GADCHIROLI	532
AHMEDNAGAR	553
SOLAPUR	710
WARDHA	733
PARBHANI	744
JALGAON	792
GONDIA	878
YAVATMAL	1074
AMRAVATI	1113
PALGHAR	1114
JALNA	1343
AKOLA	1686
OSMANABAD	1846
LATUR	1892
AURANGABAD	2150
HINGOLI	2363
BEED	2423
NANDED	3791

State Schemes 2nd Ins Pending

SINDHUDURG	121
RATNAGIRI	298
THANE	334
SATARA	494
RAIGAD	575
PALGHAR	728
GONDIA	757
NAGPUR	861
SANGLI	998
WARDHA	1038
PUNE	1100
BHANDARA	1115
KOLHAPUR	1155
NANDURBAR	1160
NASHIK	1486
SOLAPUR	1605
DHULE	1678
WASHIM	1693
PARBHANI	1895
AKOLA	2095
GADCHIROLI	2152
CHANDRAPUR	2290
JALGAON	2332
AMRAVATI	2419
HINGOLI	2452
AHMEDNAGAR	2469
BULDHANA	2826
OSMANABAD	3290
NANDED	3303
AURANGABAD	3765
JALNA	4090
LATUR	4355
YAVATMAL	4526
BEED	5710

State Schemes 3rd Ins Pending

SINDHUDURG	89
RATNAGIRI	188
SATARA	295
NAGPUR	298
THANE	300
KOLHAPUR	345
SANGLI	382
RAIGAD	391
WARDHA	395
BHANDARA	415
GONDIA	507
PALGHAR	621
PUNE	700
WASHIM	736
SOLAPUR	750
HINGOLI	773
PARBHANI	856
AMRAVATI	858
AKOLA	925
AURANGABAD	999
NASHIK	1050
DHULE	1057
NANDURBAR	1117
NANDED	1127
GADCHIROLI	1215
OSMANABAD	1243
CHANDRAPUR	1253
JALGAON	1302
AHMEDNAGAR	1501
YAVATMAL	1528
BULDHANA	1646
LATUR	1696
BEED	2134
JALNA	2464

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	SATARA	-1	180	2	494	0	295
2	PALGHAR	1	1114	0	728	0	621
3	AKOLA	0	1686	0	2095	0	925
4	AMRAVATI	0	1113	0	2419	0	858
5	AURANGABAD	0	2150	0	3765	0	999
6	BEED	0	2423	0	5710	0	2134
7	BHANDARA	0	349	0	1115	0	415
8	BULDHANA	0	417	0	2826	0	1646
9	CHANDRAPUR	0	69	0	2290	0	1253
10	DHULE	0	155	0	1678	0	1057
11	GADCHIROLI	0	532	0	2152	0	1215
12	GONDIA	0	878	0	757	0	507
13	HINGOLI	0	2363	0	2452	0	773
14	JALGAON	0	792	0	2332	0	1302
15	JALNA	0	1343	0	4090	0	2464
16	KOLHAPUR	0	375	0	1155	0	345
17	LATUR	0	1892	0	4355	0	1696
18	NAGPUR	0	241	0	861	0	298
19	NANDED	0	3791	0	3303	0	1127
20	NANDURBAR	0	141	0	1160	0	1117
21	NASHIK	0	177	0	1486	0	1050
22	OSMANABAD	0	1846	0	3290	0	1243
23	PARBHANI	0	744	0	1895	0	856
24	PUNE	0	299	0	1100	0	700
25	RAIGAD	0	94	0	575	0	391
26	RATNAGIRI	0	39	0	298	0	188
27	SANGLI	0	189	0	998	0	382
28	SINDHUDURG	0	12	0	121	0	89
29	SOLAPUR	0	710	0	1605	0	750
30	THANE	0	82	0	334	0	300
31	WARDHA	0	733	0	1038	0	395
32	WASHIM	0	395	0	1693	0	736
33	YAVATMAL	0	1074	0	4526	0	1528
34	AHMEDNAGAR	-2	553	0	2469	0	1501
	Total	1	28951	2	67165	0	31156
