



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १९.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१२९६७	७	१००१९७८	३६०	११५३	१०४८	१०९९
राज्य योजना	५४१६४१	०	३९२७०२	१२८	०	०	०
एकूण	१९५४६०८	७	१३९४६८०	४८८	११५३	१०४८	१०९९

PMAY-G Completion Progress Bar

70.9%



PMAY-G Incomplete Houses bifurcation

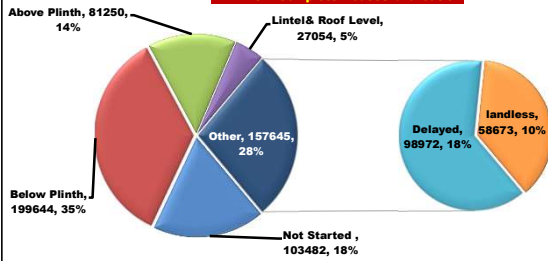


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

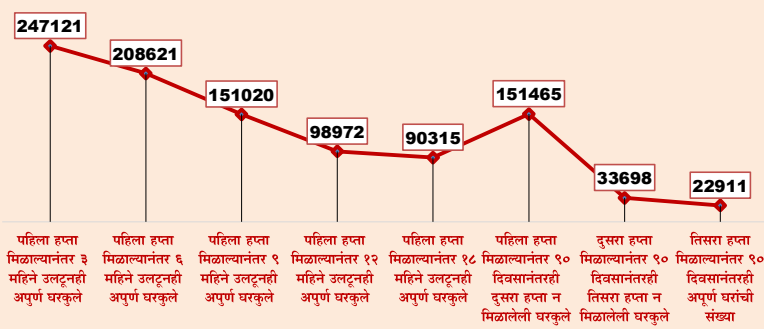


Abhiyan Achievement Day 119

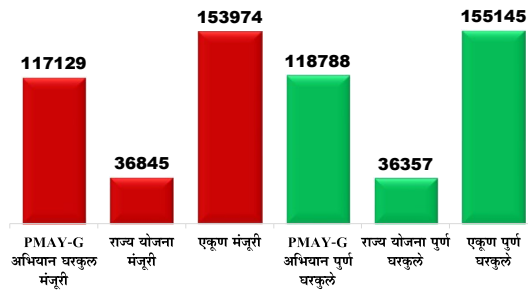

PMAY-G : House completion ( Abhiyan Achievement)

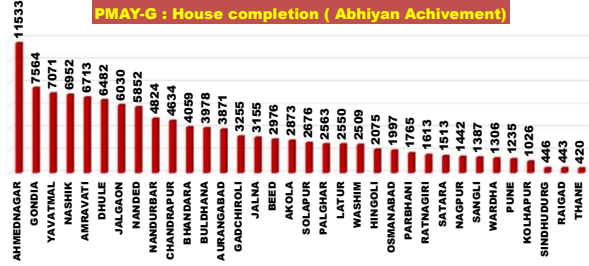

State Schemes : House completion ( Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	18.03.2023	19.03.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414691	413723	413728	5	963
2	AURANGABAD DIV.	238197	237442	237444	2	753
3	AMRAVATI DIV.	275061	274630	274630	0	431
4	NAGPUR DIV.	292352	291701	291700	0	652
5	KONKAN DIV.	69743	69616	69616	0	127
6	PUNE DIV.	126192	125851	125849	0	343
	<b>Total</b>	<b>1416236</b>	<b>1412963</b>	<b>1412967</b>	<b>7</b>	<b>3269</b>

PMAY-G Remaining Sanction

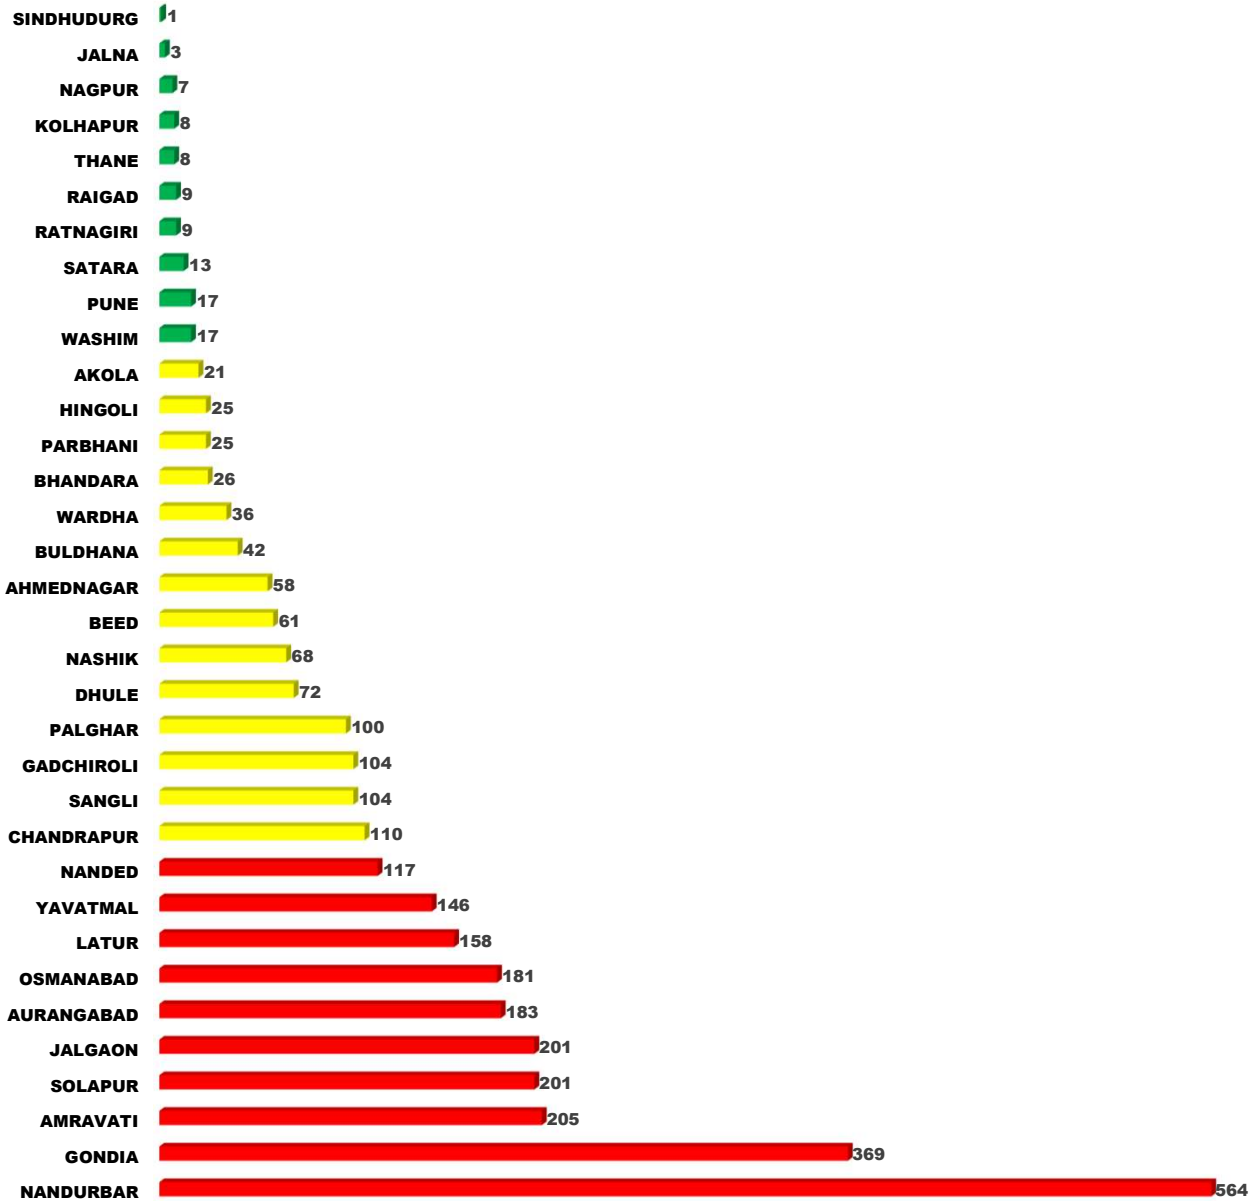


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	18.03.2023	19.03.2023	Daily_Achievement	Remaining
1	NASHIK	89724	89651	89656	5	68
2	NANDED	69551	69432	69434	2	117
3	AHMEDNAGAR	60805	60747	60747	0	58
4	AKOLA	48796	48775	48775	0	21
5	AMRAVATI	95708	95503	95503	0	205
6	AURANGABAD	36795	36612	36612	0	183
7	BEED	35319	35258	35258	0	61
8	BULDHANA	44769	44727	44727	0	42
9	CHANDRAPUR	43228	43118	43118	0	110
10	DHULE	64947	64875	64875	0	72
11	GADCHIROLI	31677	31573	31573	0	104
12	GONDIA	96485	96116	96116	0	369
13	HINGOLI	18108	18083	18083	0	25
14	JALGAON	79787	79586	79586	0	201
15	JALNA	24047	24044	24044	0	3
16	KOLHAPUR	17773	17765	17765	0	8
17	LATUR	20729	20571	20571	0	158
18	NAGPUR	37193	37186	37186	0	7
19	NANDURBAR	119428	118864	118864	0	564
20	OSMANABAD	14545	14364	14364	0	181
21	PALGHAR	35223	35123	35123	0	100
22	PARBHANI	19103	19078	19078	0	25
23	PUNE	20978	20961	20961	0	17
24	RAIGAD	9844	9835	9835	0	9
25	RATNAGIRI	9922	9913	9913	0	9
26	SANGLI	22175	22071	22071	0	104
27	SINDHUDURG	5148	5147	5147	0	1
28	SOLAPUR	49826	49625	49625	0	201
29	THANE	9606	9598	9598	0	8
30	WARDHA	18645	18609	18609	0	36
31	WASHIM	20412	20395	20395	0	17
32	YAVATMAL	65376	65230	65230	0	146
33	BHANDARA	65124	65099	65098	-1	26
34	SATARA	15440	15429	15427	-2	13
<b>Total</b>		<b>1416236</b>	<b>1412963</b>	<b>1412967</b>	<b>7</b>	<b>3269</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	18.03.2023	19.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413728	319179	319335	156	94393	301	7866
2	AMRAVATI DIV.	274630	180228	180301	73	94329	194	7861
3	AURANGABAD DIV.	237444	131743	131802	59	105642	204	8804
4	KONKAN DIV.	69616	54860	54893	33	14723	46	1227
5	NAGPUR DIV.	291700	230356	230388	32	61312	187	5109
6	PUNE DIV.	125849	85252	85259	7	40590	66	3383
<b>Total</b>		<b>1412967</b>	<b>1001618</b>	<b>1001978</b>	<b>360</b>	<b>410989</b>	<b>998</b>	<b>34249</b>

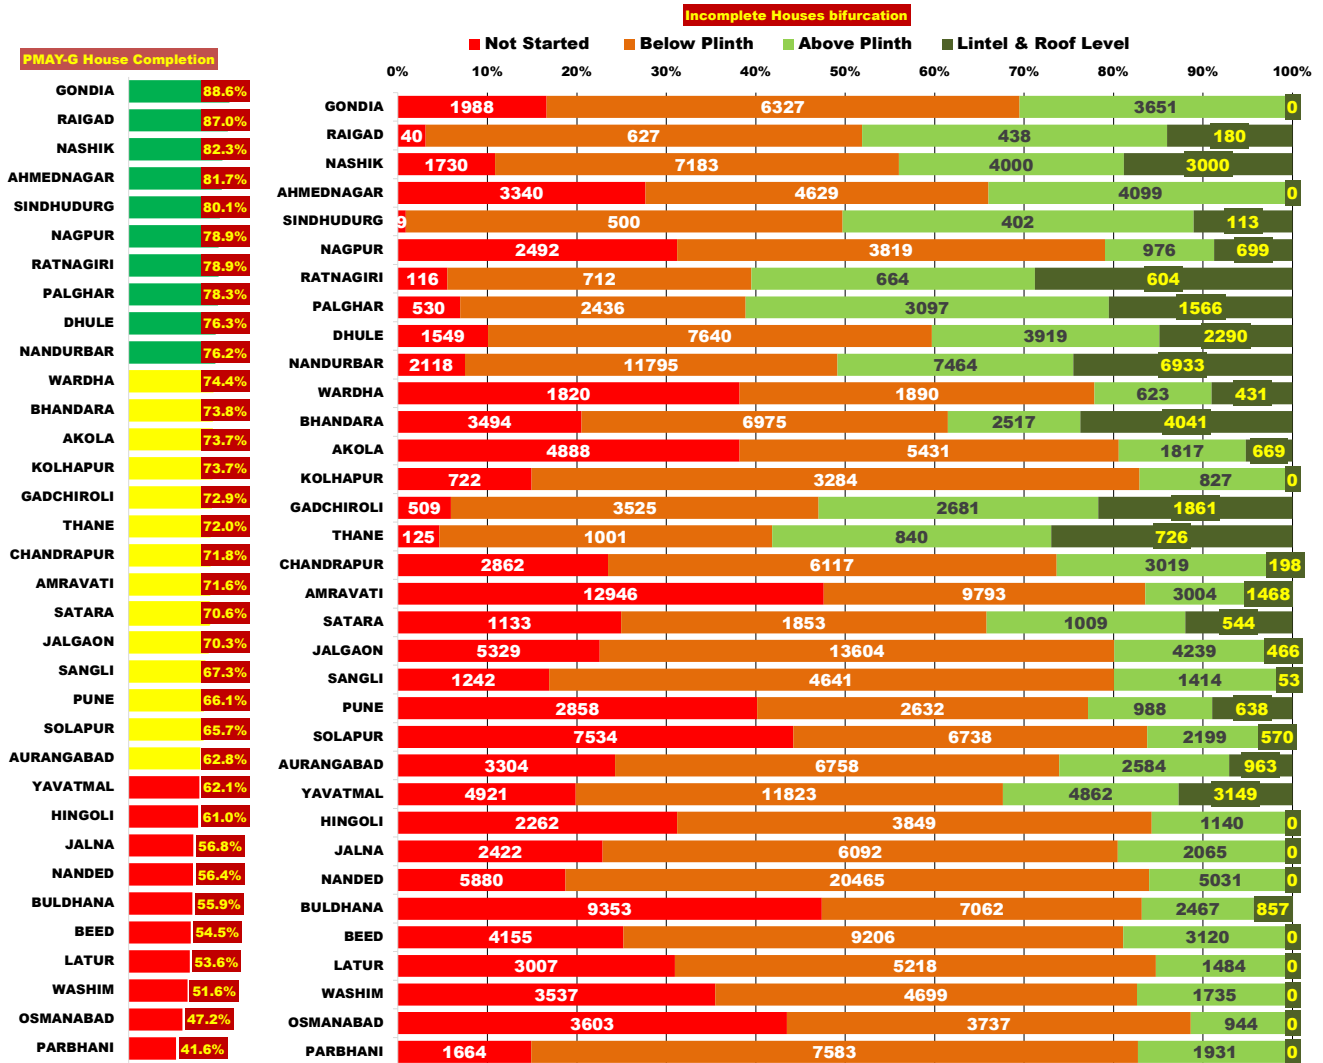


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	18.03.2023	19.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	60747	49535	49613	78	11134	97	928
2	NASHIK	89656	73689	73743	54	15913	58	1326
3	AMRAVATI	95503	68297	68338	41	27165	56	2264
4	PALGHAR	35123	27464	27494	30	7629	22	636
5	DHULE	64875	49453	49477	24	15398	54	1283
6	NANDED	69434	39145	39162	17	30272	49	2523
7	AURANGABAD	36612	22988	23003	15	13609	33	1134
8	GADCHIROLI	31573	23007	23022	15	8551	27	713
9	BULDHANA	44727	24986	24999	13	19728	33	1644
10	CHANDRAPUR	43118	30962	30973	11	12145	39	1012
11	OSMANABAD	14364	6767	6777	10	7587	17	632
12	AKOLA	48775	35961	35970	9	12805	24	1067
13	YAVATMAL	65230	40470	40479	9	24751	59	2063
14	SATARA	15427	10882	10888	6	4539	13	378
15	BEED	35258	19199	19204	5	16054	25	1338
16	LATUR	20571	11019	11024	5	9547	21	796
17	GONDIA	96116	85139	85142	3	10974	64	915
18	HINGOLI	18083	11030	11033	3	7050	17	588
19	JALNA	24044	13658	13661	3	10383	27	865
20	RATNAGIRI	9913	7814	7817	3	2096	14	175
21	WARDHA	18609	13842	13845	3	4764	11	397
22	PARBHANI	19078	7937	7938	1	11140	15	928
23	SOLAPUR	49625	32583	32584	1	17041	22	1420
24	WASHIM	20395	10514	10515	1	9880	21	823
25	BHANDARA	65098	48071	48071	0	17027	34	1419
26	JALGAON	79586	55948	55948	0	23638	51	1970
27	KOLHAPUR	17765	13088	13088	0	4677	9	390
28	NAGPUR	37186	29335	29335	0	7851	12	654
29	NANDURBAR	118864	90554	90554	0	28310	41	2359
30	PUNE	20961	13845	13845	0	7116	10	593
31	RAIGAD	9835	8553	8553	0	1282	4	107
32	SANGLI	22071	14854	14854	0	7217	12	601
33	SINDHUDURG	5147	4123	4123	0	1024	4	85
34	THANE	9598	6906	6906	0	2692	4	224
Total		1412967	1001618	1001978	360	410989	998	34249

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	18.03.2023	19.03.2023	Daily Achievement	Remaining
1	KONKAN DIV.	34729	29664	29664	0	5065
2	PUNE DIV.	65334	62909	62909	0	2425
3	NASHIK DIV.	141360	108472	108472	0	32888
4	AURANGABAD DIV.	199331	160595	160595	0	38736
5	AMRAVATI DIV.	109702	92584	92582	0	17120
6	NAGPUR DIV.	116255	87419	87419	0	28836
	<b>Total</b>	<b>666711</b>	<b>541643</b>	<b>541641</b>	<b>0</b>	<b>125070</b>

State Scheme Remaining Sanction

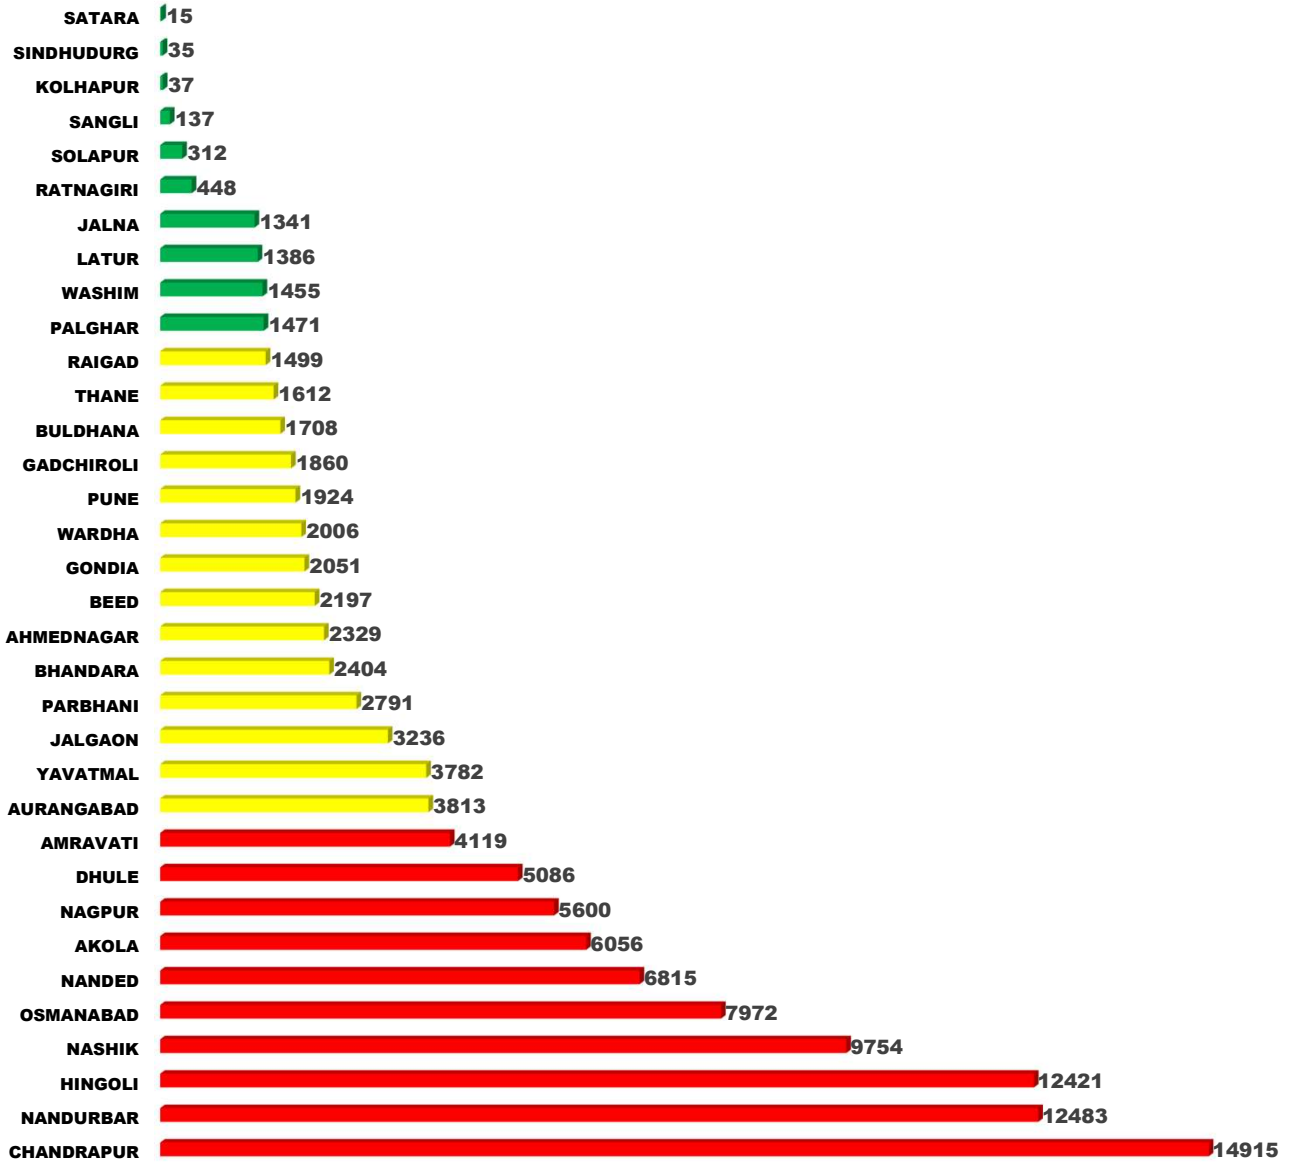


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	18.03.2023	19.03.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	35298	32969	32969	0	2329
2	AKOLA	23681	17625	17625	0	6056
3	AMRAVATI	23224	19105	19105	0	4119
4	AURANGABAD	26141	22328	22328	0	3813
5	BEED	26878	24681	24681	0	2197
6	BHANDARA	17590	15186	15186	0	2404
7	BULDHANA	21616	19908	19908	0	1708
8	CHANDRAPUR	38147	23232	23232	0	14915
9	DHULE	21790	16704	16704	0	5086
10	GADCHIROLI	16834	14974	14974	0	1860
11	GONDIA	14246	12195	12195	0	2051
12	HINGOLI	27298	14877	14877	0	12421
13	JALGAON	25659	22423	22423	0	3236
14	JALNA	20446	19105	19105	0	1341
15	KOLHAPUR	12565	12528	12528	0	37
16	LATUR	27171	25785	25785	0	1386
17	NAGPUR	16291	10691	10691	0	5600
18	NANDED	26760	19945	19945	0	6815
19	NANDURBAR	26578	14095	14095	0	12483
20	NASHIK	32035	22281	22281	0	9754
21	OSMANABAD	24853	16881	16881	0	7972
22	PALGHAR	11792	10321	10321	0	1471
23	PARBHANI	19784	16993	16993	0	2791
24	PUNE	14672	12748	12748	0	1924
25	RAIGAD	7406	5907	5907	0	1499
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10632	10632	0	15
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18406	18406	0	312
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	11141	11141	0	2006
33	YAVATMAL	29681	25899	25899	0	3782
34	WASHIM	11500	10047	10045	-2	1455
<b>Total</b>		<b>666711</b>	<b>541643</b>	<b>541641</b>	<b>0</b>	<b>125070</b>



## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	18.03.2023	19.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108472	86722	86782	60	21690	73	1808
2	AMRAVATI DIV.	92582	62618	62653	35	29929	54	2494
3	AURANGABAD DIV.	160595	101377	101403	26	59192	95	4933
4	NAGPUR DIV.	87419	67793	67798	5	19621	44	1635
5	PUNE DIV.	62909	51151	51153	2	11756	26	980
6	KONKAN DIV.	29664	22913	22913	0	6751	13	563
<b>Total</b>		<b>541641</b>	<b>392574</b>	<b>392702</b>	<b>128</b>	<b>148939</b>	<b>306</b>	<b>12412</b>

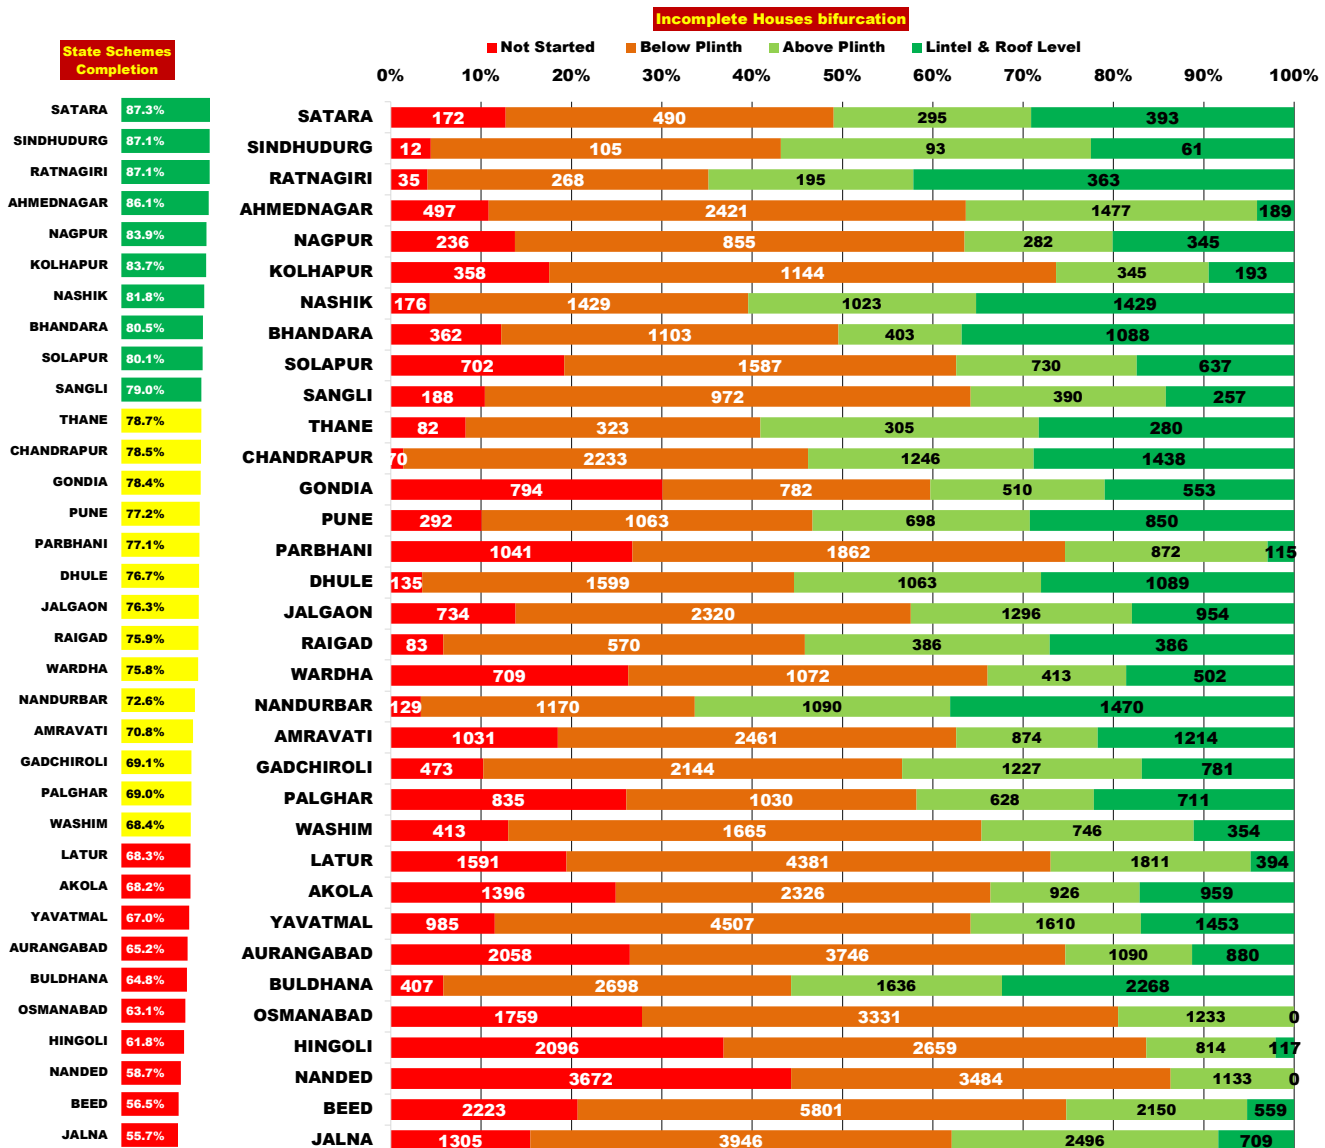

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	18.03.2023	19.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32969	28340	28385	45	4584	32	382
2	WASHIM	10045	6856	6867	11	3178	7	265
3	BULDHANA	19908	12889	12899	10	7009	16	584
4	NASHIK	22281	18214	18224	10	4057	13	338
5	AMRAVATI	19105	13518	13525	7	5580	9	465
6	NANDED	19945	11692	11699	7	8246	9	687
7	AURANGABAD	22328	14549	14554	5	7774	8	648
8	DHULE	16704	12813	12818	5	3886	11	324
9	BEED	24681	13944	13948	4	10733	14	894
10	GADCHIROLI	14974	10345	10349	4	4625	9	385
11	JALNA	19105	10645	10649	4	8456	29	705
12	YAVATMAL	25899	17340	17344	4	8555	13	713
13	AKOLA	17625	12015	12018	3	5607	9	467
14	HINGOLI	14877	9188	9191	3	5686	6	474
15	SOLAPUR	18406	14748	14750	2	3656	8	305
16	LATUR	25785	17607	17608	1	8177	12	681
17	OSMANABAD	16881	10650	10651	1	6230	12	519
18	PARBHANI	16993	13102	13103	1	3890	4	324
19	WARDHA	11141	8444	8445	1	2696	7	225
20	BHANDARA	15186	12230	12230	0	2956	4	246
21	CHANDRAPUR	23232	18245	18245	0	4987	14	416
22	GONDIA	12195	9556	9556	0	2639	8	220
23	JALGAON	22423	17119	17119	0	5304	11	442
24	KOLHAPUR	12528	10488	10488	0	2040	3	170
25	NAGPUR	10691	8973	8973	0	1718	4	143
26	NANDURBAR	14095	10236	10236	0	3859	6	322
27	PALGHAR	10321	7117	7117	0	3204	6	267
28	PUNE	12748	9845	9845	0	2903	6	242
29	RAIGAD	5907	4482	4482	0	1425	3	119
30	RATNAGIRI	6678	5817	5817	0	861	2	72
31	SANGLI	8595	6788	6788	0	1807	4	151
32	SATARA	10632	9282	9282	0	1350	5	113
33	SINDHUDURG	2106	1835	1835	0	271	1	23
34	THANE	4652	3662	3662	0	990	2	83
	<b>Total</b>	<b>541641</b>	<b>392574</b>	<b>392702</b>	<b>128</b>	<b>148939</b>	<b>306</b>	<b>12412</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD DIV.	699	26267	412	62908	323	18299
2	NASHIK DIV.	174	14066	205	44851	304	23721
3	AMRAVATI DIV.	215	35581	176	38808	175	13885
4	NAGPUR DIV.	42	12954	173	28653	173	13467
5	KONKAN DIV.	14	817	30	5276	79	5441
6	PUNE DIV.	9	13356	52	19148	45	6437
	<b>Total</b>	<b>1153</b>	<b>103041</b>	<b>1048</b>	<b>199644</b>	<b>1099</b>	<b>81250</b>

PMAY-G 1st Ins Pending

SINDHUDURG	9
RAIGAD	37
RATNAGIRI	116
THANE	125
GADCHIROLI	484
PALGHAR	530
KOLHAPUR	722
SANGLI	1109
SATARA	1133
DHULE	1549
PARBHANI	1664
NASHIK	1730
WARDHA	1820
GONDIA	1988
NANDURBAR	2118
HINGOLI	2262
NAGPUR	2357
JALNA	2392
CHANDRAPUR	2811
PUNE	2858
LATUR	3007
AURANGABAD	3304
AHMEDNAGAR	3340
BHANDARA	3494
WASHIM	3534
OSMANABAD	3603
BEED	4155
AKOLA	4888
YAVATMAL	4917
JALGAON	5329
NANDED	5880
SOLAPUR	7534
BULDHANA	9342
AMRAVATI	12900

PMAY-G 2nd Ins Pending

SINDHUDURG	500
RAIGAD	627
RATNAGIRI	712
THANE	1001
SATARA	1853
WARDHA	1890
PALGHAR	2436
PUNE	2632
KOLHAPUR	3284
GADCHIROLI	3525
OSMANABAD	3737
NAGPUR	3819
HINGOLI	3849
AHMEDNAGAR	4629
SANGLI	4641
WASHIM	4699
LATUR	5218
AKOLA	5431
JALNA	6092
CHANDRAPUR	6117
GONDIA	6327
SOLAPUR	6738
AURANGABAD	6758
BHANDARA	6975
BULDHANA	7062
NASHIK	7183
PARBHANI	7583
DHULE	7640
BEED	9206
AMRAVATI	9793
NANDURBAR	11795
YAVATMAL	11823
JALGAON	13604
NANDED	20465

PMAY-G 3rd Ins Pending

SINDHUDURG	402
RAIGAD	438
WARDHA	623
RATNAGIRI	664
KOLHAPUR	827
THANE	840
OSMANABAD	944
NAGPUR	976
PUNE	988
SATARA	1009
HINGOLI	1140
SANGLI	1414
LATUR	1484
WASHIM	1735
AKOLA	1817
PARBHANI	1931
JALNA	2065
SOLAPUR	2199
BULDHANA	2467
BHANDARA	2517
AURANGABAD	2584
GADCHIROLI	2681
AMRAVATI	3004
CHANDRAPUR	3019
PALGHAR	3097
BEED	3120
GONDIA	3651
DHULE	3919
NASHIK	4000
AHMEDNAGAR	4099
JALGAON	4239
YAVATMAL	4862
NANDED	5031
NANDURBAR	7464

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NANDED	315	5880	193	20465	122	5031
2	NASHIK	86	1730	105	7183	174	4000
3	AKOLA	138	4888	83	5431	67	1817
4	BEED	117	4155	26	9206	30	3120
5	JALNA	77	2392	38	6092	44	2065
6	LATUR	78	3007	51	5218	24	1484
7	AHMEDNAGAR	19	3340	40	4629	85	4099
8	GADCHIROLI	8	484	59	3525	74	2681
9	BULDHANA	42	9342	51	7062	46	2467
10	HINGOLI	31	2262	54	3849	52	1140
11	PARBHANI	72	1664	28	7583	18	1931
12	BHANDARA	1	3494	58	6975	57	2517
13	NANDURBAR	63	2118	27	11795	18	7464
14	WASHIM	28	3534	20	4699	31	1735
15	JALGAON	6	5329	33	13604	27	4239
16	THANE	2	125	22	1001	33	840
17	AURANGABAD	2	3304	18	6758	29	2584
18	KOLHAPUR	0	722	26	3284	23	827
19	GONDIA	7	1988	18	6327	16	3651
20	AMRAVATI	7	12900	13	9793	16	3004
21	WARDHA	14	1820	14	1890	6	623
22	CHANDRAPUR	9	2811	10	6117	14	3019
23	PUNE	1	2858	16	2632	14	988
24	RATNAGIRI	2	116	6	712	18	664
25	YAVATMAL	0	4917	9	11823	15	4862
26	NAGPUR	3	2357	14	3819	6	976
27	RAIGAD	9	37	2	627	9	438
28	PALGHAR	0	530	0	2436	19	3097
29	SOLAPUR	0	7534	9	6738	8	2199
30	OSMANABAD	7	3603	4	3737	4	944
31	SATARA	8	1133	1	1853	0	1009
32	SINDHUDURG	1	9	0	500	0	402
33	DHULE	0	1549	0	7640	0	3919
34	SANGLI	0	1109	0	4641	0	1414
	<b>Total</b>	<b>1153</b>	<b>103041</b>	<b>1048</b>	<b>199644</b>	<b>1099</b>	<b>81250</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	1671	0	8939	0	5949
2	AMRAVATI DIV.	0	4232	0	13657	0	5792
3	AURANGABAD DIV.	0	15745	0	29210	0	11599
4	NAGPUR DIV.	0	2644	0	8189	0	4081
5	KONKAN DIV.	0	1047	0	2296	0	1607
6	PUNE DIV.	0	1712	0	5256	0	2458
	<b>Total</b>	<b>0</b>	<b>27051</b>	<b>0</b>	<b>67547</b>	<b>0</b>	<b>31486</b>

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	35
CHANDRAPUR	70
THANE	82
RAIGAD	83
NANDURBAR	129
DHULE	135
SATARA	172
NASHIK	176
SANGLI	188
NAGPUR	236
PUNE	292
KOLHAPUR	358
BHANDARA	362
BULDHANA	407
WASHIM	413
GADCHIROLI	473
AHMEDNAGAR	497
SOLAPUR	702
WARDHA	709
JALGAON	734
GONDIA	794
PALGHAR	835
YAVATMAL	985
AMRAVATI	1031
PARBHANI	1041
JALNA	1305
AKOLA	1396
LATUR	1591
OSMANABAD	1759
AURANGABAD	2058
HINGOLI	2096
BEED	2223
NANDED	3672

State Schemes 2nd Ins Pending

SINDHUDURG	105
RATNAGIRI	268
THANE	323
SATARA	490
RAIGAD	570
GONDIA	782
NAGPUR	855
SANGLI	972
PALGHAR	1030
PUNE	1063
WARDHA	1072
BHANDARA	1103
KOLHAPUR	1144
NANDURBAR	1170
NASHIK	1429
SOLAPUR	1587
DHULE	1599
WASHIM	1665
PARBHANI	1862
GADCHIROLI	2144
CHANDRAPUR	2233
JALGAON	2320
AKOLA	2326
AHMEDNAGAR	2421
AMRAVATI	2461
HINGOLI	2659
BULDHANA	2698
OSMANABAD	3331
NANDED	3484
AURANGABAD	3746
JALNA	3946
LATUR	4381
YAVATMAL	4507
BEED	5801

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	195
NAGPUR	282
SATARA	295
THANE	305
KOLHAPUR	345
RAIGAD	386
SANGLI	390
BHANDARA	403
WARDHA	413
GONDIA	510
PALGHAR	628
PUNE	698
SOLAPUR	730
WASHIM	746
HINGOLI	814
PARBHANI	872
AMRAVATI	874
AKOLA	926
NASHIK	1023
DHULE	1063
NANDURBAR	1090
AURANGABAD	1090
NANDED	1133
GADCHIROLI	1227
OSMANABAD	1233
CHANDRAPUR	1246
JALGAON	1296
AHMEDNAGAR	1477
YAVATMAL	1610
BULDHANA	1636
LATUR	1811
BEED	2150
JALNA	2496

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	497	0	2421	0	1477
2	AKOLA	0	1396	0	2326	0	926
3	AMRAVATI	0	1031	0	2461	0	874
4	AURANGABAD	0	2058	0	3746	0	1090
5	BEED	0	2223	0	5801	0	2150
6	BHANDARA	0	362	0	1103	0	403
7	BULDHANA	0	407	0	2698	0	1636
8	CHANDRAPUR	0	70	0	2233	0	1246
9	DHULE	0	135	0	1599	0	1063
10	GADCHIROLI	0	473	0	2144	0	1227
11	GONDIA	0	794	0	782	0	510
12	HINGOLI	0	2096	0	2659	0	814
13	JALGAON	0	734	0	2320	0	1296
14	JALNA	0	1305	0	3946	0	2496
15	KOLHAPUR	0	358	0	1144	0	345
16	LATUR	0	1591	0	4381	0	1811
17	NAGPUR	0	236	0	855	0	282
18	NANDED	0	3672	0	3484	0	1133
19	NANDURBAR	0	129	0	1170	0	1090
20	NASHIK	0	176	0	1429	0	1023
21	OSMANABAD	0	1759	0	3331	0	1233
22	PALGHAR	0	835	0	1030	0	628
23	PARBHANI	0	1041	0	1862	0	872
24	PUNE	0	292	0	1063	0	698
25	RAIGAD	0	83	0	570	0	386
26	RATNAGIRI	0	35	0	268	0	195
27	SANGLI	0	188	0	972	0	390
28	SATARA	0	172	0	490	0	295
29	SINDHUDURG	0	12	0	105	0	93
30	SOLAPUR	0	702	0	1587	0	730
31	THANE	0	82	0	323	0	305
32	WARDHA	0	709	0	1072	0	413
33	WASHIM	0	413	0	1665	0	746
34	YAVATMAL	0	985	0	4507	0	1610
	<b>Total</b>	<b>0</b>	<b>27051</b>	<b>0</b>	<b>67547</b>	<b>0</b>	<b>31486</b>
