



# अमृत महा आवास अभियान २०२२-२३

## दैनिक प्रगती अहवाल : २०.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण  
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१२९७१	४	१००२२६६	२८८	१०८९	१४८९	१८३२
राज्य योजना	५४१८६८	२३२	३९२७८५	८३	८८	२४८	२५१
एकूण	१९५४८३९	२३६	१३९५०५१	३७१	११७७	१७२९	२०८३

PMAY-G Completion Progress Bar

70.9%



PMAY-G Incomplete Houses bifurcation

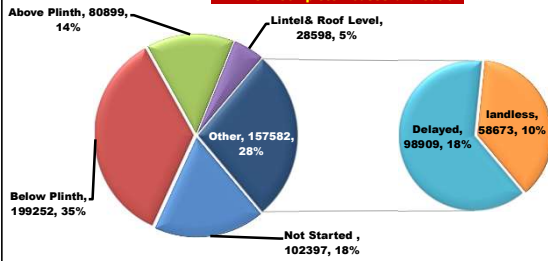


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

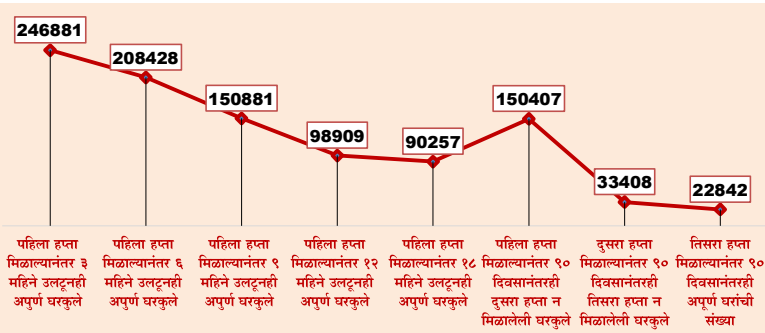


Abhiyan Achievement Day 120

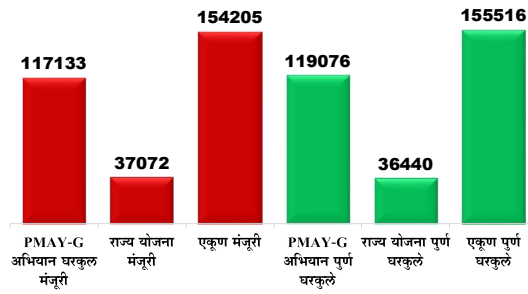

PMAY-G : House completion ( Abhiyan Achievement)

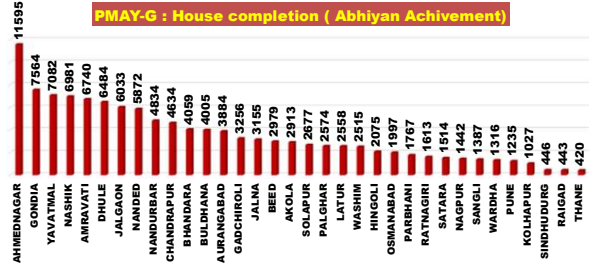

State Schemes : House completion ( Abhiyan Achievement)

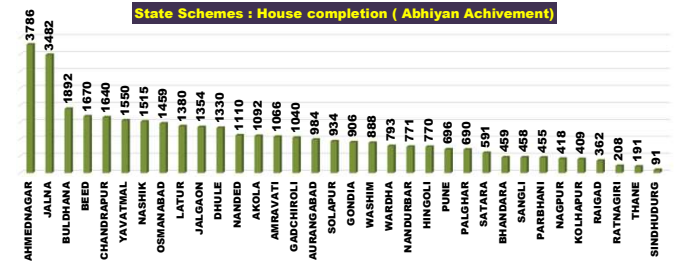


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	19.03.2023	20.03.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414691	413728	413732	4	959
2	AMRAVATI DIV.	275061	274630	274630	0	431
3	AURANGABAD DIV.	238197	237444	237444	0	753
4	NAGPUR DIV.	292352	291700	291700	0	652
5	KONKAN DIV.	69743	69616	69616	0	127
6	PUNE DIV.	126192	125849	125849	0	343
	<b>Total</b>	<b>1416236</b>	<b>1412967</b>	<b>1412971</b>	<b>4</b>	<b>3265</b>

PMAY-G Remaining Sanction

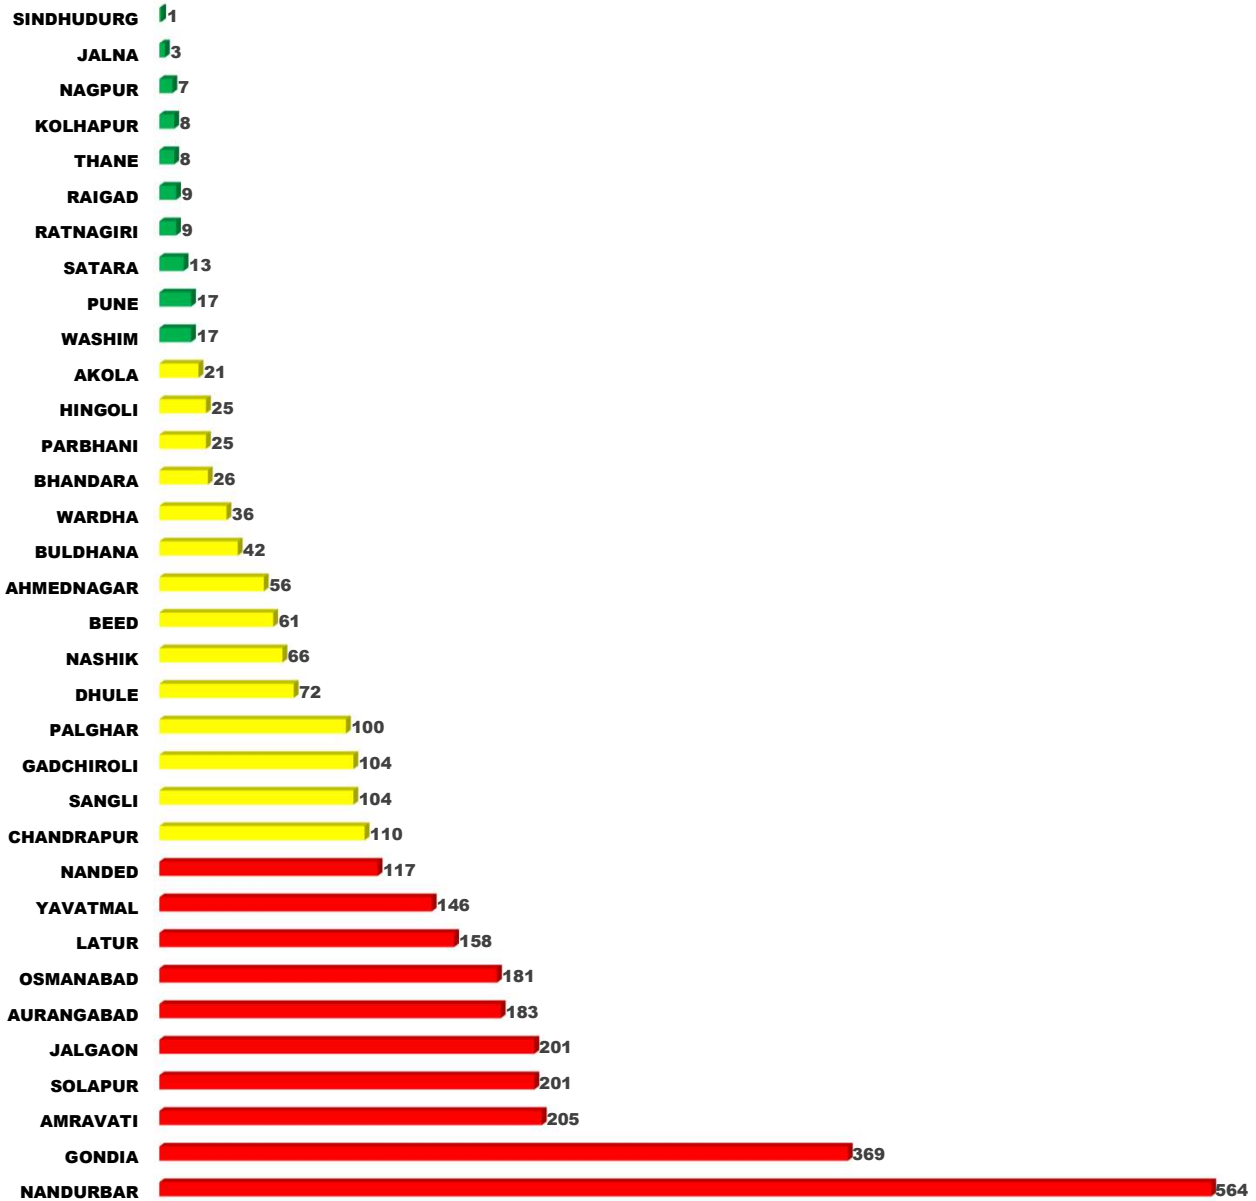


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	19.03.2023	20.03.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60805	60747	60749	2	56
2	NASHIK	89724	89656	89658	2	66
3	AKOLA	48796	48775	48775	0	21
4	AMRAVATI	95708	95503	95503	0	205
5	AURANGABAD	36795	36612	36612	0	183
6	BEED	35319	35258	35258	0	61
7	BHANDARA	65124	65098	65098	0	26
8	BULDHANA	44769	44727	44727	0	42
9	CHANDRAPUR	43228	43118	43118	0	110
10	DHULE	64947	64875	64875	0	72
11	GADCHIROLI	31677	31573	31573	0	104
12	GONDIA	96485	96116	96116	0	369
13	HINGOLI	18108	18083	18083	0	25
14	JALGAON	79787	79586	79586	0	201
15	JALNA	24047	24044	24044	0	3
16	KOLHAPUR	17773	17765	17765	0	8
17	LATUR	20729	20571	20571	0	158
18	NAGPUR	37193	37186	37186	0	7
19	NANDED	69551	69434	69434	0	117
20	NANDURBAR	119428	118864	118864	0	564
21	OSMANABAD	14545	14364	14364	0	181
22	PALGHAR	35223	35123	35123	0	100
23	PARBHANI	19103	19078	19078	0	25
24	PUNE	20978	20961	20961	0	17
25	RAIGAD	9844	9835	9835	0	9
26	RATNAGIRI	9922	9913	9913	0	9
27	SANGLI	22175	22071	22071	0	104
28	SATARA	15440	15427	15427	0	13
29	SINDHUDURG	5148	5147	5147	0	1
30	SOLAPUR	49826	49625	49625	0	201
31	THANE	9606	9598	9598	0	8
32	WARDHA	18645	18609	18609	0	36
33	WASHIM	20412	20395	20395	0	17
34	YAVATMAL	65376	65230	65230	0	146
<b>Total</b>		<b>1416236</b>	<b>1412967</b>	<b>1412971</b>	<b>4</b>	<b>3265</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	19.03.2023	20.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI DIV.	274630	180301	180412	111	94218	194	8565
2	NASHIK DIV.	413732	319335	319441	106	94291	299	8572
3	AURANGABAD DIV.	237444	131802	131848	46	105596	202	9600
4	KONKAN DIV.	69616	54893	54904	11	14712	46	1337
5	NAGPUR DIV.	291700	230388	230399	11	61301	186	5573
6	PUNE DIV.	125849	85259	85262	3	40587	65	3690
<b>Total</b>		<b>1412971</b>	<b>1001978</b>	<b>1002266</b>	<b>288</b>	<b>410705</b>	<b>992</b>	<b>37337</b>

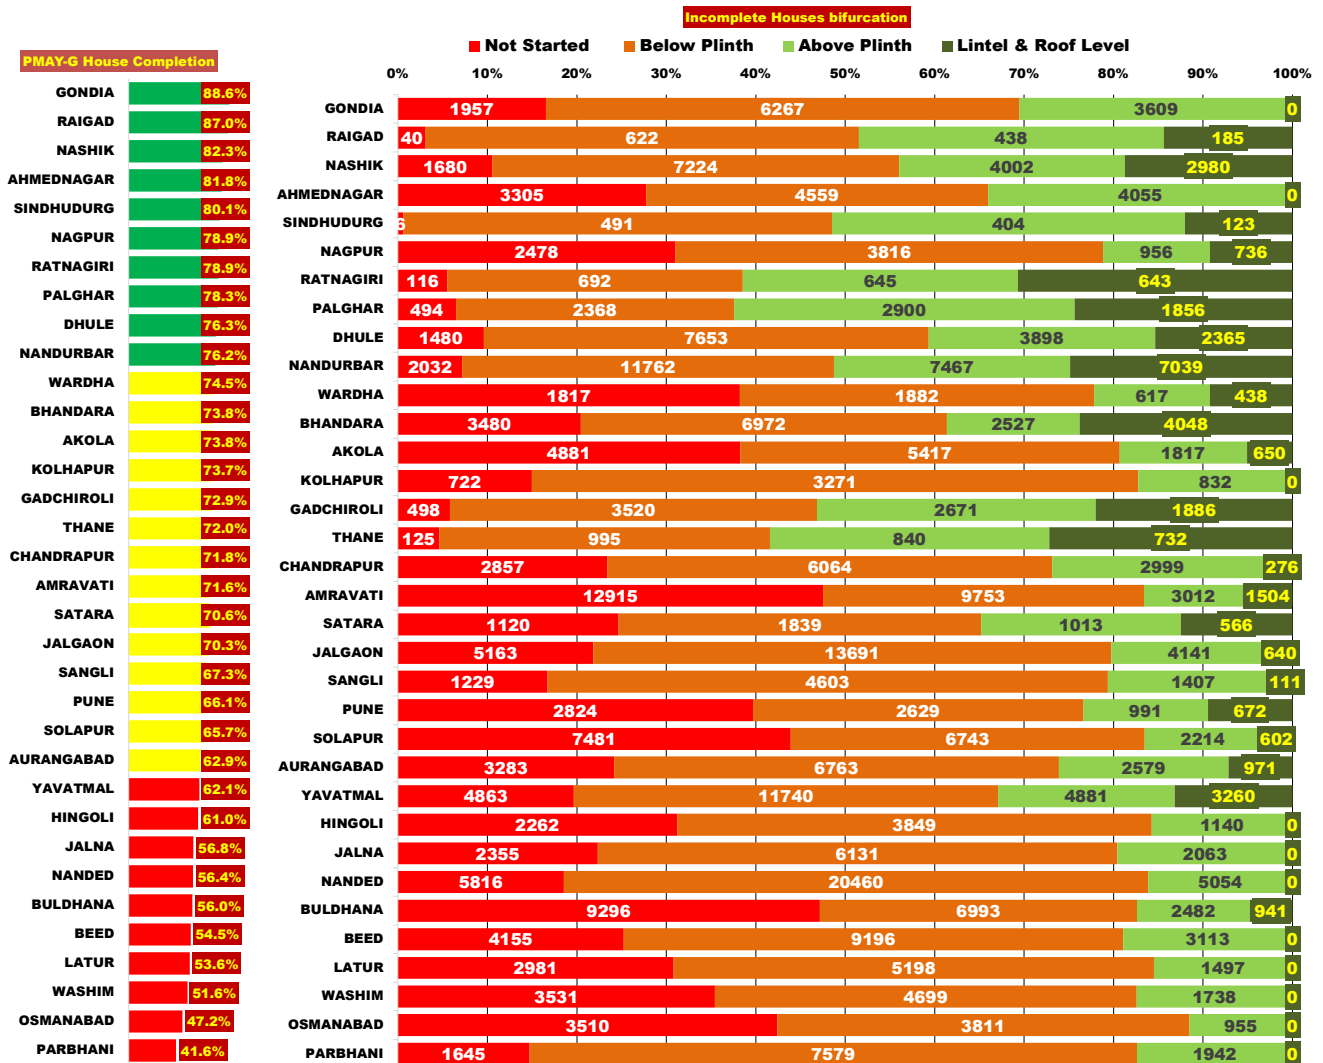


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	19.03.2023	20.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	60749	49613	49675	62	11074	97	1007
2	AKOLA	48775	35970	36010	40	12765	24	1160
3	NASHIK	89658	73743	73772	29	15886	58	1444
4	AMRAVATI	95503	68338	68365	27	27138	56	2467
5	BULDHANA	44727	24999	25026	27	19701	33	1791
6	NANDED	69434	39162	39182	20	30252	49	2750
7	AURANGABAD	36612	23003	23016	13	13596	32	1236
8	PALGHAR	35123	27494	27505	11	7618	21	693
9	YAVATMAL	65230	40479	40490	11	24740	59	2249
10	NANDURBAR	118864	90554	90564	10	28300	40	2573
11	WARDHA	18609	13845	13855	10	4754	11	432
12	LATUR	20571	11024	11032	8	9539	21	867
13	WASHIM	20395	10515	10521	6	9874	21	898
14	BEED	35258	19204	19207	3	16051	25	1459
15	JALGAON	79586	55948	55951	3	23635	50	2149
16	DHULE	64875	49477	49479	2	15396	54	1400
17	PARBHANI	19078	7938	7940	2	11138	15	1013
18	GADCHIROLI	31573	23022	23023	1	8550	27	777
19	KOLHAPUR	17765	13088	13089	1	4676	9	425
20	SATARA	15427	10888	10889	1	4538	13	413
21	SOLAPUR	49625	32584	32585	1	17040	22	1549
22	BHANDARA	65098	48071	48071	0	17027	34	1548
23	CHANDRAPUR	43118	30973	30973	0	12145	39	1104
24	GONDIA	96116	85142	85142	0	10974	63	998
25	HINGOLI	18083	11033	11033	0	7050	17	641
26	JALNA	24044	13661	13661	0	10383	26	944
27	NAGPUR	37186	29335	29335	0	7851	12	714
28	OSMANABAD	14364	6777	6777	0	7587	17	690
29	PUNE	20961	13845	13845	0	7116	10	647
30	RAIGAD	9835	8553	8553	0	1282	4	117
31	RATNAGIRI	9913	7817	7817	0	2096	13	191
32	SANGLI	22071	14854	14854	0	7217	12	656
33	SINDHUDURG	5147	4123	4123	0	1024	4	93
34	THANE	9598	6906	6906	0	2692	4	245
Total		1412971	1001978	1002266	288	410705	992	37337

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	19.03.2023	20.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	160595	160827	232	38504
2	KONKAN DIV.	34729	29664	29664	0	5065
3	PUNE DIV.	65334	62909	62909	0	2425
4	NASHIK DIV.	141360	108472	108472	0	32888
5	AMRAVATI DIV.	109702	92582	92577	0	17125
6	NAGPUR DIV.	116255	87419	87419	0	28836
	<b>Total</b>	<b>666711</b>	<b>541641</b>	<b>541868</b>	<b>232</b>	<b>124843</b>

State Scheme Remaining Sanction

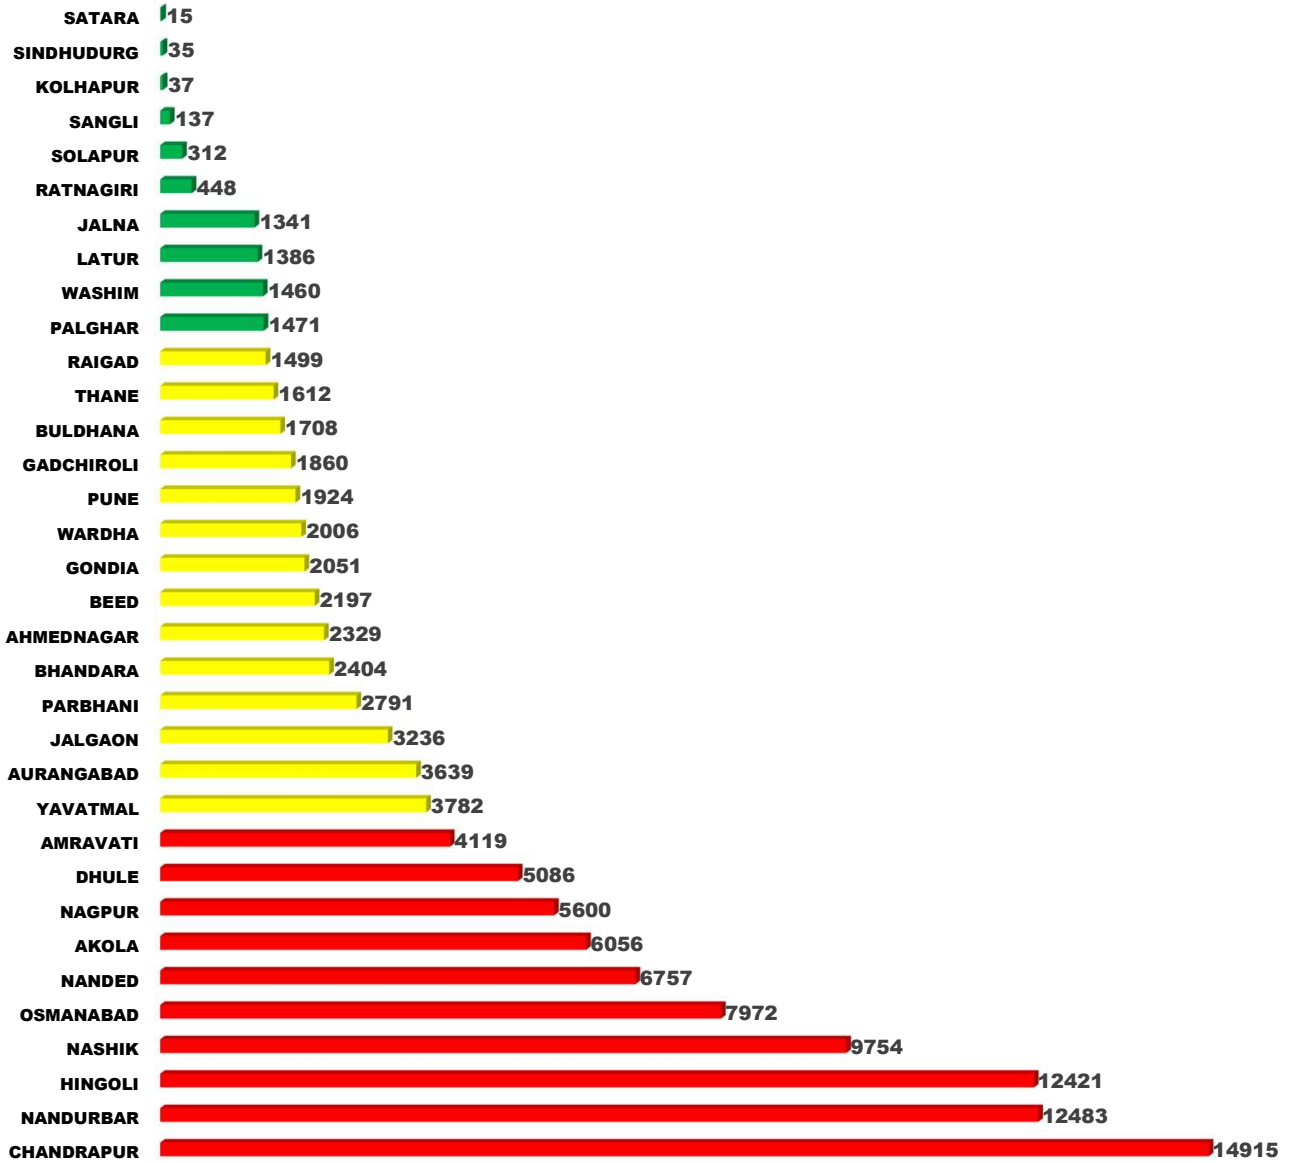


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	19.03.2023	20.03.2023	Daily_Achievement	Remaining
1	AURANGABAD	26141	22328	22502	174	3639
2	NANDED	26760	19945	20003	58	6757
3	AHMEDNAGAR	35298	32969	32969	0	2329
4	AKOLA	23681	17625	17625	0	6056
5	AMRAVATI	23224	19105	19105	0	4119
6	BEED	26878	24681	24681	0	2197
7	BHANDARA	17590	15186	15186	0	2404
8	BULDHANA	21616	19908	19908	0	1708
9	CHANDRAPUR	38147	23232	23232	0	14915
10	DHULE	21790	16704	16704	0	5086
11	GADCHIROLI	16834	14974	14974	0	1860
12	GONDIA	14246	12195	12195	0	2051
13	HINGOLI	27298	14877	14877	0	12421
14	JALGAON	25659	22423	22423	0	3236
15	JALNA	20446	19105	19105	0	1341
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	25785	25785	0	1386
18	NAGPUR	16291	10691	10691	0	5600
19	NANDURBAR	26578	14095	14095	0	12483
20	NASHIK	32035	22281	22281	0	9754
21	OSMANABAD	24853	16881	16881	0	7972
22	PALGHAR	11792	10321	10321	0	1471
23	PARBHANI	19784	16993	16993	0	2791
24	PUNE	14672	12748	12748	0	1924
25	RAIGAD	7406	5907	5907	0	1499
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10632	10632	0	15
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18406	18406	0	312
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	11141	11141	0	2006
33	YAVATMAL	29681	25899	25899	0	3782
34	WASHIM	11500	10045	10040	-5	1460
<b>Total</b>		<b>666711</b>	<b>541641</b>	<b>541868</b>	<b>232</b>	<b>124843</b>



## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	19.03.2023	20.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AMRAVATI DIV.	92577	62653	62686	33	29891	54	2717
2	NASHIK DIV.	108472	86782	86813	31	21659	73	1969
3	AURANGABAD DIV.	160827	101403	101416	13	59411	94	5401
4	KONKAN DIV.	29664	22913	22916	3	6748	13	613
5	NAGPUR DIV.	87419	67798	67801	3	19618	44	1783
6	PUNE DIV.	62909	51153	51153	0	11756	26	1069
<b>Total</b>		<b>541868</b>	<b>392702</b>	<b>392785</b>	<b>83</b>	<b>149083</b>	<b>304</b>	<b>13553</b>

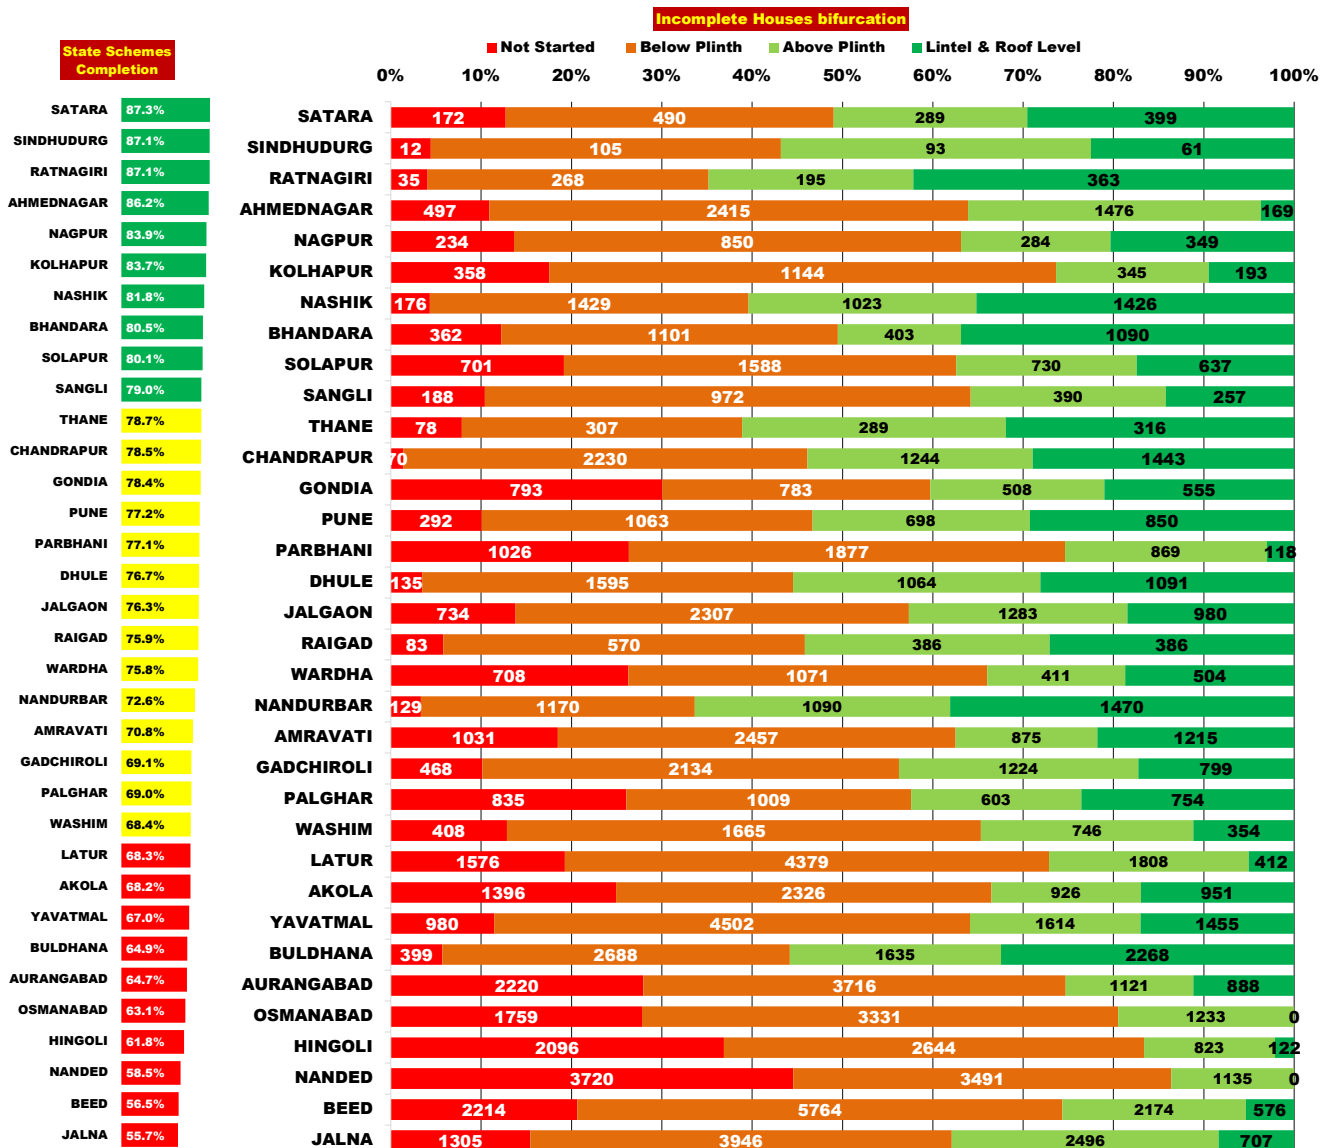

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	19.03.2023	20.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32969	28385	28412	27	4557	32	414
2	BULDHANA	19908	12899	12918	19	6990	16	635
3	AKOLA	17625	12018	12026	8	5599	9	509
4	BEED	24681	13948	13953	5	10728	14	975
5	YAVATMAL	25899	17344	17348	4	8551	13	777
6	AURANGABAD	22502	14554	14557	3	7945	8	722
7	NASHIK	22281	18224	18227	3	4054	13	369
8	PALGHAR	10321	7117	7120	3	3201	6	291
9	AMRAVATI	19105	13525	13527	2	5578	9	507
10	JALNA	19105	10649	10651	2	8454	29	769
11	LATUR	25785	17608	17610	2	8175	12	743
12	WARDHA	11141	8445	8447	2	2694	7	245
13	DHULE	16704	12818	12819	1	3885	11	353
14	HINGOLI	14877	9191	9192	1	5685	6	517
15	NAGPUR	10691	8973	8974	1	1717	3	156
16	BHANDARA	15186	12230	12230	0	2956	4	269
17	CHANDRAPUR	23232	18245	18245	0	4987	14	453
18	GADCHIROLI	14974	10349	10349	0	4625	9	420
19	GONDIA	12195	9556	9556	0	2639	8	240
20	JALGAON	22423	17119	17119	0	5304	11	482
21	KOLHAPUR	12528	10488	10488	0	2040	3	185
22	NANDED	20003	11699	11699	0	8304	9	755
23	NANDURBAR	14095	10236	10236	0	3859	6	351
24	OSMANABAD	16881	10651	10651	0	6230	12	566
25	PARBHANI	16993	13103	13103	0	3890	4	354
26	PUNE	12748	9845	9845	0	2903	6	264
27	RAIGAD	5907	4482	4482	0	1425	3	130
28	RATNAGIRI	6678	5817	5817	0	861	2	78
29	SANGLI	8595	6788	6788	0	1807	4	164
30	SATARA	10632	9282	9282	0	1350	5	123
31	SINDHUDURG	2106	1835	1835	0	271	1	25
32	SOLAPUR	18406	14750	14750	0	3656	8	332
33	THANE	4652	3662	3662	0	990	2	90
34	WASHIM	10040	6867	6867	0	3173	7	288
	<b>Total</b>	<b>541868</b>	<b>392702</b>	<b>392785</b>	<b>83</b>	<b>149083</b>	<b>304</b>	<b>13553</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	410	13660	372	44889	530	23563
2	AMRAVATI DIV.	159	35422	365	38602	320	13930
3	AURANGABAD DIV.	290	25977	211	62987	167	18343
4	NAGPUR DIV.	78	12876	210	28521	298	13379
5	KONKAN DIV.	39	778	147	5168	361	5227
6	PUNE DIV.	113	13243	176	19085	156	6457
	<b>Total</b>	<b>1089</b>	<b>101956</b>	<b>1481</b>	<b>199252</b>	<b>1832</b>	<b>80899</b>

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	37
RATNAGIRI	116
THANE	125
GADCHIROLI	473
PALGHAR	494
KOLHAPUR	722
SANGLI	1096
SATARA	1120
DHULE	1480
PARBHANI	1645
NASHIK	1680
WARDHA	1817
GONDIA	1957
NANDURBAR	2032
HINGOLI	2262
JALNA	2325
NAGPUR	2343
CHANDRAPUR	2806
PUNE	2824
LATUR	2981
AURANGABAD	3283
AHMEDNAGAR	3305
BHANDARA	3480
OSMANABAD	3510
WASHIM	3528
BEED	4155
YAVATMAL	4859
AKOLA	4881
JALGAON	5163
NANDED	5816
SOLAPUR	7481
BULDHANA	9285
AMRAVATI	12869

PMAY-G 2nd Ins Pending

SINDHUDURG	491
RAIGAD	622
RATNAGIRI	692
THANE	995
SATARA	1839
WARDHA	1882
PALGHAR	2368
PUNE	2629
KOLHAPUR	3271
GADCHIROLI	3520
OSMANABAD	3811
NAGPUR	3816
HINGOLI	3849
AHMEDNAGAR	4559
SANGLI	4603
WASHIM	4699
LATUR	5198
AKOLA	5417
CHANDRAPUR	6064
JALNA	6131
GONDIA	6267
SOLAPUR	6743
AURANGABAD	6763
BHANDARA	6972
BULDHANA	6993
NASHIK	7224
PARBHANI	7579
DHULE	7653
BEED	9196
AMRAVATI	9753
YAVATMAL	11740
NANDURBAR	11762
JALGAON	13691
NANDED	20460

PMAY-G 3rd Ins Pending

SINDHUDURG	404
RAIGAD	438
WARDHA	617
RATNAGIRI	645
KOLHAPUR	832
THANE	840
OSMANABAD	955
NAGPUR	956
PUNE	991
SATARA	1013
HINGOLI	1140
SANGLI	1407
LATUR	1497
WASHIM	1738
AKOLA	1817
PARBHANI	1942
JALNA	2063
SOLAPUR	2214
BULDHANA	2482
BHANDARA	2527
AURANGABAD	2579
GADCHIROLI	2671
PALGHAR	2900
CHANDRAPUR	2999
AMRAVATI	3012
BEED	3113
GONDIA	3609
DHULE	3898
NASHIK	4002
AHMEDNAGAR	4055
JALGAON	4141
YAVATMAL	4881
NANDED	5054
NANDURBAR	7467

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	PALGHAR	36	494	104	2368	301	2900
2	JALGAON	166	5163	79	13691	177	4141
3	NANDURBAR	86	2032	119	11762	116	7467
4	YAVATMAL	58	4859	141	11740	122	4881
5	AHMEDNAGAR	37	3305	107	4559	151	4055
6	BULDHANA	57	9285	126	6993	111	2482
7	GONDIA	31	1957	91	6267	133	3609
8	DHULE	69	1480	56	7653	77	3898
9	NANDED	64	5816	69	20460	46	5054
10	AMRAVATI	31	12869	71	9753	63	3012
11	CHANDRAPUR	5	2806	58	6064	78	2999
12	SOLAPUR	53	7481	48	6743	33	2214
13	JALNA	67	2325	28	6131	30	2063
14	SANGLI	13	1096	51	4603	58	1407
15	OSMANABAD	93	3510	19	3811	8	955
16	LATUR	26	2981	46	5198	33	1497
17	PUNE	34	2824	37	2629	34	991
18	NASHIK	52	1680	11	7224	9	4002
19	NAGPUR	14	2343	17	3816	37	956
20	SATARA	13	1120	27	1839	23	1013
21	RATNAGIRI	0	116	20	692	39	645
22	AURANGABAD	21	3283	16	6763	21	2579
23	PARBHANI	19	1645	23	7579	12	1942
24	GADCHIROLI	11	473	16	3520	26	2671
25	AKOLA	7	4881	21	5417	21	1817
26	BHANDARA	14	3480	17	6972	7	2527
27	WARDHA	3	1817	11	1882	17	617
28	BEED	0	4155	10	9196	17	3113
29	SINDHUDURG	3	6	12	491	10	404
30	KOLHAPUR	0	722	13	3271	8	832
31	WASHIM	6	3528	6	4699	3	1738
32	THANE	0	125	6	995	6	840
33	RAIGAD	0	37	5	622	5	438
34	HINGOLI	0	2262	0	3849	0	1140
	<b>Total</b>	<b>1089</b>	<b>101956</b>	<b>1481</b>	<b>199252</b>	<b>1832</b>	<b>80899</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AURANGABAD DIV.	61	15916	123	29148	63	11659
2	KONKAN DIV.	4	1043	41	2259	82	1566
3	NAGPUR DIV.	9	2635	29	8169	36	4074
4	AMRAVATI DIV.	13	4214	32	13638	28	5796
5	NASHIK DIV.	0	1671	23	8916	36	5936
6	PUNE DIV.	1	1711	0	5257	6	2452
<b>Total</b>		<b>88</b>	<b>27190</b>	<b>248</b>	<b>67387</b>	<b>251</b>	<b>31483</b>

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	35
CHANDRAPUR	70
THANE	78
RAIGAD	83
NANDURBAR	129
DHULE	135
SATARA	172
NASHIK	176
SANGLI	188
NAGPUR	234
PUNE	292
KOLHAPUR	358
BHANDARA	362
BULDHANA	399
WASHIM	408
GADCHIROLI	468
AHMEDNAGAR	497
SOLAPUR	701
WARDHA	708
JALGAON	734
GONDIA	793
PALGHAR	835
YAVATMAL	980
PARBHANI	1026
AMRAVATI	1031
JALNA	1305
AKOLA	1396
LATUR	1576
OSMANABAD	1759
HINGOLI	2096
BEED	2214
AURANGABAD	2220
NANDED	3720

State Schemes 2nd Ins Pending

SINDHUDURG	105
RATNAGIRI	268
THANE	307
SATARA	490
RAIGAD	570
GONDIA	783
NAGPUR	850
SANGLI	972
PALGHAR	1009
PUNE	1063
WARDHA	1071
BHANDARA	1101
KOLHAPUR	1144
NANDURBAR	1170
NASHIK	1429
SOLAPUR	1588
DHULE	1595
WASHIM	1665
PARBHANI	1877
GADCHIROLI	2134
CHANDRAPUR	2230
JALGAON	2307
AKOLA	2326
AHMEDNAGAR	2415
AMRAVATI	2457
HINGOLI	2644
BULDHANA	2688
OSMANABAD	3331
NANDED	3491
AURANGABAD	3716
JALNA	3946
LATUR	4379
YAVATMAL	4502
BEED	5764

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	195
NAGPUR	284
THANE	289
SATARA	289
KOLHAPUR	345
RAIGAD	386
SANGLI	390
BHANDARA	403
WARDHA	411
GONDIA	508
PALGHAR	603
PUNE	698
SOLAPUR	730
WASHIM	746
HINGOLI	823
PARBHANI	869
AMRAVATI	875
AKOLA	926
NASHIK	1023
DHULE	1064
NANDURBAR	1090
AURANGABAD	1121
NANDED	1135
GADCHIROLI	1224
OSMANABAD	1233
CHANDRAPUR	1244
JALGAON	1283
AHMEDNAGAR	1476
YAVATMAL	1614
BULDHANA	1635
LATUR	1808
BEED	2174
JALNA	2496

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	BEED	9	2214	46	5764	22	2174
2	PALGHAR	0	835	21	1009	46	603
3	AURANGABAD	12	2220	42	3716	11	1121
4	THANE	4	78	20	307	36	289
5	LATUR	15	1576	17	4379	20	1808
6	BULDHANA	8	399	18	2688	19	1635
7	JALGAON	0	734	13	2307	26	1283
8	GADCHIROLI	5	468	15	2134	18	1224
9	HINGOLI	0	2096	15	2644	6	823
10	YAVATMAL	5	980	10	4502	6	1614
11	PARBHANI	15	1026	0	1877	3	869
12	NAGPUR	2	234	7	850	5	284
13	NANDED	10	3720	3	3491	1	1135
14	AHMEDNAGAR	0	497	6	2415	7	1476
15	CHANDRAPUR	0	70	3	2230	5	1244
16	AMRAVATI	0	1031	4	2457	3	875
17	DHULE	0	135	4	1595	3	1064
18	WARDHA	1	708	2	1071	4	411
19	SATARA	0	172	0	490	6	289
20	BHANDARA	0	362	2	1101	2	403
21	GONDIA	1	793	0	783	2	508
22	SOLAPUR	1	701	0	1588	0	730
23	AKOLA	0	1396	0	2326	0	926
24	JALNA	0	1305	0	3946	0	2496
25	KOLHAPUR	0	358	0	1144	0	345
26	NANDURBAR	0	129	0	1170	0	1090
27	NASHIK	0	176	0	1429	0	1023
28	OSMANABAD	0	1759	0	3331	0	1233
29	PUNE	0	292	0	1063	0	698
30	RAIGAD	0	83	0	570	0	386
31	RATNAGIRI	0	35	0	268	0	195
32	SANGLI	0	188	0	972	0	390
33	SINDHUDURG	0	12	0	105	0	93
34	WASHIM	0	408	0	1665	0	746
	<b>Total</b>	<b>88</b>	<b>27190</b>	<b>248</b>	<b>67387</b>	<b>251</b>	<b>31483</b>
