



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २१.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१२९४४	८२	१००३१३२	८६६	०	०	०
राज्य योजना	५४२१६४	२९६	३९३०५९	२७४	०	०	०
एकूण	१९५५१०८	३७८	१३९६१९१	११४०	०	०	०

PMAY-G Completion Progress Bar

71.0%


PMAY-G: Incomplete Houses bifurcation

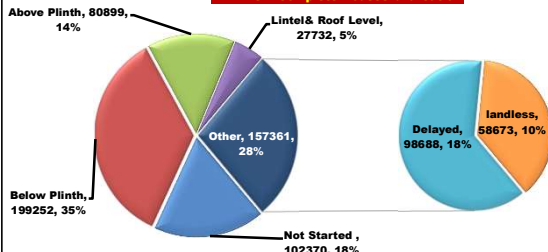



State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation




Abhiyan Achievement Day 121

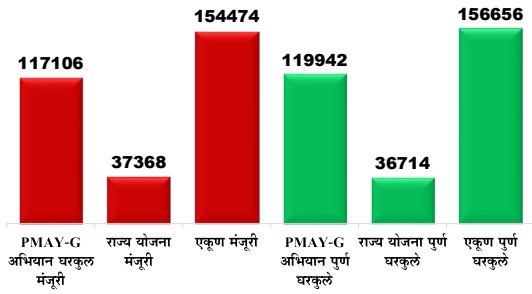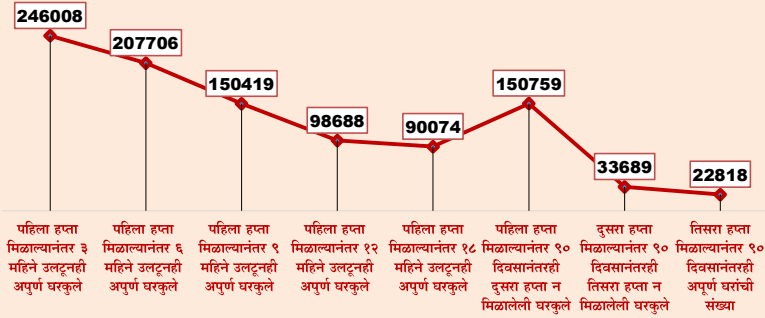

PMAY-G : House completion (Abhiyan Achievement)

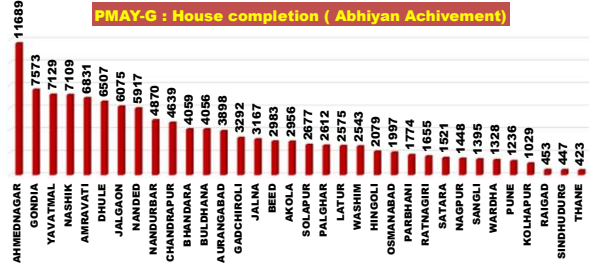

State Schemes : House completion (Abhiyan Achievement)

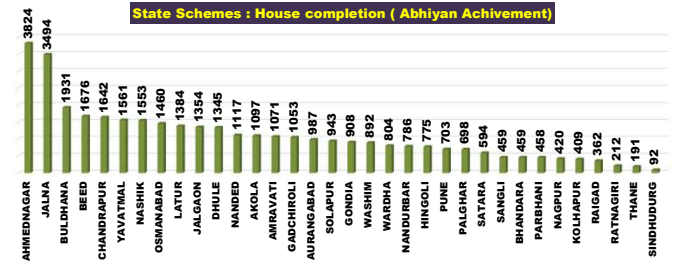


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	20.03.2023	21.03.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	238165	237444	237477	33	688
2	KONKAN DIV.	69743	69616	69638	22	105
3	NASHIK DIV.	414674	413732	413736	20	938
4	NAGPUR DIV.	292300	291700	291659	6	641
5	AMRAVATI DIV.	275059	274630	274607	1	452
6	PUNE DIV.	126169	125849	125827	0	342
	Total	1416110	1412971	1412944	82	3166

PMAY-G Remaining Sanction

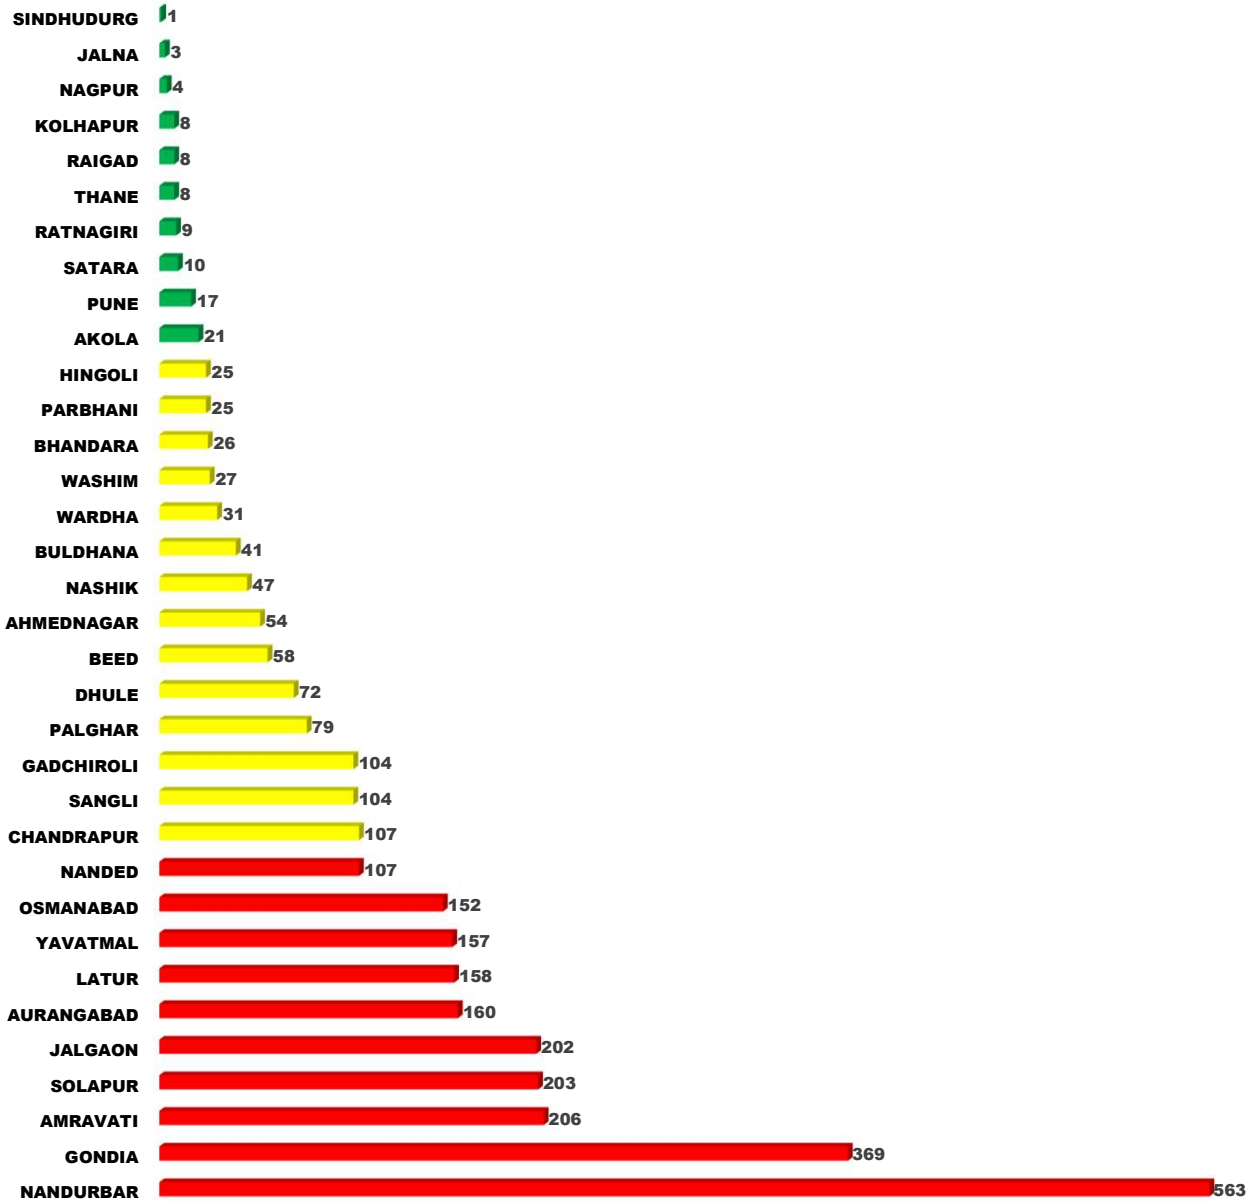


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	20.03.2023	21.03.2023	Daily_Achievement	Remaining
1	AURANGABAD	36795	36612	36635	23	160
2	PALGHAR	35223	35123	35144	21	79
3	NASHIK	89724	89658	89677	19	47
4	NANDED	69548	69434	69441	7	107
5	WARDHA	18645	18609	18614	5	31
6	BEED	35319	35258	35261	3	58
7	BULDHANA	44769	44727	44728	1	41
8	NAGPUR	37191	37186	37187	1	4
9	NANDURBAR	119428	118864	118865	1	563
10	RAIGAD	9844	9835	9836	1	8
11	AKOLA	48796	48775	48775	0	21
12	BHANDARA	65124	65098	65098	0	26
13	DHULE	64947	64875	64875	0	72
14	GADCHIROLI	31677	31573	31573	0	104
15	GONDIA	96485	96116	96116	0	369
16	HINGOLI	18108	18083	18083	0	25
17	JALNA	24047	24044	24044	0	3
18	KOLHAPUR	17773	17765	17765	0	8
19	LATUR	20729	20571	20571	0	158
20	OSMANABAD	14516	14364	14364	0	152
21	PARBHANI	19103	19078	19078	0	25
22	PUNE	20978	20961	20961	0	17
23	RATNAGIRI	9922	9913	9913	0	9
24	SANGLI	22175	22071	22071	0	104
25	SINDHUDURG	5148	5147	5147	0	1
26	THANE	9606	9598	9598	0	8
27	AHMEDNAGAR	60802	60749	60748	-1	54
28	AMRAVATI	95708	95503	95502	-1	206
29	SATARA	15436	15427	15426	-1	10
30	WASHIM	20412	20395	20385	-10	27
31	YAVATMAL	65374	65230	65217	-13	157
32	JALGAON	79773	79586	79571	-15	202
33	SOLAPUR	49807	49625	49604	-21	203
34	CHANDRAPUR	43178	43118	43071	-47	107
Total		1416110	1412971	1412944	82	3166

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	20.03.2023	21.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413736	319441	319764	323	93972	300	9397
2	AMRAVATI DIV.	274607	180412	180672	260	93935	194	9394
3	AURANGABAD DIV.	237477	131848	131951	103	105526	202	10553
4	KONKAN DIV.	69638	54904	54998	94	14640	46	1464
5	NAGPUR DIV.	291659	230399	230467	68	61192	185	6119
6	PUNE DIV.	125827	85262	85280	18	40547	65	4055
Total		1412944	1002266	1003132	866	409812	991	40981

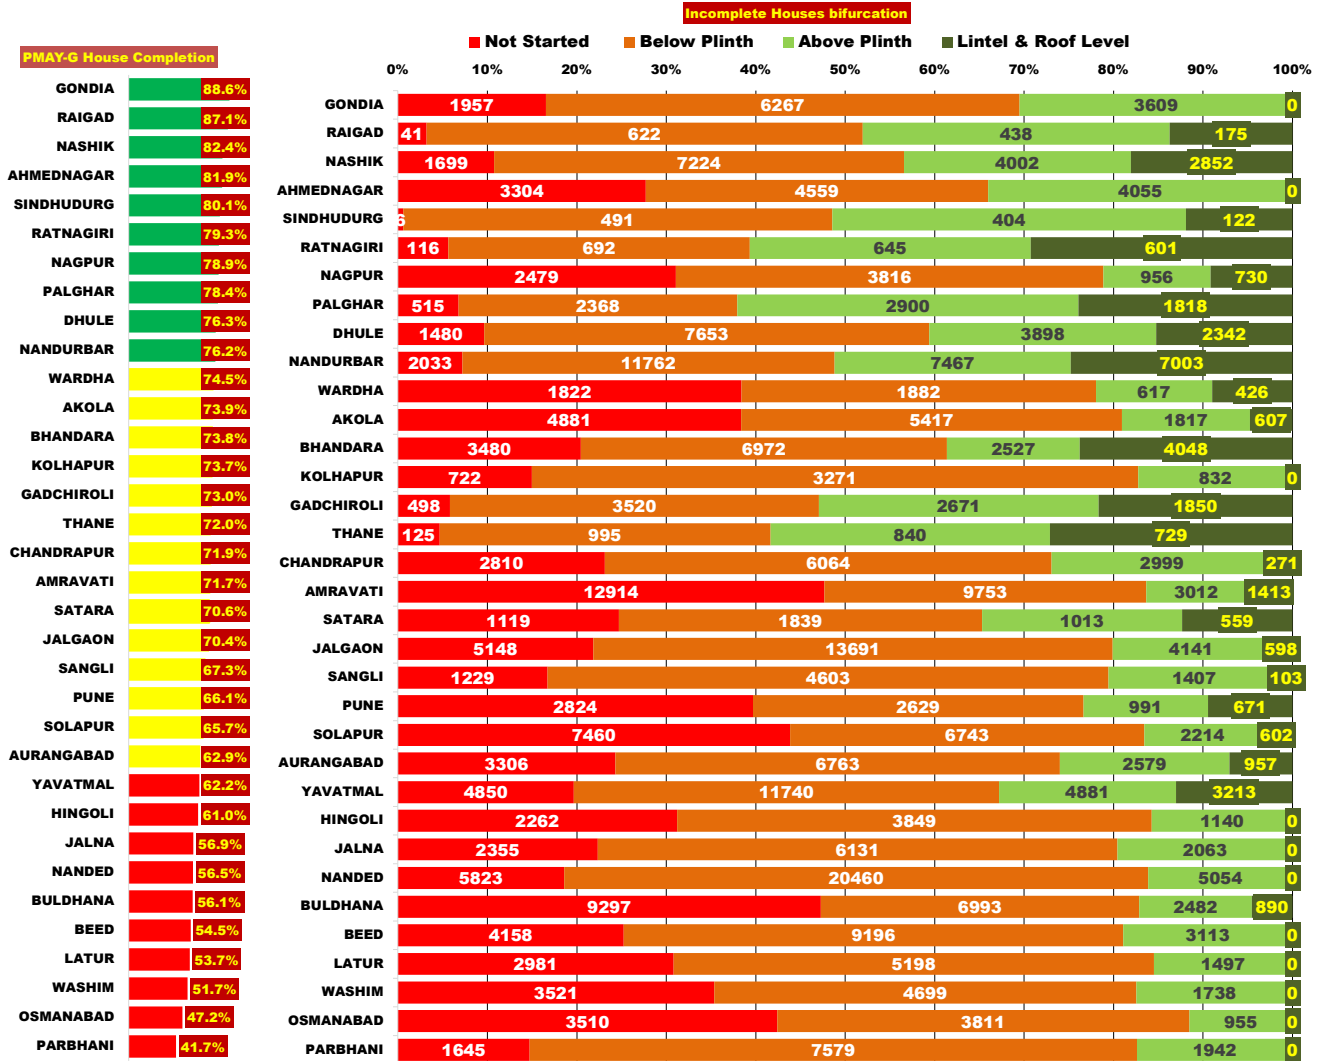


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	20.03.2023	21.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK	89677	73772	73900	128	15777	59	1578
2	AHMEDNAGAR	60748	49675	49769	94	10979	97	1098
3	AMRAVATI	95502	68365	68456	91	27046	56	2705
4	BULDHANA	44728	25026	25077	51	19651	34	1965
5	YAVATMAL	65217	40490	40537	47	24680	59	2468
6	NANDED	69441	39182	39227	45	30214	49	3021
7	AKOLA	48775	36010	36053	43	12722	24	1272
8	JALGAON	79571	55951	55993	42	23578	50	2358
9	RATNAGIRI	9913	7817	7859	42	2054	14	205
10	PALGHAR	35144	27505	27543	38	7601	22	760
11	GADCHIROLI	31573	23023	23059	36	8514	27	851
12	NANDURBAR	118865	90564	90600	36	28265	40	2827
13	WASHIM	20385	10521	10549	28	9836	21	984
14	DHULE	64875	49479	49502	23	15373	54	1537
15	LATUR	20571	11032	11049	17	9522	21	952
16	AURANGABAD	36635	23016	23030	14	13605	32	1361
17	JALNA	24044	13661	13673	12	10371	26	1037
18	WARDHA	18614	13855	13867	12	4747	11	475
19	RAIGAD	9836	8553	8563	10	1273	4	127
20	GONDIA	96116	85142	85151	9	10965	63	1097
21	SANGLI	22071	14854	14862	8	7209	12	721
22	PARBHANI	19078	7940	7947	7	11131	15	1113
23	SATARA	15426	10889	10896	7	4530	13	453
24	NAGPUR	37187	29335	29341	6	7846	12	785
25	CHANDRAPUR	43071	30973	30978	5	12093	38	1209
26	BEED	35261	19207	19211	4	16050	25	1605
27	HINGOLI	18083	11033	11037	4	7046	17	705
28	THANE	9598	6906	6909	3	2689	3	269
29	KOLHAPUR	17765	13089	13091	2	4674	9	467
30	PUNE	20961	13845	13846	1	7115	10	712
31	SINDHUDURG	5147	4123	4124	1	1023	4	102
32	BHANDARA	65098	48071	48071	0	17027	34	1703
33	OSMANABAD	14364	6777	6777	0	7587	17	759
34	SOLAPUR	49604	32585	32585	0	17019	22	1702
Total		1412944	1002266	1003132	866	409812	991	40981

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	20.03.2023	21.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	160827	161006	179	38325
2	NAGPUR DIV.	116255	87419	87504	85	28751
3	AMRAVATI DIV.	109702	92577	92605	28	17097
4	NASHIK DIV.	141360	108472	108475	3	32885
5	PUNE DIV.	65334	62909	62910	1	2424
6	KONKAN DIV.	34729	29664	29664	0	5065
	Total	666711	541868	542164	296	124547

State Scheme Remaining Sanction

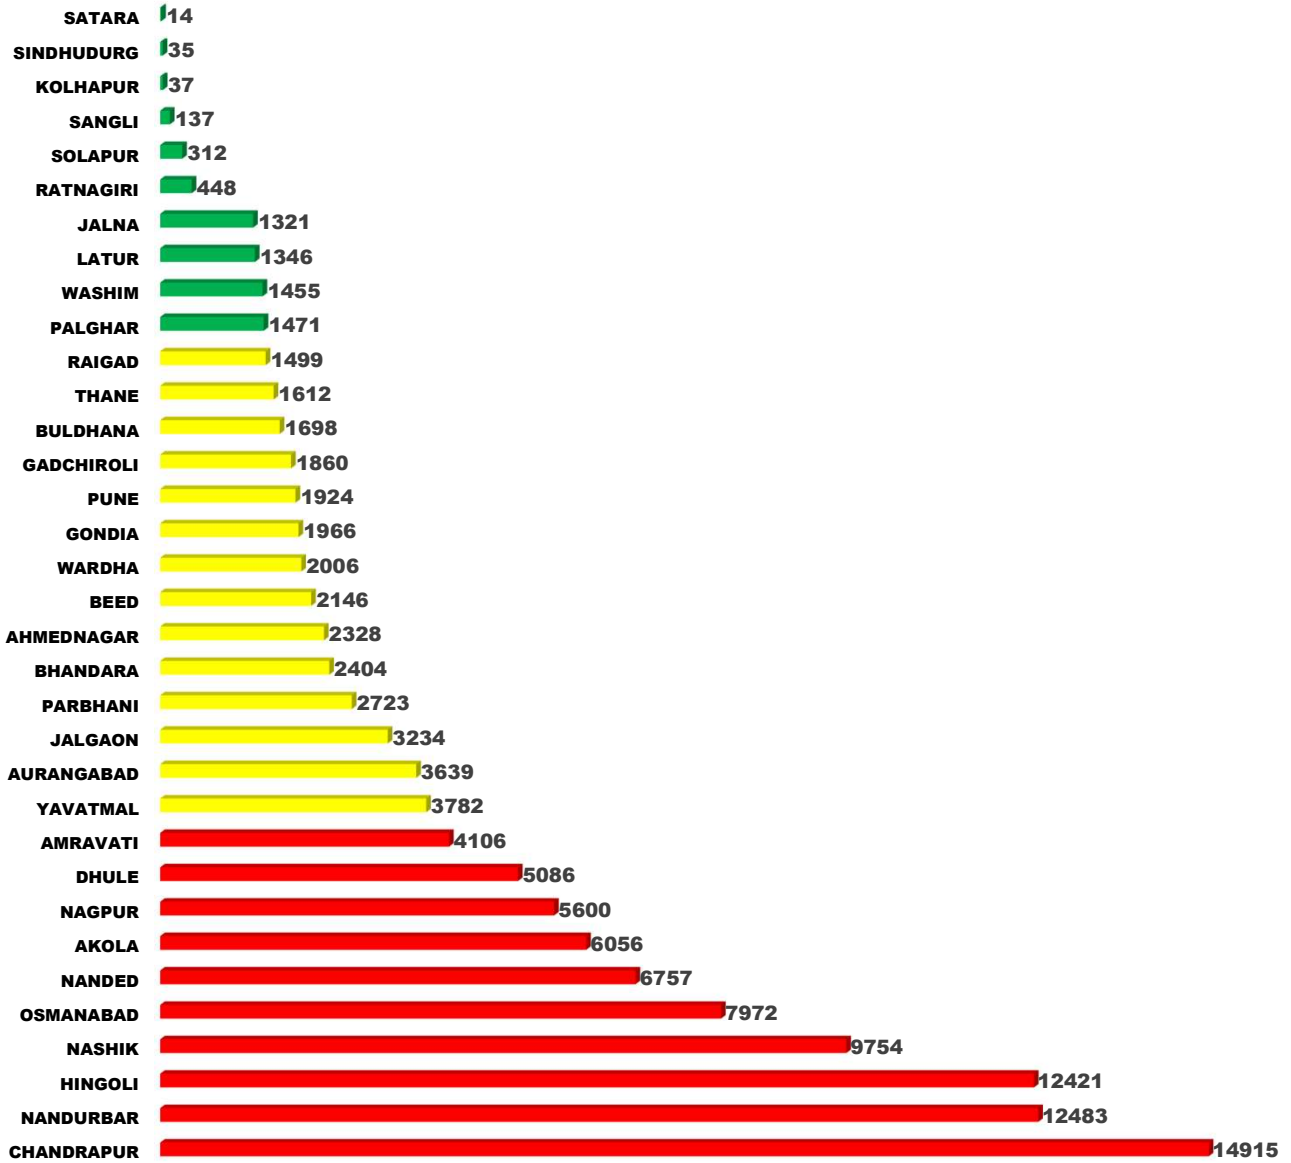


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	20.03.2023	21.03.2023	Daily_Achievement	Remaining
1	GONDIA	14246	12195	12280	85	1966
2	PARBHANI	19784	16993	17061	68	2723
3	BEED	26878	24681	24732	51	2146
4	LATUR	27171	25785	25825	40	1346
5	JALNA	20446	19105	19125	20	1321
6	AMRAVATI	23224	19105	19118	13	4106
7	BULDHANA	21616	19908	19918	10	1698
8	WASHIM	11500	10040	10045	5	1455
9	JALGAON	25659	22423	22425	2	3234
10	AHMEDNAGAR	35298	32969	32970	1	2328
11	SATARA	10647	10632	10633	1	14
12	AKOLA	23681	17625	17625	0	6056
13	AURANGABAD	26141	22502	22502	0	3639
14	BHANDARA	17590	15186	15186	0	2404
15	CHANDRAPUR	38147	23232	23232	0	14915
16	DHULE	21790	16704	16704	0	5086
17	GADCHIROLI	16834	14974	14974	0	1860
18	HINGOLI	27298	14877	14877	0	12421
19	KOLHAPUR	12565	12528	12528	0	37
20	NAGPUR	16291	10691	10691	0	5600
21	NANDED	26760	20003	20003	0	6757
22	NANDURBAR	26578	14095	14095	0	12483
23	NASHIK	32035	22281	22281	0	9754
24	OSMANABAD	24853	16881	16881	0	7972
25	PALGHAR	11792	10321	10321	0	1471
26	PUNE	14672	12748	12748	0	1924
27	RAIGAD	7406	5907	5907	0	1499
28	RATNAGIRI	7126	6678	6678	0	448
29	SANGLI	8732	8595	8595	0	137
30	SINDHUDURG	2141	2106	2106	0	35
31	SOLAPUR	18718	18406	18406	0	312
32	THANE	6264	4652	4652	0	1612
33	WARDHA	13147	11141	11141	0	2006
34	YAVATMAL	29681	25899	25899	0	3782
Total		666711	541868	542164	296	124547

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	20.03.2023	21.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108475	86813	86919	106	21556	73	2156
2	AMRAVATI DIV.	92605	62686	62750	64	29855	54	2986
3	AURANGABAD DIV.	161006	101416	101457	41	59549	94	5955
4	NAGPUR DIV.	87504	67801	67831	30	19673	44	1967
5	PUNE DIV.	62910	51153	51173	20	11737	26	1174
6	KONKAN DIV.	29664	22916	22929	13	6735	13	674
Total		542164	392785	393059	274	149105	303	14911

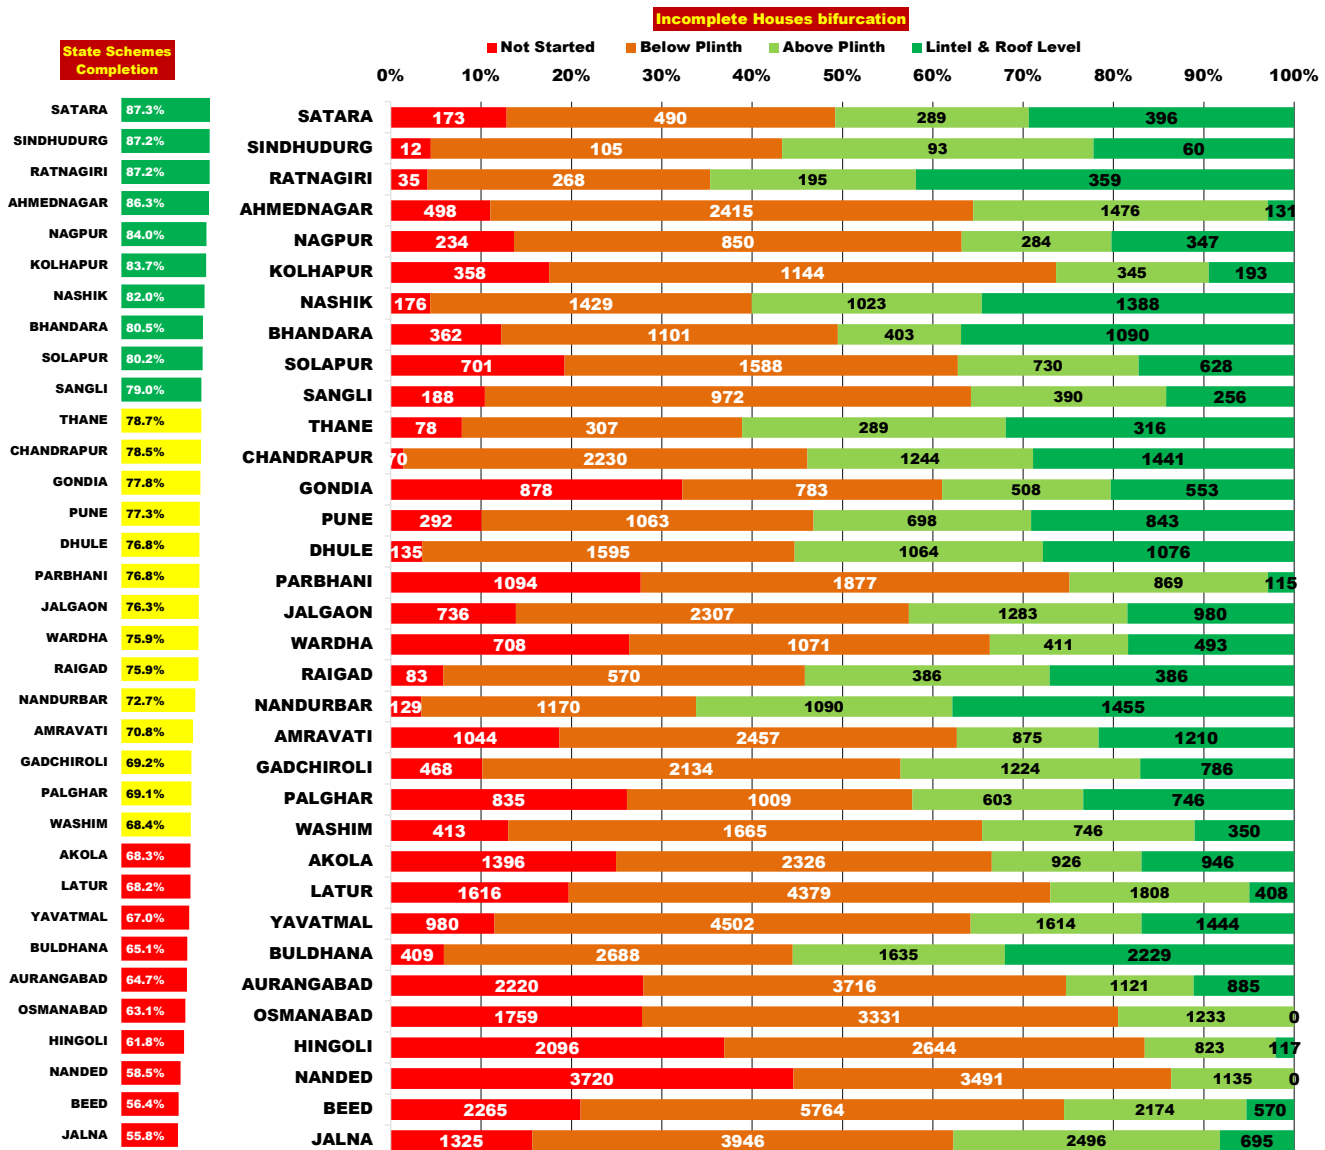

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	20.03.2023	21.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	BULDHANA	19918	12918	12957	39	6961	16	696
2	AHMEDNAGAR	32970	28412	28450	38	4520	32	452
3	NASHIK	22281	18227	18265	38	4016	13	402
4	DHULE	16704	12819	12834	15	3870	11	387
5	NANDURBAR	14095	10236	10251	15	3844	6	384
6	GADCHIROLI	14974	10349	10362	13	4612	9	461
7	JALNA	19125	10651	10663	12	8462	29	846
8	WARDHA	11141	8447	8458	11	2683	7	268
9	YAVATMAL	25899	17348	17359	11	8540	13	854
10	SOLAPUR	18406	14750	14759	9	3647	8	365
11	PALGHAR	10321	7120	7128	8	3193	6	319
12	NANDED	20003	11699	11706	7	8297	9	830
13	PUNE	12748	9845	9852	7	2896	6	290
14	BEED	24732	13953	13959	6	10773	14	1077
15	AKOLA	17625	12026	12031	5	5594	9	559
16	AMRAVATI	19118	13527	13532	5	5586	9	559
17	HINGOLI	14877	9192	9197	5	5680	6	568
18	LATUR	25825	17610	17614	4	8211	11	821
19	RATNAGIRI	6678	5817	5821	4	857	2	86
20	WASHIM	10045	6867	6871	4	3174	7	317
21	AURANGABAD	22502	14557	14560	3	7942	8	794
22	PARBHANI	17061	13103	13106	3	3955	4	396
23	SATARA	10633	9282	9285	3	1348	5	135
24	CHANDRAPUR	23232	18245	18247	2	4985	14	499
25	GONDIA	12280	9556	9558	2	2722	8	272
26	NAGPUR	10691	8974	8976	2	1715	3	172
27	OSMANABAD	16881	10651	10652	1	6229	12	623
28	SANGLI	8595	6788	6789	1	1806	4	181
29	SINDHUDURG	2106	1835	1836	1	270	1	27
30	BHANDARA	15186	12230	12230	0	2956	4	296
31	JALGAON	22425	17119	17119	0	5306	11	531
32	KOLHAPUR	12528	10488	10488	0	2040	3	204
33	RAIGAD	5907	4482	4482	0	1425	3	143
34	THANE	4652	3662	3662	0	990	2	99
	Total	542164	392785	393059	274	149105	303	14911

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	13664	0	44889	0	23563
2	AMRAVATI DIV.	0	35399	0	38602	0	13930
3	AURANGABAD DIV.	0	26010	0	62987	0	18343
4	NAGPUR DIV.	0	12835	0	28521	0	13379
5	KONKAN DIV.	0	800	0	5168	0	5227
6	PUNE DIV.	0	13221	0	19085	0	6457
	Total	0	101929	0	199252	0	80899

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	38
RATNAGIRI	116
THANE	125
GADCHIROLI	473
PALGHAR	515
KOLHAPUR	722
SANGLI	1096
SATARA	1119
DHULE	1480
PARBHANI	1645
NASHIK	1699
WARDHA	1822
GONDIA	1957
NANDURBAR	2033
HINGOLI	2262
JALNA	2325
NAGPUR	2344
CHANDRAPUR	2759
PUNE	2824
LATUR	2981
AHMEDNAGAR	3304
AURANGABAD	3306
BHANDARA	3480
OSMANABAD	3510
WASHIM	3518
BEED	4158
YAVATMAL	4846
AKOLA	4881
JALGAON	5148
NANDED	5823
SOLAPUR	7460
BULDHANA	9286
AMRAVATI	12868

PMAY-G 2nd Ins Pending

SINDHUDURG	491
RAIGAD	622
RATNAGIRI	692
THANE	995
SATARA	1839
WARDHA	1882
PALGHAR	2368
PUNE	2629
KOLHAPUR	3271
GADCHIROLI	3520
OSMANABAD	3811
NAGPUR	3816
HINGOLI	3849
AHMEDNAGAR	4559
SANGLI	4603
WASHIM	4699
LATUR	5198
AKOLA	5417
CHANDRAPUR	6064
JALNA	6131
GONDIA	6267
SOLAPUR	6743
AURANGABAD	6763
BHANDARA	6972
BULDHANA	6993
NASHIK	7224
PARBHANI	7579
DHULE	7653
BEED	9196
AMRAVATI	9753
YAVATMAL	11740
NANDURBAR	11762
JALGAON	13691
NANDED	20460

PMAY-G 3rd Ins Pending

SINDHUDURG	404
RAIGAD	438
WARDHA	617
RATNAGIRI	645
KOLHAPUR	832
THANE	840
OSMANABAD	955
NAGPUR	956
PUNE	991
SATARA	1013
HINGOLI	1140
SANGLI	1407
LATUR	1497
WASHIM	1738
AKOLA	1817
PARBHANI	1942
JALNA	2063
SOLAPUR	2214
BULDHANA	2482
BHANDARA	2527
AURANGABAD	2579
GADCHIROLI	2671
PALGHAR	2900
CHANDRAPUR	2999
AMRAVATI	3012
BEED	3113
GONDIA	3609
DHULE	3898
NASHIK	4002
AHMEDNAGAR	4055
JALGAON	4141
YAVATMAL	4881
NANDED	5054
NANDURBAR	7467

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3304	0	4559	0	4055
2	AKOLA	0	4881	0	5417	0	1817
3	AMRAVATI	0	12868	0	9753	0	3012
4	AURANGABAD	0	3306	0	6763	0	2579
5	BEED	0	4158	0	9196	0	3113
6	BHANDARA	0	3480	0	6972	0	2527
7	BULDHANA	0	9286	0	6993	0	2482
8	CHANDRAPUR	0	2759	0	6064	0	2999
9	DHULE	0	1480	0	7653	0	3898
10	GADCHIROLI	0	473	0	3520	0	2671
11	GONDIA	0	1957	0	6267	0	3609
12	HINGOLI	0	2262	0	3849	0	1140
13	JALGAON	0	5148	0	13691	0	4141
14	JALNA	0	2325	0	6131	0	2063
15	KOLHAPUR	0	722	0	3271	0	832
16	LATUR	0	2981	0	5198	0	1497
17	NAGPUR	0	2344	0	3816	0	956
18	NANDED	0	5823	0	20460	0	5054
19	NANDURBAR	0	2033	0	11762	0	7467
20	NASHIK	0	1699	0	7224	0	4002
21	OSMANABAD	0	3510	0	3811	0	955
22	PALGHAR	0	515	0	2368	0	2900
23	PARBHANI	0	1645	0	7579	0	1942
24	PUNE	0	2824	0	2629	0	991
25	RAIGAD	0	38	0	622	0	438
26	RATNAGIRI	0	116	0	692	0	645
27	SANGLI	0	1096	0	4603	0	1407
28	SATARA	0	1119	0	1839	0	1013
29	SINDHUDURG	0	6	0	491	0	404
30	SOLAPUR	0	7460	0	6743	0	2214
31	THANE	0	125	0	995	0	840
32	WARDHA	0	1822	0	1882	0	617
33	WASHIM	0	3518	0	4699	0	1738
34	YAVATMAL	0	4846	0	11740	0	4881
	Total	0	101929	0	199252	0	80899

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	NASHIK DIV.	0	1674	0	8916	0	5936
2	AMRAVATI DIV.	0	4242	0	13638	0	5796
3	AURANGABAD DIV.	0	16095	0	29148	0	11659
4	NAGPUR DIV.	0	2720	0	8169	0	4074
5	KONKAN DIV.	0	1043	0	2259	0	1566
6	PUNE DIV.	0	1712	0	5257	0	2452
	Total	0	27486	0	67387	0	31483

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	35
CHANDRAPUR	70
THANE	78
RAIGAD	83
NANDURBAR	129
DHULE	135
SATARA	173
NASHIK	176
SANGLI	188
NAGPUR	234
PUNE	292
KOLHAPUR	358
BHANDARA	362
BULDHANA	409
WASHIM	413
GADCHIROLI	468
AHMEDNAGAR	498
SOLAPUR	701
WARDHA	708
JALGAON	736
PALGHAR	835
GONDIA	878
YAVATMAL	980
AMRAVATI	1044
PARBHANI	1094
JALNA	1325
AKOLA	1396
LATUR	1616
OSMANABAD	1759
HINGOLI	2096
AURANGABAD	2220
BEED	2265
NANDED	3720

State Schemes 2nd Ins Pending

SINDHUDURG	105
RATNAGIRI	268
THANE	307
SATARA	490
RAIGAD	570
GONDIA	783
NAGPUR	850
SANGLI	972
PALGHAR	1009
PUNE	1063
WARDHA	1071
BHANDARA	1101
KOLHAPUR	1144
NANDURBAR	1170
NASHIK	1429
SOLAPUR	1588
DHULE	1595
WASHIM	1665
PARBHANI	1877
GADCHIROLI	2134
CHANDRAPUR	2230
JALGAON	2307
AKOLA	2326
AHMEDNAGAR	2415
AMRAVATI	2457
HINGOLI	2644
BULDHANA	2688
OSMANABAD	3331
NANDED	3491
AURANGABAD	3716
JALNA	3946
LATUR	4379
YAVATMAL	4502
BEED	5764

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	195
NAGPUR	284
THANE	289
SATARA	289
KOLHAPUR	345
RAIGAD	386
SANGLI	390
BHANDARA	403
WARDHA	411
GONDIA	508
PALGHAR	603
PUNE	698
SOLAPUR	730
WASHIM	746
HINGOLI	823
PARBHANI	869
AMRAVATI	875
AKOLA	926
NASHIK	1023
DHULE	1064
NANDURBAR	1090
AURANGABAD	1121
NANDED	1135
GADCHIROLI	1224
OSMANABAD	1233
CHANDRAPUR	1244
JALGAON	1283
AHMEDNAGAR	1476
YAVATMAL	1614
BULDHANA	1635
LATUR	1808
BEED	2174
JALNA	2496

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	498	0	2415	0	1476
2	AKOLA	0	1396	0	2326	0	926
3	AMRAVATI	0	1044	0	2457	0	875
4	AURANGABAD	0	2220	0	3716	0	1121
5	BEED	0	2265	0	5764	0	2174
6	BHANDARA	0	362	0	1101	0	403
7	BULDHANA	0	409	0	2688	0	1635
8	CHANDRAPUR	0	70	0	2230	0	1244
9	DHULE	0	135	0	1595	0	1064
10	GADCHIROLI	0	468	0	2134	0	1224
11	GONDIA	0	878	0	783	0	508
12	HINGOLI	0	2096	0	2644	0	823
13	JALGAON	0	736	0	2307	0	1283
14	JALNA	0	1325	0	3946	0	2496
15	KOLHAPUR	0	358	0	1144	0	345
16	LATUR	0	1616	0	4379	0	1808
17	NAGPUR	0	234	0	850	0	284
18	NANDED	0	3720	0	3491	0	1135
19	NANDURBAR	0	129	0	1170	0	1090
20	NASHIK	0	176	0	1429	0	1023
21	OSMANABAD	0	1759	0	3331	0	1233
22	PALGHAR	0	835	0	1009	0	603
23	PARBHANI	0	1094	0	1877	0	869
24	PUNE	0	292	0	1063	0	698
25	RAIGAD	0	83	0	570	0	386
26	RATNAGIRI	0	35	0	268	0	195
27	SANGLI	0	188	0	972	0	390
28	SATARA	0	173	0	490	0	289
29	SINDHUDURG	0	12	0	105	0	93
30	SOLAPUR	0	701	0	1588	0	730
31	THANE	0	78	0	307	0	289
32	WARDHA	0	708	0	1071	0	411
33	WASHIM	0	413	0	1665	0	746
34	YAVATMAL	0	980	0	4502	0	1614
	Total	0	27486	0	67387	0	31483
