



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २२.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१३०५३	१३९	१००४४५०	१३१८	०	०	०
राज्य योजना	५४२९२१	७५७	३९३५३३	४७४	०	०	०
एकूण	१९५५९७४	८९६	१३९७९८३	१७९२	०	०	०

PMAY-G Completion Progress Bar

71.1%



PMAY-G: Incomplete Houses bifurcation

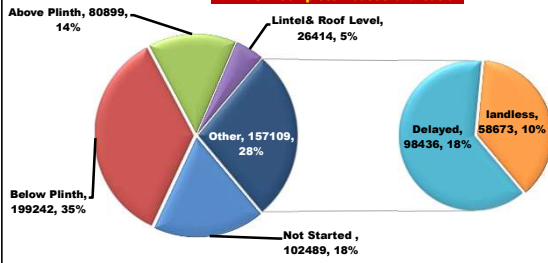


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

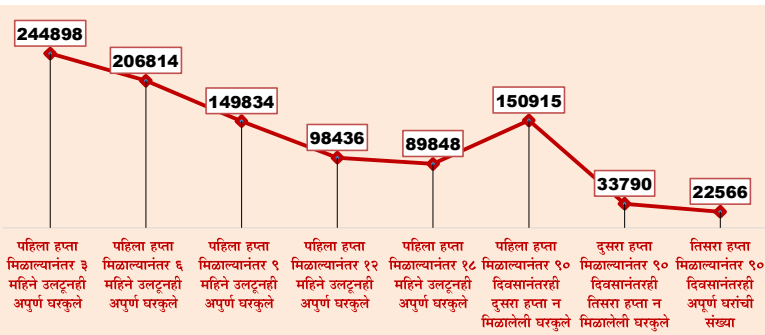


Abhiyan Achievement Day 122

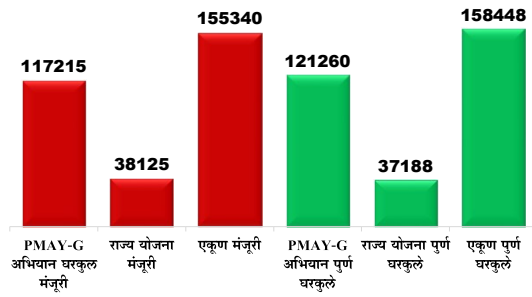

PMAY-G : House completion (Abhiyan Achievement)

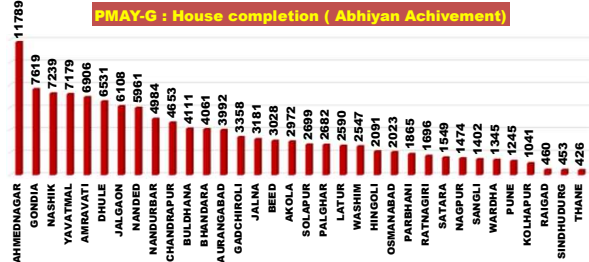

State Schemes : House completion (Abhiyan Achievement)

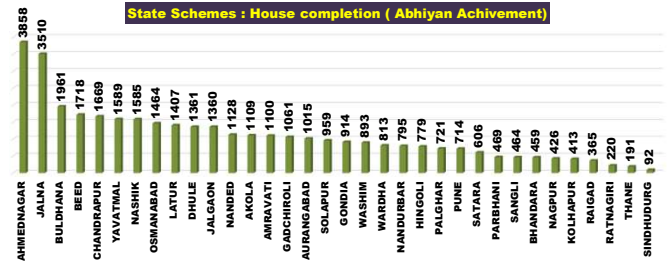


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.



PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	21.03.2023	22.03.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414652	413736	413783	64	869
2	AURANGABAD DIV.	238162	237477	237520	43	642
3	KONKAN DIV.	69737	69638	69663	25	74
4	NAGPUR DIV.	292292	291659	291659	7	633
5	AMRAVATI DIV.	275053	274607	274602	0	451
6	PUNE DIV.	126164	125827	125826	0	338
	Total	1416060	1412944	1413053	139	3007

PMAY-G Remaining Sanction

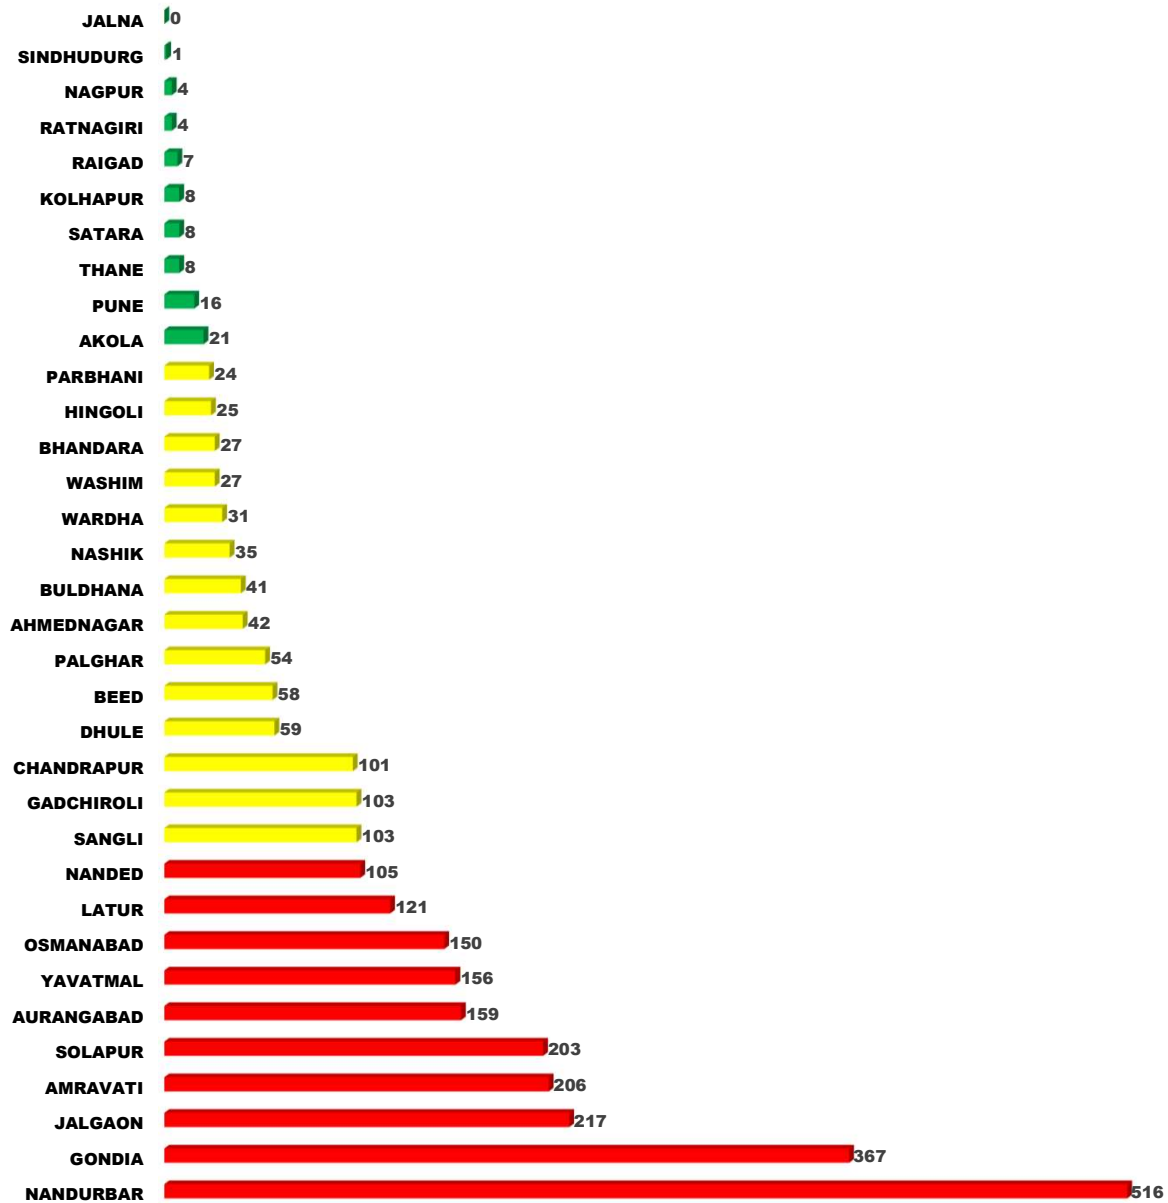


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	21.03.2023	22.03.2023	Daily_Achievement	Remaining
1	LATUR	20729	20571	20608	37	121
2	NANDURBAR	119410	118865	118894	29	516
3	PALGHAR	35222	35144	35168	24	54
4	DHULE	64947	64875	64888	13	59
5	AHMEDNAGAR	60801	60748	60759	11	42
6	NASHIK	89723	89677	89688	11	35
7	CHANDRAPUR	43177	43071	43076	5	101
8	GONDIA	96485	96116	96118	2	367
9	NANDED	69548	69441	69443	2	105
10	OSMANABAD	14516	14364	14366	2	150
11	AURANGABAD	36795	36635	36636	1	159
12	PARBHANI	19103	19078	19079	1	24
13	RAIGAD	9844	9836	9837	1	7
14	AKOLA	48796	48775	48775	0	21
15	AMRAVATI	95708	95502	95502	0	206
16	BEED	35319	35261	35261	0	58
17	GADCHIROLI	31676	31573	31573	0	103
18	HINGOLI	18108	18083	18083	0	25
19	JALNA	24044	24044	24044	0	0
20	KOLHAPUR	17773	17765	17765	0	8
21	NAGPUR	37191	37187	37187	0	4
22	PUNE	20977	20961	20961	0	16
23	RATNAGIRI	9917	9913	9913	0	4
24	SANGLI	22174	22071	22071	0	103
25	SINDHUDURG	5148	5147	5147	0	1
26	SOLAPUR	49807	49604	49604	0	203
27	THANE	9606	9598	9598	0	8
28	WARDHA	18645	18614	18614	0	31
29	WASHIM	20412	20385	20385	0	27
30	YAVATMAL	65373	65217	65217	0	156
31	SATARA	15433	15426	15425	-1	8
32	BULDHANA	44764	44728	44723	-5	41
33	BHANDARA	65118	65098	65091	-7	27
34	JALGAON	79771	79571	79554	-17	217
Total		1416060	1412944	1413053	139	3007

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	21.03.2023	22.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413783	319764	320165	401	93618	300	10402
2	AURANGABAD DIV.	237520	131951	132292	341	105228	203	11692
3	AMRAVATI DIV.	274602	180672	180872	200	93730	194	10414
4	NAGPUR DIV.	291659	230467	230638	171	61021	185	6780
5	KONKAN DIV.	69663	54998	55125	127	14538	47	1615
6	PUNE DIV.	125826	85280	85358	78	40468	65	4496
Total		1413053	1003132	1004450	1318	408603	994	45400

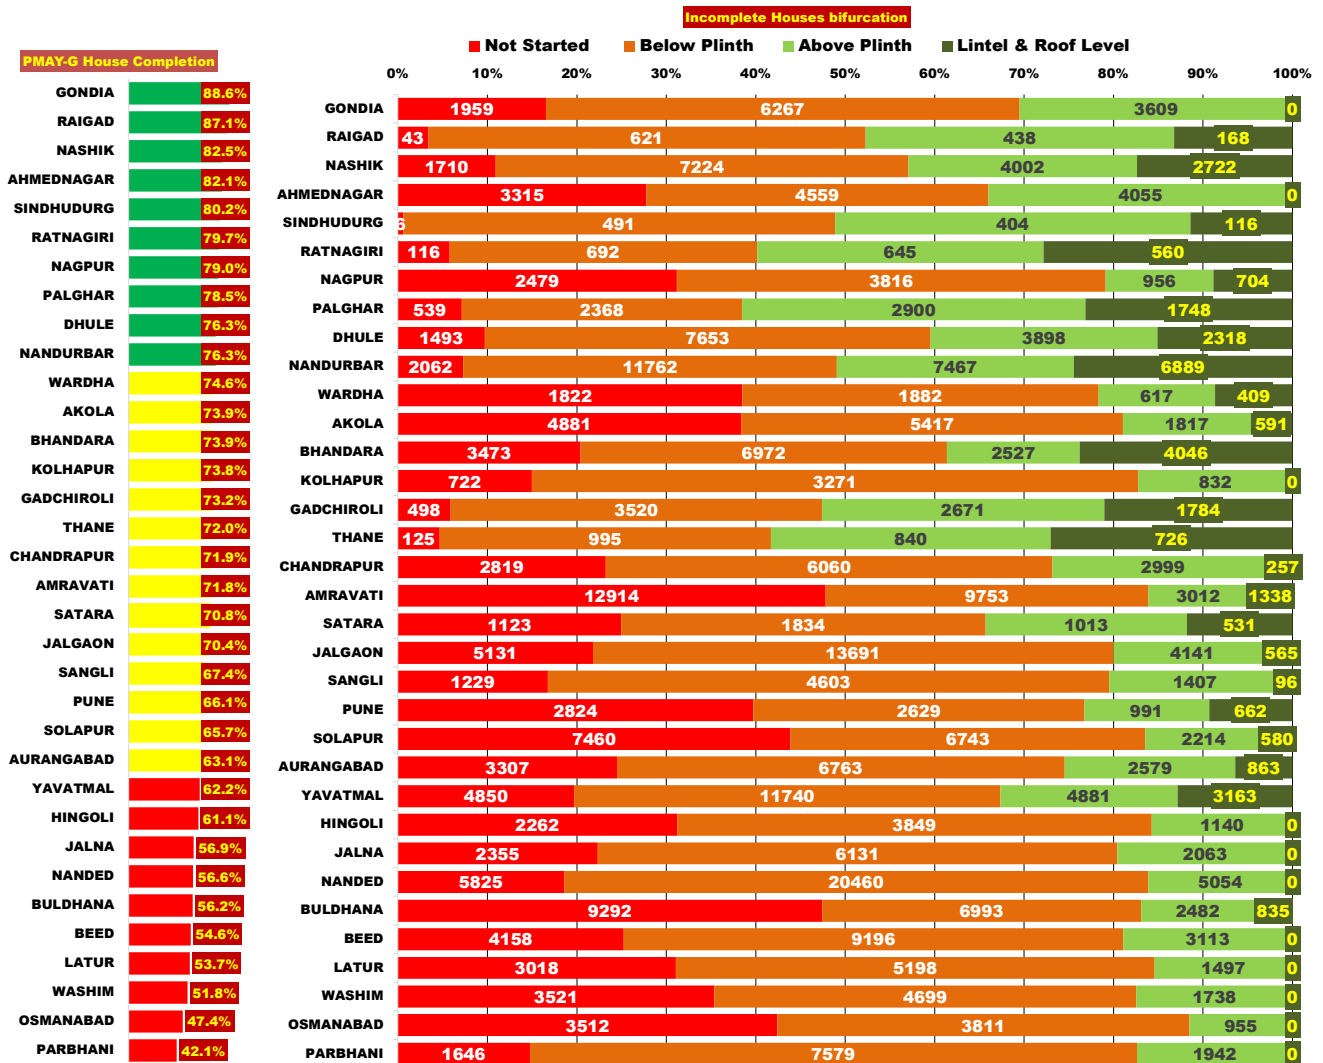


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	21.03.2023	22.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK	89688	73900	74030	130	15658	59	1740
2	NANDURBAR	118894	90600	90714	114	28180	41	3131
3	AHMEDNAGAR	60759	49769	49869	100	10890	97	1210
4	AURANGABAD	36636	23030	23124	94	13512	33	1501
5	PARBHANI	19079	7947	8038	91	11041	15	1227
6	AMRAVATI	95502	68456	68531	75	26971	57	2997
7	PALGHAR	35168	27543	27613	70	7555	22	839
8	GADCHIROLI	31573	23059	23125	66	8448	28	939
9	BULDHANA	44723	25077	25132	55	19591	34	2177
10	YAVATMAL	65217	40537	40587	50	24630	59	2737
11	GONDIA	96118	85151	85197	46	10921	62	1213
12	BEED	35261	19211	19256	45	16005	25	1778
13	NANDED	69443	39227	39271	44	30172	49	3352
14	RATNAGIRI	9913	7859	7900	41	2013	14	224
15	JALGAON	79554	55993	56026	33	23528	50	2614
16	SATARA	15425	10896	10924	28	4501	13	500
17	NAGPUR	37187	29341	29367	26	7820	12	869
18	OSMANABAD	14366	6777	6803	26	7563	17	840
19	DHULE	64888	49502	49526	24	15362	54	1707
20	SOLAPUR	49604	32585	32607	22	16997	22	1889
21	WARDHA	18614	13867	13884	17	4730	11	526
22	AKOLA	48775	36053	36069	16	12706	24	1412
23	LATUR	20608	11049	11064	15	9544	21	1060
24	CHANDRAPUR	43076	30978	30992	14	12084	38	1343
25	JALNA	24044	13673	13687	14	10357	26	1151
26	HINGOLI	18083	11037	11049	12	7034	17	782
27	KOLHAPUR	17765	13091	13103	12	4662	9	518
28	PUNE	20961	13846	13855	9	7106	10	790
29	RAIGAD	9837	8563	8570	7	1267	4	141
30	SANGLI	22071	14862	14869	7	7202	11	800
31	SINDHUDURG	5147	4124	4130	6	1017	4	113
32	WASHIM	20385	10549	10553	4	9832	21	1092
33	THANE	9598	6909	6912	3	2686	3	298
34	BHANDARA	65091	48071	48073	2	17018	33	1891
Total		1413053	1003132	1004450	1318	408603	994	45400

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	21.03.2023	22.03.2023	Daily Achievement	Remaining
1	NAGPUR DIV.	116255	87504	87813	309	28442
2	AURANGABAD DIV.	199331	161006	161291	285	38040
3	KONKAN DIV.	34729	29664	29800	136	4929
4	AMRAVATI DIV.	109702	92605	92628	23	17074
5	NASHIK DIV.	141360	108475	108479	4	32881
6	PUNE DIV.	65334	62910	62910	0	2424
	Total	666711	542164	542921	757	123790

State Scheme Remaining Sanction

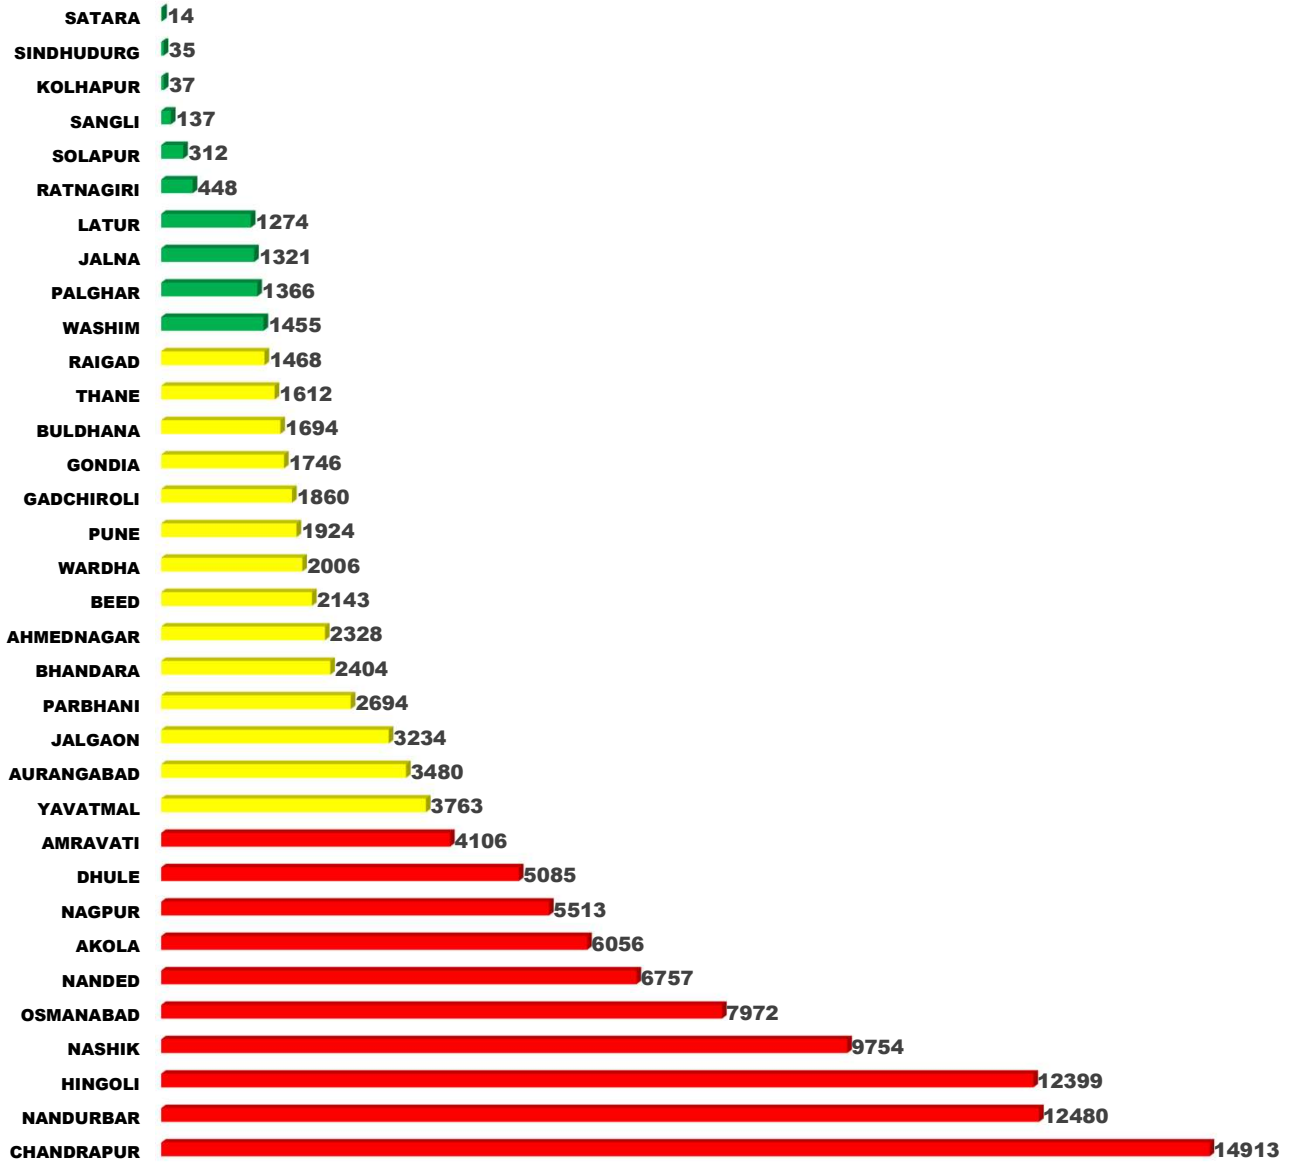


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	21.03.2023	22.03.2023	Daily_Achievement	Remaining
1	GONDIA	14246	12280	12500	220	1746
2	AURANGABAD	26141	22502	22661	159	3480
3	PALGHAR	11792	10321	10426	105	1366
4	NAGPUR	16291	10691	10778	87	5513
5	LATUR	27171	25825	25897	72	1274
6	RAIGAD	7406	5907	5938	31	1468
7	PARBHANI	19784	17061	17090	29	2694
8	HINGOLI	27298	14877	14899	22	12399
9	YAVATMAL	29681	25899	25918	19	3763
10	BULDHANA	21616	19918	19922	4	1694
11	BEED	26878	24732	24735	3	2143
12	NANDURBAR	26578	14095	14098	3	12480
13	CHANDRAPUR	38147	23232	23234	2	14913
14	DHULE	21790	16704	16705	1	5085
15	AHMEDNAGAR	35298	32970	32970	0	2328
16	AKOLA	23681	17625	17625	0	6056
17	AMRAVATI	23224	19118	19118	0	4106
18	BHANDARA	17590	15186	15186	0	2404
19	GADCHIROLI	16834	14974	14974	0	1860
20	JALGAON	25659	22425	22425	0	3234
21	JALNA	20446	19125	19125	0	1321
22	KOLHAPUR	12565	12528	12528	0	37
23	NANDED	26760	20003	20003	0	6757
24	NASHIK	32035	22281	22281	0	9754
25	OSMANABAD	24853	16881	16881	0	7972
26	PUNE	14672	12748	12748	0	1924
27	RATNAGIRI	7126	6678	6678	0	448
28	SANGLI	8732	8595	8595	0	137
29	SATARA	10647	10633	10633	0	14
30	SINDHUDURG	2141	2106	2106	0	35
31	SOLAPUR	18718	18406	18406	0	312
32	THANE	6264	4652	4652	0	1612
33	WARDHA	13147	11141	11141	0	2006
34	WASHIM	11500	10045	10045	0	1455
Total		666711	542164	542921	757	123790

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	21.03.2023	22.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AURANGABAD DIV.	161291	101457	101596	139	59695	94	6633
2	AMRAVATI DIV.	92628	62750	62850	100	29778	55	3309
3	NASHIK DIV.	108479	86919	87016	97	21463	73	2385
4	NAGPUR DIV.	87813	67831	67887	56	19926	44	2214
5	PUNE DIV.	62910	51173	51221	48	11689	26	1299
6	KONKAN DIV.	29800	22929	22963	34	6837	13	760
Total		542921	393059	393533	474	149388	305	16599

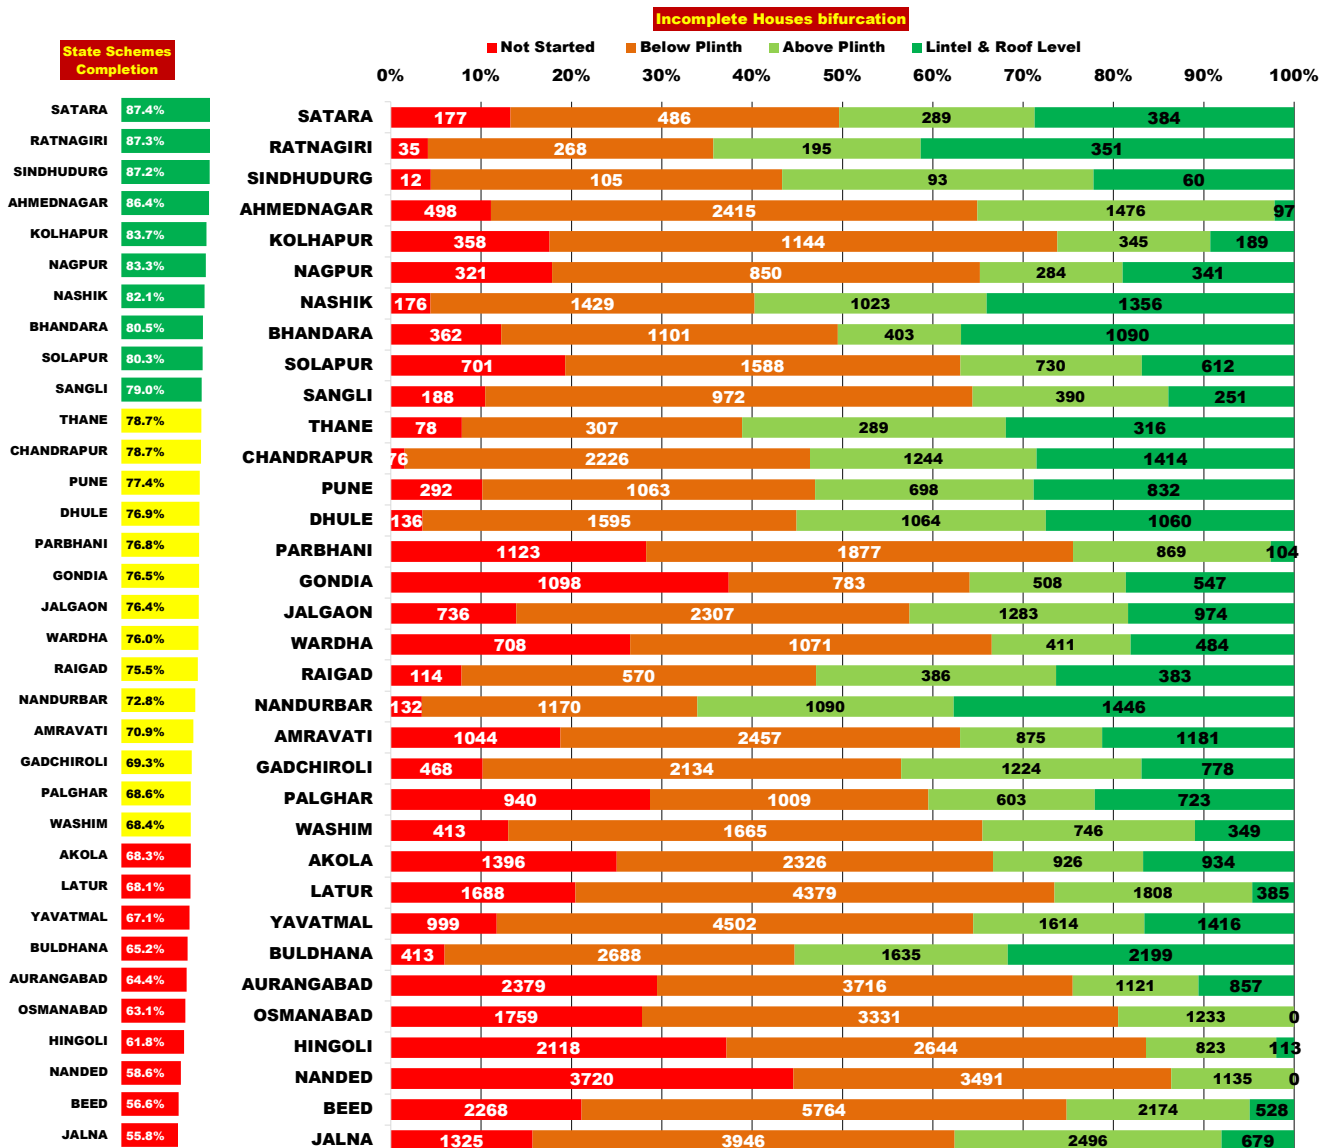

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	21.03.2023	22.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	BEED	24735	13959	14001	42	10734	14	1193
2	AHMEDNAGAR	32970	28450	28484	34	4486	32	498
3	NASHIK	22281	18265	18297	32	3984	13	443
4	BULDHANA	19922	12957	12987	30	6935	16	771
5	AMRAVATI	19118	13532	13561	29	5557	9	617
6	AURANGABAD	22661	14560	14588	28	8073	8	897
7	YAVATMAL	25918	17359	17387	28	8531	13	948
8	CHANDRAPUR	23234	18247	18274	27	4960	14	551
9	LATUR	25897	17614	17637	23	8260	12	918
10	PALGHAR	10426	7128	7151	23	3275	6	364
11	DHULE	16705	12834	12850	16	3855	11	428
12	JALNA	19125	10663	10679	16	8446	29	938
13	SOLAPUR	18406	14759	14775	16	3631	8	403
14	AKOLA	17625	12031	12043	12	5582	9	620
15	SATARA	10633	9285	9297	12	1336	5	148
16	NANDED	20003	11706	11717	11	8286	9	921
17	PARBHANI	17090	13106	13117	11	3973	4	441
18	PUNE	12748	9852	9863	11	2885	6	321
19	NANDURBAR	14098	10251	10260	9	3838	7	426
20	WARDHA	11141	8458	8467	9	2674	7	297
21	GADCHIROLI	14974	10362	10370	8	4604	9	512
22	RATNAGIRI	6678	5821	5829	8	849	2	94
23	GONDIA	12500	9558	9564	6	2936	7	326
24	JALGAON	22425	17119	17125	6	5300	11	589
25	NAGPUR	10778	8976	8982	6	1796	3	200
26	SANGLI	8595	6789	6794	5	1801	4	200
27	HINGOLI	14899	9197	9201	4	5698	6	633
28	KOLHAPUR	12528	10488	10492	4	2036	3	226
29	OSMANABAD	16881	10652	10656	4	6225	12	692
30	RAIGAD	5938	4482	4485	3	1453	3	161
31	WASHIM	10045	6871	6872	1	3173	7	353
32	BHANDARA	15186	12230	12230	0	2956	4	328
33	SINDHUDURG	2106	1836	1836	0	270	1	30
34	THANE	4652	3662	3662	0	990	2	110
	Total	542921	393059	393533	474	149388	305	16599

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	13711	0	44889	0	23563
2	AMRAVATI DIV.	0	35394	0	38602	0	13930
3	AURANGABAD DIV.	0	26053	0	62987	0	18343
4	NAGPUR DIV.	0	12839	0	28517	0	13379
5	KONKAN DIV.	0	826	0	5167	0	5227
6	PUNE DIV.	0	13225	0	19080	0	6457
	Total	0	102048	0	199242	0	80899

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	40
RATNAGIRI	116
THANE	125
GADCHIROLI	473
PALGHAR	539
KOLHAPUR	722
SANGLI	1096
SATARA	1123
DHULE	1493
PARBHANI	1646
NASHIK	1710
WARDHA	1822
GONDIA	1959
NANDURBAR	2062
HINGOLI	2262
JALNA	2325
NAGPUR	2344
CHANDRAPUR	2768
PUNE	2824
LATUR	3018
AURANGABAD	3307
AHMEDNAGAR	3315
BHANDARA	3473
OSMANABAD	3512
WASHIM	3518
BEED	4158
YAVATMAL	4846
AKOLA	4881
JALGAON	5131
NANDED	5825
SOLAPUR	7460
BULDHANA	9281
AMRAVATI	12868

PMAY-G 2nd Ins Pending

SINDHUDURG	491
RAIGAD	621
RATNAGIRI	692
THANE	995
SATARA	1834
WARDHA	1882
PALGHAR	2368
PUNE	2629
KOLHAPUR	3271
GADCHIROLI	3520
OSMANABAD	3811
NAGPUR	3816
HINGOLI	3849
AHMEDNAGAR	4559
SANGLI	4603
WASHIM	4699
LATUR	5198
AKOLA	5417
CHANDRAPUR	6060
JALNA	6131
GONDIA	6267
SOLAPUR	6743
AURANGABAD	6763
BHANDARA	6972
BULDHANA	6993
NASHIK	7224
PARBHANI	7579
DHULE	7653
BEED	9196
AMRAVATI	9753
YAVATMAL	11740
NANDURBAR	11762
JALGAON	13691
NANDED	20460

PMAY-G 3rd Ins Pending

SINDHUDURG	404
RAIGAD	438
WARDHA	617
RATNAGIRI	645
KOLHAPUR	832
THANE	840
OSMANABAD	955
NAGPUR	956
PUNE	991
SATARA	1013
HINGOLI	1140
SANGLI	1407
LATUR	1497
WASHIM	1738
AKOLA	1817
PARBHANI	1942
JALNA	2063
SOLAPUR	2214
BULDHANA	2482
BHANDARA	2527
AURANGABAD	2579
GADCHIROLI	2671
PALGHAR	2900
CHANDRAPUR	2999
AMRAVATI	3012
BEED	3113
GONDIA	3609
DHULE	3898
NASHIK	4002
AHMEDNAGAR	4055
JALGAON	4141
YAVATMAL	4881
NANDED	5054
NANDURBAR	7467

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3315	0	4559	0	4055
2	AKOLA	0	4881	0	5417	0	1817
3	AMRAVATI	0	12868	0	9753	0	3012
4	AURANGABAD	0	3307	0	6763	0	2579
5	BEED	0	4158	0	9196	0	3113
6	BHANDARA	0	3473	0	6972	0	2527
7	BULDHANA	0	9281	0	6993	0	2482
8	DHULE	0	1493	0	7653	0	3898
9	GADCHIROLI	0	473	0	3520	0	2671
10	GONDIA	0	1959	0	6267	0	3609
11	HINGOLI	0	2262	0	3849	0	1140
12	JALGAON	0	5131	0	13691	0	4141
13	JALNA	0	2325	0	6131	0	2063
14	KOLHAPUR	0	722	0	3271	0	832
15	LATUR	0	3018	0	5198	0	1497
16	NAGPUR	0	2344	0	3816	0	956
17	NANDED	0	5825	0	20460	0	5054
18	NANDURBAR	0	2062	0	11762	0	7467
19	NASHIK	0	1710	0	7224	0	4002
20	OSMANABAD	0	3512	0	3811	0	955
21	PALGHAR	0	539	0	2368	0	2900
22	PARBHANI	0	1646	0	7579	0	1942
23	PUNE	0	2824	0	2629	0	991
24	RATNAGIRI	0	116	0	692	0	645
25	SANGLI	0	1096	0	4603	0	1407
26	SINDHUDURG	0	6	0	491	0	404
27	SOLAPUR	0	7460	0	6743	0	2214
28	THANE	0	125	0	995	0	840
29	WARDHA	0	1822	0	1882	0	617
30	WASHIM	0	3518	0	4699	0	1738
31	YAVATMAL	0	4846	0	11740	0	4881
32	RAIGAD	-1	40	0	621	0	438
33	CHANDRAPUR	-4	2768	0	6060	0	2999
34	SATARA	-5	1123	0	1834	0	1013
	Total	0	102048	0	199242	0	80899

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	1678	0	8916	0	5936
2	AMRAVATI DIV.	0	4265	0	13638	0	5796
3	AURANGABAD DIV.	0	16380	0	29148	0	11659
4	NAGPUR DIV.	0	3033	0	8165	0	4074
5	KONKAN DIV.	0	1179	0	2259	0	1566
6	PUNE DIV.	0	1716	0	5253	0	2452
	Total	0	28251	0	67379	0	31483

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	35
CHANDRAPUR	76
THANE	78
RAIGAD	114
NANDURBAR	132
DHULE	136
NASHIK	176
SATARA	177
SANGLI	188
PUNE	292
NAGPUR	321
KOLHAPUR	358
BHANDARA	362
WASHIM	413
BULDHANA	413
GADCHIROLI	468
AHMEDNAGAR	498
SOLAPUR	701
WARDHA	708
JALGAON	736
PALGHAR	940
YAVATMAL	999
AMRAVATI	1044
GONDIA	1098
PARBHANI	1123
JALNA	1325
AKOLA	1396
LATUR	1688
OSMANABAD	1759
HINGOLI	2118
BEED	2268
AURANGABAD	2379
NANDED	3720

State Schemes 2nd Ins Pending

SINDHUDURG	105
RATNAGIRI	268
THANE	307
SATARA	486
RAIGAD	570
GONDIA	783
NAGPUR	850
SANGLI	972
PALGHAR	1009
PUNE	1063
WARDHA	1071
BHANDARA	1101
KOLHAPUR	1144
NANDURBAR	1170
NASHIK	1429
SOLAPUR	1588
DHULE	1595
WASHIM	1665
PARBHANI	1877
GADCHIROLI	2134
CHANDRAPUR	2226
JALGAON	2307
AKOLA	2326
AHMEDNAGAR	2415
AMRAVATI	2457
HINGOLI	2644
BULDHANA	2688
OSMANABAD	3331
NANDED	3491
AURANGABAD	3716
JALNA	3946
LATUR	4379
YAVATMAL	4502
BEED	5764

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	195
NAGPUR	284
THANE	289
SATARA	289
KOLHAPUR	345
RAIGAD	386
SANGLI	390
BHANDARA	403
WARDHA	411
GONDIA	508
PALGHAR	603
PUNE	698
SOLAPUR	730
WASHIM	746
HINGOLI	823
PARBHANI	869
AMRAVATI	875
AKOLA	926
NASHIK	1023
DHULE	1064
NANDURBAR	1090
AURANGABAD	1121
NANDED	1135
GADCHIROLI	1224
OSMANABAD	1233
CHANDRAPUR	1244
JALGAON	1283
AHMEDNAGAR	1476
YAVATMAL	1614
BULDHANA	1635
LATUR	1808
BEED	2174
JALNA	2496

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	498	0	2415	0	1476
2	AKOLA	0	1396	0	2326	0	926
3	AMRAVATI	0	1044	0	2457	0	875
4	AURANGABAD	0	2379	0	3716	0	1121
5	BEED	0	2268	0	5764	0	2174
6	BHANDARA	0	362	0	1101	0	403
7	BULDHANA	0	413	0	2688	0	1635
8	DHULE	0	136	0	1595	0	1064
9	GADCHIROLI	0	468	0	2134	0	1224
10	GONDIA	0	1098	0	783	0	508
11	HINGOLI	0	2118	0	2644	0	823
12	JALGAON	0	736	0	2307	0	1283
13	JALNA	0	1325	0	3946	0	2496
14	KOLHAPUR	0	358	0	1144	0	345
15	LATUR	0	1688	0	4379	0	1808
16	NAGPUR	0	321	0	850	0	284
17	NANDED	0	3720	0	3491	0	1135
18	NANDURBAR	0	132	0	1170	0	1090
19	NASHIK	0	176	0	1429	0	1023
20	OSMANABAD	0	1759	0	3331	0	1233
21	PALGHAR	0	940	0	1009	0	603
22	PARBHANI	0	1123	0	1877	0	869
23	PUNE	0	292	0	1063	0	698
24	RAIGAD	0	114	0	570	0	386
25	RATNAGIRI	0	35	0	268	0	195
26	SANGLI	0	188	0	972	0	390
27	SINDHUDURG	0	12	0	105	0	93
28	SOLAPUR	0	701	0	1588	0	730
29	THANE	0	78	0	307	0	289
30	WARDHA	0	708	0	1071	0	411
31	WASHIM	0	413	0	1665	0	746
32	YAVATMAL	0	999	0	4502	0	1614
33	CHANDRAPUR	-4	76	0	2226	0	1244
34	SATARA	-4	177	0	486	0	289
	Total	0	28251	0	67379	0	31483
