



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २३.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१३०६०	७	१००४८७८	४२८	०	०	०
राज्य योजना	५४२९६७	४६	३९३६२१	८८	४०३	३७०	२४९
एकूण	१९५६०२७	५३	१३९८४९९	५१६	४०३	३७०	२४९

PMAY-G Completion Progress Bar

71.1%





PMAY-G: Incomplete Houses bifurcation

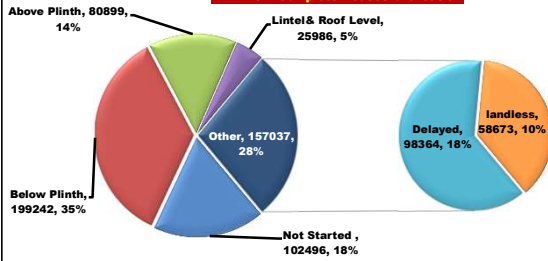


State Schemes Progress Bar

72.5%

State Schemes: Incomplete Houses bifurcation

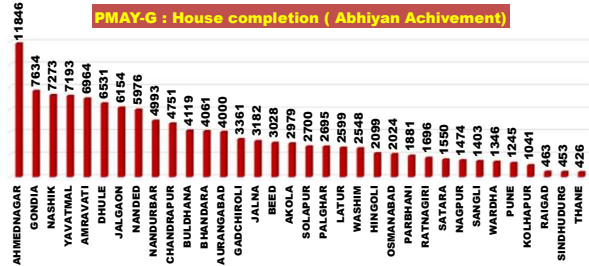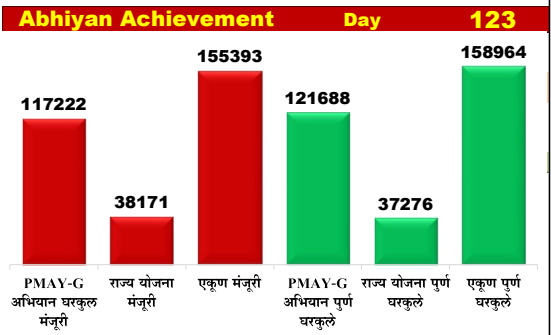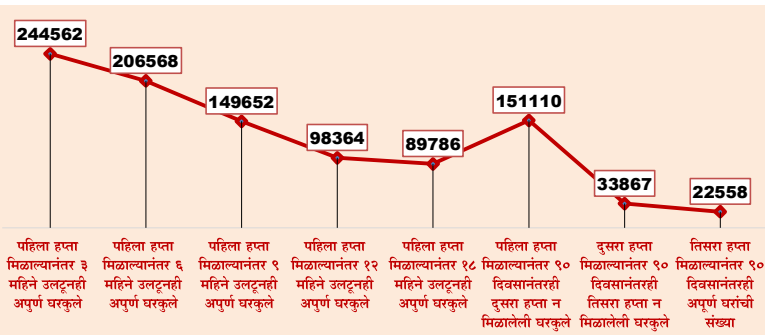

State Schemes: House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	22.03.2023	23.03.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	238162	237520	237527	7	635
2	NASHIK DIV.	414691	413783	413783	0	908
3	AMRAVATI DIV.	275070	274602	274602	0	468
4	NAGPUR DIV.	292306	291659	291659	0	647
5	KONKAN DIV.	69748	69663	69663	0	85
6	PUNE DIV.	126166	125826	125826	0	340
	Total	1416143	1413053	1413060	7	3083

PMAY-G Remaining Sanction

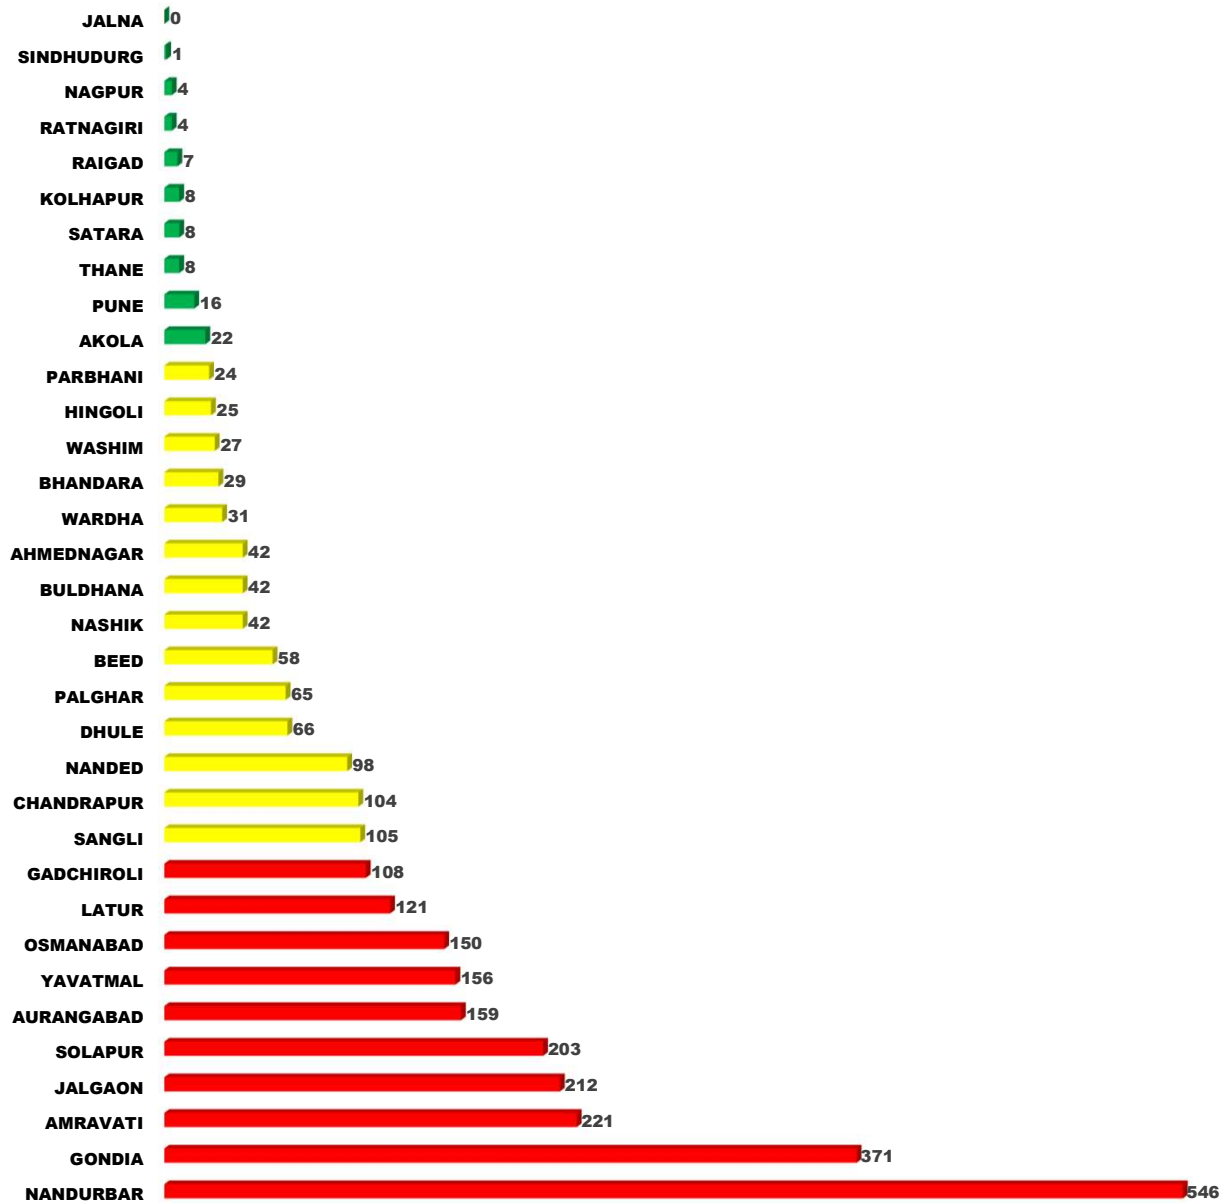


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	22.03.2023	23.03.2023	Daily_Achievement	Remaining
1	NANDED	69548	69443	69450	7	98
2	AHMEDNAGAR	60801	60759	60759	0	42
3	AKOLA	48797	48775	48775	0	22
4	AMRAVATI	95723	95502	95502	0	221
5	AURANGABAD	36795	36636	36636	0	159
6	BEED	35319	35261	35261	0	58
7	BHANDARA	65120	65091	65091	0	29
8	BULDHANA	44765	44723	44723	0	42
9	CHANDRAPUR	43180	43076	43076	0	104
10	DHULE	64954	64888	64888	0	66
11	GADCHIROLI	31681	31573	31573	0	108
12	GONDIA	96489	96118	96118	0	371
13	HINGOLI	18108	18083	18083	0	25
14	JALGAON	79766	79554	79554	0	212
15	JALNA	24044	24044	24044	0	0
16	KOLHAPUR	17773	17765	17765	0	8
17	LATUR	20729	20608	20608	0	121
18	NAGPUR	37191	37187	37187	0	4
19	NANDURBAR	119440	118894	118894	0	546
20	NASHIK	89730	89688	89688	0	42
21	OSMANABAD	14516	14366	14366	0	150
22	PALGHAR	35233	35168	35168	0	65
23	PARBHANI	19103	19079	19079	0	24
24	PUNE	20977	20961	20961	0	16
25	RAIGAD	9844	9837	9837	0	7
26	RATNAGIRI	9917	9913	9913	0	4
27	SANGLI	22176	22071	22071	0	105
28	SATARA	15433	15425	15425	0	8
29	SINDHUDURG	5148	5147	5147	0	1
30	SOLAPUR	49807	49604	49604	0	203
31	THANE	9606	9598	9598	0	8
32	WARDHA	18645	18614	18614	0	31
33	WASHIM	20412	20385	20385	0	27
34	YAVATMAL	65373	65217	65217	0	156
Total		1416143	1413053	1413060	7	3083

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	22.03.2023	23.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413783	320165	320311	146	93472	299	11684
2	NAGPUR DIV.	291659	230638	230755	117	60904	184	7613
3	AMRAVATI DIV.	274602	180872	180960	88	93642	194	11705
4	AURANGABAD DIV.	237527	132292	132350	58	105177	202	13147
5	KONKAN DIV.	69663	55125	55141	16	14522	47	1815
6	PUNE DIV.	125826	85358	85361	3	40465	65	5058
Total		1413060	1004450	1004878	428	408182	989	51023

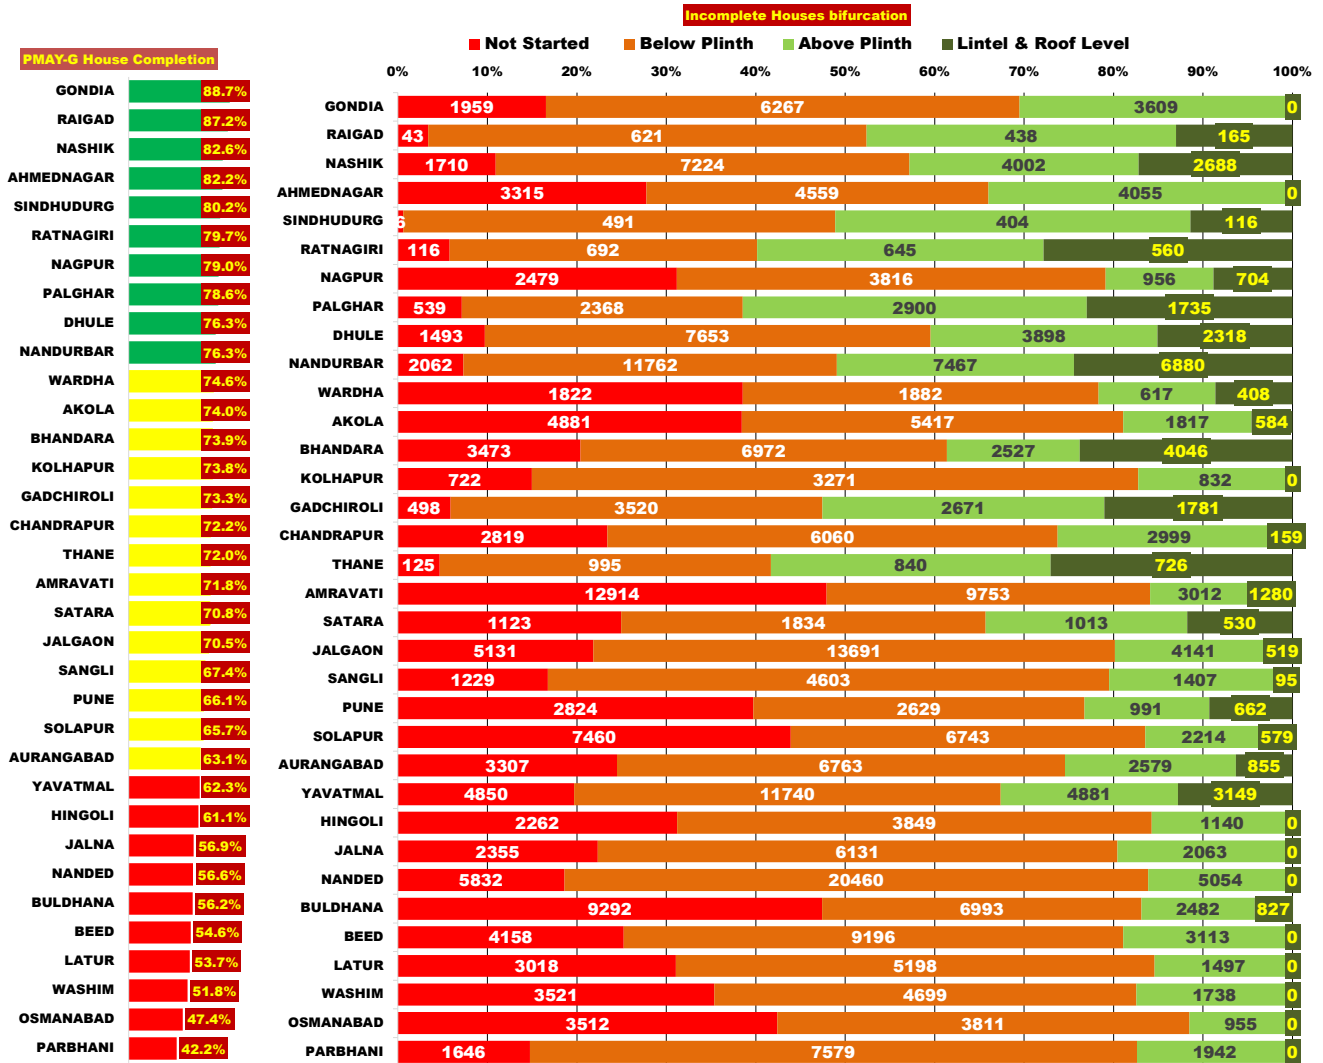


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	22.03.2023	23.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	CHANDRAPUR	43076	30992	31090	98	11986	39	1498
2	AMRAVATI	95502	68531	68589	58	26913	57	3364
3	AHMEDNAGAR	60759	49869	49926	57	10833	96	1354
4	JALGAON	79554	56026	56072	46	23482	50	2935
5	NASHIK	89688	74030	74064	34	15624	59	1953
6	PARBHANI	19079	8038	8054	16	11025	15	1378
7	GONDIA	96118	85197	85212	15	10906	62	1363
8	NANDED	69450	39271	39286	15	30164	49	3771
9	YAVATMAL	65217	40587	40601	14	24616	58	3077
10	PALGHAR	35168	27613	27626	13	7542	22	943
11	LATUR	20608	11064	11073	9	9535	21	1192
12	NANDURBAR	118894	90714	90723	9	28171	41	3521
13	AURANGABAD	36636	23124	23132	8	13504	33	1688
14	BULDHANA	44723	25132	25140	8	19583	33	2448
15	HINGOLI	18083	11049	11057	8	7026	17	878
16	AKOLA	48775	36069	36076	7	12699	24	1587
17	GADCHIROLI	31573	23125	23128	3	8445	27	1056
18	RAIGAD	9837	8570	8573	3	1264	4	158
19	JALNA	24044	13687	13688	1	10356	26	1295
20	OSMANABAD	14366	6803	6804	1	7562	16	945
21	SANGLI	22071	14869	14870	1	7201	11	900
22	SATARA	15425	10924	10925	1	4500	13	563
23	SOLAPUR	49604	32607	32608	1	16996	22	2125
24	WARDHA	18614	13884	13885	1	4729	11	591
25	WASHIM	20385	10553	10554	1	9831	21	1229
26	BEED	35261	19256	19256	0	16005	25	2001
27	BHANDARA	65091	48073	48073	0	17018	33	2127
28	DHULE	64888	49526	49526	0	15362	53	1920
29	KOLHAPUR	17765	13103	13103	0	4662	8	583
30	NAGPUR	37187	29367	29367	0	7820	12	978
31	PUNE	20961	13855	13855	0	7106	10	888
32	RATNAGIRI	9913	7900	7900	0	2013	14	252
33	SINDHUDURG	5147	4130	4130	0	1017	4	127
34	THANE	9598	6912	6912	0	2686	3	336
Total		1413060	1004450	1004878	428	408182	989	51023

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	22.03.2023	23.03.2023	Daily Achievement	Remaining
1	AMRAVATI DIV.	109702	92628	92669	41	17033
2	AURANGABAD DIV.	199331	161291	161296	5	38035
3	KONKAN DIV.	34729	29800	29800	0	4929
4	PUNE DIV.	65334	62910	62910	0	2424
5	NASHIK DIV.	141360	108479	108479	0	32881
6	NAGPUR DIV.	116255	87813	87813	0	28442
	Total	666711	542921	542967	46	123744

State Scheme Remaining Sanction

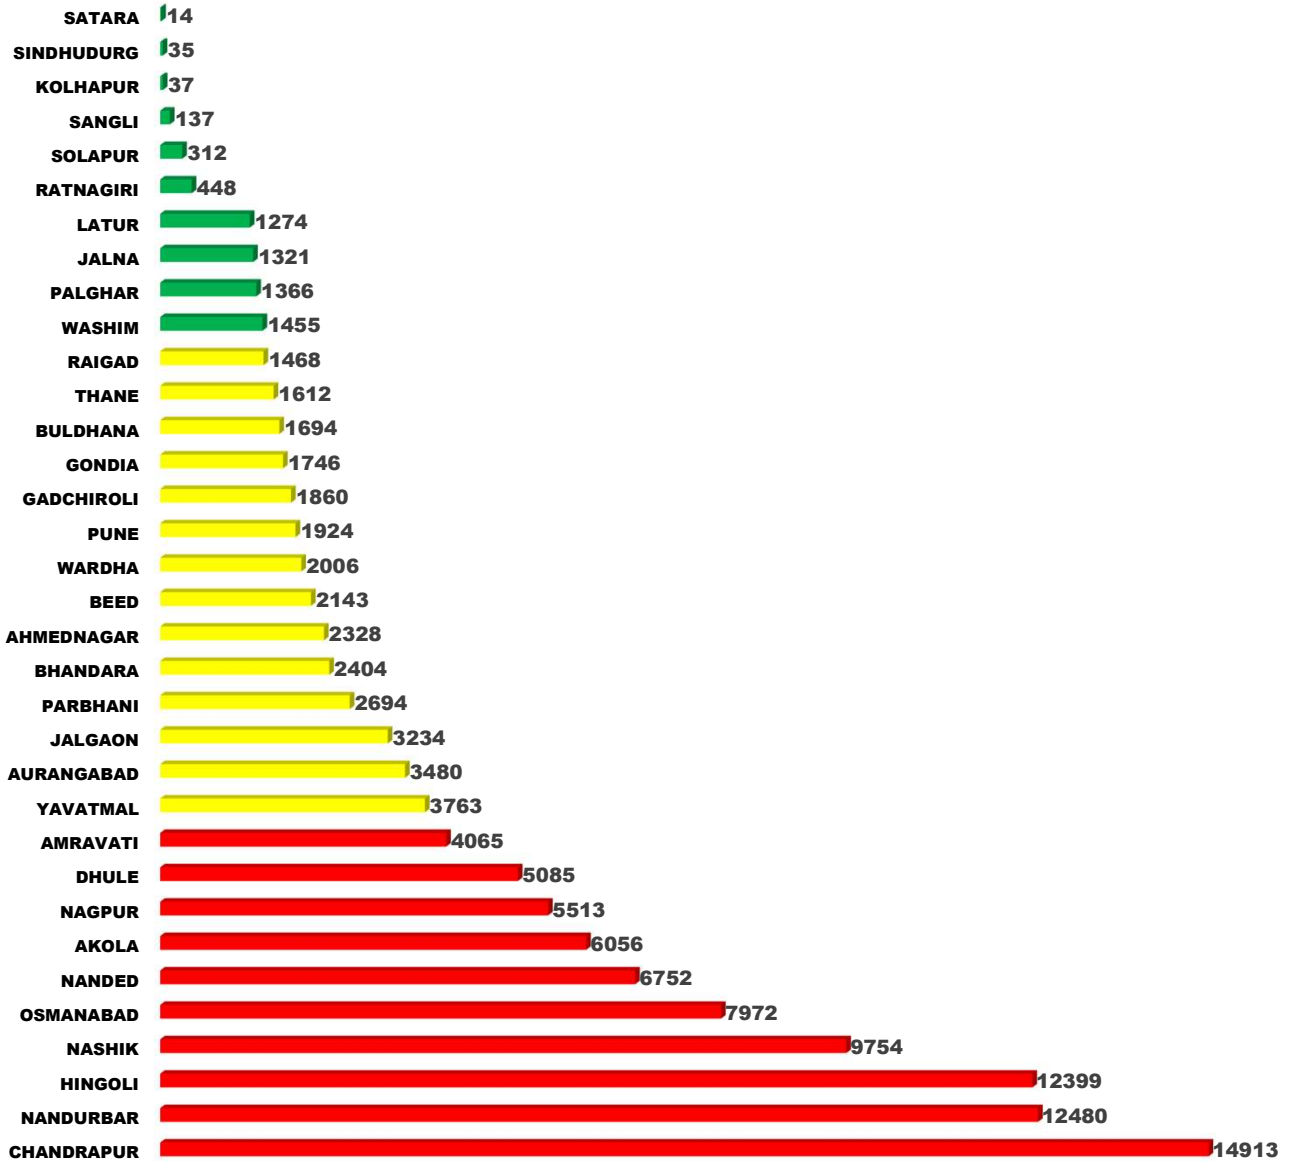


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	22.03.2023	23.03.2023	Daily_Achievement	Remaining
1	AMRAVATI	23224	19118	19159	41	4065
2	NANDED	26760	20003	20008	5	6752
3	AHMEDNAGAR	35298	32970	32970	0	2328
4	AKOLA	23681	17625	17625	0	6056
5	AURANGABAD	26141	22661	22661	0	3480
6	BEED	26878	24735	24735	0	2143
7	BHANDARA	17590	15186	15186	0	2404
8	BULDHANA	21616	19922	19922	0	1694
9	CHANDRAPUR	38147	23234	23234	0	14913
10	DHULE	21790	16705	16705	0	5085
11	GADCHIROLI	16834	14974	14974	0	1860
12	GONDIA	14246	12500	12500	0	1746
13	HINGOLI	27298	14899	14899	0	12399
14	JALGAON	25659	22425	22425	0	3234
15	JALNA	20446	19125	19125	0	1321
16	KOLHAPUR	12565	12528	12528	0	37
17	LATUR	27171	25897	25897	0	1274
18	NAGPUR	16291	10778	10778	0	5513
19	NANDURBAR	26578	14098	14098	0	12480
20	NASHIK	32035	22281	22281	0	9754
21	OSMANABAD	24853	16881	16881	0	7972
22	PALGHAR	11792	10426	10426	0	1366
23	PARBHANI	19784	17090	17090	0	2694
24	PUNE	14672	12748	12748	0	1924
25	RAIGAD	7406	5938	5938	0	1468
26	RATNAGIRI	7126	6678	6678	0	448
27	SANGLI	8732	8595	8595	0	137
28	SATARA	10647	10633	10633	0	14
29	SINDHUDURG	2141	2106	2106	0	35
30	SOLAPUR	18718	18406	18406	0	312
31	THANE	6264	4652	4652	0	1612
32	WARDHA	13147	11141	11141	0	2006
33	WASHIM	11500	10045	10045	0	1455
34	YAVATMAL	29681	25918	25918	0	3763
Total		666711	542921	542967	46	123744

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	22.03.2023	23.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AURANGABAD DIV.	161296	101596	101632	36	59664	94	7458
2	NASHIK DIV.	108479	87016	87044	28	21435	73	2679
3	AMRAVATI DIV.	92669	62850	62861	11	29808	54	3726
4	NAGPUR DIV.	87813	67887	67894	7	19919	43	2490
5	KONKAN DIV.	29800	22963	22969	6	6831	13	854
6	PUNE DIV.	62910	51221	51221	0	11689	26	1461
Total		542967	393533	393621	88	149346	303	18668

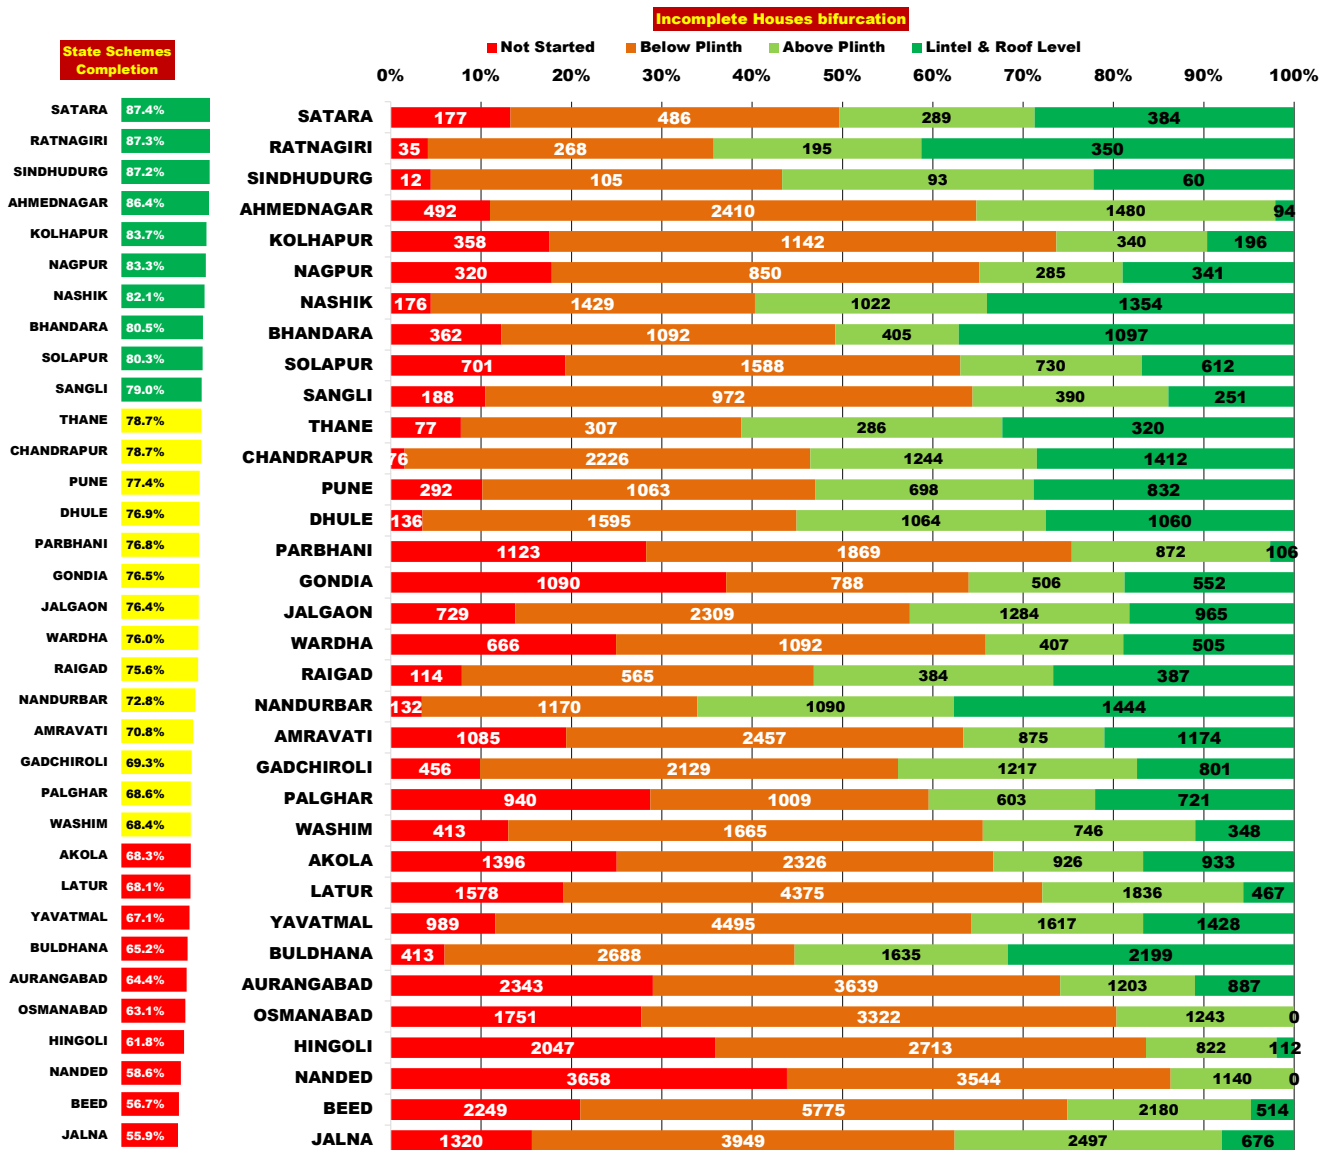

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	22.03.2023	23.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	BEED	24735	14001	14017	16	10718	14	1340
2	JALGAON	22425	17125	17138	13	5287	11	661
3	AHMEDNAGAR	32970	28484	28494	10	4476	31	560
4	AMRAVATI	19159	13561	13568	7	5591	9	699
5	HINGOLI	14899	9201	9205	4	5694	6	712
6	JALNA	19125	10679	10683	4	8442	29	1055
7	LATUR	25897	17637	17641	4	8256	11	1032
8	NANDED	20008	11717	11721	4	8287	9	1036
9	WARDHA	11141	8467	8471	4	2670	7	334
10	NASHIK	22281	18297	18300	3	3981	13	498
11	PARBHANI	17090	13117	13120	3	3970	4	496
12	RAIGAD	5938	4485	4488	3	1450	3	181
13	CHANDRAPUR	23234	18274	18276	2	4958	14	620
14	NANDURBAR	14098	10260	10262	2	3836	6	480
15	PALGHAR	10426	7151	7153	2	3273	6	409
16	YAVATMAL	25918	17387	17389	2	8529	13	1066
17	AKOLA	17625	12043	12044	1	5581	9	698
18	AURANGABAD	22661	14588	14589	1	8072	8	1009
19	GADCHIROLI	14974	10370	10371	1	4603	9	575
20	RATNAGIRI	6678	5829	5830	1	848	2	106
21	WASHIM	10045	6872	6873	1	3172	7	397
22	BHANDARA	15186	12230	12230	0	2956	4	370
23	BULDHANA	19922	12987	12987	0	6935	16	867
24	DHULE	16705	12850	12850	0	3855	11	482
25	GONDIA	12500	9564	9564	0	2936	7	367
26	KOLHAPUR	12528	10492	10492	0	2036	3	255
27	NAGPUR	10778	8982	8982	0	1796	3	225
28	OSMANABAD	16881	10656	10656	0	6225	12	778
29	PUNE	12748	9863	9863	0	2885	6	361
30	SANGLI	8595	6794	6794	0	1801	4	225
31	SATARA	10633	9297	9297	0	1336	5	167
32	SINDHUDURG	2106	1836	1836	0	270	1	34
33	SOLAPUR	18406	14775	14775	0	3631	8	454
34	THANE	4652	3662	3662	0	990	2	124
	Total	542967	393533	393621	88	149346	303	18668

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	13711	0	44889	0	23563
2	AMRAVATI DIV.	0	35394	0	38602	0	13930
3	AURANGABAD DIV.	0	26060	0	62987	0	18343
4	NAGPUR DIV.	0	12839	0	28517	0	13379
5	KONKAN DIV.	0	826	0	5167	0	5227
6	PUNE DIV.	0	13225	0	19080	0	6457
	Total	0	102055	0	199242	0	80899

PMAY-G 1st Ins Pending

SINDHUDURG	6
RAIGAD	40
RATNAGIRI	116
THANE	125
GADCHIROLI	473
PALGHAR	539
KOLHAPUR	722
SANGLI	1096
SATARA	1123
DHULE	1493
PARBHANI	1646
NASHIK	1710
WARDHA	1822
GONDIA	1959
NANDURBAR	2062
HINGOLI	2262
JALNA	2325
NAGPUR	2344
CHANDRAPUR	2768
PUNE	2824
LATUR	3018
AURANGABAD	3307
AHMEDNAGAR	3315
BHANDARA	3473
OSMANABAD	3512
WASHIM	3518
BEED	4158
YAVATMAL	4846
AKOLA	4881
JALGAON	5131
NANDED	5832
SOLAPUR	7460
BULDHANA	9281
AMRAVATI	12868

PMAY-G 2nd Ins Pending

SINDHUDURG	491
RAIGAD	621
RATNAGIRI	692
THANE	995
SATARA	1834
WARDHA	1882
PALGHAR	2368
PUNE	2629
KOLHAPUR	3271
GADCHIROLI	3520
OSMANABAD	3811
NAGPUR	3816
HINGOLI	3849
AHMEDNAGAR	4559
SANGLI	4603
WASHIM	4699
LATUR	5198
AKOLA	5417
CHANDRAPUR	6060
JALNA	6131
GONDIA	6267
SOLAPUR	6743
AURANGABAD	6763
BHANDARA	6972
BULDHANA	6993
NASHIK	7224
PARBHANI	7579
DHULE	7653
BEED	9196
AMRAVATI	9753
YAVATMAL	11740
NANDURBAR	11762
JALGAON	13691
NANDED	20460

PMAY-G 3rd Ins Pending

SINDHUDURG	404
RAIGAD	438
WARDHA	617
RATNAGIRI	645
KOLHAPUR	832
THANE	840
OSMANABAD	955
NAGPUR	956
PUNE	991
SATARA	1013
HINGOLI	1140
SANGLI	1407
LATUR	1497
WASHIM	1738
AKOLA	1817
PARBHANI	1942
JALNA	2063
SOLAPUR	2214
BULDHANA	2482
BHANDARA	2527
AURANGABAD	2579
GADCHIROLI	2671
PALGHAR	2900
CHANDRAPUR	2999
AMRAVATI	3012
BEED	3113
GONDIA	3609
DHULE	3898
NASHIK	4002
AHMEDNAGAR	4055
JALGAON	4141
YAVATMAL	4881
NANDED	5054
NANDURBAR	7467

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3315	0	4559	0	4055
2	AKOLA	0	4881	0	5417	0	1817
3	AMRAVATI	0	12868	0	9753	0	3012
4	AURANGABAD	0	3307	0	6763	0	2579
5	BEED	0	4158	0	9196	0	3113
6	BHANDARA	0	3473	0	6972	0	2527
7	BULDHANA	0	9281	0	6993	0	2482
8	CHANDRAPUR	0	2768	0	6060	0	2999
9	DHULE	0	1493	0	7653	0	3898
10	GADCHIROLI	0	473	0	3520	0	2671
11	GONDIA	0	1959	0	6267	0	3609
12	HINGOLI	0	2262	0	3849	0	1140
13	JALGAON	0	5131	0	13691	0	4141
14	JALNA	0	2325	0	6131	0	2063
15	KOLHAPUR	0	722	0	3271	0	832
16	LATUR	0	3018	0	5198	0	1497
17	NAGPUR	0	2344	0	3816	0	956
18	NANDED	0	5832	0	20460	0	5054
19	NANDURBAR	0	2062	0	11762	0	7467
20	NASHIK	0	1710	0	7224	0	4002
21	OSMANABAD	0	3512	0	3811	0	955
22	PALGHAR	0	539	0	2368	0	2900
23	PARBHANI	0	1646	0	7579	0	1942
24	PUNE	0	2824	0	2629	0	991
25	RAIGAD	0	40	0	621	0	438
26	RATNAGIRI	0	116	0	692	0	645
27	SANGLI	0	1096	0	4603	0	1407
28	SATARA	0	1123	0	1834	0	1013
29	SINDHUDURG	0	6	0	491	0	404
30	SOLAPUR	0	7460	0	6743	0	2214
31	THANE	0	125	0	995	0	840
32	WARDHA	0	1822	0	1882	0	617
33	WASHIM	0	3518	0	4699	0	1738
34	YAVATMAL	0	4846	0	11740	0	4881
	Total	0	102055	0	199242	0	80899

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD DIV.	316	16069	278	29186	144	11793
2	NAGPUR DIV.	63	2970	51	8177	61	4064
3	NASHIK DIV.	13	1665	16	8913	12	5940
4	AMRAVATI DIV.	10	4296	17	13631	14	5799
5	KONKAN DIV.	1	1178	6	2254	11	1561
6	PUNE DIV.	0	1716	2	5251	7	2447
Total		403	27894	370	67412	249	31604

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	35
CHANDRAPUR	76
THANE	77
RAIGAD	114
NANDURBAR	132
DHULE	136
NASHIK	176
SATARA	177
SANGLI	188
PUNE	292
NAGPUR	320
KOLHAPUR	358
BHANDARA	362
WASHIM	413
BULDHANA	413
GADCHIROLI	456
AHMEDNAGAR	492
WARDHA	666
SOLAPUR	701
JALGAON	729
PALGHAR	940
YAVATMAL	989
AMRAVATI	1085
GONDIA	1090
PARBHANI	1123
JALNA	1320
AKOLA	1396
LATUR	1578
OSMANABAD	1751
HINGOLI	2047
BEED	2249
AURANGABAD	2343
NANDED	3658

State Schemes 2nd Ins Pending

SINDHUDURG	105
RATNAGIRI	268
THANE	307
SATARA	486
RAIGAD	565
GONDIA	788
NAGPUR	850
SANGLI	972
PALGHAR	1009
PUNE	1063
WARDHA	1092
BHANDARA	1092
KOLHAPUR	1142
NANDURBAR	1170
NASHIK	1429
SOLAPUR	1588
DHULE	1595
WASHIM	1665
PARBHANI	1869
GADCHIROLI	2129
CHANDRAPUR	2226
JALGAON	2309
AKOLA	2326
AHMEDNAGAR	2410
AMRAVATI	2457
BULDHANA	2688
HINGOLI	2713
OSMANABAD	3322
NANDED	3544
AURANGABAD	3639
JALNA	3949
LATUR	4375
YAVATMAL	4495
BEED	5775

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	195
NAGPUR	285
THANE	286
SATARA	289
KOLHAPUR	340
RAIGAD	384
SANGLI	390
BHANDARA	405
WARDHA	407
GONDIA	506
PALGHAR	603
PUNE	698
SOLAPUR	730
WASHIM	746
HINGOLI	822
PARBHANI	872
AMRAVATI	875
AKOLA	926
NASHIK	1022
DHULE	1064
NANDURBAR	1090
NANDED	1140
AURANGABAD	1203
GADCHIROLI	1217
OSMANABAD	1243
CHANDRAPUR	1244
JALGAON	1284
AHMEDNAGAR	1480
YAVATMAL	1617
BULDHANA	1635
LATUR	1836
BEED	2180
JALNA	2497

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	LATUR	110	1578	114	4375	86	1836
2	AURANGABAD	36	2343	113	3639	31	1203
3	NANDED	67	3658	14	3544	9	1140
4	WARDHA	42	666	21	1092	25	407
5	HINGOLI	71	2047	2	2713	3	822
6	GADCHIROLI	12	456	17	2129	24	1217
7	YAVATMAL	10	989	17	4495	14	1617
8	OSMANABAD	8	1751	17	3322	7	1243
9	BEED	19	2249	8	5775	2	2180
10	AHMEDNAGAR	6	492	11	2410	7	1480
11	BHANDARA	0	362	9	1092	7	405
12	GONDIA	8	1090	3	788	5	506
13	JALGAON	7	729	5	2309	4	1284
14	PARBHANI	0	1123	8	1869	5	872
15	RAIGAD	0	114	5	565	7	384
16	KOLHAPUR	0	358	2	1142	7	340
17	JALNA	5	1320	2	3949	1	2497
18	THANE	1	77	1	307	4	286
19	NAGPUR	1	320	1	850	0	285
20	NASHIK	0	176	0	1429	1	1022
21	AKOLA	0	1396	0	2326	0	926
22	AMRAVATI	0	1085	0	2457	0	875
23	BULDHANA	0	413	0	2688	0	1635
24	CHANDRAPUR	0	76	0	2226	0	1244
25	DHULE	0	136	0	1595	0	1064
26	NANDURBAR	0	132	0	1170	0	1090
27	PALGHAR	0	940	0	1009	0	603
28	PUNE	0	292	0	1063	0	698
29	RATNAGIRI	0	35	0	268	0	195
30	SANGLI	0	188	0	972	0	390
31	SATARA	0	177	0	486	0	289
32	SINDHUDURG	0	12	0	105	0	93
33	SOLAPUR	0	701	0	1588	0	730
34	WASHIM	0	413	0	1665	0	746
	Total	403	27894	370	67412	249	31604
