



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २५.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१२६४०	५५	१००७३४३	१२२३	०	०	०
राज्य योजना	५४४०९४	७८५	३९४४५२	४०७	४०४	५६५	६१६
एकूण	१९५६७३४	८४०	१४०१७९५	१६३०	४०४	५६५	६१६

PMAY-G Completion Progress Bar

71.3%



PMAY-G Incomplete Houses bifurcation

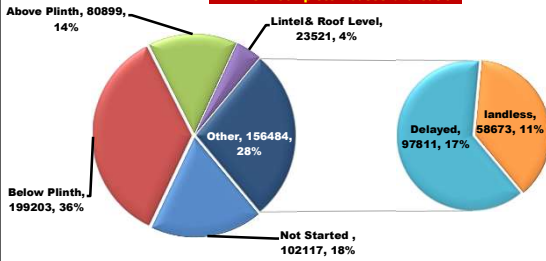


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

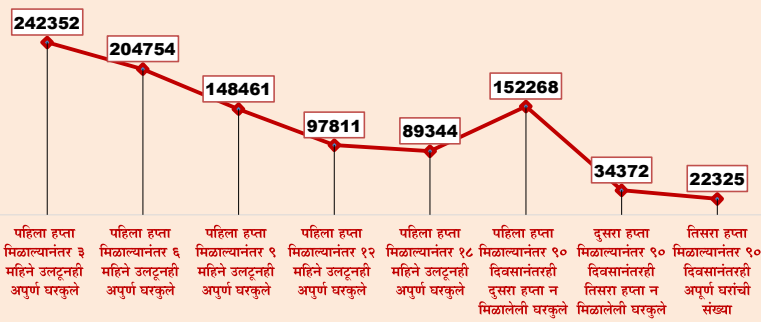


Abhiyan Achievement Day 125

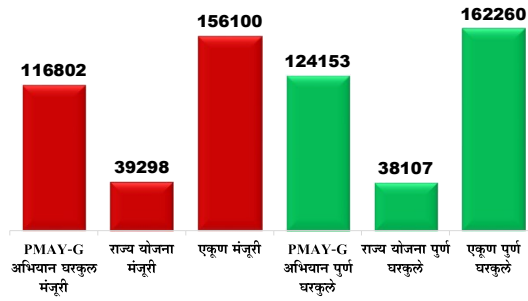

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	24.03.2023	25.03.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	275070	274608	274643	35	427
2	AURANGABAD DIV.	238162	237539	237547	11	615
3	KONKAN DIV.	69747	69659	69664	5	83
4	NASHIK DIV.	414671	413791	413776	2	895
5	NAGPUR DIV.	292302	291677	291675	2	627
6	PUNE DIV.	125739	125708	125335	0	404
Total		1415691	1412982	1412640	55	3051

PMAY-G Remaining Sanction

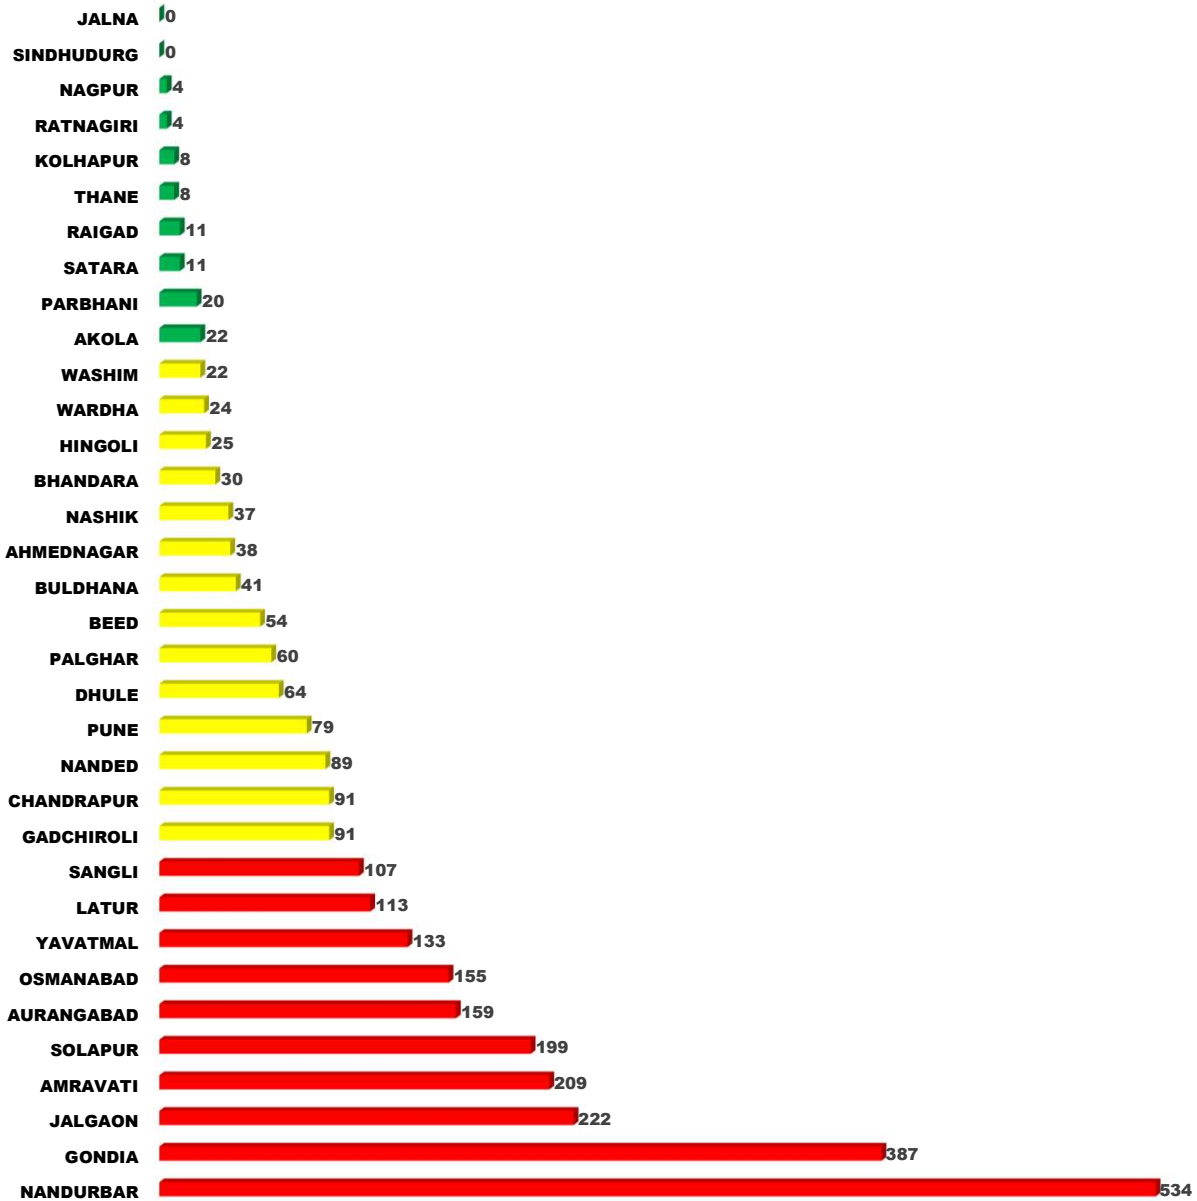


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	24.03.2023	25.03.2023	Daily_Achievement	Remaining
1	YAVATMAL	65373	65217	65240	23	133
2	AMRAVATI	95723	95502	95514	12	209
3	NANDED	69548	69450	69459	9	89
4	PALGHAR	35233	35168	35173	5	60
5	GADCHIROLI	31681	31588	31590	2	91
6	NANDURBAR	119440	118904	118906	2	534
7	BEED	35319	35264	35265	1	54
8	PARBHANI	19103	19082	19083	1	20
9	AKOLA	48797	48775	48775	0	22
10	AURANGABAD	36795	36636	36636	0	159
11	BHANDARA	65120	65090	65090	0	30
12	BULDHANA	44765	44724	44724	0	41
13	DHULE	64954	64890	64890	0	64
14	GONDIA	96489	96102	96102	0	387
15	HINGOLI	18108	18083	18083	0	25
16	JALGAON	79766	79544	79544	0	222
17	JALNA	24044	24044	24044	0	0
18	KOLHAPUR	17773	17765	17765	0	8
19	LATUR	20729	20616	20616	0	113
20	NAGPUR	37191	37187	37187	0	4
21	RAIGAD	9843	9832	9832	0	11
22	RATNAGIRI	9917	9913	9913	0	4
23	SINDHUDURG	5148	5148	5148	0	0
24	THANE	9606	9598	9598	0	8
25	WARDHA	18645	18621	18621	0	24
26	WASHIM	20412	20390	20390	0	22
27	SANGLI	22176	22071	22069	-2	107
28	AHMEDNAGAR	60799	60764	60761	-3	38
29	OSMANABAD	14516	14364	14361	-3	155
30	CHANDRAPUR	43176	43089	43085	-4	91
31	SATARA	15428	15426	15417	-9	11
32	NASHIK	89712	89689	89675	-14	37
33	SOLAPUR	49760	49584	49561	-23	199
34	PUNE	20602	20862	20523	-339	79
Total		1415691	1412982	1412640	55	3051

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	24.03.2023	25.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	413776	320786	321238	452	92538	302	15423
2	NAGPUR DIV.	291675	230932	231204	272	60471	185	10079
3	AMRAVATI DIV.	274643	181138	181302	164	93341	193	15557
4	AURANGABAD DIV.	237547	132578	132732	154	104815	201	17469
5	KONKAN DIV.	69664	55261	55360	99	14304	48	2384
6	PUNE DIV.	125335	85425	85507	82	39828	65	6638
Total		1412640	1006120	1007343	1223	405297	993	67550

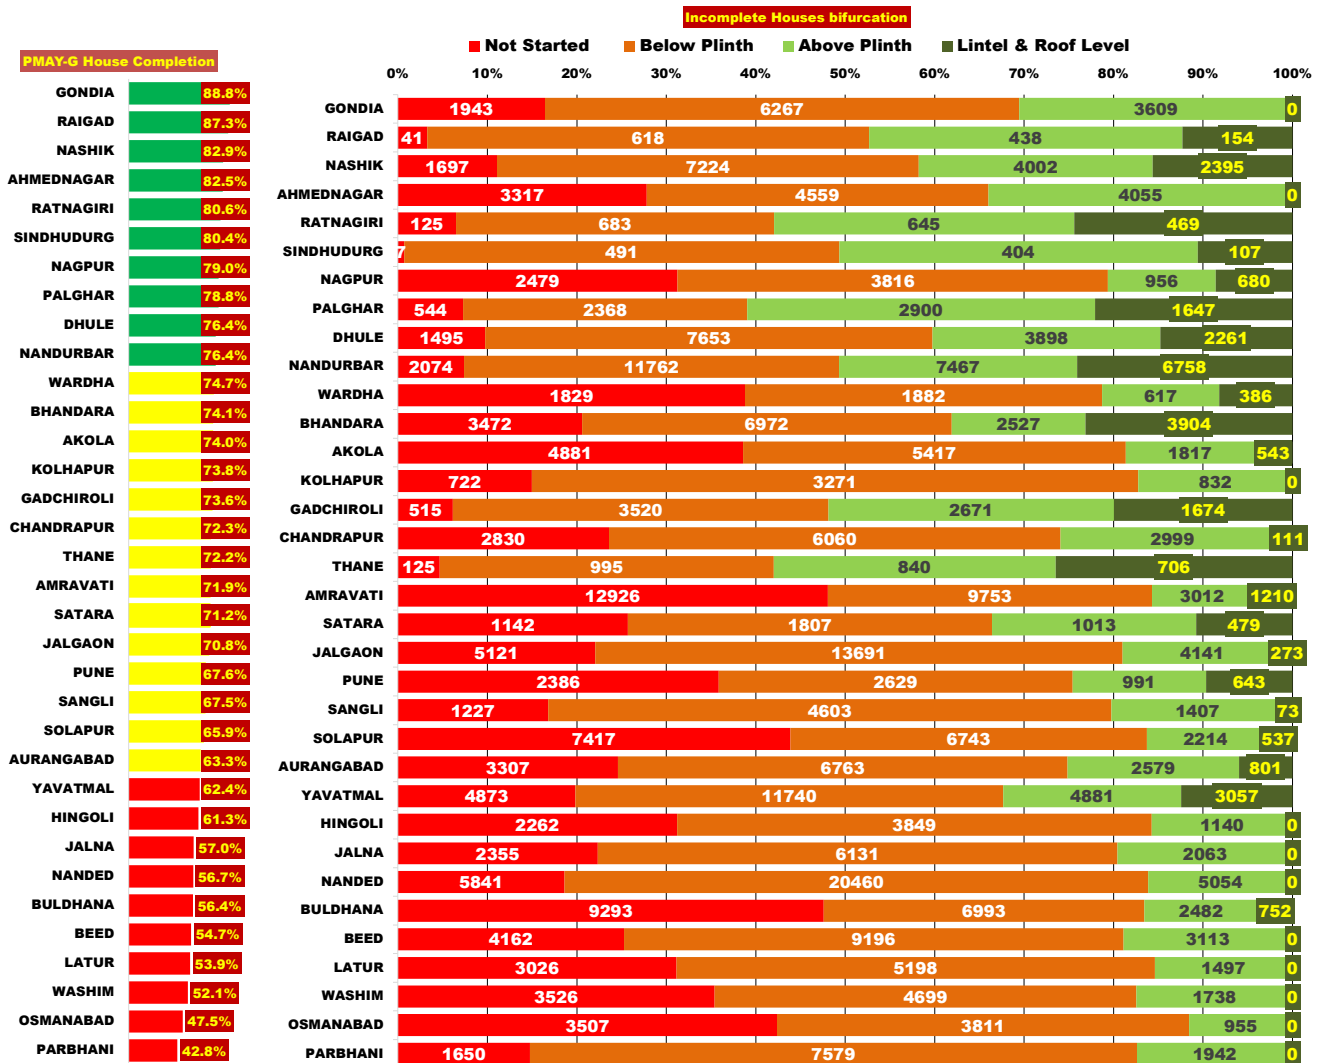


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	24.03.2023	25.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	JALGAON	79544	56177	56318	141	23226	51	3871
2	BHANDARA	65090	48089	48215	126	16875	34	2813
3	NASHIK	89675	74237	74357	120	15318	61	2553
4	AHMEDNAGAR	60761	50026	50135	109	10626	96	1771
5	NANDURBAR	118906	90783	90845	62	28061	41	4677
6	PARBHANI	19083	8097	8159	62	10924	16	1821
7	GADCHIROLI	31590	23180	23235	55	8355	28	1393
8	GONDIA	96102	85268	85318	50	10784	62	1797
9	YAVATMAL	65240	40649	40693	44	24547	58	4091
10	WASHIM	20390	10579	10618	39	9772	21	1629
11	BULDHANA	44724	25180	25215	35	19509	34	3252
12	RATNAGIRI	9913	7956	7991	35	1922	14	320
13	PALGHAR	35173	27680	27714	34	7459	22	1243
14	SATARA	15417	10944	10976	32	4441	13	740
15	AURANGABAD	36636	23159	23186	27	13450	32	2242
16	AMRAVATI	95514	68635	68659	24	26855	56	4476
17	AKOLA	48775	36095	36117	22	12658	24	2110
18	DHULE	64890	49563	49583	20	15307	53	2551
19	THANE	9598	6912	6932	20	2666	4	444
20	NAGPUR	37187	29373	29391	18	7796	12	1299
21	LATUR	20616	11104	11121	17	9495	21	1583
22	PUNE	20523	13858	13874	16	6649	10	1108
23	CHANDRAPUR	43085	31123	31138	15	11947	38	1991
24	SANGLI	22069	14878	14892	14	7177	11	1196
25	HINGOLI	18083	11067	11080	13	7003	17	1167
26	JALNA	24044	13703	13716	13	10328	26	1721
27	SOLAPUR	49561	32637	32650	13	16911	22	2819
28	BEED	35265	19284	19294	10	15971	25	2662
29	OSMANABAD	14361	6816	6824	8	7537	16	1256
30	WARDHA	18621	13899	13907	8	4714	11	786
31	KOLHAPUR	17765	13108	13115	7	4650	8	775
32	SINDHUDURG	5148	4133	4139	6	1009	4	168
33	NANDED	69459	39348	39352	4	30107	48	5018
34	RAIGAD	9832	8580	8584	4	1248	4	208
Total		1412640	1006120	1007343	1223	405297	993	67550

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	24.03.2023	25.03.2023	Daily Achievement	Remaining
1	AMRAVATI DIV.	109702	92692	92998	306	16704
2	AURANGABAD DIV.	199331	161547	161726	179	37605
3	NAGPUR DIV.	118393	87843	87995	152	30398
4	KONKAN DIV.	34729	29809	29954	145	4775
5	NASHIK DIV.	141360	108491	108494	3	32866
6	PUNE DIV.	65334	62933	62927	0	2407
Total		668849	543315	544094	785	124755

State Scheme Remaining Sanction

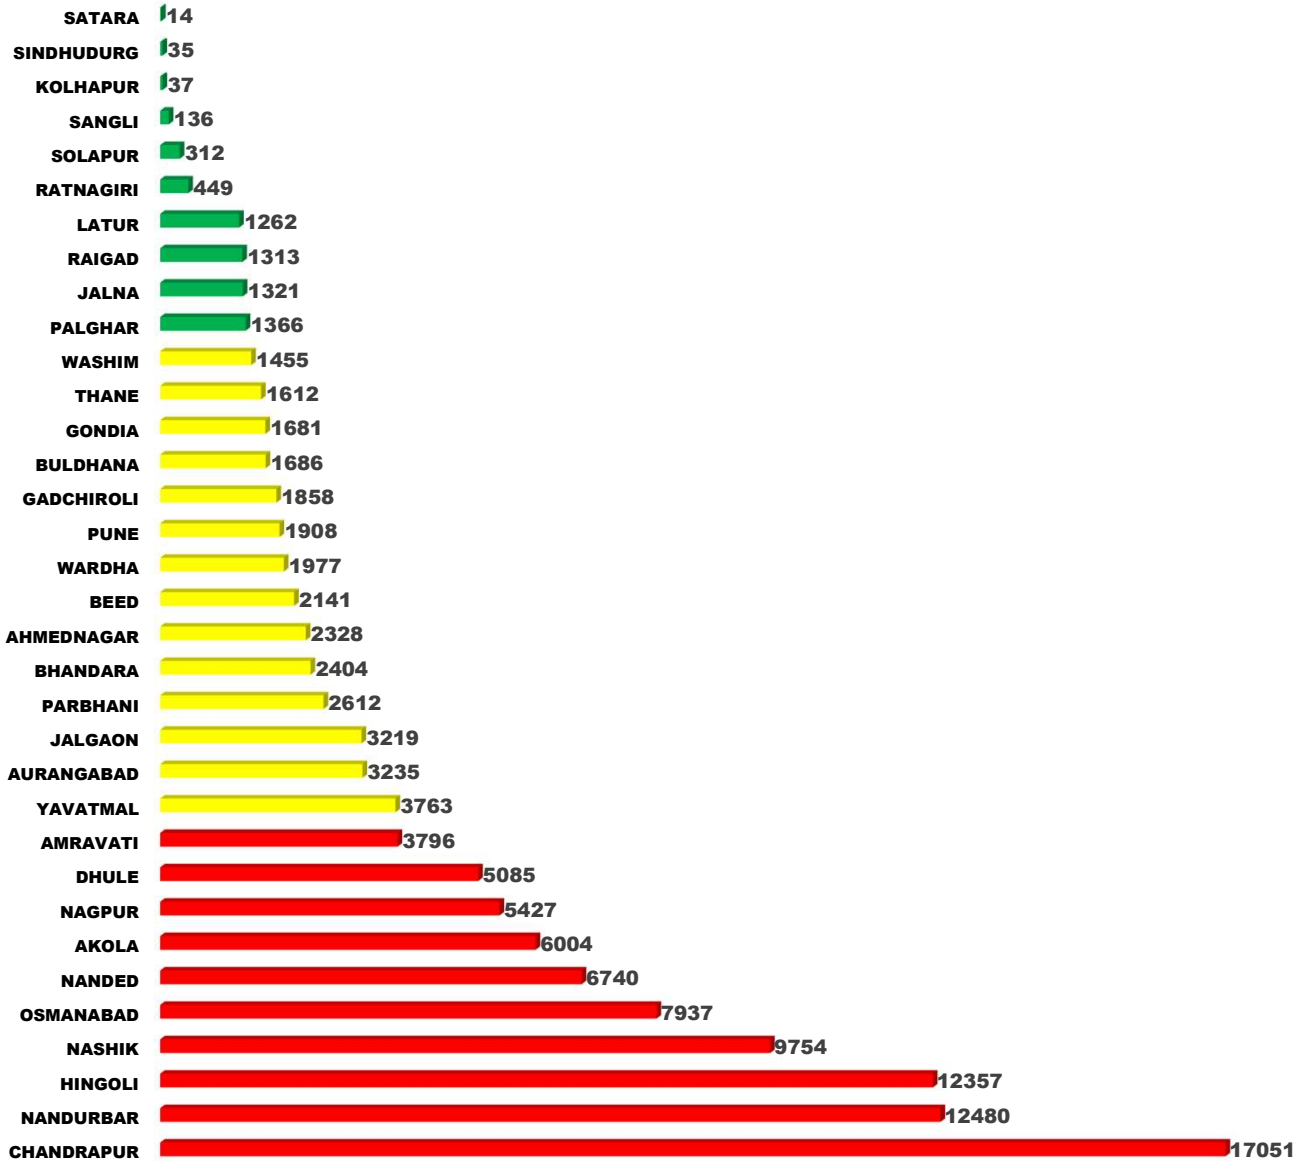


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	24.03.2023	25.03.2023	Daily_Achievement	Remaining
1	AMRAVATI	23224	19174	19428	254	3796
2	RAIGAD	7406	5948	6093	145	1313
3	GONDIA	14246	12423	12565	142	1681
4	AURANGABAD	26141	22800	22906	106	3235
5	AKOLA	23681	17625	17677	52	6004
6	OSMANABAD	24853	16875	16916	41	7937
7	PARBHANI	19784	17141	17172	31	2612
8	WARDHA	13147	11162	11170	8	1977
9	JALGAON	25659	22437	22440	3	3219
10	GADCHIROLI	16834	14974	14976	2	1858
11	BEED	26878	24736	24737	1	2141
12	AHMEDNAGAR	35298	32970	32970	0	2328
13	BHANDARA	17590	15186	15186	0	2404
14	BULDHANA	21616	19930	19930	0	1686
15	CHANDRAPUR	40285	23234	23234	0	17051
16	DHULE	21790	16705	16705	0	5085
17	HINGOLI	27298	14941	14941	0	12357
18	JALNA	20446	19125	19125	0	1321
19	KOLHAPUR	12565	12528	12528	0	37
20	LATUR	27171	25909	25909	0	1262
21	NAGPUR	16291	10864	10864	0	5427
22	NANDED	26760	20020	20020	0	6740
23	NANDURBAR	26578	14098	14098	0	12480
24	NASHIK	32035	22281	22281	0	9754
25	PALGHAR	11792	10426	10426	0	1366
26	PUNE	14672	12764	12764	0	1908
27	RATNAGIRI	7126	6677	6677	0	449
28	SANGLI	8732	8596	8596	0	136
29	SATARA	10647	10633	10633	0	14
30	SINDHUDURG	2141	2106	2106	0	35
31	THANE	6264	4652	4652	0	1612
32	WASHIM	11500	10045	10045	0	1455
33	YAVATMAL	29681	25918	25918	0	3763
34	SOLAPUR	18718	18412	18406	-6	312
Total		668849	543315	544094	785	124755

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	24.03.2023	25.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108494	87182	87305	123	21189	74	3532
2	AMRAVATI DIV.	92998	62928	63001	73	29997	54	5000
3	NAGPUR DIV.	87995	67972	68044	72	19951	44	3325
4	AURANGABAD DIV.	161726	101721	101791	70	59935	93	9989
5	PUNE DIV.	62927	51255	51294	39	11633	26	1939
6	KONKAN DIV.	29954	22987	23017	30	6937	13	1156
Total		544094	394045	394452	407	149642	305	24940

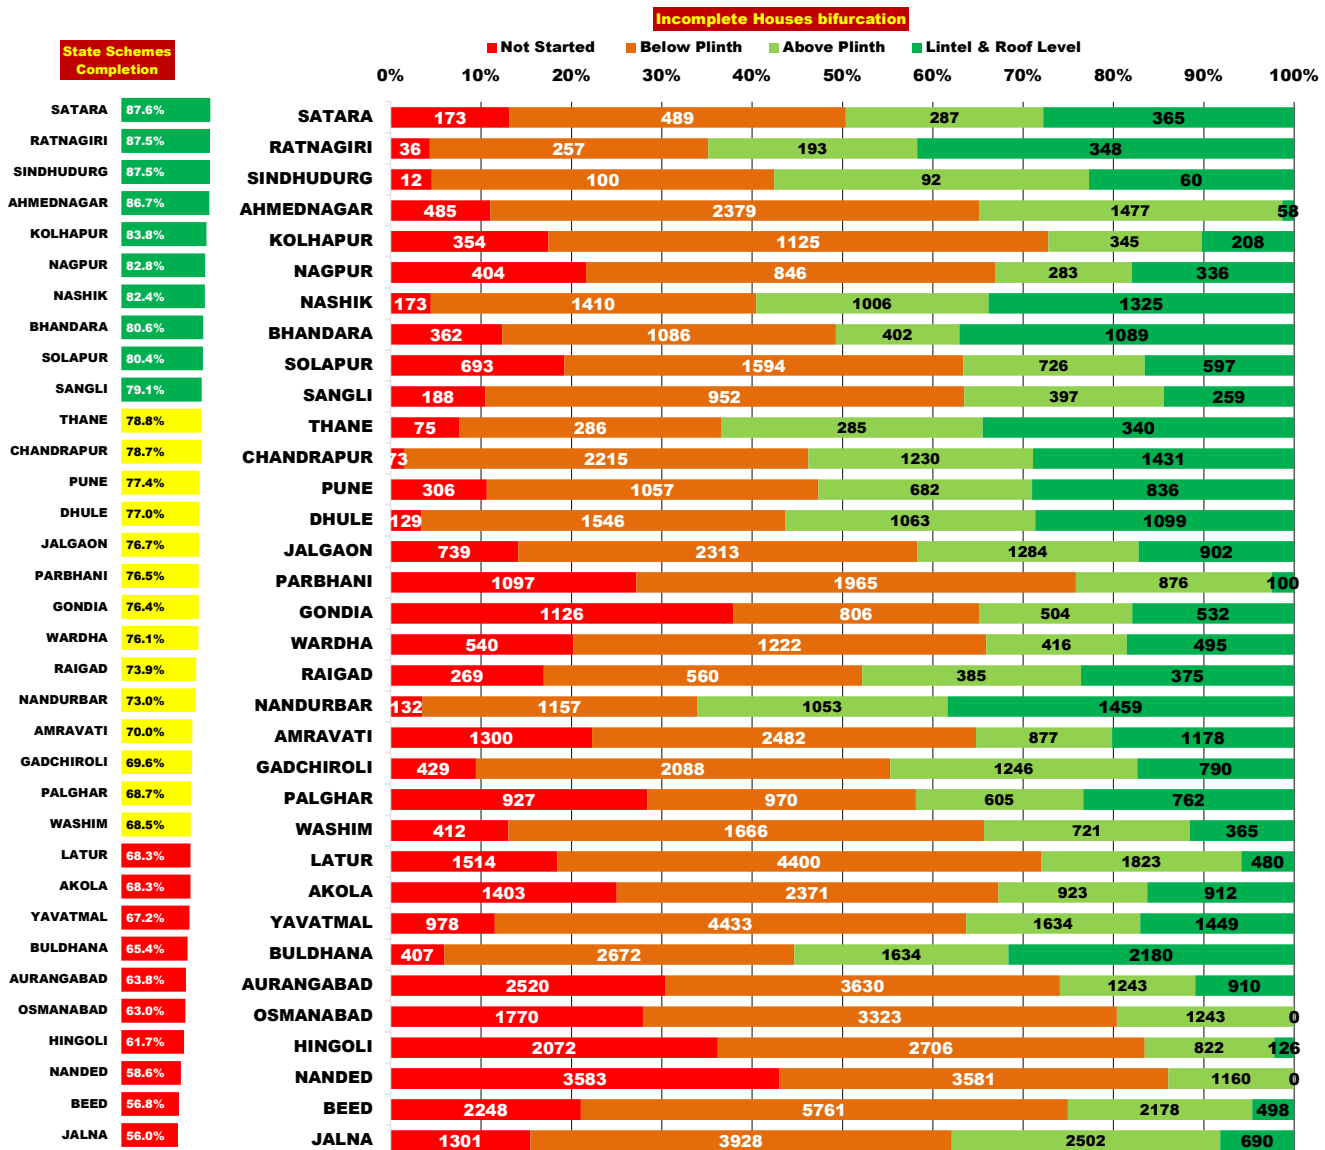

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	24.03.2023	25.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	AHMEDNAGAR	32970	28529	28571	42	4399	32	733
2	JALGAON	22440	17176	17202	26	5238	11	873
3	LATUR	25909	17666	17692	26	8217	12	1370
4	GADCHIROLI	14976	10398	10423	25	4553	9	759
5	YAVATMAL	25918	17399	17424	25	8494	13	1416
6	BULDHANA	19930	13013	13037	24	6893	16	1149
7	NASHIK	22281	18343	18367	24	3914	13	652
8	NANDURBAR	14098	10275	10297	22	3801	7	634
9	SATARA	10633	9301	9319	18	1314	5	219
10	PUNE	12764	9866	9883	17	2881	6	480
11	AKOLA	17677	12055	12068	13	5609	9	935
12	BHANDARA	15186	12234	12247	13	2939	4	490
13	GONDIA	12565	9586	9597	11	2968	8	495
14	WARDHA	11170	8487	8497	10	2673	7	446
15	AMRAVATI	19428	13582	13591	9	5837	9	973
16	DHULE	16705	12859	12868	9	3837	11	640
17	OSMANABAD	16916	10655	10664	9	6252	12	1042
18	PARBHANI	17172	13125	13134	9	4038	4	673
19	JALNA	19125	10696	10704	8	8421	28	1404
20	NAGPUR	10864	8987	8995	8	1869	4	312
21	PALGHAR	10426	7154	7162	8	3264	6	544
22	RAIGAD	6093	4497	4504	7	1589	3	265
23	RATNAGIRI	6677	5836	5843	7	834	2	139
24	AURANGABAD	22906	14597	14603	6	8303	8	1384
25	BEED	24737	14046	14052	6	10685	14	1781
26	CHANDRAPUR	23234	18280	18285	5	4949	13	825
27	HINGOLI	14941	9210	9215	5	5726	6	954
28	SINDHUDURG	2106	1838	1842	4	264	1	44
29	THANE	4652	3662	3666	4	986	2	164
30	SOLAPUR	18406	14794	14796	2	3610	8	602
31	WASHIM	10045	6879	6881	2	3164	7	527
32	KOLHAPUR	12528	10495	10496	1	2032	3	339
33	NANDED	20020	11726	11727	1	8293	9	1382
34	SANGLI	8596	6799	6800	1	1796	4	299
	Total	544094	394045	394452	407	149642	305	24940

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	13704	0	44889	0	23563
2	AMRAVATI DIV.	0	35435	0	38602	0	13930
3	AURANGABAD DIV.	0	26080	0	62987	0	18343
4	NAGPUR DIV.	0	12855	0	28517	0	13379
5	KONKAN DIV.	0	839	0	5155	0	5227
6	PUNE DIV.	0	12761	0	19053	0	6457
	Total	0	101674	0	199203	0	80899

PMAY-G 1st Ins Pending

SINDHUDURG	7
RAIGAD	38
RATNAGIRI	125
THANE	125
GADCHIROLI	490
PALGHAR	544
KOLHAPUR	722
SANGLI	1094
SATARA	1142
DHULE	1495
PARBHANI	1650
NASHIK	1697
WARDHA	1829
GONDIA	1943
NANDURBAR	2074
HINGOLI	2262
JALNA	2325
NAGPUR	2344
PUNE	2386
CHANDRAPUR	2777
LATUR	3026
AURANGABAD	3307
AHMEDNAGAR	3317
BHANDARA	3472
OSMANABAD	3507
WASHIM	3523
BEED	4162
YAVATMAL	4869
AKOLA	4881
JALGAON	5121
NANDED	5841
SOLAPUR	7417
BULDHANA	9282
AMRAVATI	12880

PMAY-G 2nd Ins Pending

SINDHUDURG	491
RAIGAD	618
RATNAGIRI	683
THANE	995
SATARA	1807
WARDHA	1882
PALGHAR	2368
PUNE	2629
KOLHAPUR	3271
GADCHIROLI	3520
OSMANABAD	3811
NAGPUR	3816
HINGOLI	3849
AHMEDNAGAR	4559
SANGLI	4603
WASHIM	4699
LATUR	5198
AKOLA	5417
CHANDRAPUR	6060
JALNA	6131
GONDIA	6267
SOLAPUR	6743
AURANGABAD	6763
BHANDARA	6972
BULDHANA	6993
NASHIK	7224
PARBHANI	7579
DHULE	7653
BEED	9196
AMRAVATI	9753
YAVATMAL	11740
NANDURBAR	11762
JALGAON	13691
NANDED	20460

PMAY-G 3rd Ins Pending

SINDHUDURG	404
RAIGAD	438
WARDHA	617
RATNAGIRI	645
KOLHAPUR	832
THANE	840
OSMANABAD	955
NAGPUR	956
PUNE	991
SATARA	1013
HINGOLI	1140
SANGLI	1407
LATUR	1497
WASHIM	1738
AKOLA	1817
PARBHANI	1942
JALNA	2063
SOLAPUR	2214
BULDHANA	2482
BHANDARA	2527
AURANGABAD	2579
GADCHIROLI	2671
PALGHAR	2900
CHANDRAPUR	2999
AMRAVATI	3012
BEED	3113
GONDIA	3609
DHULE	3898
NASHIK	4002
AHMEDNAGAR	4055
JALGAON	4141
YAVATMAL	4881
NANDED	5054
NANDURBAR	7467

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3317	0	4559	0	4055
2	AKOLA	0	4881	0	5417	0	1817
3	AMRAVATI	0	12880	0	9753	0	3012
4	AURANGABAD	0	3307	0	6763	0	2579
5	BEED	0	4162	0	9196	0	3113
6	BHANDARA	0	3472	0	6972	0	2527
7	BULDHANA	0	9282	0	6993	0	2482
8	CHANDRAPUR	0	2777	0	6060	0	2999
9	DHULE	0	1495	0	7653	0	3898
10	GADCHIROLI	0	490	0	3520	0	2671
11	GONDIA	0	1943	0	6267	0	3609
12	HINGOLI	0	2262	0	3849	0	1140
13	JALGAON	0	5121	0	13691	0	4141
14	JALNA	0	2325	0	6131	0	2063
15	KOLHAPUR	0	722	0	3271	0	832
16	LATUR	0	3026	0	5198	0	1497
17	NAGPUR	0	2344	0	3816	0	956
18	NANDED	0	5841	0	20460	0	5054
19	NANDURBAR	0	2074	0	11762	0	7467
20	NASHIK	0	1697	0	7224	0	4002
21	OSMANABAD	0	3507	0	3811	0	955
22	PALGHAR	0	544	0	2368	0	2900
23	PARBHANI	0	1650	0	7579	0	1942
24	PUNE	0	2386	0	2629	0	991
25	RATNAGIRI	0	125	0	683	0	645
26	SANGLI	0	1094	0	4603	0	1407
27	SINDHUDURG	0	7	0	491	0	404
28	SOLAPUR	0	7417	0	6743	0	2214
29	THANE	0	125	0	995	0	840
30	WARDHA	0	1829	0	1882	0	617
31	WASHIM	0	3523	0	4699	0	1738
32	YAVATMAL	0	4869	0	11740	0	4881
33	RAIGAD	-3	38	0	618	0	438
34	SATARA	-27	1142	0	1807	0	1013
	Total	0	101674	0	199203	0	80899

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AURANGABAD DIV.	217	16105	174	29294	141	11847
2	AMRAVATI DIV.	84	4500	110	13624	123	5789
3	NAGPUR DIV.	62	2934	106	8263	96	4081
4	NASHIK DIV.	15	1658	76	8805	137	5883
5	KONKAN DIV.	13	1319	51	2173	62	1560
6	PUNE DIV.	13	1714	48	5217	57	2437
	Total	404	28230	565	67376	616	31597

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	36
CHANDRAPUR	73
THANE	75
DHULE	129
NANDURBAR	132
SATARA	173
NASHIK	173
SANGLI	188
RAIGAD	269
PUNE	306
KOLHAPUR	354
BHANDARA	362
NAGPUR	404
BULDHANA	407
WASHIM	412
GADCHIROLI	429
AHMEDNAGAR	485
WARDHA	540
SOLAPUR	693
JALGAON	739
PALGHAR	927
YAVATMAL	978
PARBHANI	1097
GONDIA	1126
AMRAVATI	1300
JALNA	1301
AKOLA	1403
LATUR	1514
OSMANABAD	1770
HINGOLI	2072
BEED	2248
AURANGABAD	2520
NANDED	3583

State Schemes 2nd Ins Pending

SINDHUDURG	100
RATNAGIRI	257
THANE	286
SATARA	489
RAIGAD	560
GONDIA	806
NAGPUR	846
SANGLI	952
PALGHAR	970
PUNE	1057
BHANDARA	1086
KOLHAPUR	1125
NANDURBAR	1157
WARDHA	1222
NASHIK	1410
DHULE	1546
SOLAPUR	1594
WASHIM	1666
PARBHANI	1965
GADCHIROLI	2088
CHANDRAPUR	2215
JALGAON	2313
AKOLA	2371
AHMEDNAGAR	2379
AMRAVATI	2482
BULDHANA	2672
HINGOLI	2706
OSMANABAD	3323
NANDED	3581
AURANGABAD	3630
JALNA	3928
LATUR	4400
YAVATMAL	4433
BEED	5761

State Schemes 3rd Ins Pending

SINDHUDURG	92
RATNAGIRI	193
NAGPUR	283
THANE	285
SATARA	287
KOLHAPUR	345
RAIGAD	385
SANGLI	397
BHANDARA	402
WARDHA	416
GONDIA	504
PALGHAR	605
PUNE	682
WASHIM	721
SOLAPUR	726
HINGOLI	822
PARBHANI	876
AMRAVATI	877
AKOLA	923
NASHIK	1006
NANDURBAR	1053
DHULE	1063
NANDED	1160
CHANDRAPUR	1230
OSMANABAD	1243
AURANGABAD	1243
GADCHIROLI	1246
JALGAON	1284
AHMEDNAGAR	1477
BULDHANA	1634
YAVATMAL	1634
LATUR	1823
BEED	2178
JALNA	2502

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	GADCHIROLI	29	429	70	2088	41	1246
2	PARBHANI	108	1097	12	1965	8	876
3	YAVATMAL	9	978	61	4433	48	1634
4	NANDED	53	3583	32	3581	16	1160
5	LATUR	23	1514	21	4400	43	1823
6	AHMEDNAGAR	7	485	32	2379	34	1477
7	PALGHAR	13	927	28	970	32	605
8	AMRAVATI	15	1300	25	2482	25	877
9	NANDURBAR	0	132	13	1157	50	1053
10	OSMANABAD	22	1770	20	3323	20	1243
11	BULDHANA	14	407	24	2672	22	1634
12	NASHIK	3	173	20	1410	36	1006
13	HINGOLI	6	2072	24	2706	23	822
14	AKOLA	45	1403	0	2371	3	923
15	CHANDRAPUR	3	73	14	2215	27	1230
16	JALNA	2	1301	29	3928	10	2502
17	GONDIA	26	1126	6	806	8	504
18	KOLHAPUR	4	354	21	1125	15	345
19	BEED	3	2248	17	5761	19	2178
20	SANGLI	1	188	21	952	14	397
21	PUNE	2	306	8	1057	24	682
22	DHULE	0	129	10	1546	16	1063
23	WASHIM	1	412	0	1666	25	721
24	AURANGABAD	0	2520	19	3630	2	1243
25	RATNAGIRI	0	36	9	257	11	193
26	WARDHA	4	540	9	1222	7	416
27	BHANDARA	0	362	6	1086	9	402
28	THANE	0	75	4	286	9	285
29	SINDHUDURG	0	12	5	100	6	92
30	RAIGAD	0	269	5	560	4	385
31	SATARA	4	173	1	489	3	287
32	JALGAON	5	739	1	2313	1	1284
33	NAGPUR	0	404	1	846	4	283
34	SOLAPUR	2	693	-3	1594	1	726
	Total	404	28230	568	67376	616	31597
