



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २८.०३.२०२३


प्रधानमंत्री आवास योजना ग्रामीण — मंजूरी, पूर्ण घरकुले, हप्ते वितरण
राज्य पुरस्कृत ग्रामीण आवास योजना — मंजूरी, पूर्ण घरकुले, हप्ते वितरण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१२५४१	२०	१०११२४९	१७९२	०	०	०
राज्य योजना	५४५३५२	८९६	३९५६१७	५५०	०	०	०
एकूण	१९५७८९३	९१६	१४०६८६६	२३४२	०	०	०

PMAY-G Completion Progress Bar

71.6%




PMAY-G Incomplete Houses bifurcation

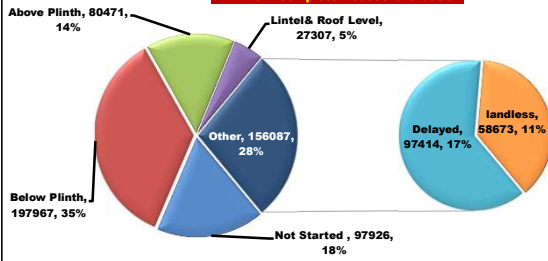


State Schemes Progress Bar

72.5%


State Schemes: Incomplete Houses bifurcation

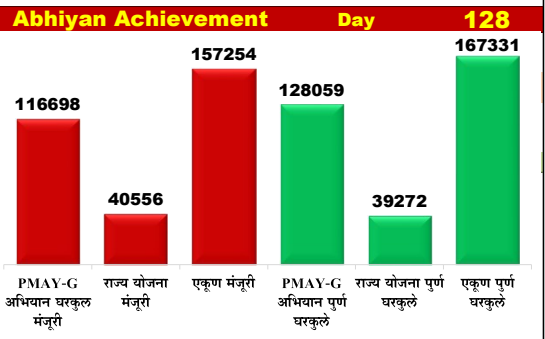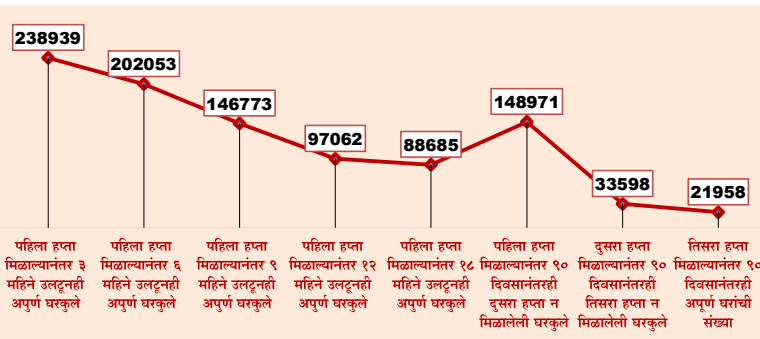

PMAY-G : House completion (Abhiyan Achievement)

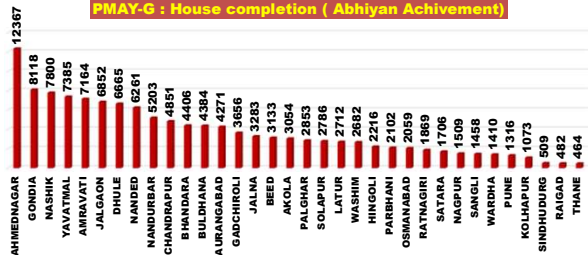

State Schemes : House completion (Abhiyan Achievement)

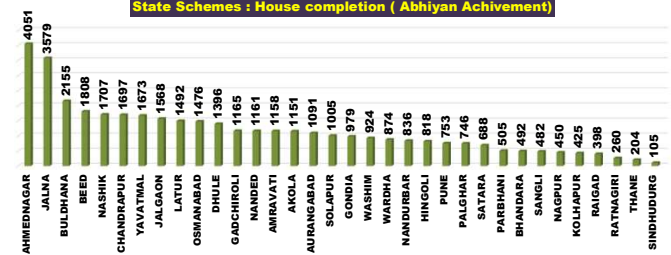


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day




State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	27.03.2023	28.03.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	275070	274642	274654	12	428
2	NASHIK DIV.	414671	413793	413794	3	879
3	NAGPUR DIV.	292302	291677	291671	2	633
4	PUNE DIV.	125736	125375	125234	2	491
5	KONKAN DIV.	69741	69660	69652	1	90
6	AURANGABAD DIV.	238162	237538	237536	0	625
	Total	1415682	1412685	1412541	20	3146

PMAY-G Remaining Sanction

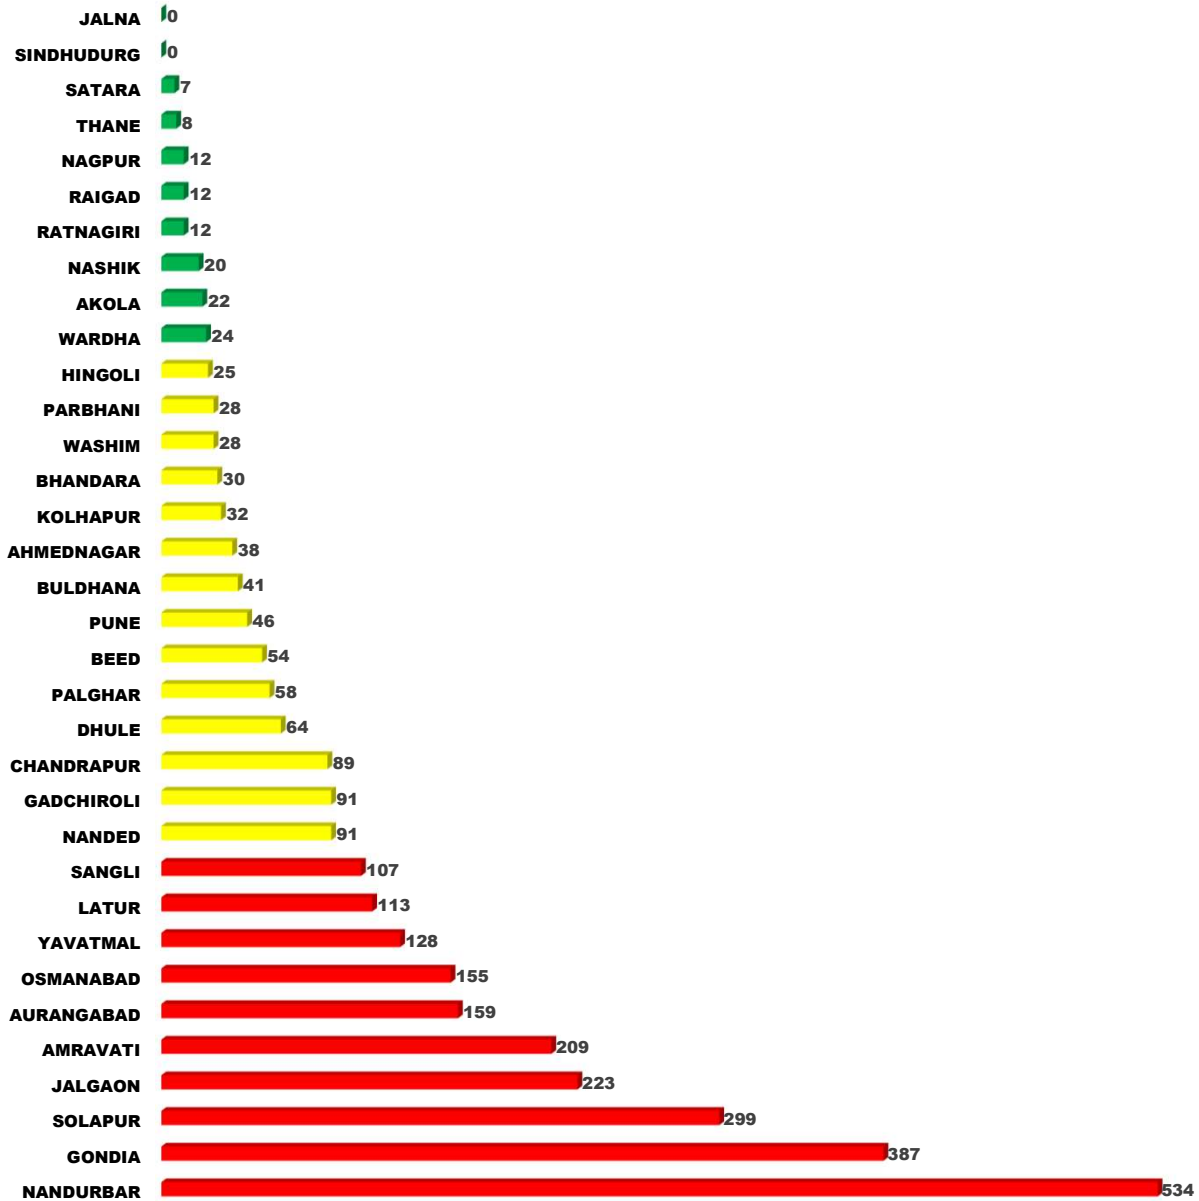


प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	District	Target (PWL+Awaas Plus)	27.03.2023	28.03.2023	Daily_Achievement	Remaining
1	AMRAVATI	95723	95514	95526	12	209
2	AHMEDNAGAR	60799	60761	60763	2	38
3	SATARA	15425	15419	15421	2	7
4	BHANDARA	65120	65090	65091	1	30
5	GADCHIROLI	31681	31590	31591	1	91
6	NASHIK	89712	89693	89694	1	20
7	PALGHAR	35233	35175	35176	1	58
8	AKOLA	48797	48775	48775	0	22
9	AURANGABAD	36795	36636	36636	0	159
10	BEED	35319	35265	35265	0	54
11	BULDHANA	44765	44724	44724	0	41
12	CHANDRAPUR	43176	43087	43087	0	89
13	DHULE	64954	64890	64890	0	64
14	GONDIA	96489	96102	96102	0	387
15	HINGOLI	18108	18083	18083	0	25
16	JALNA	24044	24044	24044	0	0
17	LATUR	20729	20616	20616	0	113
18	NANDED	69548	69457	69457	0	91
19	NANDURBAR	119440	118906	118906	0	534
20	OSMANABAD	14516	14361	14361	0	155
21	SANGLI	22176	22069	22069	0	107
22	SINDHUDURG	5142	5142	5142	0	0
23	THANE	9606	9598	9598	0	8
24	WARDHA	18645	18621	18621	0	24
25	WASHIM	20412	20384	20384	0	28
26	YAVATMAL	65373	65245	65245	0	128
27	RAIGAD	9843	9832	9831	-1	12
28	JALGAON	79766	79543	79541	-2	223
29	PARBHANI	19103	19076	19074	-2	28
30	PUNE	20602	20556	20551	-5	46
31	NAGPUR	37191	37187	37179	-8	12
32	RATNAGIRI	9917	9913	9905	-8	12
33	KOLHAPUR	17773	17765	17741	-24	32
34	SOLAPUR	49760	49566	49452	-114	299
Total		1415682	1412685	1412541	20	3146

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	27.03.2023	28.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NAGPUR DIV.	291671	231510	232078	568	59593	187	19864
2	NASHIK DIV.	413794	321894	322401	507	91393	304	30464
3	AURANGABAD DIV.	237536	133286	133598	312	103938	203	34646
4	AMRAVATI DIV.	274654	181652	181826	174	92828	193	30939
5	KONKAN DIV.	69652	55447	55585	138	14067	48	4689
6	PUNE DIV.	125234	85668	85761	93	39473	65	13161
Total		1412541	1009457	1011249	1792	401292	1000	133762

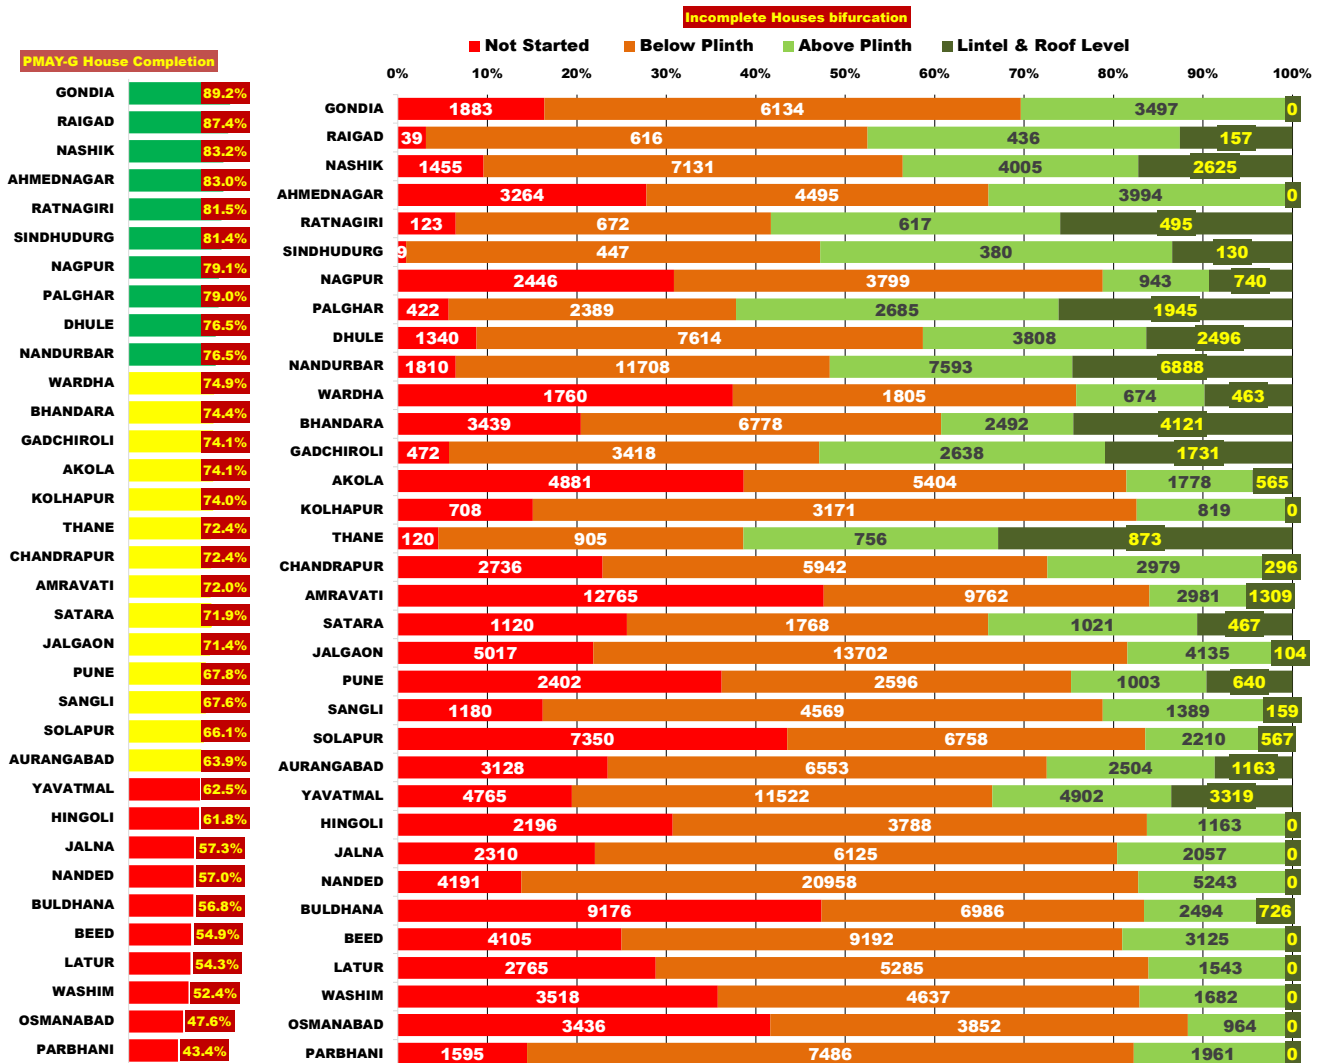


प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	27.03.2023	28.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	GONDIA	96102	85394	85696	302	10406	63	3469
2	JALGAON	79541	56585	56770	185	22771	54	7591
3	BHANDARA	65091	48260	48418	158	16673	34	5557
4	AHMEDNAGAR	60763	50293	50447	154	10316	97	3438
5	AURANGABAD	36636	23288	23403	115	13233	33	4411
6	NASHIK	89694	74477	74591	114	15103	61	5034
7	GADCHIROLI	31591	23356	23423	67	8168	29	2722
8	RATNAGIRI	9905	8006	8073	67	1832	15	611
9	NANDED	69457	39511	39571	60	29886	49	9962
10	BULDHANA	44724	25353	25405	52	19319	34	6440
11	YAVATMAL	65245	40741	40793	52	24452	58	8151
12	PALGHAR	35176	27734	27784	50	7392	22	2464
13	PARBHANI	19074	8228	8275	47	10799	16	3600
14	AMRAVATI	95526	68743	68789	46	26737	56	8908
15	SATARA	15421	11043	11081	38	4340	13	1446
16	HINGOLI	18083	11137	11174	37	6909	17	2303
17	WARDHA	18621	13919	13949	30	4672	11	1557
18	DHULE	64890	49632	49660	28	15230	52	5077
19	NANDURBAR	118906	90907	90933	26	27973	41	9324
20	LATUR	20616	11162	11186	24	9430	21	3143
21	SANGLI	22069	14905	14925	20	7144	11	2381
22	WASHIM	20384	10668	10688	20	9696	21	3232
23	JALNA	24044	13773	13789	16	10255	26	3418
24	SOLAPUR	49452	32681	32694	13	16758	22	5589
25	BEED	35265	19349	19361	12	15904	24	5301
26	KOLHAPUR	17741	13124	13135	11	4606	8	1535
27	PUNE	20551	13915	13926	11	6625	10	2210
28	SINDHUDURG	5142	4176	4186	10	956	4	319
29	NAGPUR	37179	29394	29402	8	7777	12	2592
30	THANE	9598	6944	6950	6	2648	4	883
31	RAIGAD	9831	8587	8592	5	1239	4	413
32	AKOLA	48775	36147	36151	4	12624	24	4208
33	CHANDRAPUR	43087	31187	31190	3	11897	38	3966
34	OSMANABAD	14361	6838	6839	1	7522	16	2507
Total		1412541	1009457	1011249	1792	401292	1000	133762

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	27.03.2023	28.03.2023	Daily Achievement	Remaining
1	AURANGABAD DIV.	199331	161983	162440	457	36891
2	NASHIK DIV.	141360	108528	108850	322	32510
3	AMRAVATI DIV.	109702	93061	93120	59	16582
4	KONKAN DIV.	34729	29961	30012	51	4717
5	NAGPUR DIV.	118393	87998	88004	7	30389
6	PUNE DIV.	65334	62927	62926	0	2408
	Total	668849	544458	545352	896	123497

State Scheme Remaining Sanction

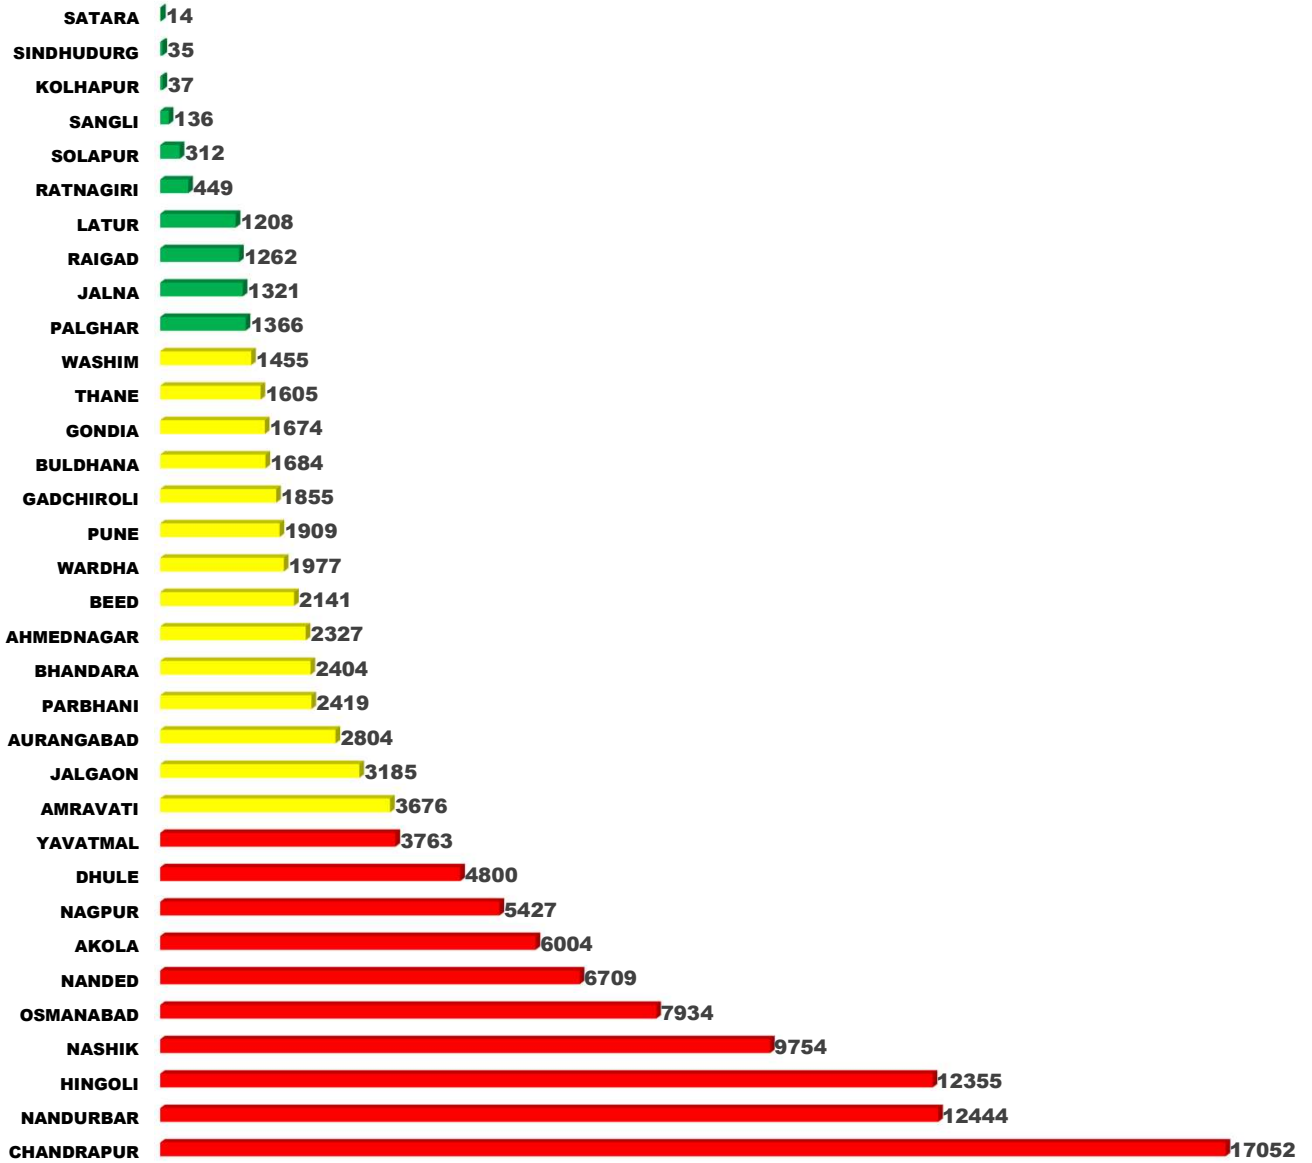


राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	District	Target	27.03.2023	28.03.2023	Daily_Achievement	Remaining
1	DHULE	21790	16705	16990	285	4800
2	AURANGABAD	26141	23130	23337	207	2804
3	PARBHANI	19784	17172	17365	193	2419
4	AMRAVATI	23224	19491	19548	57	3676
5	RAIGAD	7406	6093	6144	51	1262
6	NANDURBAR	26578	14098	14134	36	12444
7	NANDED	26760	20020	20051	31	6709
8	LATUR	27171	25940	25963	23	1208
9	GONDIA	14246	12565	12572	7	1674
10	OSMANABAD	24853	16916	16919	3	7934
11	BULDHANA	21616	19930	19932	2	1684
12	AHMEDNAGAR	35298	32970	32971	1	2327
13	AKOLA	23681	17677	17677	0	6004
14	BEED	26878	24737	24737	0	2141
15	BHANDARA	17590	15186	15186	0	2404
16	GADCHIROLI	16834	14979	14979	0	1855
17	HINGOLI	27298	14943	14943	0	12355
18	JALGAON	25659	22474	22474	0	3185
19	JALNA	20446	19125	19125	0	1321
20	KOLHAPUR	12565	12528	12528	0	37
21	NAGPUR	16291	10864	10864	0	5427
22	NASHIK	32035	22281	22281	0	9754
23	PALGHAR	11792	10426	10426	0	1366
24	RATNAGIRI	7126	6677	6677	0	449
25	SANGLI	8732	8596	8596	0	136
26	SATARA	10647	10633	10633	0	14
27	SINDHUDURG	2141	2106	2106	0	35
28	SOLAPUR	18718	18406	18406	0	312
29	THANE	6264	4659	4659	0	1605
30	WARDHA	13147	11170	11170	0	1977
31	WASHIM	11500	10045	10045	0	1455
32	YAVATMAL	29681	25918	25918	0	3763
33	CHANDRAPUR	40285	23234	23233	-1	17052
34	PUNE	14672	12764	12763	-1	1909
Total		668849	544458	545352	896	123497

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	27.03.2023	28.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	NASHIK DIV.	108850	87471	87615	144	21235	75	7078
2	AURANGABAD DIV.	162440	101933	102036	103	60404	93	20135
3	AMRAVATI DIV.	93120	63159	63259	100	29861	55	9954
4	NAGPUR DIV.	88004	68113	68202	89	19802	44	6601
5	PUNE DIV.	62926	51354	51418	64	11508	26	3836
6	KONKAN DIV.	30012	23037	23087	50	6925	13	2308
Total		545352	395067	395617	550	149735	307	49912

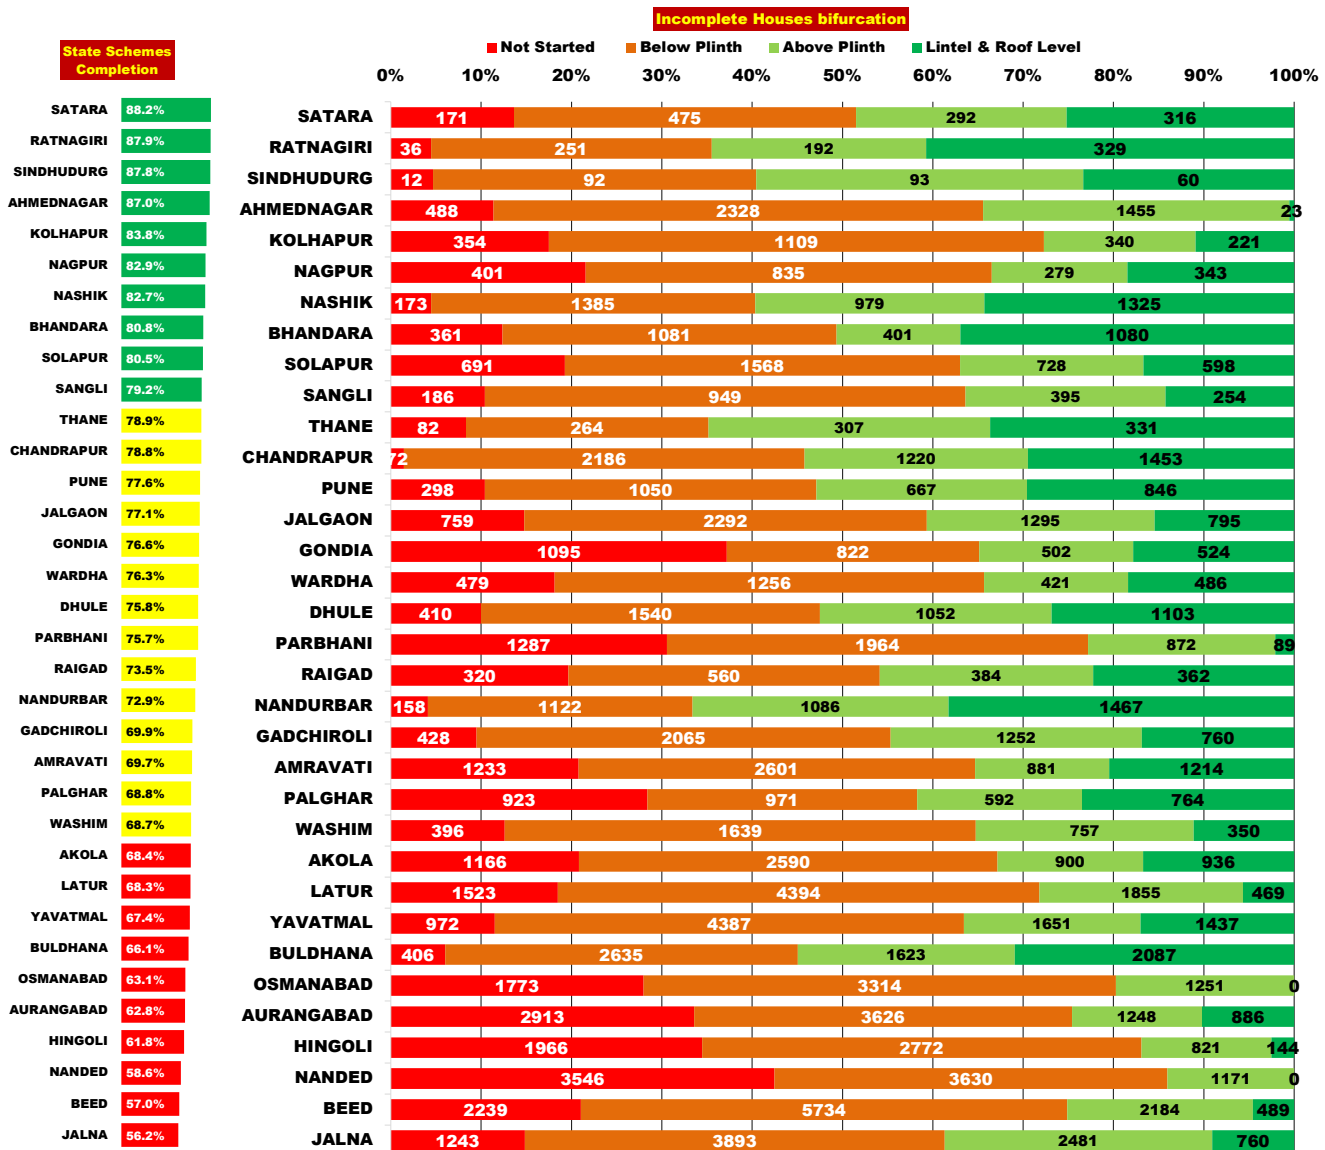

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	27.03.2023	28.03.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 31.03.23
1	JALGAON	22474	17261	17333	72	5141	12	1714
2	AURANGABAD	23337	14618	14664	46	8673	9	2891
3	AHMEDNAGAR	32971	28634	28677	43	4294	32	1431
4	SATARA	10633	9336	9379	43	1254	5	418
5	BULDHANA	19932	13141	13181	40	6751	17	2250
6	YAVATMAL	25918	17433	17471	38	8447	13	2816
7	GONDIA	12572	9598	9629	31	2943	8	981
8	WARDHA	11170	8505	8528	23	2642	7	881
9	RATNAGIRI	6677	5848	5869	21	808	2	269
10	NASHIK	22281	18400	18419	19	3862	13	1287
11	JALNA	19125	10731	10748	17	8377	28	2792
12	GADCHIROLI	14979	10459	10474	15	4505	9	1502
13	RAIGAD	6144	4504	4518	14	1626	3	542
14	BHANDARA	15186	12252	12263	11	2923	4	974
15	AMRAVATI	19548	13609	13619	10	5929	9	1976
16	HINGOLI	14943	9230	9240	10	5703	6	1901
17	PALGHAR	10426	7166	7176	10	3250	6	1083
18	SOLAPUR	18406	14811	14821	10	3585	8	1195
19	WASHIM	10045	6893	6903	10	3142	7	1047
20	BEED	24737	14082	14091	9	10646	14	3549
21	NAGPUR	10864	8997	9006	9	1858	4	619
22	DHULE	16990	12877	12885	8	4105	11	1368
23	NANDED	20051	11742	11750	8	8301	9	2767
24	LATUR	25963	17716	17722	6	8241	12	2747
25	SANGLI	8596	6807	6812	5	1784	4	595
26	THANE	4659	3670	3675	5	984	2	328
27	PARBHANI	17365	13149	13153	4	4212	4	1404
28	KOLHAPUR	12528	10501	10504	3	2024	3	675
29	OSMANABAD	16919	10665	10668	3	6251	12	2084
30	PUNE	12763	9899	9902	3	2861	6	954
31	AKOLA	17677	12083	12085	2	5592	9	1864
32	NANDURBAR	14134	10299	10301	2	3833	7	1278
33	CHANDRAPUR	23233	18302	18302	0	4931	13	1644
34	SINDHUDURG	2106	1849	1849	0	257	1	86
Total		545352	395067	395617	550	149735	307	49912

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	12898	0	44640	0	23535
2	AMRAVATI DIV.	0	35053	0	38311	0	13837
3	AURANGABAD DIV.	0	23694	0	63239	0	18560
4	NAGPUR DIV.	0	12517	0	27876	0	13223
5	KONKAN DIV.	0	702	0	5029	0	4874
6	PUNE DIV.	0	12487	0	18861	0	6442
	Total	0	97351	0	197956	0	80471

PMAY-G 1st Ins Pending

SINDHUDURG	9
RAIGAD	35
RATNAGIRI	115
THANE	120
PALGHAR	423
GADCHIROLI	448
KOLHAPUR	684
SANGLI	1047
SATARA	1123
DHULE	1340
NASHIK	1456
PARBHANI	1593
WARDHA	1760
NANDURBAR	1810
GONDIA	1883
HINGOLI	2196
JALNA	2280
NAGPUR	2303
PUNE	2397
CHANDRAPUR	2683
LATUR	2765
AURANGABAD	3128
AHMEDNAGAR	3277
OSMANABAD	3436
BHANDARA	3440
WASHIM	3515
BEED	4105
NANDED	4191
YAVATMAL	4761
AKOLA	4881
JALGAON	5015
SOLAPUR	7236
BULDHANA	9165
AMRAVATI	12731

PMAY-G 2nd Ins Pending

SINDHUDURG	447
RAIGAD	616
RATNAGIRI	672
THANE	905
SATARA	1767
WARDHA	1805
PALGHAR	2389
PUNE	2596
KOLHAPUR	3171
GADCHIROLI	3418
HINGOLI	3788
NAGPUR	3799
OSMANABAD	3852
AHMEDNAGAR	4485
SANGLI	4569
WASHIM	4637
LATUR	5285
AKOLA	5404
CHANDRAPUR	5942
JALNA	6125
GONDIA	6134
AURANGABAD	6553
SOLAPUR	6758
BHANDARA	6778
BULDHANA	6986
NASHIK	7131
PARBHANI	7486
DHULE	7614
BEED	9192
AMRAVATI	9762
YAVATMAL	11522
NANDURBAR	11708
JALGAON	13702
NANDED	20958

PMAY-G 3rd Ins Pending

SINDHUDURG	380
RAIGAD	436
RATNAGIRI	617
WARDHA	674
THANE	756
KOLHAPUR	819
NAGPUR	943
OSMANABAD	964
PUNE	1003
SATARA	1021
HINGOLI	1163
SANGLI	1389
LATUR	1543
WASHIM	1682
AKOLA	1778
PARBHANI	1961
JALNA	2057
SOLAPUR	2210
BHANDARA	2492
BULDHANA	2494
AURANGABAD	2504
GADCHIROLI	2638
PALGHAR	2685
CHANDRAPUR	2979
AMRAVATI	2981
BEED	3125
GONDIA	3497
DHULE	3808
AHMEDNAGAR	3994
NASHIK	4005
JALGAON	4135
YAVATMAL	4902
NANDED	5243
NANDURBAR	7593

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	4881	0	5404	0	1778
2	AMRAVATI	0	12731	0	9762	0	2981
3	AURANGABAD	0	3128	0	6553	0	2504
4	BEED	0	4105	0	9192	0	3125
5	BHANDARA	0	3440	0	6778	0	2492
6	BULDHANA	0	9165	0	6986	0	2494
7	CHANDRAPUR	0	2683	0	5942	0	2979
8	DHULE	0	1340	0	7614	0	3808
9	GADCHIROLI	0	448	0	3418	0	2638
10	GONDIA	0	1883	0	6134	0	3497
11	HINGOLI	0	2196	0	3788	0	1163
12	JALGAON	0	5015	0	13702	0	4135
13	JALNA	0	2280	0	6125	0	2057
14	KOLHAPUR	0	684	0	3171	0	819
15	LATUR	0	2765	0	5285	0	1543
16	NAGPUR	0	2303	0	3799	0	943
17	NANDED	0	4191	0	20958	0	5243
18	NANDURBAR	0	1810	0	11708	0	7593
19	NASHIK	0	1456	0	7131	0	4005
20	OSMANABAD	0	3436	0	3852	0	964
21	PALGHAR	0	423	0	2389	0	2685
22	PARBHANI	0	1593	0	7486	0	1961
23	PUNE	0	2397	0	2596	0	1003
24	RAIGAD	0	35	0	616	0	436
25	RATNAGIRI	0	115	0	672	0	617
26	SANGLI	0	1047	0	4569	0	1389
27	SINDHUDURG	0	9	0	447	0	380
28	SOLAPUR	0	7236	0	6758	0	2210
29	THANE	0	120	0	905	0	756
30	WARDHA	0	1760	0	1805	0	674
31	WASHIM	0	3515	0	4637	0	1682
32	YAVATMAL	0	4761	0	11522	0	4902
33	SATARA	-1	1123	0	1767	0	1021
34	AHMEDNAGAR	-11	3277	-1	4485	-1	3994
	Total	0	97351	0	197956	0	80471

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	NASHIK DIV.	0	1988	0	8667	0	5867
2	AMRAVATI DIV.	0	4173	0	13852	0	5812
3	AURANGABAD DIV.	0	16490	0	29327	0	11883
4	NAGPUR DIV.	0	2836	0	8245	0	4075
5	KONKAN DIV.	0	1373	0	2138	0	1568
6	PUNE DIV.	0	1700	0	5151	0	2422
	Total	0	28560	0	67380	0	31627

State Schemes 1st Ins Pending

SINDHUDURG	12
RATNAGIRI	36
CHANDRAPUR	72
THANE	82
NANDURBAR	158
SATARA	171
NASHIK	173
SANGLI	186
PUNE	298
RAIGAD	320
KOLHAPUR	354
BHANDARA	361
WASHIM	396
NAGPUR	401
BULDHANA	406
DHULE	410
GADCHIROLI	428
WARDHA	479
AHMEDNAGAR	488
SOLAPUR	691
JALGAON	759
PALGHAR	923
YAVATMAL	972
GONDIA	1095
AKOLA	1166
AMRAVATI	1233
JALNA	1243
PARBHANI	1287
LATUR	1523
OSMANABAD	1773
HINGOLI	1966
BEED	2239
AURANGABAD	2913
NANDED	3546

State Schemes 2nd Ins Pending

SINDHUDURG	92
RATNAGIRI	251
THANE	264
SATARA	475
RAIGAD	560
GONDIA	822
NAGPUR	835
SANGLI	949
PALGHAR	971
PUNE	1050
BHANDARA	1081
KOLHAPUR	1109
NANDURBAR	1122
WARDHA	1256
NASHIK	1385
DHULE	1540
SOLAPUR	1568
WASHIM	1639
PARBHANI	1964
GADCHIROLI	2065
CHANDRAPUR	2186
JALGAON	2292
AHMEDNAGAR	2328
AKOLA	2590
AMRAVATI	2601
BULDHANA	2635
HINGOLI	2772
OSMANABAD	3314
AURANGABAD	3626
NANDED	3630
JALNA	3893
YAVATMAL	4387
LATUR	4394
BEED	5734

State Schemes 3rd Ins Pending

SINDHUDURG	93
RATNAGIRI	192
NAGPUR	279
SATARA	292
THANE	307
KOLHAPUR	340
RAIGAD	384
SANGLI	395
BHANDARA	401
WARDHA	421
GONDIA	502
PALGHAR	592
PUNE	667
SOLAPUR	728
WASHIM	757
HINGOLI	821
PARBHANI	872
AMRAVATI	881
AKOLA	900
NASHIK	979
DHULE	1052
NANDURBAR	1086
NANDED	1171
CHANDRAPUR	1220
AURANGABAD	1248
OSMANABAD	1251
GADCHIROLI	1252
JALGAON	1295
AHMEDNAGAR	1455
BULDHANA	1623
YAVATMAL	1651
LATUR	1855
BEED	2184
JALNA	2481

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	1166	0	2590	0	900
2	AMRAVATI	0	1233	0	2601	0	881
3	AURANGABAD	0	2913	0	3626	0	1248
4	BEED	0	2239	0	5734	0	2184
5	BHANDARA	0	361	0	1081	0	401
6	BULDHANA	0	406	0	2635	0	1623
7	CHANDRAPUR	0	72	0	2186	0	1220
8	DHULE	0	410	0	1540	0	1052
9	GADCHIROLI	0	428	0	2065	0	1252
10	GONDIA	0	1095	0	822	0	502
11	HINGOLI	0	1966	0	2772	0	821
12	JALGAON	0	759	0	2292	0	1295
13	JALNA	0	1243	0	3893	0	2481
14	KOLHAPUR	0	354	0	1109	0	340
15	LATUR	0	1523	0	4394	0	1855
16	NAGPUR	0	401	0	835	0	279
17	NANDED	0	3546	0	3630	0	1171
18	NANDURBAR	0	158	0	1122	0	1086
19	NASHIK	0	173	0	1385	0	979
20	OSMANABAD	0	1773	0	3314	0	1251
21	PALGHAR	0	923	0	971	0	592
22	PARBHANI	0	1287	0	1964	0	872
23	PUNE	0	298	0	1050	0	667
24	RAIGAD	0	320	0	560	0	384
25	RATNAGIRI	0	36	0	251	0	192
26	SANGLI	0	186	0	949	0	395
27	SINDHUDURG	0	12	0	92	0	93
28	SOLAPUR	0	691	0	1568	0	728
29	THANE	0	82	0	264	0	307
30	WARDHA	0	479	0	1256	0	421
31	WASHIM	0	396	0	1639	0	757
32	YAVATMAL	0	972	0	4387	0	1651
33	SATARA	-1	171	0	475	0	292
34	AHMEDNAGAR	-3	488	0	2328	0	1455
	Total	0	28560	0	67380	0	31627
