



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०२.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१०३६६	९	१०३९४६९	५६	०	०	०
राज्य योजना	५५८७१८	१९६	४०३९९९	२४	०	०	०
एकूण	१९६९०८४	२०५	१४४३४६८	८०	०	०	०

PMAY-G Completion Progress Bar

73.7%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.3%


State Schemes: Incomplete Houses bifurcation

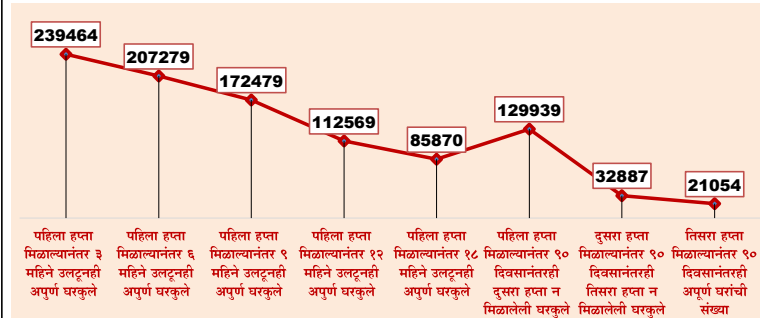

Abhiyan Achievement Day 163

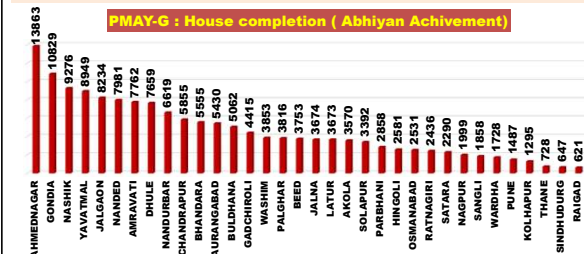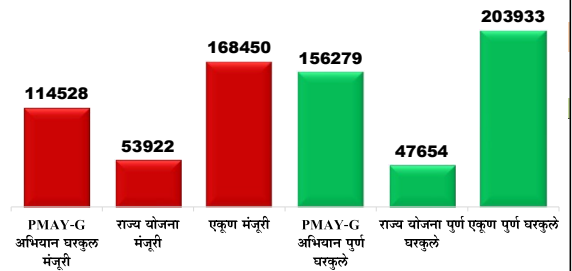

State Schemes: House completion (Abhiyan Achievement)



राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.



State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	01.05.2023	02.05.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	238004	237295	237303	8	701
2	AMRAVATI DIV.	275012	274615	274616	1	396
3	NASHIK DIV.	414805	413719	413719	0	1086
4	NAGPUR DIV.	291968	291321	291321	0	647
5	KONKAN DIV.	69804	69627	69627	0	177
6	PUNE DIV.	124645	123780	123780	0	865
Total		1414238	1410357	1410366	9	3872

Sr. No.	District	Target (PWL+Awaas Plus)	01.05.2023	02.05.2023	Daily_Achievement	Remaining
1	JALNA	24039	24018	24023	5	16
2	AURANGABAD	36740	36511	36514	3	226
3	YAVATMAL	65355	65245	65246	1	109
4	AHMEDNAGAR	60792	60757	60757	0	35
5	AKOLA	48792	48778	48778	0	14
6	AMRAVATI	95714	95515	95515	0	199
7	BEED	35310	35253	35253	0	57
8	BHANDARA	65003	64949	64949	0	54
9	BULDHANA	44757	44714	44714	0	43
10	CHANDRAPUR	43100	42975	42975	0	125
11	DHULE	64989	64917	64917	0	72
12	GADCHIROLI	31702	31624	31624	0	78
13	GONDIA	96493	96144	96144	0	349
14	HINGOLI	18109	18083	18083	0	26
15	JALGAON	79735	79403	79403	0	332
16	KOLHAPUR	17680	17680	17680	0	0
17	LATUR	20679	20493	20493	0	186
18	NAGPUR	37037	37022	37022	0	15
19	NANDED	69533	69463	69463	0	70
20	NANDURBAR	119564	118959	118959	0	605
21	NASHIK	89725	89683	89683	0	42
22	OSMANABAD	14506	14412	14412	0	94
23	PALGHAR	35344	35188	35188	0	156
24	PARBHANI	19088	19062	19062	0	26
25	PUNE	20543	20529	20529	0	14
26	RAIGAD	9830	9821	9821	0	9
27	RATNAGIRI	9892	9885	9885	0	7
28	SANGLI	21885	21741	21741	0	144
29	SATARA	15347	15347	15347	0	0
30	SINDHUDURG	5133	5133	5133	0	0
31	SOLAPUR	49190	48483	48483	0	707
32	THANE	9605	9600	9600	0	5
33	WARDHA	18633	18607	18607	0	26
34	WASHIM	20394	20363	20363	0	31
Total		1414238	1410357	1410366	9	3872

Remaining Sanction RANK


KOLHAPUR	0
SATARA	0
SINDHUDURG	0
THANE	5
RATNAGIRI	7
RAIGAD	9
AKOLA	14
PUNE	14
NAGPUR	15
JALNA	16
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	31
AHMEDNAGAR	35
NASHIK	42
BULDHANA	43
BHANDARA	54
BEED	57
NANDED	70
DHULE	72
GADCHIROLI	78
OSMANABAD	94
YAVATMAL	109
CHANDRAPUR	125
SANGLI	144
PALGHAR	156
LATUR	186
AMRAVATI	199
AURANGABAD	226
JALGAON	332
GONDIA	349
NANDURBAR	605
SOLAPUR	707

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	416	416	0	4
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	428	141	287	2
14	PARBHANI	332	15	317	331	13	318	2
15	SATARA	1309	598	711	1304	630	674	-32
16	NASHIK	1824	1475	349	1803	1001	802	474
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2737	1454	1283	9
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2803	1245	1558	39
21	NAGPUR	5134	3397	1737	5038	3422	1616	-25
22	JALGAON	22872	21026	1846	22945	20953	1992	73
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2299	203	2096	2299	255	2044	-52
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	YAVATMAL	3437	1119	2318	3612	1181	2431	-62
27	BHANDARA	5825	3230	2595	5686	3231	2455	-1
28	WASHIM	3477	865	2612	3443	865	2578	0
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7365	3844	3521	-2
31	AHMEDNAGAR	7762	4828	2934	7759	4161	3598	667
32	SOLAPUR	7960	2595	5365	7263	1370	5893	1225
33	BULDHANA	15085	8586	6499	15214	7097	8117	1489
34	AMRAVATI	21721	11392	10329	21721	11392	10329	0
	Total	127895	73533	54362	127412	67445	59967	6262

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.05.2023	02.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	291321	238484	238509	25	52812	186	1553
2	NASHIK DIV.	413719	329154	329165	11	84554	280	2487
3	AMRAVATI DIV.	274616	186343	186353	10	88263	179	2596
4	AURANGABAD DIV.	237303	140034	140042	8	97261	199	2861
5	KONKAN DIV.	69627	57655	57656	1	11971	51	352
6	PUNE DIV.	123780	87743	87744	1	36036	63	1060
Total		1410366	1039413	1039469	56	370897	959	10909

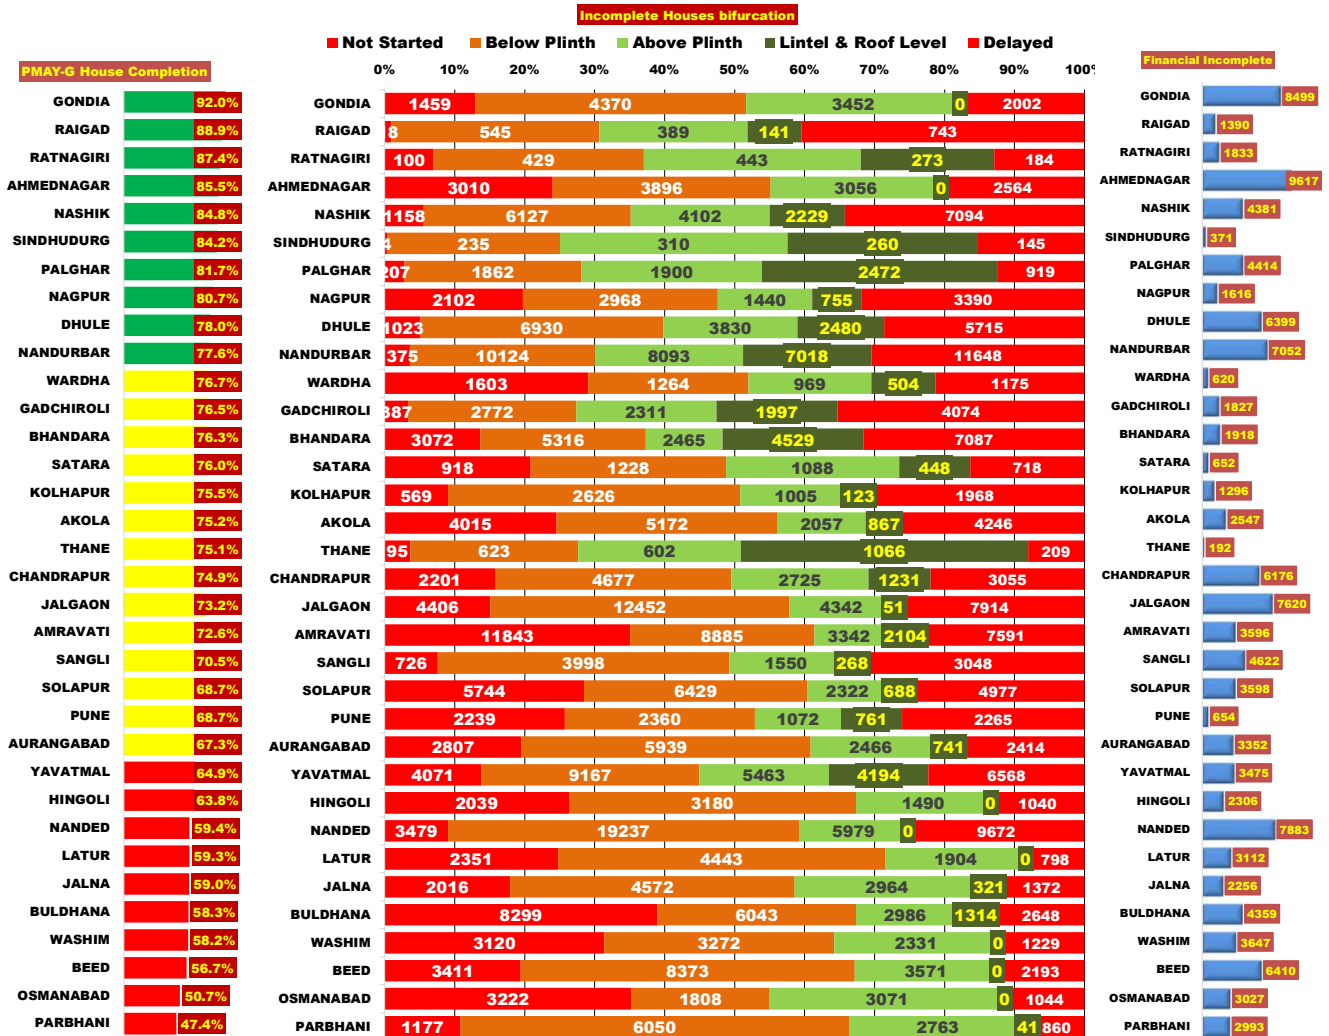

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.05.2023	02.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	96144	88382	88407	25	7737	66	228
2	YAVATMAL	65246	42348	42357	9	22889	55	673
3	NANDED	69463	41285	41291	6	28172	49	829
4	JALGAON	79403	58147	58152	5	21251	51	625
5	NANDURBAR	118959	92344	92349	5	26610	41	783
6	AURANGABAD	36514	24560	24562	2	11952	33	352
7	AHMEDNAGAR	60757	51942	51943	1	8814	85	259
8	AKOLA	48778	36666	36667	1	12111	22	356
9	RATNAGIRI	9885	8639	8640	1	1245	15	37
10	SOLAPUR	48483	33299	33300	1	15183	21	447
11	AMRAVATI	95515	69387	69387	0	26128	48	768
12	BEED	35253	19981	19981	0	15272	23	449
13	BHANDARA	64949	49567	49567	0	15382	34	452
14	BULDHANA	44714	26083	26083	0	18631	31	548
15	CHANDRAPUR	42975	32194	32194	0	10781	36	317
16	DHULE	64917	50654	50654	0	14263	47	420
17	GADCHIROLI	31624	24182	24182	0	7442	27	219
18	HINGOLI	18083	11539	11539	0	6544	16	192
19	JALNA	24023	14180	14180	0	9843	23	290
20	KOLHAPUR	17680	13357	13357	0	4323	8	127
21	LATUR	20493	12147	12147	0	8346	23	245
22	NAGPUR	37022	29892	29892	0	7130	12	210
23	NASHIK	89683	76067	76067	0	13616	57	400
24	OSMANABAD	14412	7311	7311	0	7101	16	209
25	PALGHAR	35188	28747	28747	0	6441	23	189
26	PARBHANI	19062	9031	9031	0	10031	18	295
27	PUNE	20529	14097	14097	0	6432	9	189
28	RAIGAD	9821	8731	8731	0	1090	4	32
29	SANGLI	21741	15325	15325	0	6416	11	189
30	SATARA	15347	11665	11665	0	3682	14	108
31	SINDHUDURG	5133	4324	4324	0	809	4	24
32	THANE	9600	7214	7214	0	2386	4	70
33	WARDHA	18607	14267	14267	0	4340	11	128
34	WASHIM	20363	11859	11859	0	8504	24	250
Total		1410366	1039413	1039469	56	370897	959	10909

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	01.05.2023	02.05.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	200269	166872	166977	105	33292
2	NAGPUR DIV.	118430	92710	92760	50	25670
3	PUNE DIV.	65859	63000	63027	27	2832
4	AMRAVATI DIV.	109705	93924	93938	14	15767
5	KONKAN DIV.	34744	31292	31292	0	3452
6	NASHIK DIV.	141552	110724	110724	0	30828
Total		670559	558522	558718	196	111841


Sr. No.	District	Target	01.05.2023	02.05.2023	Daily_Achievement	Remaining
1	NANDED	26760	21269	21374	105	5386
2	CHANDRAPUR	40285	26611	26661	50	13624
3	SOLAPUR	18718	18448	18475	27	243
4	BULDHANA	21616	19994	20005	11	1611
5	AMRAVATI	23224	19846	19849	3	3375
6	AHMEDNAGAR	35298	32974	32974	0	2324
7	AKOLA	23681	17768	17768	0	5913
8	AURANGABAD	26141	23833	23833	0	2308
9	BEED	26878	25644	25644	0	1234
10	BHANDARA	17612	15566	15566	0	2046
11	DHULE	21790	18081	18081	0	3709
12	GADCHIROLI	16834	15245	15245	0	1589
13	GONDIA	14261	12863	12863	0	1398
14	HINGOLI	27298	15888	15888	0	11410
15	JALGAON	25851	22675	22675	0	3176
16	JALNA	20551	19259	19259	0	1292
17	KOLHAPUR	13090	12528	12528	0	562
18	LATUR	28004	26294	26294	0	1710
19	NAGPUR	16291	11203	11203	0	5088
20	NANDURBAR	26578	14137	14137	0	12441
21	NASHIK	32035	22857	22857	0	9178
22	OSMANABAD	24853	17039	17039	0	7814
23	PALGHAR	11792	11049	11049	0	743
24	PARBHANI	19784	17646	17646	0	2138
25	PUNE	14672	12773	12773	0	1899
26	RAIGAD	7418	6475	6475	0	943
27	RATNAGIRI	7129	6691	6691	0	438
28	SANGLI	8732	8604	8604	0	128
29	SATARA	10647	10647	10647	0	0
30	SINDHUDURG	2141	2108	2108	0	33
31	THANE	6264	4969	4969	0	1295
32	WARDHA	13147	11222	11222	0	1925
33	WASHIM	11503	10153	10153	0	1350
34	YAVATMAL	29681	26163	26163	0	3518
Total		670559	558522	558718	196	111841

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	562
PALGHAR	743
RAIGAD	943
BEED	1234
JALNA	1292
THANE	1295
WASHIM	1350
GONDIA	1398
GADCHIROLI	1589
BULDHANA	1611
LATUR	1710
PUNE	1899
WARDHA	1925
BHANDARA	2046
PARBHANI	2138
AURANGABAD	2308
AHMEDNAGAR	2324
JALGAON	3176
AMRAVATI	3375
YAVATMAL	3518
DHULE	3709
NAGPUR	5088
NANDED	5386
AKOLA	5913
OSMANABAD	7814
NASHIK	9178
HINGOLI	11410
NANDURBAR	12441
CHANDRAPUR	13624

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	01.05.2023	02.05.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	166977	104433	104447	14	62530	88	1839
2	AMRAVATI DIV.	93938	65009	65015	6	28923	54	851
3	NASHIK DIV.	110724	89102	89105	3	21619	68	636
4	NAGPUR DIV.	92760	69607	69608	1	23152	43	681
5	KONKAN DIV.	31292	23775	23775	0	7517	15	221
6	PUNE DIV.	63027	52049	52049	0	10978	24	323
Total		558718	403975	403999	24	154719	292	4551

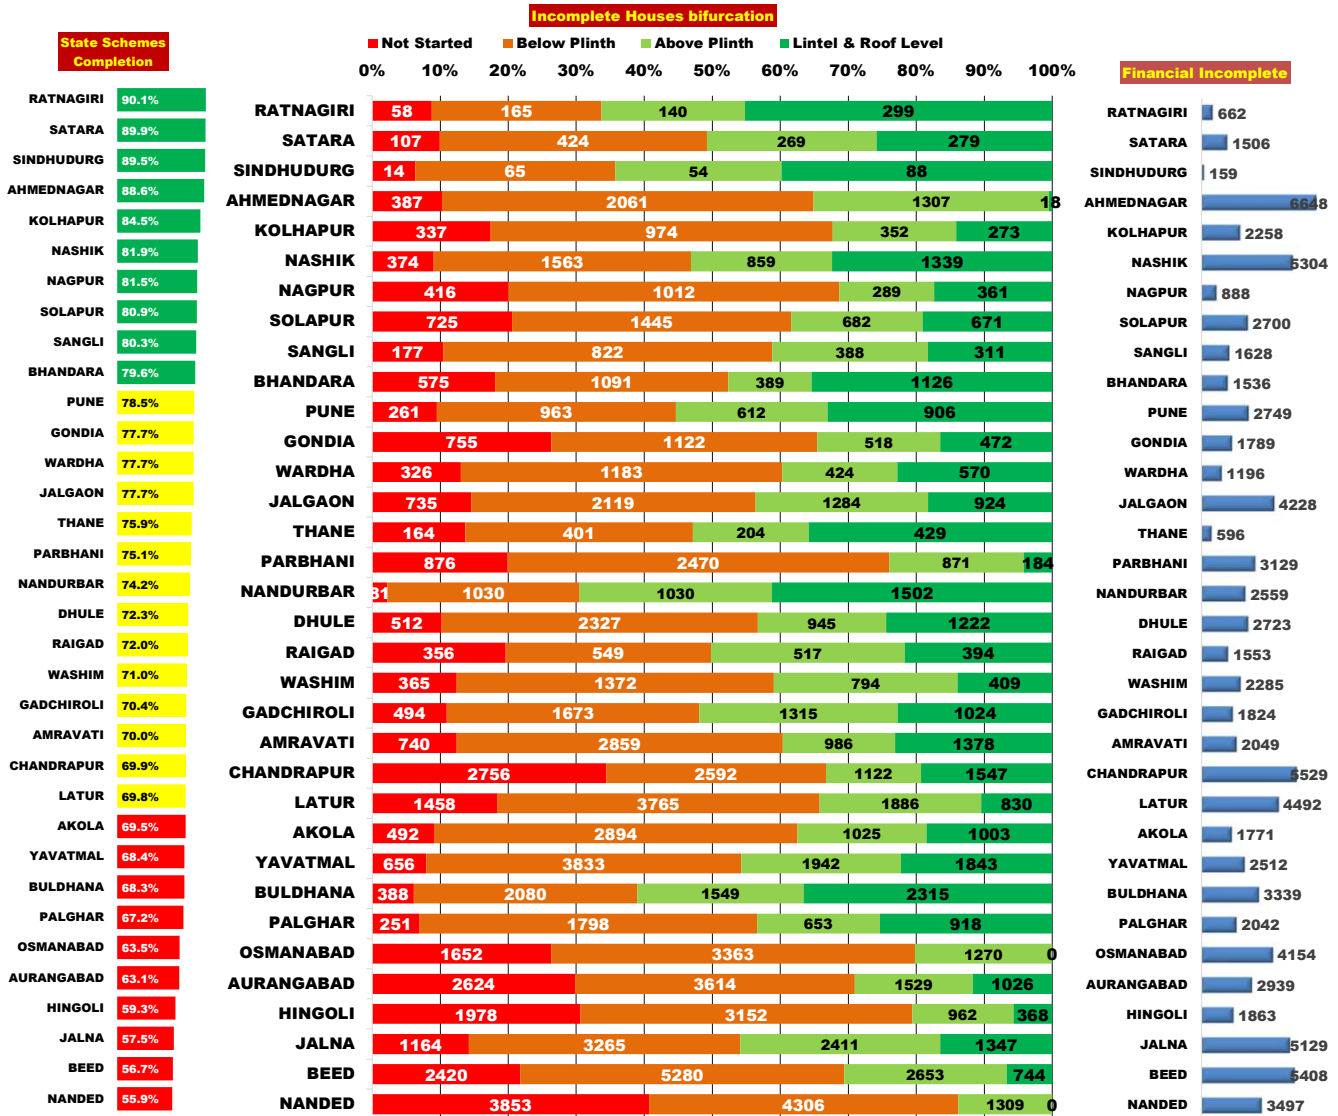

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	01.05.2023	02.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD	23833	15035	15040	5	8793	9	259
2	BEED	25644	14542	14547	5	11097	14	326
3	YAVATMAL	26163	17884	17889	5	8274	13	243
4	LATUR	26294	18351	18355	4	7939	13	234
5	AHMEDNAGAR	32974	29198	29201	3	3773	28	111
6	AKOLA	17768	12353	12354	1	5414	9	159
7	GONDIA	12863	9995	9996	1	2867	8	84
8	AMRAVATI	19849	13886	13886	0	5963	9	175
9	BHANDARA	15566	12385	12385	0	3181	4	94
10	BULDHANA	20005	13673	13673	0	6332	16	186
11	CHANDRAPUR	26661	18644	18644	0	8017	13	236
12	DHULE	18081	13075	13075	0	5006	10	147
13	GADCHIROLI	15245	10739	10739	0	4506	9	133
14	HINGOLI	15888	9428	9428	0	6460	6	190
15	JALGAON	22675	17613	17613	0	5062	11	149
16	JALNA	19259	11072	11072	0	8187	24	241
17	KOLHAPUR	12528	10592	10592	0	1936	3	57
18	NAGPUR	11203	9125	9125	0	2078	3	61
19	NANDED	21374	11948	11948	0	9426	8	277
20	NANDURBAR	14137	10494	10494	0	3643	6	107
21	NASHIK	22857	18722	18722	0	4135	12	122
22	OSMANABAD	17039	10812	10812	0	6227	10	183
23	PALGHAR	11049	7429	7429	0	3620	6	106
24	PARBHANI	17646	13245	13245	0	4401	4	129
25	PUNE	12773	10031	10031	0	2742	5	81
26	RAIGAD	6475	4659	4659	0	1816	3	53
27	RATNAGIRI	6691	6029	6029	0	662	3	19
28	SANGLI	8604	6906	6906	0	1698	4	50
29	SATARA	10647	9568	9568	0	1079	5	32
30	SINDHUDURG	2108	1887	1887	0	221	1	7
31	SOLAPUR	18475	14952	14952	0	3523	7	104
32	THANE	4969	3771	3771	0	1198	2	35
33	WARDHA	11222	8719	8719	0	2503	7	74
34	WASHIM	10153	7213	7213	0	2940	8	86
	Total	558718	403975	403999	24	154719	292	4551

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10972	0	39529	0	23423
2	AMRAVATI DIV.	0	31282	0	32539	0	16179
3	AURANGABAD DIV.	0	20471	0	53602	0	24208
4	NAGPUR DIV.	0	10611	0	21367	0	13362
5	KONKAN DIV.	0	421	0	3694	0	3644
6	PUNE DIV.	0	10070	0	16641	0	7037
	Total	0	83827	0	167372	0	87853

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	15
THANE	95
RATNAGIRI	100
PALGHAR	207
GADCHIROLI	362
KOLHAPUR	569
SANGLI	600
SATARA	918
DHULE	1023
NASHIK	1158
PARBHANI	1177
NANDURBAR	1375
GONDIA	1459
WARDHA	1603
NAGPUR	1967
JALNA	1986
HINGOLI	2039
CHANDRAPUR	2148
PUNE	2239
LATUR	2351
AURANGABAD	2806
AHMEDNAGAR	3010
BHANDARA	3072
WASHIM	3117
OSMANABAD	3222
BEED	3411
NANDED	3479
AKOLA	4015
YAVATMAL	4065
JALGAON	4406
SOLAPUR	5744
BULDHANA	8288
AMRAVATI	11797

PMAY-G 2nd Ins Pending

SINDHUDURG	235
RATNAGIRI	429
RAIGAD	545
THANE	623
SATARA	1228
WARDHA	1264
OSMANABAD	1808
PALGHAR	1862
PUNE	2360
KOLHAPUR	2626
GADCHIROLI	2772
NAGPUR	2968
HINGOLI	3180
WASHIM	3272
AHMEDNAGAR	3896
SANGLI	3998
GONDIA	4370
LATUR	4443
JALNA	4572
CHANDRAPUR	4677
AKOLA	5172
BHANDARA	5316
AURANGABAD	5939
BULDHANA	6043
PARBHANI	6050
NASHIK	6127
SOLAPUR	6429
DHULE	6930
BEED	8373
AMRAVATI	8885
YAVATMAL	9167
NANDURBAR	10124
JALGAON	12452
NANDED	19237

PMAY-G 3rd Ins Pending

SINDHUDURG	310
RAIGAD	389
RATNAGIRI	443
THANE	602
WARDHA	969
KOLHAPUR	1005
PUNE	1072
SATARA	1088
NAGPUR	1440
HINGOLI	1490
SANGLI	1550
PALGHAR	1900
LATUR	1904
AKOLA	2057
GADCHIROLI	2311
SOLAPUR	2322
WASHIM	2331
BHANDARA	2465
AURANGABAD	2466
CHANDRAPUR	2725
PARBHANI	2763
JALNA	2964
BULDHANA	2986
AHMEDNAGAR	3056
OSMANABAD	3071
AMRAVATI	3342
GONDIA	3452
BEED	3571
DHULE	3830
NASHIK	4102
JALGAON	4342
YAVATMAL	5463
NANDED	5979
NANDURBAR	8093

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3010	0	3896	0	3056
2	AKOLA	0	4015	0	5172	0	2057
3	AMRAVATI	0	11797	0	8885	0	3342
4	AURANGABAD	0	2806	0	5939	0	2466
5	BEED	0	3411	0	8373	0	3571
6	BHANDARA	0	3072	0	5316	0	2465
7	BULDHANA	0	8288	0	6043	0	2986
8	CHANDRAPUR	0	2148	0	4677	0	2725
9	DHULE	0	1023	0	6930	0	3830
10	GADCHIROLI	0	362	0	2772	0	2311
11	GONDIA	0	1459	0	4370	0	3452
12	HINGOLI	0	2039	0	3180	0	1490
13	JALGAON	0	4406	0	12452	0	4342
14	JALNA	0	1986	0	4572	0	2964
15	KOLHAPUR	0	569	0	2626	0	1005
16	LATUR	0	2351	0	4443	0	1904
17	NAGPUR	0	1967	0	2968	0	1440
18	NANDED	0	3479	0	19237	0	5979
19	NANDURBAR	0	1375	0	10124	0	8093
20	NASHIK	0	1158	0	6127	0	4102
21	OSMANABAD	0	3222	0	1808	0	3071
22	PALGHAR	0	207	0	1862	0	1900
23	PARBHANI	0	1177	0	6050	0	2763
24	PUNE	0	2239	0	2360	0	1072
25	RAIGAD	0	15	0	545	0	389
26	RATNAGIRI	0	100	0	429	0	443
27	SANGLI	0	600	0	3998	0	1550
28	SATARA	0	918	0	1228	0	1088
29	SINDHUDURG	0	4	0	235	0	310
30	SOLAPUR	0	5744	0	6429	0	2322
31	THANE	0	95	0	623	0	602
32	WARDHA	0	1603	0	1264	0	969
33	WASHIM	0	3117	0	3272	0	2331
34	YAVATMAL	0	4065	0	9167	0	5463
	Total	0	83827	0	167372	0	87853

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2089	0	9100	0	5425
2	AMRAVATI DIV.	0	2641	0	13038	0	6296
3	AURANGABAD DIV.	0	16025	0	29215	0	12891
4	NAGPUR DIV.	0	5322	0	8673	0	4057
5	KONKAN DIV.	0	843	0	2978	0	1568
6	PUNE DIV.	0	1607	0	4628	0	2303
Total		0	28527	0	67632	0	32540

State Schemes 1st Ins Pending

SINDHUDURG	14
RATNAGIRI	58
NANDURBAR	81
SATARA	107
THANE	164
SANGLI	177
PALGHAR	251
PUNE	261
WARDHA	326
KOLHAPUR	337
RAIGAD	356
WASHIM	365
NASHIK	374
AHMEDNAGAR	387
BULDHANA	388
NAGPUR	416
AKOLA	492
GADCHIROLI	494
DHULE	512
BHANDARA	575
YAVATMAL	656
SOLAPUR	725
JALGAON	735
AMRAVATI	740
GONDIA	755
PARBHANI	876
JALNA	1164
LATUR	1458
OSMANABAD	1652
HINGOLI	1978
BEED	2420
AURANGABAD	2624
CHANDRAPUR	2756
NANDED	3853

State Schemes 2nd Ins Pending

SINDHUDURG	65
RATNAGIRI	165
THANE	401
SATARA	424
RAIGAD	549
SANGLI	822
PUNE	963
KOLHAPUR	974
NAGPUR	1012
NANDURBAR	1030
BHANDARA	1091
GONDIA	1122
WARDHA	1183
WASHIM	1372
SOLAPUR	1445
NASHIK	1563
GADCHIROLI	1673
PALGHAR	1798
AHMEDNAGAR	2061
BULDHANA	2080
JALGAON	2119
DHULE	2327
PARBHANI	2470
CHANDRAPUR	2592
AMRAVATI	2859
AKOLA	2894
HINGOLI	3152
JALNA	3265
OSMANABAD	3363
AURANGABAD	3614
LATUR	3765
YAVATMAL	3833
NANDED	4306
BEED	5280

State Schemes 3rd Ins Pending

SINDHUDURG	54
RATNAGIRI	140
THANE	204
SATARA	269
NAGPUR	289
KOLHAPUR	352
SANGLI	388
BHANDARA	389
WARDHA	424
RAIGAD	517
GONDIA	518
PUNE	612
PALGHAR	653
SOLAPUR	682
WASHIM	794
NASHIK	859
PARBHANI	871
DHULE	945
HINGOLI	962
AMRAVATI	986
AKOLA	1025
NANDURBAR	1030
CHANDRAPUR	1122
OSMANABAD	1270
JALGAON	1284
AHMEDNAGAR	1307
NANDED	1309
GADCHIROLI	1315
AURANGABAD	1529
BULDHANA	1549
LATUR	1886
YAVATMAL	1942
JALNA	2411
BEED	2653

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	387	0	2061	0	1307
2	AKOLA	0	492	0	2894	0	1025
3	AMRAVATI	0	740	0	2859	0	986
4	AURANGABAD	0	2624	0	3614	0	1529
5	BEED	0	2420	0	5280	0	2653
6	BHANDARA	0	575	0	1091	0	389
7	BULDHANA	0	388	0	2080	0	1549
8	CHANDRAPUR	0	2756	0	2592	0	1122
9	DHULE	0	512	0	2327	0	945
10	GADCHIROLI	0	494	0	1673	0	1315
11	GONDIA	0	755	0	1122	0	518
12	HINGOLI	0	1978	0	3152	0	962
13	JALGAON	0	735	0	2119	0	1284
14	JALNA	0	1164	0	3265	0	2411
15	KOLHAPUR	0	337	0	974	0	352
16	LATUR	0	1458	0	3765	0	1886
17	NAGPUR	0	416	0	1012	0	289
18	NANDED	0	3853	0	4306	0	1309
19	NANDURBAR	0	81	0	1030	0	1030
20	NASHIK	0	374	0	1563	0	859
21	OSMANABAD	0	1652	0	3363	0	1270
22	PALGHAR	0	251	0	1798	0	653
23	PARBHANI	0	876	0	2470	0	871
24	PUNE	0	261	0	963	0	612
25	RAIGAD	0	356	0	549	0	517
26	RATNAGIRI	0	58	0	165	0	140
27	SANGLI	0	177	0	822	0	388
28	SATARA	0	107	0	424	0	269
29	SINDHUDURG	0	14	0	65	0	54
30	SOLAPUR	0	725	0	1445	0	682
31	THANE	0	164	0	401	0	204
32	WARDHA	0	326	0	1183	0	424
33	WASHIM	0	365	0	1372	0	794
34	YAVATMAL	0	656	0	3833	0	1942
	Total	0	28527	0	67632	0	32540

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2564	1805	3114	1377	50
AKOLA	4246	3537	3497	868	589
AMRAVATI	7591	5669	7118	1466	1029
AURANGABAD	2414	2256	4879	1036	389
BEED	2193	1871	6637	1569	417
BHANDARA	7087	5317	4812	739	2180
BULDHANA	2648	2165	3944	832	696
CHANDRAPUR	3055	1962	3473	682	287
DHULE	5715	4109	5923	2165	1567
GADCHIROLI	4074	2496	2281	1182	892
GONDIA	2002	1926	3173	1012	149
HINGOLI	1040	672	2585	458	101
JALGAON	7914	6663	11110	1988	665
JALNA	1372	1084	3127	760	275
KOLHAPUR	1968	748	2362	284	91
LATUR	798	729	2678	438	47
NAGPUR	3390	2356	2568	446	577
NANDED	9672	9182	14698	1975	358
NANDURBAR	11648	10042	6982	4570	5104
NASHIK	7094	3588	4789	2035	1522
OSMANABAD	1044	585	1249	460	7
PALGHAR	919	656	1305	615	408
PARBHANI	860	738	4287	536	90
PUNE	2265	1740	1944	492	446
RAIGAD	743	240	481	239	160
RATNAGIRI	184	44	341	114	50
SANGLI	3048	2334	3448	528	133
SATARA	718	389	885	209	140
SINDHUDURG	145	89	209	65	25
SOLAPUR	4977	4608	5011	1206	503
THANE	209	188	566	156	136
WARDHA	1175	812	947	209	233
WASHIM	1229	869	2591	394	93
YAVATMAL	6568	4401	6925	1782	1645
