



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०३.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४१०३२५	०	१०३९८५१	३८२	०	०	०
राज्य योजना	५५९९०४	३८६	४०४१२४	१२५	०	०	०
एकूण	१९६९४२९	३८६	१४४३९७५	५०७	०	०	०

PMAY-G Completion Progress Bar

73.7%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.3%


State Schemes: Incomplete Houses bifurcation

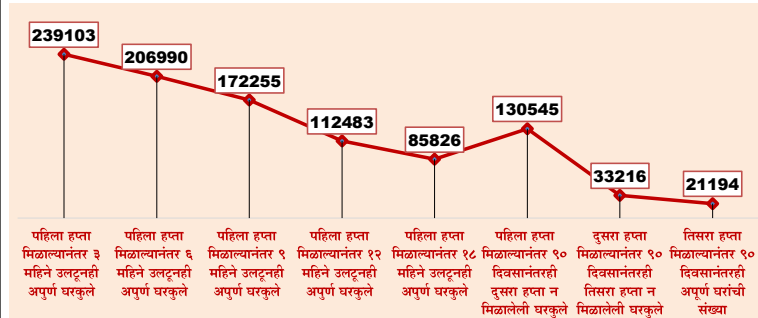

Abhiyan Achievement Day 164

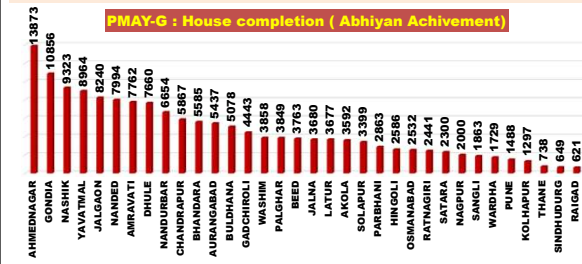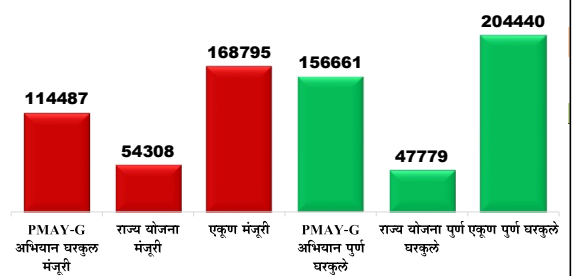


State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण
४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	02.05.2023	03.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414868	413719	413719	0	1149
2	AMRAVATI DIV.	274997	274616	274609	0	388
3	AURANGABAD DIV.	238003	237303	237303	0	700
4	NAGPUR DIV.	291964	291321	291319	0	645
5	KONKAN DIV.	69835	69627	69627	0	208
6	PUNE DIV.	124617	123780	123748	0	869
Total		1414284	1410366	1410325	0	3959

Sr. No.	District	Target (PWL+Awaas Plus)	02.05.2023	03.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60792	60757	60757	0	35
2	AKOLA	48792	48778	48778	0	14
3	AURANGABAD	36740	36514	36514	0	226
4	BEED	35310	35253	35253	0	57
5	BHANDARA	65000	64949	64949	0	51
6	CHANDRAPUR	43097	42975	42975	0	122
7	DHULE	64999	64917	64917	0	82
8	GADCHIROLI	31706	31624	31624	0	82
9	GONDIA	96493	96144	96144	0	349
10	HINGOLI	18109	18083	18083	0	26
11	JALGAON	79735	79403	79403	0	332
12	JALNA	24038	24023	24023	0	15
13	LATUR	20679	20493	20493	0	186
14	NANDED	69533	69463	69463	0	70
15	NANDURBAR	119607	118959	118959	0	648
16	NASHIK	89735	89683	89683	0	52
17	OSMANABAD	14506	14412	14412	0	94
18	PALGHAR	35376	35188	35188	0	188
19	PARBHANI	19088	19062	19062	0	26
20	PUNE	20543	20529	20529	0	14
21	RAIGAD	9830	9821	9821	0	9
22	RATNAGIRI	9891	9885	9885	0	6
23	SANGLI	21885	21741	21741	0	144
24	SINDHUDURG	5133	5133	5133	0	0
25	SOLAPUR	49180	48483	48483	0	697
26	THANE	9605	9600	9600	0	5
27	WARDHA	18633	18607	18607	0	26
28	WASHIM	20390	20363	20363	0	27
29	YAVATMAL	65355	65246	65246	0	109
30	BULDHANA	44752	44714	44713	-1	39
31	NAGPUR	37035	37022	37020	-2	15
32	SATARA	15347	15347	15343	-4	4
33	AMRAVATI	95708	95515	95509	-6	199
34	KOLHAPUR	17662	17680	17652	-28	10
Total		1414284	1410366	1410325	0	3959

Remaining Sanction RANK


SINDHUDURG	0
SATARA	4
THANE	5
RATNAGIRI	6
RAIGAD	9
KOLHAPUR	10
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	15
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	27
AHMEDNAGAR	35
BULDHANA	39
BHANDARA	51
NASHIK	52
BEED	57
NANDED	70
DHULE	82
GADCHIROLI	82
OSMANABAD	94
YAVATMAL	109
CHANDRAPUR	122
SANGLI	144
LATUR	186
PALGHAR	188
AMRAVATI	199
AURANGABAD	226
JALGAON	332
GONDIA	349
NANDURBAR	648
SOLAPUR	697

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	419	419	0	1
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	428	145	283	-2
14	PARBHANI	332	15	317	331	13	318	2
15	SATARA	1309	598	711	1304	630	674	-32
16	NASHIK	1824	1475	349	1803	1001	802	474
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2737	1454	1283	9
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2803	1245	1558	39
21	NAGPUR	5134	3397	1737	5038	3422	1616	-25
22	JALGAON	22872	21026	1846	22945	20953	1992	73
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2299	203	2096	2299	255	2044	-52
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	YAVATMAL	3437	1119	2318	3612	1181	2431	-62
27	BHANDARA	5825	3230	2595	5686	3231	2455	-1
28	WASHIM	3477	865	2612	3443	865	2578	0
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7365	3844	3521	-2
31	AHMEDNAGAR	7762	4828	2934	7759	4161	3598	667
32	SOLAPUR	7960	2595	5365	7263	1412	5851	1183
33	BULDHANA	15085	8586	6499	15213	7097	8116	1489
34	AMRAVATI	21721	11392	10329	21718	11392	10326	0
	Total	127895	73533	54362	127411	67494	59917	6215

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.05.2023	03.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK DIV.	413719	329165	329264	99	84455	279	2559
2	NAGPUR DIV.	291319	238509	238608	99	52711	186	1597
3	AMRAVATI DIV.	274609	186353	186411	58	88198	178	2673
4	AURANGABAD DIV.	237303	140042	140093	51	97210	198	2946
5	KONKAN DIV.	69627	57656	57706	50	11921	51	361
6	PUNE DIV.	123748	87744	87769	25	35979	63	1090
Total		1410325	1039469	1039851	382	370474	955	11226

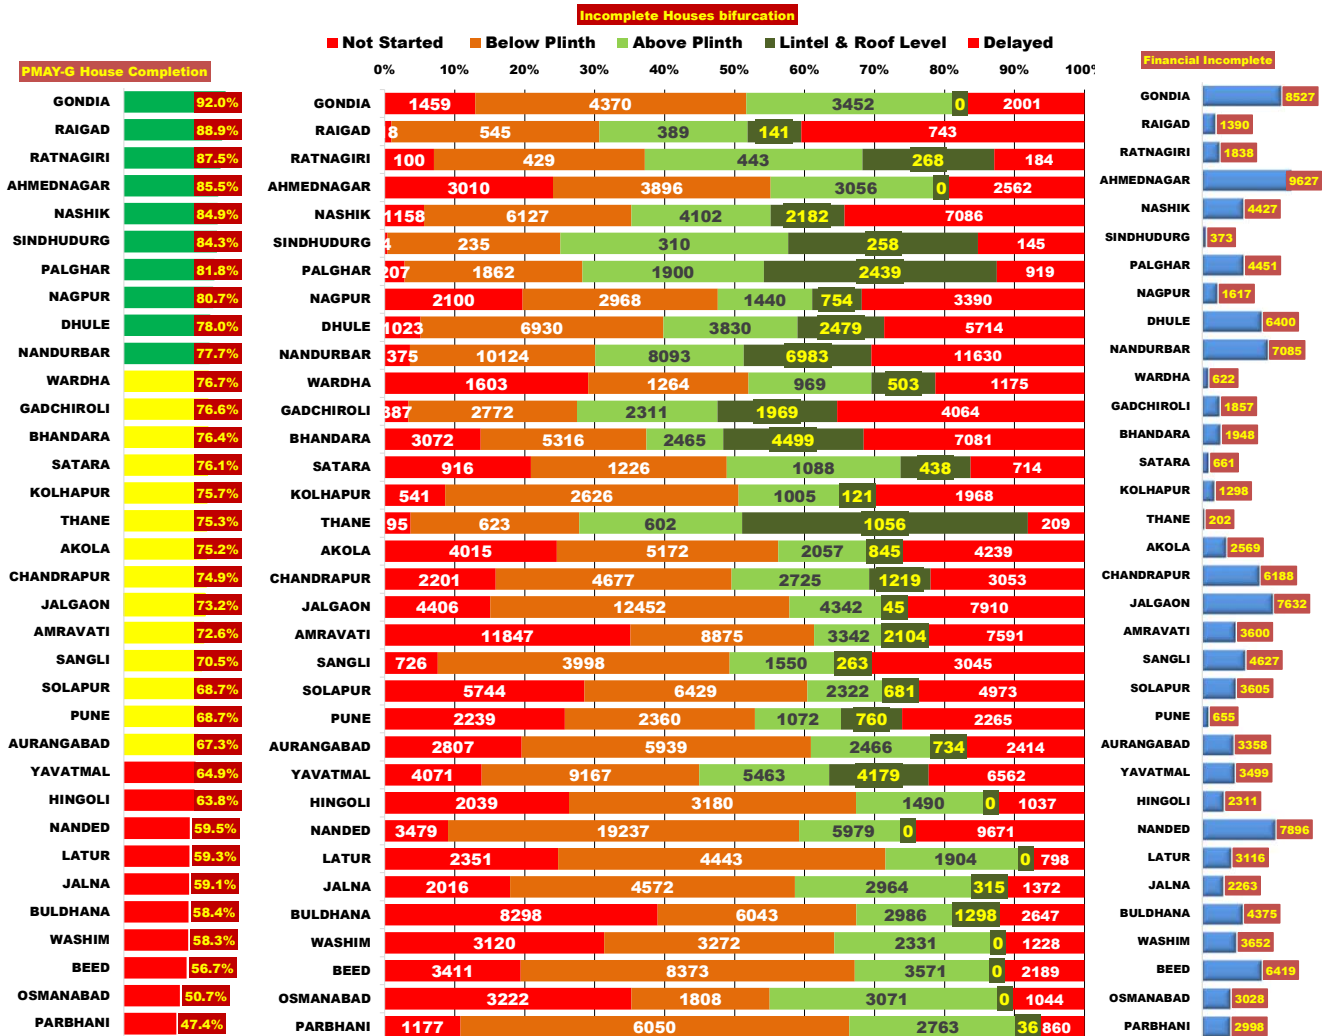

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.05.2023	03.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK	89683	76067	76114	47	13569	57	411
2	NANDURBAR	118959	92349	92384	35	26575	41	805
3	PALGHAR	35188	28747	28780	33	6408	23	194
4	BHANDARA	64949	49567	49597	30	15352	34	465
5	GADCHIROLI	31624	24182	24210	28	7414	27	225
6	GONDIA	96144	88407	88434	27	7710	66	234
7	AKOLA	48778	36667	36689	22	12089	22	366
8	BULDHANA	44713	26083	26099	16	18614	31	564
9	YAVATMAL	65246	42357	42372	15	22874	55	693
10	NANDED	69463	41291	41304	13	28159	49	853
11	CHANDRAPUR	42975	32194	32206	12	10769	36	326
12	AHMEDNAGAR	60757	51943	51953	10	8804	85	267
13	BEED	35253	19981	19991	10	15262	23	462
14	SATARA	15343	11665	11675	10	3668	14	111
15	THANE	9600	7214	7224	10	2376	5	72
16	AURANGABAD	36514	24562	24569	7	11945	33	362
17	SOLAPUR	48483	33300	33307	7	15176	21	460
18	JALGAON	79403	58152	58158	6	21245	50	644
19	JALNA	24023	14180	14186	6	9837	22	298
20	HINGOLI	18083	11539	11544	5	6539	16	198
21	PARBHANI	19062	9031	9036	5	10026	17	304
22	RATNAGIRI	9885	8640	8645	5	1240	15	38
23	SANGLI	21741	15325	15330	5	6411	11	194
24	WASHIM	20363	11859	11864	5	8499	24	258
25	LATUR	20493	12147	12151	4	8342	22	253
26	KOLHAPUR	17652	13357	13359	2	4293	8	130
27	SINDHUDURG	5133	4324	4326	2	807	4	24
28	DHULE	64917	50654	50655	1	14262	47	432
29	NAGPUR	37020	29892	29893	1	7127	12	216
30	OSMANABAD	14412	7311	7312	1	7100	15	215
31	PUNE	20529	14097	14098	1	6431	9	195
32	WARDHA	18607	14267	14268	1	4339	11	131
33	AMRAVATI	95509	69387	69387	0	26122	47	792
34	RAIGAD	9821	8731	8731	0	1090	4	33
Total		1410325	1039469	1039851	382	370474	955	11226

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	02.05.2023	03.05.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	200269	166977	167157	180	33112
2	AMRAVATI DIV.	109705	93938	94102	164	15603
3	NASHIK DIV.	141552	110724	110753	29	30799
4	NAGPUR DIV.	118430	92760	92773	13	25657
5	KONKAN DIV.	34744	31292	31292	0	3452
6	PUNE DIV.	65859	63027	63027	0	2832
Total		670559	558718	559104	386	111455


Sr. No.	District	Target	02.05.2023	03.05.2023	Daily_Achievement	Remaining
1	BEED	26878	25644	25767	123	1111
2	WASHIM	11503	10153	10264	111	1239
3	HINGOLI	27298	15888	15943	55	11355
4	AKOLA	23681	17768	17803	35	5878
5	JALGAON	25851	22675	22703	28	3148
6	BULDHANA	21616	20005	20016	11	1600
7	GADCHIROLI	16834	15245	15254	9	1580
8	YAVATMAL	29681	26163	26168	5	3513
9	NAGPUR	16291	11203	11206	3	5085
10	AMRAVATI	23224	19849	19851	2	3373
11	GONDIA	14261	12863	12864	1	1397
12	JALNA	20551	19259	19260	1	1291
13	NANDED	26760	21374	21375	1	5385
14	NASHIK	32035	22857	22858	1	9177
15	AHMEDNAGAR	35298	32974	32974	0	2324
16	AURANGABAD	26141	23833	23833	0	2308
17	BHANDARA	17612	15566	15566	0	2046
18	CHANDRAPUR	40285	26661	26661	0	13624
19	DHULE	21790	18081	18081	0	3709
20	KOLHAPUR	13090	12528	12528	0	562
21	LATUR	28004	26294	26294	0	1710
22	NANDURBAR	26578	14137	14137	0	12441
23	OSMANABAD	24853	17039	17039	0	7814
24	PALGHAR	11792	11049	11049	0	743
25	PARBHANI	19784	17646	17646	0	2138
26	PUNE	14672	12773	12773	0	1899
27	RAIGAD	7418	6475	6475	0	943
28	RATNAGIRI	7129	6691	6691	0	438
29	SANGLI	8732	8604	8604	0	128
30	SATARA	10647	10647	10647	0	0
31	SINDHUDURG	2141	2108	2108	0	33
32	SOLAPUR	18718	18475	18475	0	243
33	THANE	6264	4969	4969	0	1295
34	WARDHA	13147	11222	11222	0	1925
Total		670559	558718	559104	386	111455

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	562
PALGHAR	743
RAIGAD	943
BEED	1111
WASHIM	1239
JALNA	1291
THANE	1295
GONDIA	1397
GADCHIROLI	1580
BULDHANA	1600
LATUR	1710
PUNE	1899
WARDHA	1925
BHANDARA	2046
PARBHANI	2138
AURANGABAD	2308
AHMEDNAGAR	2324
JALGAON	3148
AMRAVATI	3373
YAVATMAL	3513
DHULE	3709
NAGPUR	5085
NANDED	5385
AKOLA	5878
OSMANABAD	7814
NASHIK	9177
HINGOLI	11355
NANDURBAR	12441
CHANDRAPUR	13624

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	02.05.2023	03.05.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI DIV.	94102	65015	65045	30	29057	54	881
2	NASHIK DIV.	110753	89105	89130	25	21623	68	655
3	NAGPUR DIV.	92773	69608	69632	24	23141	43	701
4	AURANGABAD DIV.	167157	104447	104470	23	62687	88	1900
5	KONKAN DIV.	31292	23775	23794	19	7498	15	227
6	PUNE DIV.	63027	52049	52053	4	10974	24	333
Total		559104	403999	404124	125	154980	291	4696

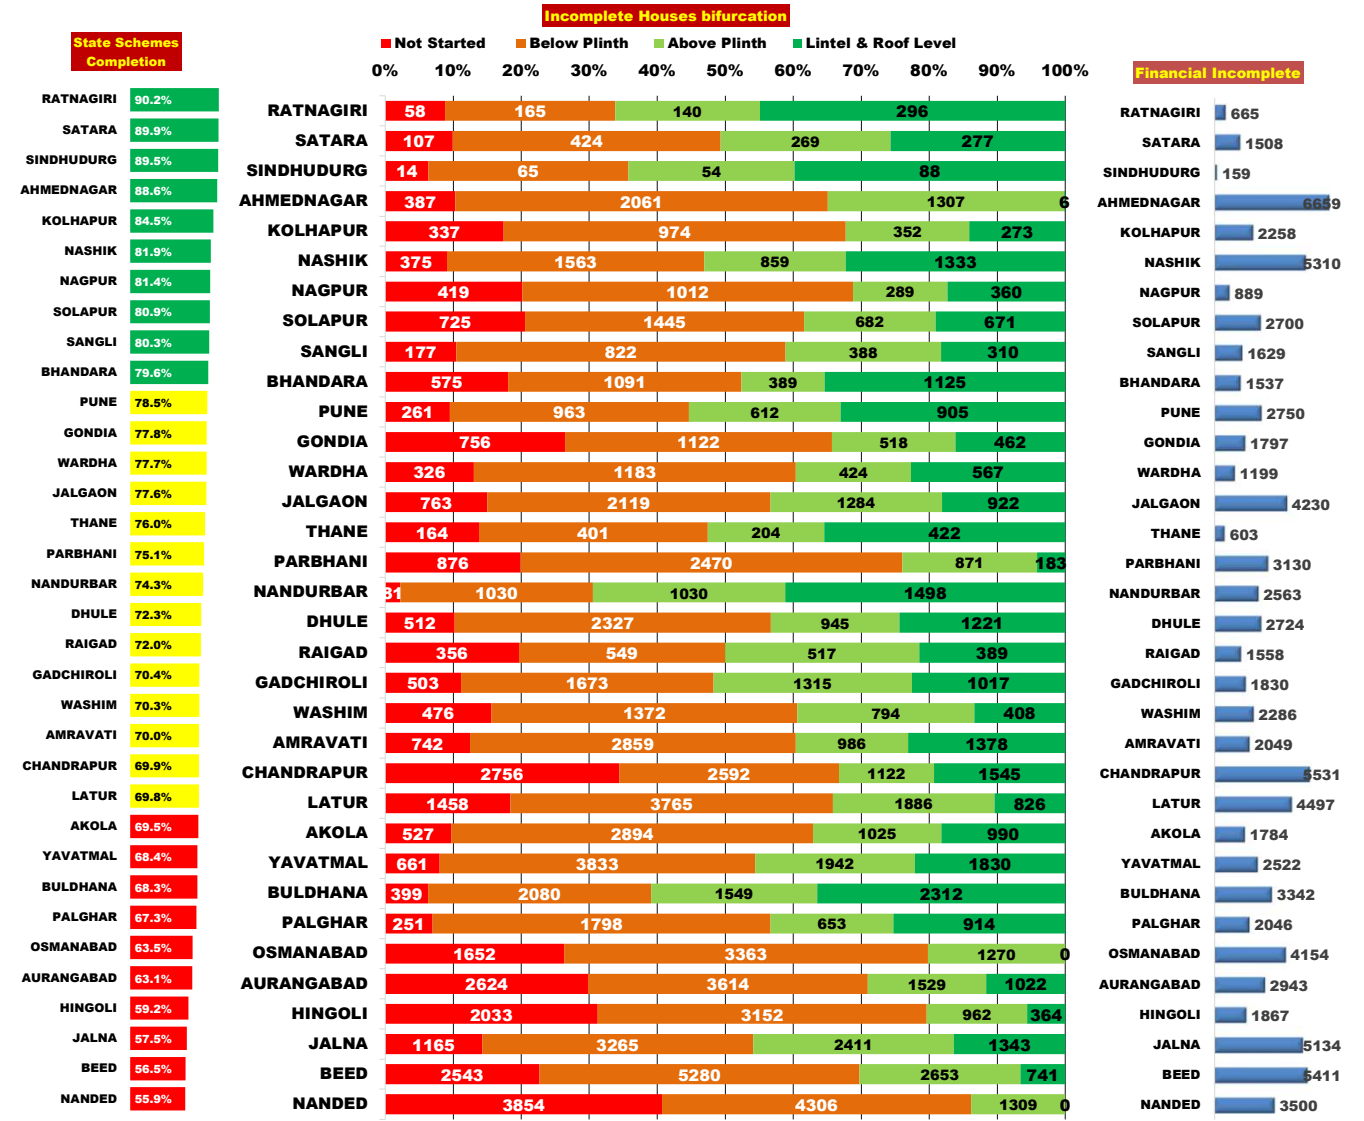

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	02.05.2023	03.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AKOLA	17803	12354	12367	13	5436	9	165
2	YAVATMAL	26168	17889	17902	13	8266	13	250
3	AHMEDNAGAR	32974	29201	29213	12	3761	28	114
4	GONDIA	12864	9996	10006	10	2858	8	87
5	GADCHIROLI	15254	10739	10746	7	4508	9	137
6	THANE	4969	3771	3778	7	1191	2	36
7	NASHIK	22858	18722	18728	6	4130	12	125
8	RAIGAD	6475	4659	4664	5	1811	3	55
9	AURANGABAD	23833	15040	15044	4	8789	9	266
10	HINGOLI	15943	9428	9432	4	6511	6	197
11	JALNA	19260	11072	11076	4	8184	24	248
12	LATUR	26294	18355	18359	4	7935	13	240
13	NANDURBAR	14137	10494	10498	4	3639	6	110
14	PALGHAR	11049	7429	7433	4	3616	6	110
15	BEED	25767	14547	14550	3	11217	14	340
16	BULDHANA	20016	13673	13676	3	6340	16	192
17	NANDED	21375	11948	11951	3	9424	8	286
18	RATNAGIRI	6691	6029	6032	3	659	3	20
19	WARDHA	11222	8719	8722	3	2500	7	76
20	CHANDRAPUR	26661	18644	18646	2	8015	12	243
21	JALGAON	22703	17613	17615	2	5088	11	154
22	SATARA	10647	9568	9570	2	1077	5	33
23	BHANDARA	15566	12385	12386	1	3180	4	96
24	DHULE	18081	13075	13076	1	5005	10	152
25	NAGPUR	11206	9125	9126	1	2080	3	63
26	PARBHANI	17646	13245	13246	1	4400	4	133
27	PUNE	12773	10031	10032	1	2741	5	83
28	SANGLI	8604	6906	6907	1	1697	4	51
29	WASHIM	10264	7213	7214	1	3050	8	92
30	AMRAVATI	19851	13886	13886	0	5965	9	181
31	KOLHAPUR	12528	10592	10592	0	1936	3	59
32	OSMANABAD	17039	10812	10812	0	6227	10	189
33	SINDHUDURG	2108	1887	1887	0	221	1	7
34	SOLAPUR	18475	14952	14952	0	3523	7	107
Total		559104	403999	404124	125	154980	291	4696

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10972	0	39529	0	23423
2	AMRAVATI DIV.	0	31285	0	32529	0	16179
3	AURANGABAD DIV.	0	20471	0	53602	0	24208
4	NAGPUR DIV.	0	10609	0	21367	0	13362
5	KONKAN DIV.	0	421	0	3694	0	3644
6	PUNE DIV.	0	10040	0	16639	0	7037
Total		0	83798	0	167360	0	87853

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	15
THANE	95
RATNAGIRI	100
PALGHAR	207
GADCHIROLI	362
KOLHAPUR	541
SANGLI	600
SATARA	916
DHULE	1023
NASHIK	1158
PARBHANI	1177
NANDURBAR	1375
GONDIA	1459
WARDHA	1603
NAGPUR	1965
JALNA	1986
HINGOLI	2039
CHANDRAPUR	2148
PUNE	2239
LATUR	2351
AURANGABAD	2806
AHMEDNAGAR	3010
BHANDARA	3072
WASHIM	3117
OSMANABAD	3222
BEED	3411
NANDED	3479
AKOLA	4015
YAVATMAL	4065
JALGAON	4406
SOLAPUR	5744
BULDHANA	8287
AMRAVATI	11801

PMAY-G 2nd Ins Pending

SINDHUDURG	235
RATNAGIRI	429
RAIGAD	545
THANE	623
SATARA	1226
WARDHA	1264
OSMANABAD	1808
PALGHAR	1862
PUNE	2360
KOLHAPUR	2626
GADCHIROLI	2772
NAGPUR	2968
HINGOLI	3180
WASHIM	3272
AHMEDNAGAR	3896
SANGLI	3998
GONDIA	4370
LATUR	4443
JALNA	4572
CHANDRAPUR	4677
AKOLA	5172
BHANDARA	5316
AURANGABAD	5939
BULDHANA	6043
PARBHANI	6050
NASHIK	6127
SOLAPUR	6429
DHULE	6930
BEED	8373
AMRAVATI	8875
YAVATMAL	9167
NANDURBAR	10124
JALGAON	12452
NANDED	19237

PMAY-G 3rd Ins Pending

SINDHUDURG	310
RAIGAD	389
RATNAGIRI	443
THANE	602
WARDHA	969
KOLHAPUR	1005
PUNE	1072
SATARA	1088
NAGPUR	1440
HINGOLI	1490
SANGLI	1550
PALGHAR	1900
LATUR	1904
AKOLA	2057
GADCHIROLI	2311
SOLAPUR	2322
WASHIM	2331
BHANDARA	2465
AURANGABAD	2466
CHANDRAPUR	2725
PARBHANI	2763
JALNA	2964
BULDHANA	2986
AHMEDNAGAR	3056
OSMANABAD	3071
AMRAVATI	3342
GONDIA	3452
BEED	3571
DHULE	3830
NASHIK	4102
JALGAON	4342
YAVATMAL	5463
NANDED	5979
NANDURBAR	8093

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3010	0	3896	0	3056
2	AKOLA	0	4015	0	5172	0	2057
3	AURANGABAD	0	2806	0	5939	0	2466
4	BEED	0	3411	0	8373	0	3571
5	BHANDARA	0	3072	0	5316	0	2465
6	BULDHANA	0	8287	0	6043	0	2986
7	CHANDRAPUR	0	2148	0	4677	0	2725
8	DHULE	0	1023	0	6930	0	3830
9	GADCHIROLI	0	362	0	2772	0	2311
10	GONDIA	0	1459	0	4370	0	3452
11	HINGOLI	0	2039	0	3180	0	1490
12	JALGAON	0	4406	0	12452	0	4342
13	JALNA	0	1986	0	4572	0	2964
14	KOLHAPUR	0	541	0	2626	0	1005
15	LATUR	0	2351	0	4443	0	1904
16	NAGPUR	0	1965	0	2968	0	1440
17	NANDED	0	3479	0	19237	0	5979
18	NANDURBAR	0	1375	0	10124	0	8093
19	NASHIK	0	1158	0	6127	0	4102
20	OSMANABAD	0	3222	0	1808	0	3071
21	PALGHAR	0	207	0	1862	0	1900
22	PARBHANI	0	1177	0	6050	0	2763
23	PUNE	0	2239	0	2360	0	1072
24	RAIGAD	0	15	0	545	0	389
25	RATNAGIRI	0	100	0	429	0	443
26	SANGLI	0	600	0	3998	0	1550
27	SINDHUDURG	0	4	0	235	0	310
28	SOLAPUR	0	5744	0	6429	0	2322
29	THANE	0	95	0	623	0	602
30	WARDHA	0	1603	0	1264	0	969
31	WASHIM	0	3117	0	3272	0	2331
32	YAVATMAL	0	4065	0	9167	0	5463
33	SATARA	-2	916	0	1226	0	1088
34	AMRAVATI	-10	11801	0	8875	0	3342
	Total	0	83798	0	167360	0	87853

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2118	0	9100	0	5425
2	AMRAVATI DIV.	0	2805	0	13038	0	6296
3	AURANGABAD DIV.	0	16205	0	29215	0	12891
4	NAGPUR DIV.	0	5335	0	8673	0	4057
5	KONKAN DIV.	0	843	0	2978	0	1568
6	PUNE DIV.	0	1607	0	4628	0	2303
Total		0	28913	0	67632	0	32540

State Schemes 1st Ins Pending

SINDHUDURG	14
RATNAGIRI	58
NANDURBAR	81
SATARA	107
THANE	164
SANGLI	177
PALGHAR	251
PUNE	261
WARDHA	326
KOLHAPUR	337
RAIGAD	356
NASHIK	375
AHMEDNAGAR	387
BULDHANA	399
NAGPUR	419
WASHIM	476
GADCHIROLI	503
DHULE	512
AKOLA	527
BHANDARA	575
YAVATMAL	661
SOLAPUR	725
AMRAVATI	742
GONDIA	756
JALGAON	763
PARBHANI	876
JALNA	1165
LATUR	1458
OSMANABAD	1652
HINGOLI	2033
BEED	2543
AURANGABAD	2624
CHANDRAPUR	2756
NANDED	3854

State Schemes 2nd Ins Pending

SINDHUDURG	65
RATNAGIRI	165
THANE	401
SATARA	424
RAIGAD	549
SANGLI	822
PUNE	963
KOLHAPUR	974
NAGPUR	1012
NANDURBAR	1030
BHANDARA	1091
GONDIA	1122
WARDHA	1183
WASHIM	1372
SOLAPUR	1445
NASHIK	1563
GADCHIROLI	1673
PALGHAR	1798
AHMEDNAGAR	2061
BULDHANA	2080
JALGAON	2119
DHULE	2327
PARBHANI	2470
CHANDRAPUR	2592
AMRAVATI	2859
AKOLA	2894
HINGOLI	3152
JALNA	3265
OSMANABAD	3363
AURANGABAD	3614
LATUR	3765
YAVATMAL	3833
NANDED	4306
BEED	5280

State Schemes 3rd Ins Pending

SINDHUDURG	54
RATNAGIRI	140
THANE	204
SATARA	269
NAGPUR	289
KOLHAPUR	352
SANGLI	388
BHANDARA	389
WARDHA	424
RAIGAD	517
GONDIA	518
PUNE	612
PALGHAR	653
SOLAPUR	682
WASHIM	794
NASHIK	859
PARBHANI	871
DHULE	945
HINGOLI	962
AMRAVATI	986
AKOLA	1025
NANDURBAR	1030
CHANDRAPUR	1122
OSMANABAD	1270
JALGAON	1284
AHMEDNAGAR	1307
NANDED	1309
GADCHIROLI	1315
AURANGABAD	1529
BULDHANA	1549
LATUR	1886
YAVATMAL	1942
JALNA	2411
BEED	2653

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	387	0	2061	0	1307
2	AKOLA	0	527	0	2894	0	1025
3	AMRAVATI	0	742	0	2859	0	986
4	AURANGABAD	0	2624	0	3614	0	1529
5	BEED	0	2543	0	5280	0	2653
6	BHANDARA	0	575	0	1091	0	389
7	BULDHANA	0	399	0	2080	0	1549
8	CHANDRAPUR	0	2756	0	2592	0	1122
9	DHULE	0	512	0	2327	0	945
10	GADCHIROLI	0	503	0	1673	0	1315
11	GONDIA	0	756	0	1122	0	518
12	HINGOLI	0	2033	0	3152	0	962
13	JALGAON	0	763	0	2119	0	1284
14	JALNA	0	1165	0	3265	0	2411
15	KOLHAPUR	0	337	0	974	0	352
16	LATUR	0	1458	0	3765	0	1886
17	NAGPUR	0	419	0	1012	0	289
18	NANDED	0	3854	0	4306	0	1309
19	NANDURBAR	0	81	0	1030	0	1030
20	NASHIK	0	375	0	1563	0	859
21	OSMANABAD	0	1652	0	3363	0	1270
22	PALGHAR	0	251	0	1798	0	653
23	PARBHANI	0	876	0	2470	0	871
24	PUNE	0	261	0	963	0	612
25	RAIGAD	0	356	0	549	0	517
26	RATNAGIRI	0	58	0	165	0	140
27	SANGLI	0	177	0	822	0	388
28	SATARA	0	107	0	424	0	269
29	SINDHUDURG	0	14	0	65	0	54
30	SOLAPUR	0	725	0	1445	0	682
31	THANE	0	164	0	401	0	204
32	WARDHA	0	326	0	1183	0	424
33	WASHIM	0	476	0	1372	0	794
34	YAVATMAL	0	661	0	3833	0	1942
	Total	0	28913	0	67632	0	32540

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2562	1804	3120	1399	50
AKOLA	4239	3530	3584	868	586
AMRAVATI	7591	5669	7126	1476	1034
AURANGABAD	2414	2256	4900	1055	406
BEED	2189	1867	6654	1606	464
BHANDARA	7081	5314	4818	743	2180
BULDHANA	2647	2165	3949	834	697
CHANDRAPUR	3053	1961	3488	686	288
DHULE	5714	4108	5923	2165	1567
GADCHIROLI	4064	2494	2280	1189	892
GONDIA	2001	1925	3184	1021	149
HINGOLI	1037	672	2615	464	101
JALGAON	7910	6663	11132	2002	674
JALNA	1372	1084	3131	763	277
KOLHAPUR	1968	748	2376	284	91
LATUR	798	729	2697	445	47
NAGPUR	3390	2356	2576	446	580
NANDED	9671	9181	14720	1992	355
NANDURBAR	11630	10028	6992	4573	5094
NASHIK	7086	3587	4805	2044	1541
OSMANABAD	1044	585	1249	466	7
PALGHAR	919	656	1359	654	420
PARBHANI	860	738	4340	552	93
PUNE	2265	1740	1945	495	447
RAIGAD	743	240	489	239	161
RATNAGIRI	184	44	340	126	52
SANGLI	3045	2333	3511	532	138
SATARA	714	388	891	209	139
SINDHUDURG	145	89	204	66	26
SOLAPUR	4973	4605	5044	1216	504
THANE	209	188	578	162	150
WARDHA	1175	812	949	213	234
WASHIM	1228	869	2611	422	92
YAVATMAL	6562	4398	6965	1809	1658
