



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०४.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९९९०	०	१०४०२४२	३९९	०	०	०
राज्य योजना	५५९६१५	५१३	४०४२६८	१४४	०	०	०
एकूण	१९६९६०५	५१३	१४४४५१०	५३५	०	०	०

PMAY-G Completion Progress Bar

73.8%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.2%


State Schemes: Incomplete Houses bifurcation

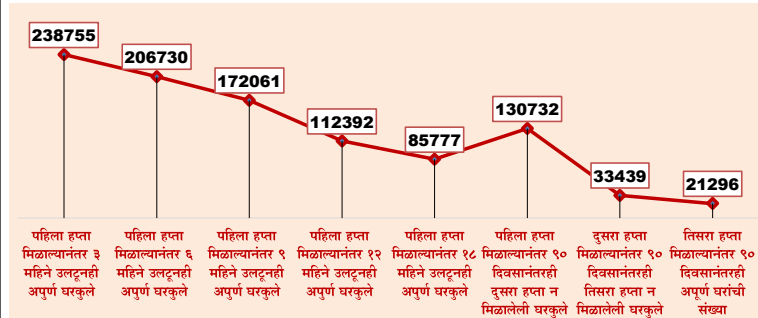


Abhiyan Achievement Day 165

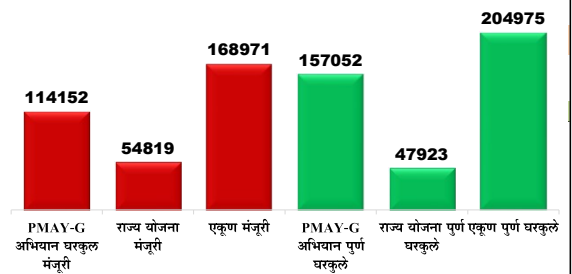

PMAY-G : House completion ( Abhiyan Achievement)

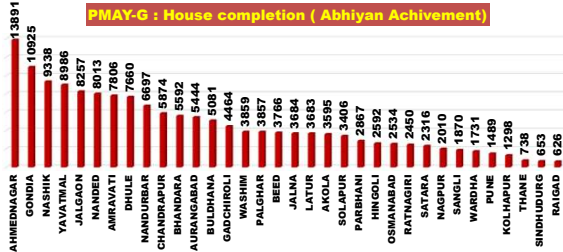

State Schemes : House completion ( Abhiyan Achievement)

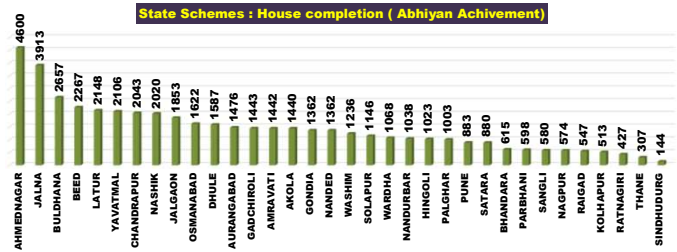


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण

४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


**PMAY-G Delayed Houses TOP 10 Dist.**




**State Schemes Sanction TOP 10 Dist.**




**PMAY-G Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Delayed Houses Bottom 10 Dist.**




**State Schemes Sanction Bottom 10 Dist.**




**PMAY-G Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Completion TOP 10 Dist.**




**State Schemes Completion TOP 10 Dist.**




**PMAY-G Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G Completion Bottom 10 Dist.**




**State Schemes Completion Bottom 10 Dist.**




**State Schemes Remaining 1st Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Top 10 Dist.**




**State Schemes Daily Completion Top 10 Dist.**




**State Schemes Remaining 2nd Installments Bottom 10 Dist.**




**PMAY-G Daily Completion Bottom 10 Dist.**




**State Schemes Daily Completion Bottom 10 Dist.**




**State Schemes Remaining 3rd Installments Bottom 10 Dist.**




**PMAY-G : Current Pace of Completion Per Day (Abhiyan)**




**State Schemes : Current Pace of Completion Per Day (Abhiyan)**



**PMAY-G Required Pace of Completion Per Day**



**State Schemes Required Pace of Completion Per Day**



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	03.05.2023	04.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414868	413719	413719	0	1149
2	AMRAVATI DIV.	274811	274609	274360	0	451
3	AURANGABAD DIV.	238003	237303	237303	0	700
4	NAGPUR DIV.	291959	291319	291314	0	645
5	KONKAN DIV.	69835	69627	69626	0	209
6	PUNE DIV.	124578	123748	123668	0	910
<b>Total</b>		<b>1414054</b>	<b>1410325</b>	<b>1409990</b>	<b>0</b>	<b>4064</b>

Sr. No.	District	Target (PWL+Awaas Plus)	03.05.2023	04.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60792	60757	60757	0	35
2	AKOLA	48792	48778	48778	0	14
3	AURANGABAD	36740	36514	36514	0	226
4	BEED	35310	35253	35253	0	57
5	BHANDARA	65000	64949	64949	0	51
6	BULDHANA	44752	44713	44713	0	39
7	CHANDRAPUR	43097	42975	42975	0	122
8	DHULE	64999	64917	64917	0	82
9	GADCHIROLI	31706	31624	31624	0	82
10	GONDIA	96493	96144	96144	0	349
11	HINGOLI	18109	18083	18083	0	26
12	JALGAON	79735	79403	79403	0	332
13	JALNA	24038	24023	24023	0	15
14	KOLHAPUR	17662	17652	17652	0	10
15	LATUR	20679	20493	20493	0	186
16	NANDED	69533	69463	69463	0	70
17	NANDURBAR	119607	118959	118959	0	648
18	NASHIK	89735	89683	89683	0	52
19	OSMANABAD	14506	14412	14412	0	94
20	PALGHAR	35376	35188	35188	0	188
21	PARBHANI	19088	19062	19062	0	26
22	PUNE	20543	20529	20529	0	14
23	RATNAGIRI	9891	9885	9885	0	6
24	SINDHUDURG	5133	5133	5133	0	0
25	SOLAPUR	49180	48483	48483	0	697
26	THANE	9605	9600	9600	0	5
27	WARDHA	18633	18607	18607	0	26
28	WASHIM	20390	20363	20363	0	27
29	RAIGAD	9830	9821	9820	-1	10
30	SATARA	15347	15343	15342	-1	5
31	NAGPUR	37030	37020	37015	-5	15
32	YAVATMAL	65355	65246	65235	-11	120
33	SANGLI	21846	21741	21662	-79	184
34	AMRAVATI	95522	95509	95271	-238	251
<b>Total</b>		<b>1414054</b>	<b>1410325</b>	<b>1409990</b>	<b>0</b>	<b>4064</b>

Remaining Sanction RANK


SINDHUDURG	0
SATARA	5
THANE	5
RATNAGIRI	6
KOLHAPUR	10
RAIGAD	10
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	15
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	27
AHMEDNAGAR	35
BULDHANA	39
BHANDARA	51
NASHIK	52
BEED	57
NANDED	70
DHULE	82
GADCHIROLI	82
OSMANABAD	94
YAVATMAL	120
CHANDRAPUR	122
SANGLI	184
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	251
JALGAON	332
GONDIA	349
NANDURBAR	648
SOLAPUR	697

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	423	144	279	-1
14	PARBHANI	332	15	317	331	13	318	2
15	SATARA	1309	598	711	1304	630	674	-32
16	NASHIK	1824	1475	349	1803	1001	802	474
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2737	1454	1283	9
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2803	1245	1558	39
21	NAGPUR	5134	3397	1737	5038	3424	1614	-27
22	JALGAON	22872	21026	1846	22945	21000	1945	26
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2299	203	2096	2299	255	2044	-52
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	YAVATMAL	3437	1119	2318	3610	1181	2429	-62
27	BHANDARA	5825	3230	2595	5686	3231	2455	-1
28	WASHIM	3477	865	2612	3443	865	2578	0
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7365	3844	3521	-2
31	AHMEDNAGAR	7762	4828	2934	7759	4161	3598	667
32	SOLAPUR	7960	2595	5365	7263	1412	5851	1183
33	BULDHANA	15085	8586	6499	15213	7097	8116	1489
34	AMRAVATI	21721	11392	10329	21561	11389	10172	3
	<b>Total</b>	<b>127895</b>	<b>73533</b>	<b>54362</b>	<b>127248</b>	<b>67540</b>	<b>59708</b>	<b>6170</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	03.05.2023	04.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	291314	238608	238724	116	52590	185	1643
2	NASHIK DIV.	413719	329264	329357	93	84362	278	2636
3	AMRAVATI DIV.	274360	186411	186484	73	87876	178	2746
4	AURANGABAD DIV.	237303	140093	140144	51	97159	197	3036
5	PUNE DIV.	123668	87769	87801	32	35867	63	1121
6	KONKAN DIV.	69626	57706	57732	26	11894	50	372
<b>Total</b>		<b>1409990</b>	<b>1039851</b>	<b>1040242</b>	<b>391</b>	<b>369748</b>	<b>952</b>	<b>11555</b>

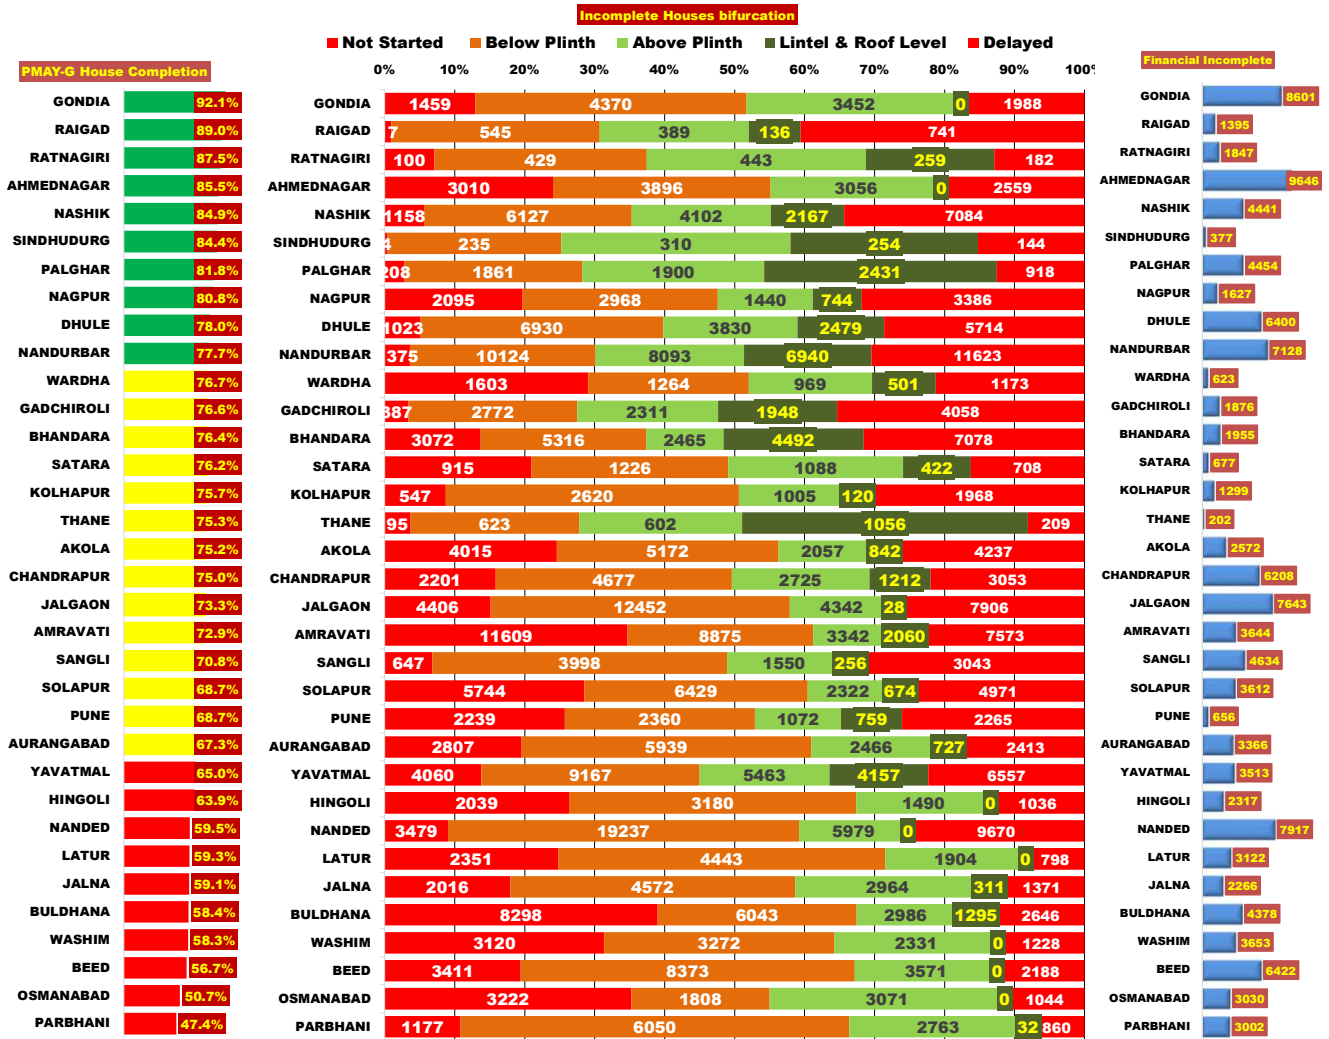

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	03.05.2023	04.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	96144	88434	88503	69	7641	66	239
2	AMRAVATI	95271	69387	69431	44	25840	47	808
3	NANDURBAR	118959	92384	92427	43	26532	41	829
4	YAVATMAL	65235	42372	42394	22	22841	54	714
5	GADCHIROLI	31624	24210	24231	21	7393	27	231
6	NANDED	69463	41304	41323	19	28140	49	879
7	AHMEDNAGAR	60757	51953	51971	18	8786	84	275
8	JALGAON	79403	58158	58175	17	21228	50	663
9	SATARA	15342	11675	11691	16	3651	14	114
10	NASHIK	89683	76114	76129	15	13554	57	424
11	NAGPUR	37015	29893	29903	10	7112	12	222
12	RATNAGIRI	9885	8645	8654	9	1231	15	38
13	PALGHAR	35188	28780	28788	8	6400	23	200
14	AURANGABAD	36514	24569	24576	7	11938	33	373
15	BHANDARA	64949	49597	49604	7	15345	34	480
16	CHANDRAPUR	42975	32206	32213	7	10762	36	336
17	SANGLI	21662	15330	15337	7	6325	11	198
18	SOLAPUR	48483	33307	33314	7	15169	21	474
19	HINGOLI	18083	11544	11550	6	6533	16	204
20	LATUR	20493	12151	12157	6	8336	22	261
21	RAIGAD	9820	8731	8736	5	1084	4	34
22	JALNA	24023	14186	14190	4	9833	22	307
23	PARBHANI	19062	9036	9040	4	10022	17	313
24	SINDHUDURG	5133	4326	4330	4	803	4	25
25	AKOLA	48778	36689	36692	3	12086	22	378
26	BEED	35253	19991	19994	3	15259	23	477
27	BULDHANA	44713	26099	26102	3	18611	31	582
28	OSMANABAD	14412	7312	7314	2	7098	15	222
29	WARDHA	18607	14268	14270	2	4337	10	136
30	KOLHAPUR	17652	13359	13360	1	4292	8	134
31	PUNE	20529	14098	14099	1	6430	9	201
32	WASHIM	20363	11864	11865	1	8498	23	266
33	DHULE	64917	50655	50655	0	14262	46	446
34	THANE	9600	7224	7224	0	2376	4	74
<b>Total</b>		<b>1409990</b>	<b>1039851</b>	<b>1040242</b>	<b>391</b>	<b>369748</b>	<b>952</b>	<b>11555</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	03.05.2023	04.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	92773	93036	263	25394
2	KONKAN DIV.	34744	31292	31453	161	3291
3	AMRAVATI DIV.	109705	94102	94191	89	15514
4	PUNE DIV.	65859	63027	63025	0	2834
5	NASHIK DIV.	141552	110753	110753	0	30799
6	AURANGABAD DIV.	200327	167157	167157	0	33170
<b>Total</b>		<b>670617</b>	<b>559104</b>	<b>559615</b>	<b>513</b>	<b>111002</b>


Sr. No.	District	Target	03.05.2023	04.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	26661	26879	218	13406
2	PALGHAR	11792	11049	11208	159	584
3	WASHIM	11503	10264	10335	71	1168
4	GADCHIROLI	16834	15254	15283	29	1551
5	AMRAVATI	23224	19851	19865	14	3359
6	GONDIA	14261	12864	12872	8	1389
7	NAGPUR	16291	11206	11214	8	5077
8	AKOLA	23681	17803	17807	4	5874
9	THANE	6264	4969	4971	2	1293
10	AHMEDNAGAR	35298	32974	32974	0	2324
11	AURANGABAD	26141	23833	23833	0	2308
12	BEED	26878	25767	25767	0	1111
13	BHANDARA	17612	15566	15566	0	2046
14	BULDHANA	21616	20016	20016	0	1600
15	DHULE	21790	18081	18081	0	3709
16	HINGOLI	27298	15943	15943	0	11355
17	JALGAON	25851	22703	22703	0	3148
18	JALNA	20609	19260	19260	0	1349
19	KOLHAPUR	13090	12528	12528	0	562
20	LATUR	28004	26294	26294	0	1710
21	NANDED	26760	21375	21375	0	5385
22	NANDURBAR	26578	14137	14137	0	12441
23	NASHIK	32035	22858	22858	0	9177
24	OSMANABAD	24853	17039	17039	0	7814
25	PARBHANI	19784	17646	17646	0	2138
26	PUNE	14672	12773	12773	0	1899
27	RAIGAD	7418	6475	6475	0	943
28	RATNAGIRI	7129	6691	6691	0	438
29	SANGLI	8732	8604	8604	0	128
30	SINDHUDURG	2141	2108	2108	0	33
31	SOLAPUR	18718	18475	18475	0	243
32	WARDHA	13147	11222	11222	0	1925
33	YAVATMAL	29681	26168	26168	0	3513
34	SATARA	10647	10647	10645	-2	2
<b>Total</b>		<b>670617</b>	<b>559104</b>	<b>559615</b>	<b>513</b>	<b>111002</b>

Remaining Sanction RANK

SATARA	2
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	562
PALGHAR	584
RAIGAD	943
BEED	1111
WASHIM	1168
THANE	1293
JALNA	1349
GONDIA	1389
GADCHIROLI	1551
BULDHANA	1600
LATUR	1710
PUNE	1899
WARDHA	1925
BHANDARA	2046
PARBHANI	2138
AURANGABAD	2308
AHMEDNAGAR	2324
JALGAON	3148
AMRAVATI	3359
YAVATMAL	3513
DHULE	3709
NAGPUR	5077
NANDED	5385
AKOLA	5874
OSMANABAD	7814
NASHIK	9177
HINGOLI	11355
NANDURBAR	12441
CHANDRAPUR	13406

## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	03.05.2023	04.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	167157	104470	104515	45	62642	87	1958
2	AMRAVATI DIV.	94191	65045	65079	34	29112	54	910
3	NASHIK DIV.	110753	89130	89155	25	21598	67	675
4	NAGPUR DIV.	93036	69632	69650	18	23386	43	731
5	PUNE DIV.	63025	52053	52067	14	10958	24	342
6	KONKAN DIV.	31453	23794	23802	8	7651	15	239
<b>Total</b>		<b>559615</b>	<b>404124</b>	<b>404268</b>	<b>144</b>	<b>155347</b>	<b>290</b>	<b>4855</b>

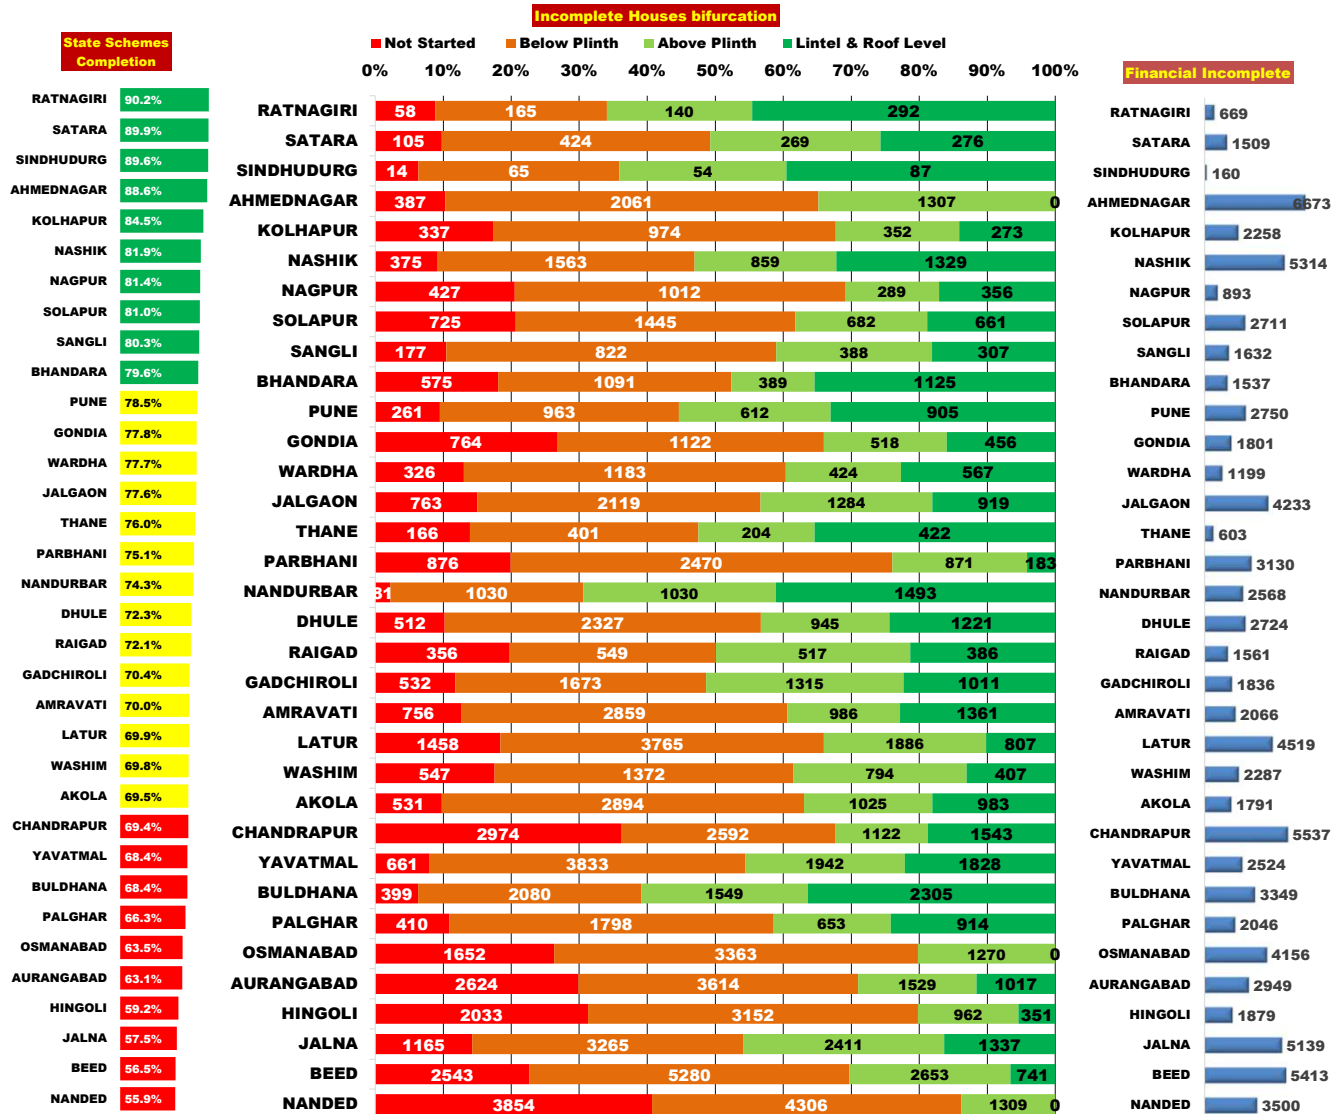



राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	03.05.2023	04.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	LATUR	26294	18359	18378	19	7916	13	247
2	AMRAVATI	19865	13886	13903	17	5962	9	186
3	AHMEDNAGAR	32974	29213	29226	13	3748	28	117
4	HINGOLI	15943	9432	9445	13	6498	6	203
5	SOLAPUR	18475	14952	14962	10	3513	7	110
6	AKOLA	17807	12367	12374	7	5433	9	170
7	BULDHANA	20016	13676	13683	7	6333	16	198
8	GADCHIROLI	15283	10746	10752	6	4531	9	142
9	GONDIA	12872	10006	10012	6	2860	8	89
10	JALNA	19260	11076	11082	6	8178	24	256
11	AURANGABAD	23833	15044	15049	5	8784	9	275
12	NANDURBAR	14137	10498	10503	5	3634	6	114
13	NAGPUR	11214	9126	9130	4	2084	3	65
14	NASHIK	22858	18728	18732	4	4126	12	129
15	RATNAGIRI	6691	6032	6036	4	655	3	20
16	JALGAON	22703	17615	17618	3	5085	11	159
17	RAIGAD	6475	4664	4667	3	1808	3	57
18	SANGLI	8604	6907	6910	3	1694	4	53
19	CHANDRAPUR	26879	18646	18648	2	8231	12	257
20	OSMANABAD	17039	10812	10814	2	6225	10	195
21	YAVATMAL	26168	17902	17904	2	8264	13	258
22	SATARA	10645	9570	9571	1	1074	5	34
23	SINDHUDURG	2108	1887	1888	1	220	1	7
24	WASHIM	10335	7214	7215	1	3120	7	98
25	BEED	25767	14550	14550	0	11217	14	351
26	BHANDARA	15566	12386	12386	0	3180	4	99
27	DHULE	18081	13076	13076	0	5005	10	156
28	KOLHAPUR	12528	10592	10592	0	1936	3	61
29	NANDED	21375	11951	11951	0	9424	8	295
30	PALGHAR	11208	7433	7433	0	3775	6	118
31	PARBHANI	17646	13246	13246	0	4400	4	138
32	PUNE	12773	10032	10032	0	2741	5	86
33	THANE	4971	3778	3778	0	1193	2	37
34	WARDHA	11222	8722	8722	0	2500	6	78
<b>Total</b>		<b>559615</b>	<b>404124</b>	<b>404268</b>	<b>144</b>	<b>155347</b>	<b>290</b>	<b>4855</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10972	0	39529	0	23423
2	AMRAVATI DIV.	0	31036	0	32529	0	16179
3	AURANGABAD DIV.	0	20471	0	53602	0	24208
4	NAGPUR DIV.	0	10604	0	21367	0	13362
5	KONKAN DIV.	0	421	0	3693	0	3644
6	PUNE DIV.	0	9966	0	16633	0	7037
	<b>Total</b>	<b>0</b>	<b>83470</b>	<b>0</b>	<b>167353</b>	<b>0</b>	<b>87853</b>

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	14
THANE	95
RATNAGIRI	100
PALGHAR	208
GADCHIROLI	362
SANGLI	521
KOLHAPUR	547
SATARA	915
DHULE	1023
NASHIK	1158
PARBHANI	1177
NANDURBAR	1375
GONDIA	1459
WARDHA	1603
NAGPUR	1960
JALNA	1986
HINGOLI	2039
CHANDRAPUR	2148
PUNE	2239
LATUR	2351
AURANGABAD	2806
AHMEDNAGAR	3010
BHANDARA	3072
WASHIM	3117
OSMANABAD	3222
BEED	3411
NANDED	3479
AKOLA	4015
YAVATMAL	4054
JALGAON	4406
SOLAPUR	5744
BULDHANA	8287
AMRAVATI	11563

PMAY-G 2nd Ins Pending

SINDHUDURG	235
RATNAGIRI	429
RAIGAD	545
THANE	623
SATARA	1226
WARDHA	1264
OSMANABAD	1808
PALGHAR	1861
PUNE	2360
KOLHAPUR	2620
GADCHIROLI	2772
NAGPUR	2968
HINGOLI	3180
WASHIM	3272
AHMEDNAGAR	3896
SANGLI	3998
GONDIA	4370
LATUR	4443
JALNA	4572
CHANDRAPUR	4677
AKOLA	5172
BHANDARA	5316
AURANGABAD	5939
BULDHANA	6043
PARBHANI	6050
NASHIK	6127
SOLAPUR	6429
DHULE	6930
BEED	8373
AMRAVATI	8875
YAVATMAL	9167
NANDURBAR	10124
JALGAON	12452
NANDED	19237

PMAY-G 3rd Ins Pending

SINDHUDURG	310
RAIGAD	389
RATNAGIRI	443
THANE	602
WARDHA	969
KOLHAPUR	1005
PUNE	1072
SATARA	1088
NAGPUR	1440
HINGOLI	1490
SANGLI	1550
PALGHAR	1900
LATUR	1904
AKOLA	2057
GADCHIROLI	2311
SOLAPUR	2322
WASHIM	2331
BHANDARA	2465
AURANGABAD	2466
CHANDRAPUR	2725
PARBHANI	2763
JALNA	2964
BULDHANA	2986
AHMEDNAGAR	3056
OSMANABAD	3071
AMRAVATI	3342
GONDIA	3452
BEED	3571
DHULE	3830
NASHIK	4102
JALGAON	4342
YAVATMAL	5463
NANDED	5979
NANDURBAR	8093

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3010	0	3896	0	3056
2	AKOLA	0	4015	0	5172	0	2057
3	AMRAVATI	0	11563	0	8875	0	3342
4	AURANGABAD	0	2806	0	5939	0	2466
5	BEED	0	3411	0	8373	0	3571
6	BHANDARA	0	3072	0	5316	0	2465
7	BULDHANA	0	8287	0	6043	0	2986
8	CHANDRAPUR	0	2148	0	4677	0	2725
9	DHULE	0	1023	0	6930	0	3830
10	GADCHIROLI	0	362	0	2772	0	2311
11	GONDIA	0	1459	0	4370	0	3452
12	HINGOLI	0	2039	0	3180	0	1490
13	JALGAON	0	4406	0	12452	0	4342
14	JALNA	0	1986	0	4572	0	2964
15	LATUR	0	2351	0	4443	0	1904
16	NAGPUR	0	1960	0	2968	0	1440
17	NANDED	0	3479	0	19237	0	5979
18	NANDURBAR	0	1375	0	10124	0	8093
19	NASHIK	0	1158	0	6127	0	4102
20	OSMANABAD	0	3222	0	1808	0	3071
21	PARBHANI	0	1177	0	6050	0	2763
22	PUNE	0	2239	0	2360	0	1072
23	RAIGAD	0	14	0	545	0	389
24	RATNAGIRI	0	100	0	429	0	443
25	SANGLI	0	521	0	3998	0	1550
26	SATARA	0	915	0	1226	0	1088
27	SINDHUDURG	0	4	0	235	0	310
28	SOLAPUR	0	5744	0	6429	0	2322
29	THANE	0	95	0	623	0	602
30	WARDHA	0	1603	0	1264	0	969
31	WASHIM	0	3117	0	3272	0	2331
32	YAVATMAL	0	4054	0	9167	0	5463
33	PALGHAR	-1	208	0	1861	0	1900
34	KOLHAPUR	-6	547	0	2620	0	1005
	<b>Total</b>	<b>0</b>	<b>83470</b>	<b>0</b>	<b>167353</b>	<b>0</b>	<b>87853</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2118	0	9100	0	5425
2	AMRAVATI DIV.	0	2894	0	13038	0	6296
3	AURANGABAD DIV.	0	16205	0	29215	0	12891
4	NAGPUR DIV.	0	5598	0	8673	0	4057
5	KONKAN DIV.	0	1004	0	2978	0	1568
6	PUNE DIV.	0	1605	0	4628	0	2303
<b>Total</b>		<b>0</b>	<b>29424</b>	<b>0</b>	<b>67632</b>	<b>0</b>	<b>32540</b>

State Schemes 1st Ins Pending

SINDHUDURG	14
RATNAGIRI	58
NANDURBAR	81
SATARA	105
THANE	166
SANGLI	177
PUNE	261
WARDHA	326
KOLHAPUR	337
RAIGAD	356
NASHIK	375
AHMEDNAGAR	387
BULDHANA	399
PALGHAR	410
NAGPUR	427
DHULE	512
AKOLA	531
GADCHIROLI	532
WASHIM	547
BHANDARA	575
YAVATMAL	661
SOLAPUR	725
AMRAVATI	756
JALGAON	763
GONDIA	764
PARBHANI	876
JALNA	1165
LATUR	1458
OSMANABAD	1652
HINGOLI	2033
BEED	2543
AURANGABAD	2624
CHANDRAPUR	2974
NANDED	3854

State Schemes 2nd Ins Pending

SINDHUDURG	65
RATNAGIRI	165
THANE	401
SATARA	424
RAIGAD	549
SANGLI	822
PUNE	963
KOLHAPUR	974
NAGPUR	1012
NANDURBAR	1030
BHANDARA	1091
GONDIA	1122
WARDHA	1183
WASHIM	1372
SOLAPUR	1445
NASHIK	1563
GADCHIROLI	1673
PALGHAR	1798
AHMEDNAGAR	2061
BULDHANA	2080
JALGAON	2119
DHULE	2327
PARBHANI	2470
CHANDRAPUR	2592
AMRAVATI	2859
AKOLA	2894
HINGOLI	3152
JALNA	3265
OSMANABAD	3363
AURANGABAD	3614
LATUR	3765
YAVATMAL	3833
NANDED	4306
BEED	5280

State Schemes 3rd Ins Pending

SINDHUDURG	54
RATNAGIRI	140
THANE	204
SATARA	269
NAGPUR	289
KOLHAPUR	352
SANGLI	388
BHANDARA	389
WARDHA	424
RAIGAD	517
GONDIA	518
PUNE	612
PALGHAR	653
SOLAPUR	682
WASHIM	794
NASHIK	859
PARBHANI	871
DHULE	945
HINGOLI	962
AMRAVATI	986
AKOLA	1025
NANDURBAR	1030
CHANDRAPUR	1122
OSMANABAD	1270
JALGAON	1284
AHMEDNAGAR	1307
NANDED	1309
GADCHIROLI	1315
AURANGABAD	1529
BULDHANA	1549
LATUR	1886
YAVATMAL	1942
JALNA	2411
BEED	2653

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	387	0	2061	0	1307
2	AKOLA	0	531	0	2894	0	1025
3	AMRAVATI	0	756	0	2859	0	986
4	AURANGABAD	0	2624	0	3614	0	1529
5	BEED	0	2543	0	5280	0	2653
6	BHANDARA	0	575	0	1091	0	389
7	BULDHANA	0	399	0	2080	0	1549
8	CHANDRAPUR	0	2974	0	2592	0	1122
9	DHULE	0	512	0	2327	0	945
10	GADCHIROLI	0	532	0	1673	0	1315
11	GONDIA	0	764	0	1122	0	518
12	HINGOLI	0	2033	0	3152	0	962
13	JALGAON	0	763	0	2119	0	1284
14	JALNA	0	1165	0	3265	0	2411
15	KOLHAPUR	0	337	0	974	0	352
16	LATUR	0	1458	0	3765	0	1886
17	NAGPUR	0	427	0	1012	0	289
18	NANDED	0	3854	0	4306	0	1309
19	NANDURBAR	0	81	0	1030	0	1030
20	NASHIK	0	375	0	1563	0	859
21	OSMANABAD	0	1652	0	3363	0	1270
22	PALGHAR	0	410	0	1798	0	653
23	PARBHANI	0	876	0	2470	0	871
24	PUNE	0	261	0	963	0	612
25	RAIGAD	0	356	0	549	0	517
26	RATNAGIRI	0	58	0	165	0	140
27	SANGLI	0	177	0	822	0	388
28	SATARA	0	105	0	424	0	269
29	SINDHUDURG	0	14	0	65	0	54
30	SOLAPUR	0	725	0	1445	0	682
31	THANE	0	166	0	401	0	204
32	WARDHA	0	326	0	1183	0	424
33	WASHIM	0	547	0	1372	0	794
34	YAVATMAL	0	661	0	3833	0	1942
	<b>Total</b>	<b>0</b>	<b>29424</b>	<b>0</b>	<b>67632</b>	<b>0</b>	<b>32540</b>

## प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले  
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2559	1803	3141	1409	51
AKOLA	4237	3528	3589	870	585
AMRAVATI	7573	5656	7127	1480	1031
AURANGABAD	2413	2255	4901	1061	406
BEED	2188	1867	6655	1614	469
BHANDARA	7078	5313	4825	744	2187
BULDHANA	2646	2164	3957	836	700
CHANDRAPUR	3053	1961	3506	689	289
DHULE	5714	4108	5926	2178	1575
GADCHIROLI	4058	2494	2281	1192	908
GONDIA	1988	1913	3184	1021	147
HINGOLI	1036	671	2616	469	99
JALGAON	7906	6660	11135	2006	678
JALNA	1371	1084	3144	766	279
KOLHAPUR	1968	748	2387	284	92
LATUR	798	729	2697	445	47
NAGPUR	3386	2354	2576	446	581
NANDED	9670	9180	14750	1998	356
NANDURBAR	11623	10023	7004	4650	5128
NASHIK	7084	3587	4815	2057	1544
OSMANABAD	1044	585	1249	466	7
PALGHAR	918	655	1359	670	436
PARBHANI	860	738	4342	553	93
PUNE	2265	1740	1953	499	450
RAIGAD	741	240	489	241	163
RATNAGIRI	182	44	341	126	53
SANGLI	3043	2333	3510	532	138
SATARA	708	386	875	221	137
SINDDHURG	144	89	205	66	26
SOLAPUR	4971	4604	5043	1220	502
THANE	209	188	578	162	150
WARDHA	1173	811	949	213	235
WASHIM	1228	869	2644	435	94
YAVATMAL	6557	4397	6979	1820	1660
