



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०६.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९९०१	०	१०४०८८१	१४६	०	०	०
राज्य योजना	५६०३९०	२४२	४०४४९७	५६	०	०	०
एकूण	१९७०२९१	२४२	१४४५३७८	२०२	०	०	०

PMAY-G Completion Progress Bar

73.8%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.2%


State Schemes: Incomplete Houses bifurcation

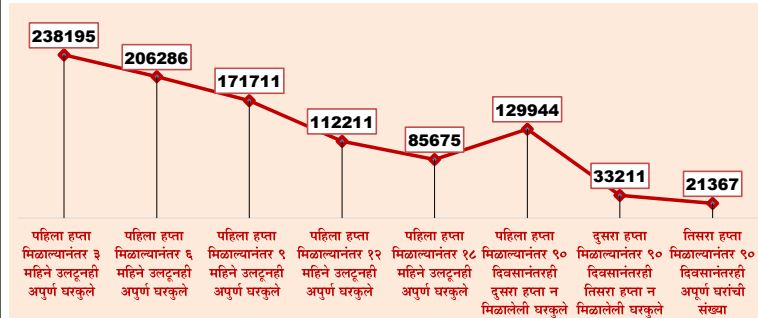


Abhiyan Achievement Day 167

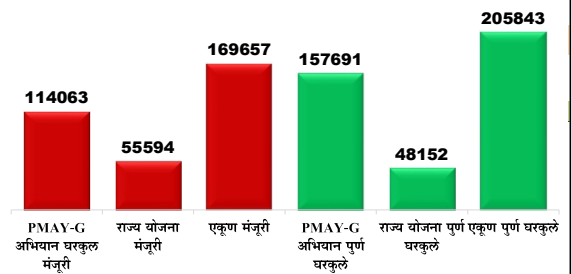

PMAY-G : House completion (Abhiyan Achievement)

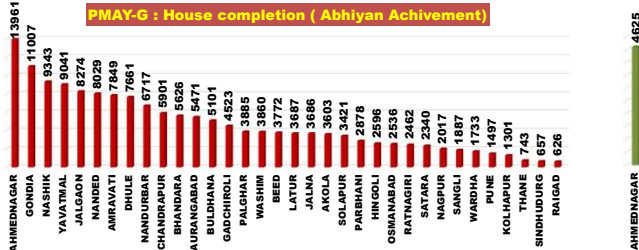

State Schemes : House completion (Abhiyan Achievement)

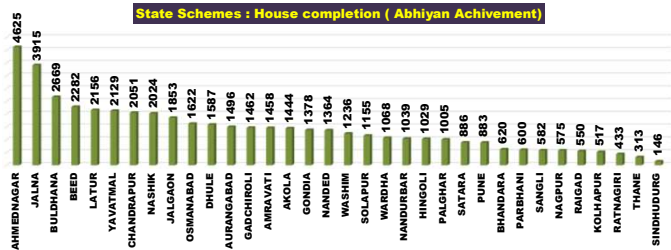


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	05.05.2023	06.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414867	413718	413718	0	1149
2	AMRAVATI DIV.	274810	274354	274354	0	456
3	AURANGABAD DIV.	238003	237302	237302	0	701
4	NAGPUR DIV.	291938	291278	291278	0	660
5	KONKAN DIV.	69835	69626	69626	0	209
6	PUNE DIV.	124547	123623	123623	0	924
Total		1414000	1409901	1409901	0	4099

Sr. No.	District	Target (PWL+Awaas Plus)	05.05.2023	06.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60791	60756	60756	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95522	95271	95271	0	251
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BHANDARA	64996	64930	64930	0	66
7	BULDHANA	44752	44713	44713	0	39
8	CHANDRAPUR	43097	42975	42975	0	122
9	DHULE	64999	64917	64917	0	82
10	GADCHIROLI	31703	31621	31621	0	82
11	GONDIA	96493	96144	96144	0	349
12	HINGOLI	18109	18083	18083	0	26
13	JALGAON	79735	79403	79403	0	332
14	JALNA	24038	24023	24023	0	15
15	KOLHAPUR	17662	17652	17652	0	10
16	LATUR	20679	20493	20493	0	186
17	NAGPUR	37016	37001	37001	0	15
18	NANDED	69533	69463	69463	0	70
19	NANDURBAR	119607	118959	118959	0	648
20	NASHIK	89735	89683	89683	0	52
21	OSMANABAD	14506	14411	14411	0	95
22	PALGHAR	35376	35188	35188	0	188
23	PARBHANI	19088	19062	19062	0	26
24	PUNE	20543	20529	20529	0	14
25	RAIGAD	9830	9820	9820	0	10
26	RATNAGIRI	9891	9885	9885	0	6
27	SANGLI	21836	21641	21641	0	195
28	SATARA	15347	15339	15339	0	8
29	SINDHUDURG	5133	5133	5133	0	0
30	SOLAPUR	49159	48462	48462	0	697
31	THANE	9605	9600	9600	0	5
32	WARDHA	18633	18607	18607	0	26
33	WASHIM	20390	20363	20363	0	27
34	YAVATMAL	65354	65229	65229	0	125
Total		1414000	1409901	1409901	0	4099

Remaining Sanction RANK


SINDHUDURG	0
THANE	5
RATNAGIRI	6
SATARA	8
KOLHAPUR	10
RAIGAD	10
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	15
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	27
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
BEED	57
BHANDARA	66
NANDED	70
DHULE	82
GADCHIROLI	82
OSMANABAD	95
CHANDRAPUR	122
YAVATMAL	125
LATUR	186
PALGHAR	188
SANGLI	195
AURANGABAD	226
AMRAVATI	251
JALGAON	332
GONDIA	349
NANDURBAR	648
SOLAPUR	697

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	418	144	274	-1
14	PARBHANI	332	15	317	331	54	277	-39
15	SATARA	1309	598	711	1304	630	674	-32
16	NASHIK	1824	1475	349	1803	1001	802	474
17	HINGOLI	1713	787	926	1713	466	1247	321
18	JALNA	1413	165	1248	1374	85	1289	80
19	CHANDRAPUR	2791	1463	1328	2748	1454	1294	9
20	WARDHA	2819	1284	1535	2803	1245	1558	39
21	NAGPUR	5134	3397	1737	5025	3423	1602	-26
22	JALGAON	22872	21026	1846	22945	21000	1945	26
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2044	255	1789	2310	255	2055	0
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	BHANDARA	5825	3230	2595	5674	3231	2443	-1
27	YAVATMAL	3437	1119	2318	3642	1181	2461	-62
28	WASHIM	3477	883	2594	3443	865	2578	18
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7365	3844	3521	-2
31	AHMEDNAGAR	7762	4828	2934	7759	4161	3598	667
32	SOLAPUR	7960	2595	5365	7248	1412	5836	1183
33	BULDHANA	15085	8586	6499	15213	7097	8116	1489
34	AMRAVATI	21721	11392	10329	21561	11389	10172	3
	Total	127640	73603	54037	127257	67580	59677	6186

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.05.2023	06.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	291278	238877	238935	58	52343	184	1745
2	NASHIK DIV.	413718	329436	329470	34	84248	275	2808
3	AURANGABAD DIV.	237302	140187	140216	29	97086	196	3236
4	AMRAVATI DIV.	274354	186593	186611	18	87743	176	2925
5	PUNE DIV.	123623	87864	87868	4	35755	63	1192
6	KONKAN DIV.	69626	57778	57781	3	11845	50	395
Total		1409901	1040735	1040881	146	369020	944	12301

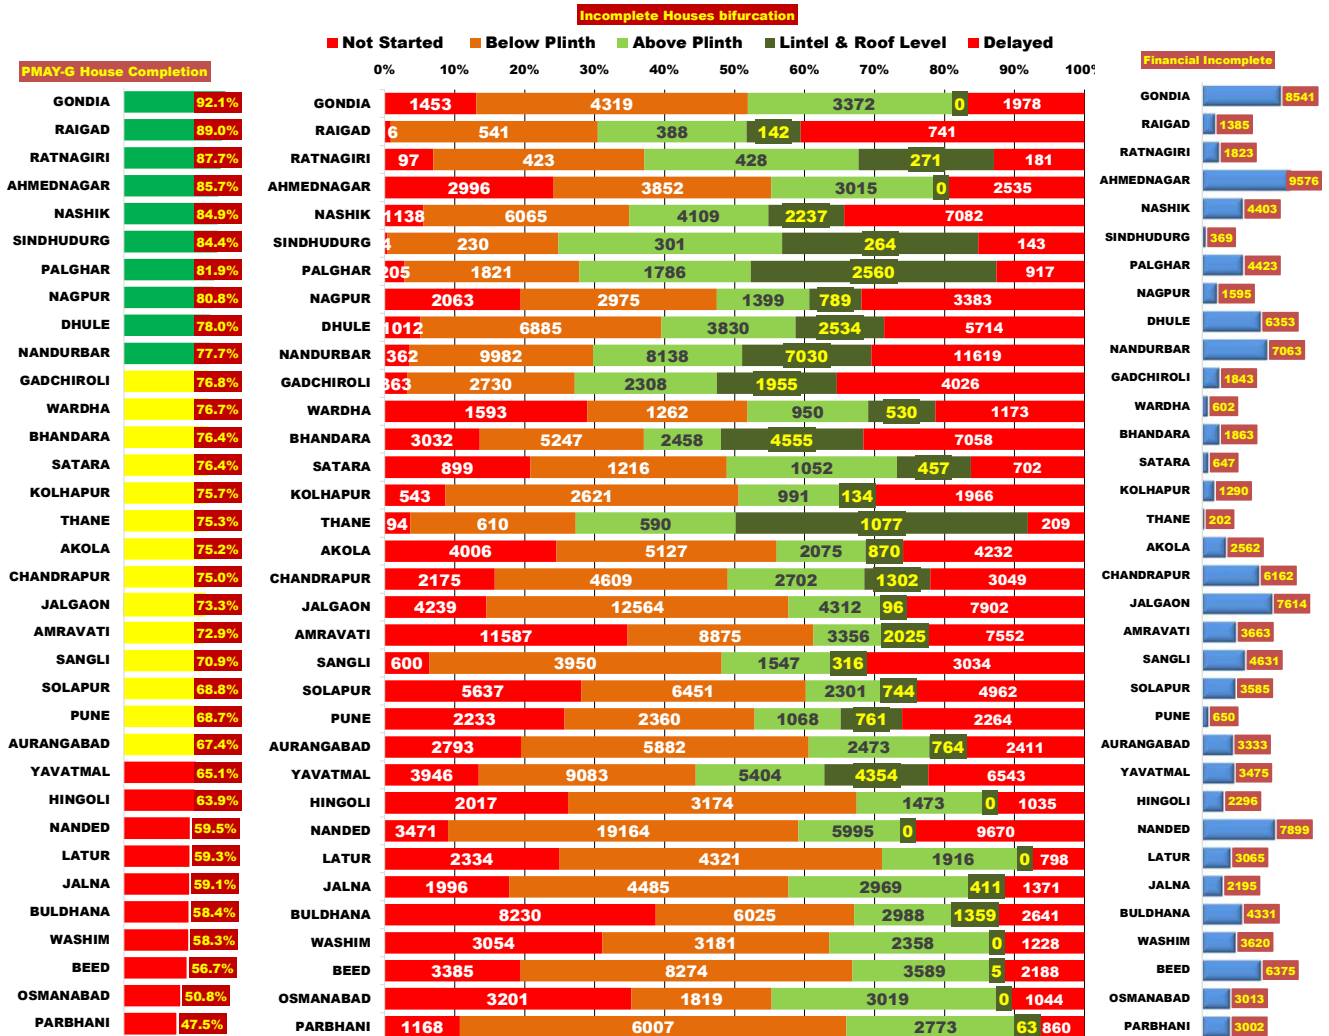

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.05.2023	06.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	96144	88550	88585	35	7559	66	252
2	AHMEDNAGAR	60756	52018	52041	23	8715	84	291
3	GADCHIROLI	31621	24269	24290	21	7331	27	244
4	AURANGABAD	36514	24584	24603	19	11911	33	397
5	JALGAON	79403	58181	58192	11	21211	50	707
6	AMRAVATI	95271	69466	69474	8	25797	47	860
7	PARBHANI	19062	9045	9051	6	10011	17	334
8	BULDHANA	44713	26118	26122	4	18591	31	620
9	YAVATMAL	65229	42445	42449	4	22780	54	759
10	NANDED	69463	41336	41339	3	28124	48	937
11	SANGLI	21641	15351	15354	3	6287	11	210
12	AKOLA	48778	36698	36700	2	12078	22	403
13	CHANDRAPUR	42975	32238	32240	2	10735	35	358
14	RATNAGIRI	9885	8664	8666	2	1219	15	41
15	OSMANABAD	14411	7315	7316	1	7095	15	237
16	PALGHAR	35188	28815	28816	1	6372	23	212
17	SOLAPUR	48462	33328	33329	1	15133	20	504
18	BEED	35253	20000	20000	0	15253	23	508
19	BHANDARA	64930	49638	49638	0	15292	34	510
20	DHULE	64917	50656	50656	0	14261	46	475
21	HINGOLI	18083	11554	11554	0	6529	16	218
22	JALNA	24023	14192	14192	0	9831	22	328
23	KOLHAPUR	17652	13363	13363	0	4289	8	143
24	LATUR	20493	12161	12161	0	8332	22	278
25	NAGPUR	37001	29910	29910	0	7091	12	236
26	NANDURBAR	118959	92447	92447	0	26512	40	884
27	NASHIK	89683	76134	76134	0	13549	56	452
28	PUNE	20529	14107	14107	0	6422	9	214
29	RAIGAD	9820	8736	8736	0	1084	4	36
30	SATARA	15339	11715	11715	0	3624	14	121
31	SINDHUDURG	5133	4334	4334	0	799	4	27
32	THANE	9600	7229	7229	0	2371	4	79
33	WARDHA	18607	14272	14272	0	4335	10	145
34	WASHIM	20363	11866	11866	0	8497	23	283
Total		1409901	1040735	1040881	146	369020	944	12301

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	05.05.2023	06.05.2023	Daily_Achievement	Remaining
1	AMRAVATI DIV.	110069	94214	94358	144	15711
2	AURANGABAD DIV.	200327	167348	167388	40	32939
3	NAGPUR DIV.	118430	93323	93361	38	25069
4	NASHIK DIV.	141552	110774	110794	20	30758
5	KONKAN DIV.	34744	31461	31461	0	3283
6	PUNE DIV.	65859	63028	63028	0	2831
Total		670981	560148	560390	242	110591


Sr. No.	District	Target	05.05.2023	06.05.2023	Daily_Achievement	Remaining
1	YAVATMAL	30045	26170	26314	144	3731
2	CHANDRAPUR	40285	27153	27191	38	13094
3	BEED	26878	25767	25803	36	1075
4	JALGAON	25851	22703	22723	20	3128
5	LATUR	28004	26294	26298	4	1706
6	AHMEDNAGAR	35298	32994	32994	0	2304
7	AKOLA	23681	17823	17823	0	5858
8	AMRAVATI	23224	19865	19865	0	3359
9	AURANGABAD	26141	23833	23833	0	2308
10	BHANDARA	17612	15568	15568	0	2044
11	BULDHANA	21616	20021	20021	0	1595
12	DHULE	21790	18081	18081	0	3709
13	GADCHIROLI	16834	15292	15292	0	1542
14	GONDIA	14261	12872	12872	0	1389
15	HINGOLI	27298	16132	16132	0	11166
16	JALNA	20609	19260	19260	0	1349
17	KOLHAPUR	13090	12529	12529	0	561
18	NAGPUR	16291	11216	11216	0	5075
19	NANDED	26760	21375	21375	0	5385
20	NANDURBAR	26578	14138	14138	0	12440
21	NASHIK	32035	22858	22858	0	9177
22	OSMANABAD	24853	17039	17039	0	7814
23	PALGHAR	11792	11208	11208	0	584
24	PARBHANI	19784	17648	17648	0	2136
25	PUNE	14672	12773	12773	0	1899
26	RAIGAD	7418	6475	6475	0	943
27	RATNAGIRI	7129	6691	6691	0	438
28	SANGLI	8732	8604	8604	0	128
29	SATARA	10647	10647	10647	0	0
30	SINDHUDURG	2141	2108	2108	0	33
31	SOLAPUR	18718	18475	18475	0	243
32	THANE	6264	4979	4979	0	1285
33	WARDHA	13147	11222	11222	0	1925
34	WASHIM	11503	10335	10335	0	1168
Total		670981	560148	560390	242	110591

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	561
PALGHAR	584
RAIGAD	943
BEED	1075
WASHIM	1168
THANE	1285
JALNA	1349
GONDIA	1389
GADCHIROLI	1542
BULDHANA	1595
LATUR	1706
PUNE	1899
WARDHA	1925
BHANDARA	2044
PARBHANI	2136
AHMEDNAGAR	2304
AURANGABAD	2308
JALGAON	3128
AMRAVATI	3359
DHULE	3709
YAVATMAL	3731
NAGPUR	5075
NANDED	5385
AKOLA	5858
OSMANABAD	7814
NASHIK	9177
HINGOLI	11166
NANDURBAR	12440
CHANDRAPUR	13094

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	05.05.2023	06.05.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	93361	69679	69699	20	23662	43	789
2	AMRAVATI DIV.	94358	65122	65134	12	29224	54	974
3	AURANGABAD DIV.	167388	104560	104570	10	62818	87	2094
4	NASHIK DIV.	110794	89176	89185	9	21609	67	720
5	PUNE DIV.	63028	52083	52088	5	10940	24	365
6	KONKAN DIV.	31461	23821	23821	0	7640	15	255
Total		560390	404441	404497	56	155893	288	5196

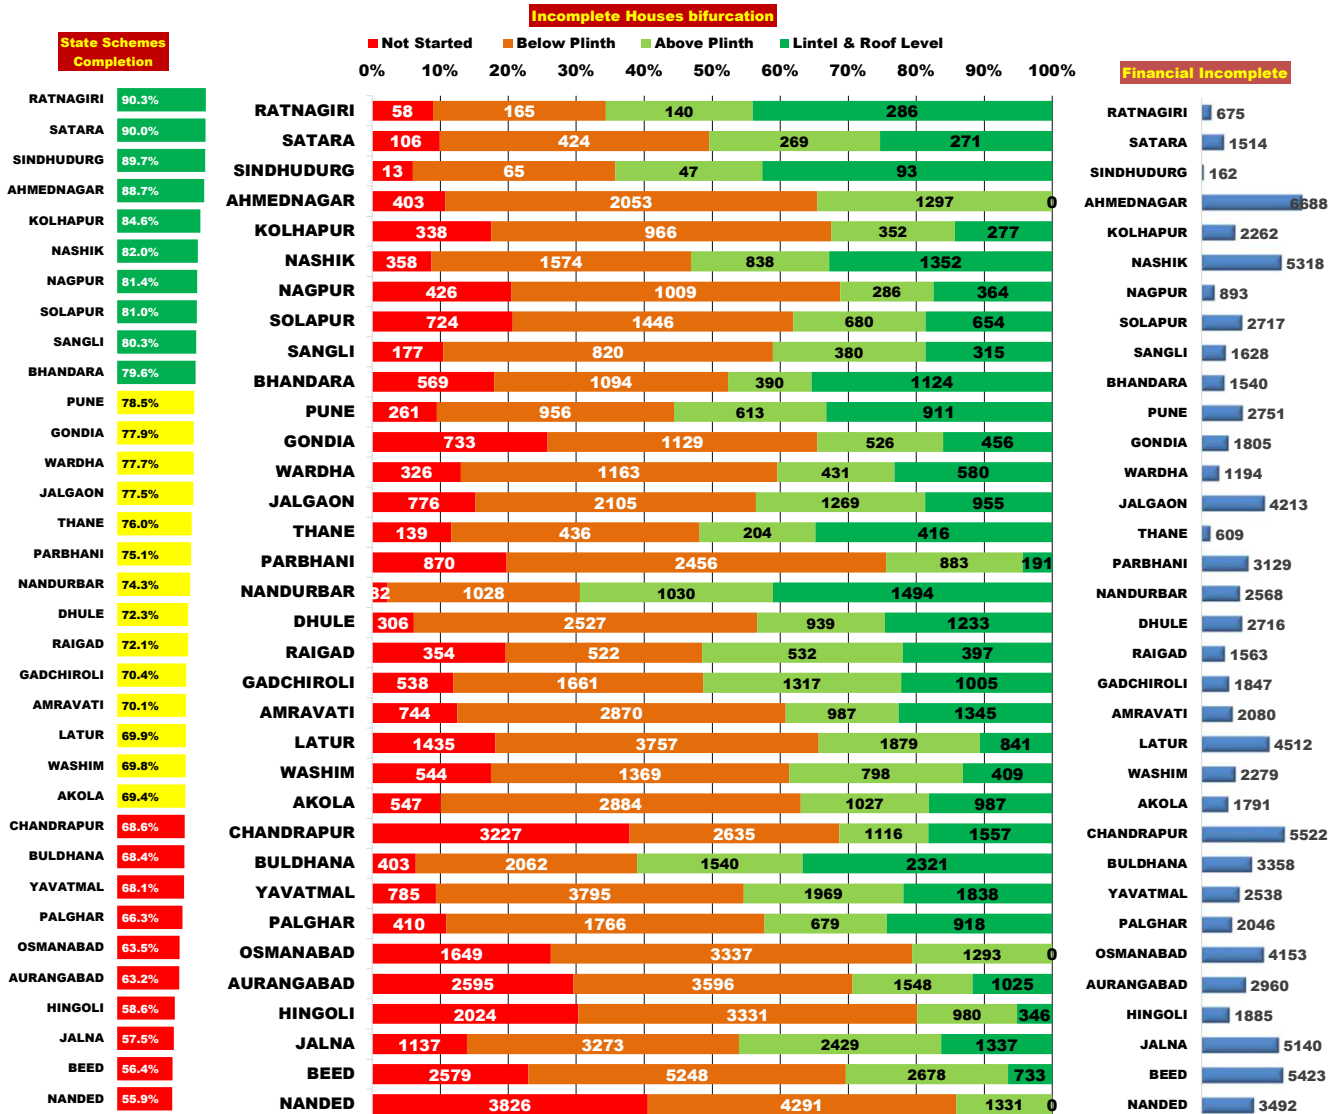

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	05.05.2023	06.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	12872	10015	10028	13	2844	8	95
2	AHMEDNAGAR	32994	29242	29251	9	3743	28	125
3	AURANGABAD	23833	15060	15069	9	8764	9	292
4	BULDHANA	20021	13688	13695	7	6326	16	211
5	GADCHIROLI	15292	10764	10771	7	4521	9	151
6	AMRAVATI	19865	13916	13919	3	5946	9	198
7	SOLAPUR	18475	14968	14971	3	3504	7	117
8	AKOLA	17823	12376	12378	2	5445	9	182
9	SANGLI	8604	6910	6912	2	1692	3	56
10	LATUR	26298	18385	18386	1	7912	13	264
11	BEED	25803	14565	14565	0	11238	14	375
12	BHANDARA	15568	12391	12391	0	3177	4	106
13	CHANDRAPUR	27191	18656	18656	0	8535	12	285
14	DHULE	18081	13076	13076	0	5005	10	167
15	HINGOLI	16132	9451	9451	0	6681	6	223
16	JALGAON	22723	17618	17618	0	5105	11	170
17	JALNA	19260	11084	11084	0	8176	23	273
18	KOLHAPUR	12529	10596	10596	0	1933	3	64
19	NAGPUR	11216	9131	9131	0	2085	3	70
20	NANDED	21375	11953	11953	0	9422	8	314
21	NANDURBAR	14138	10504	10504	0	3634	6	121
22	NASHIK	22858	18736	18736	0	4122	12	137
23	OSMANABAD	17039	10814	10814	0	6225	10	208
24	PALGHAR	11208	7435	7435	0	3773	6	126
25	PARBHANI	17648	13248	13248	0	4400	4	147
26	PUNE	12773	10032	10032	0	2741	5	91
27	RAIGAD	6475	4670	4670	0	1805	3	60
28	RATNAGIRI	6691	6042	6042	0	649	3	22
29	SATARA	10647	9577	9577	0	1070	5	36
30	SINDHUDURG	2108	1890	1890	0	218	1	7
31	THANE	4979	3784	3784	0	1195	2	40
32	WARDHA	11222	8722	8722	0	2500	6	83
33	WASHIM	10335	7215	7215	0	3120	7	104
34	YAVATMAL	26314	17927	17927	0	8387	13	280
Total		560390	404441	404497	56	155893	288	5196

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10747	0	39348	0	23404
2	AMRAVATI DIV.	0	30756	0	32291	0	16181
3	AURANGABAD DIV.	0	20334	0	53126	0	24207
4	NAGPUR DIV.	0	10466	0	21142	0	13189
5	KONKAN DIV.	0	413	0	3625	0	3493
6	PUNE DIV.	0	9786	0	16598	0	6959
	Total	0	82502	0	166130	0	87433

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	13
THANE	94
RATNAGIRI	97
PALGHAR	205
GADCHIROLI	338
SANGLI	474
KOLHAPUR	543
SATARA	899
DHULE	1012
NASHIK	1138
PARBHANI	1168
NANDURBAR	1362
GONDIA	1453
WARDHA	1593
NAGPUR	1928
JALNA	1966
HINGOLI	2017
CHANDRAPUR	2122
PUNE	2233
LATUR	2334
AURANGABAD	2792
AHMEDNAGAR	2996
BHANDARA	3032
WASHIM	3051
OSMANABAD	3201
BEED	3385
NANDED	3471
YAVATMAL	3939
AKOLA	4006
JALGAON	4239
SOLAPUR	5637
BULDHANA	8219
AMRAVATI	11541

PMAY-G 2nd Ins Pending

SINDHUDURG	230
RATNAGIRI	423
RAIGAD	541
THANE	610
SATARA	1216
WARDHA	1262
OSMANABAD	1819
PALGHAR	1821
PUNE	2360
KOLHAPUR	2621
GADCHIROLI	2730
NAGPUR	2975
HINGOLI	3174
WASHIM	3181
AHMEDNAGAR	3852
SANGLI	3950
GONDIA	4319
LATUR	4321
JALNA	4485
CHANDRAPUR	4609
AKOLA	5127
BHANDARA	5247
AURANGABAD	5882
PARBHANI	6007
BULDHANA	6025
NASHIK	6065
SOLAPUR	6451
DHULE	6885
BEED	8274
AMRAVATI	8875
YAVATMAL	9083
NANDURBAR	9982
JALGAON	12564
NANDED	19164

PMAY-G 3rd Ins Pending

SINDHUDURG	301
RAIGAD	388
RATNAGIRI	428
THANE	590
WARDHA	950
KOLHAPUR	991
SATARA	1052
PUNE	1068
NAGPUR	1399
HINGOLI	1473
SANGLI	1547
PALGHAR	1786
LATUR	1916
AKOLA	2075
SOLAPUR	2301
GADCHIROLI	2308
WASHIM	2358
BHANDARA	2458
AURANGABAD	2473
CHANDRAPUR	2702
PARBHANI	2773
JALNA	2969
BULDHANA	2988
AHMEDNAGAR	3015
OSMANABAD	3019
AMRAVATI	3356
GONDIA	3372
BEED	3589
DHULE	3830
NASHIK	4109
JALGAON	4312
YAVATMAL	5404
NANDED	5995
NANDURBAR	8138

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	2996	0	3852	0	3015
2	AKOLA	0	4006	0	5127	0	2075
3	AMRAVATI	0	11541	0	8875	0	3356
4	AURANGABAD	0	2792	0	5882	0	2473
5	BEED	0	3385	0	8274	0	3589
6	BHANDARA	0	3032	0	5247	0	2458
7	BULDHANA	0	8219	0	6025	0	2988
8	CHANDRAPUR	0	2122	0	4609	0	2702
9	DHULE	0	1012	0	6885	0	3830
10	GADCHIROLI	0	338	0	2730	0	2308
11	GONDIA	0	1453	0	4319	0	3372
12	HINGOLI	0	2017	0	3174	0	1473
13	JALGAON	0	4239	0	12564	0	4312
14	JALNA	0	1966	0	4485	0	2969
15	KOLHAPUR	0	543	0	2621	0	991
16	LATUR	0	2334	0	4321	0	1916
17	NAGPUR	0	1928	0	2975	0	1399
18	NANDED	0	3471	0	19164	0	5995
19	NANDURBAR	0	1362	0	9982	0	8138
20	NASHIK	0	1138	0	6065	0	4109
21	OSMANABAD	0	3201	0	1819	0	3019
22	PALGHAR	0	205	0	1821	0	1786
23	PARBHANI	0	1168	0	6007	0	2773
24	PUNE	0	2233	0	2360	0	1068
25	RAIGAD	0	13	0	541	0	388
26	RATNAGIRI	0	97	0	423	0	428
27	SANGLI	0	474	0	3950	0	1547
28	SATARA	0	899	0	1216	0	1052
29	SINDHUDURG	0	4	0	230	0	301
30	SOLAPUR	0	5637	0	6451	0	2301
31	THANE	0	94	0	610	0	590
32	WARDHA	0	1593	0	1262	0	950
33	WASHIM	0	3051	0	3181	0	2358
34	YAVATMAL	0	3939	0	9083	0	5404
	Total	0	82502	0	166130	0	87433

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	1925	0	9287	0	5373
2	AMRAVATI DIV.	0	3023	0	12980	0	6321
3	AURANGABAD DIV.	0	16115	0	29289	0	13021
4	NAGPUR DIV.	0	5819	0	8691	0	4066
5	KONKAN DIV.	0	974	0	2954	0	1602
6	PUNE DIV.	0	1606	0	4612	0	2294
Total		0	29462	0	67813	0	32677

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
NANDURBAR	82
SATARA	106
THANE	139
SANGLI	177
PUNE	261
DHULE	306
WARDHA	326
KOLHAPUR	338
RAIGAD	354
NASHIK	358
AHMEDNAGAR	403
BULDHANA	403
PALGHAR	410
NAGPUR	426
GADCHIROLI	538
WASHIM	544
AKOLA	547
BHANDARA	569
SOLAPUR	724
GONDIA	733
AMRAVATI	744
JALGAON	776
YAVATMAL	785
PARBHANI	870
JALNA	1137
LATUR	1435
OSMANABAD	1649
HINGOLI	2024
BEED	2579
AURANGABAD	2595
CHANDRAPUR	3227
NANDED	3826

State Schemes 2nd Ins Pending

SINDHUDURG	65
RATNAGIRI	165
SATARA	424
THANE	436
RAIGAD	522
SANGLI	820
PUNE	956
KOLHAPUR	966
NAGPUR	1009
NANDURBAR	1028
BHANDARA	1094
GONDIA	1129
WARDHA	1163
WASHIM	1369
SOLAPUR	1446
NASHIK	1574
GADCHIROLI	1661
PALGHAR	1766
AHMEDNAGAR	2053
BULDHANA	2062
JALGAON	2105
PARBHANI	2456
DHULE	2527
CHANDRAPUR	2635
AMRAVATI	2870
AKOLA	2884
JALNA	3273
HINGOLI	3331
OSMANABAD	3337
AURANGABAD	3596
LATUR	3757
YAVATMAL	3795
NANDED	4291
BEED	5248

State Schemes 3rd Ins Pending

SINDHUDURG	47
RATNAGIRI	140
THANE	204
SATARA	269
NAGPUR	286
KOLHAPUR	352
SANGLI	380
BHANDARA	390
WARDHA	431
GONDIA	526
RAIGAD	532
PUNE	613
PALGHAR	679
SOLAPUR	680
WASHIM	798
NASHIK	838
PARBHANI	883
DHULE	939
HINGOLI	980
AMRAVATI	987
AKOLA	1027
NANDURBAR	1030
CHANDRAPUR	1116
JALGAON	1269
OSMANABAD	1293
AHMEDNAGAR	1297
GADCHIROLI	1317
NANDED	1331
BULDHANA	1540
AURANGABAD	1548
LATUR	1879
YAVATMAL	1969
JALNA	2429
BEED	2678

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	403	0	2053	0	1297
2	AKOLA	0	547	0	2884	0	1027
3	AMRAVATI	0	744	0	2870	0	987
4	AURANGABAD	0	2595	0	3596	0	1548
5	BEED	0	2579	0	5248	0	2678
6	BHANDARA	0	569	0	1094	0	390
7	BULDHANA	0	403	0	2062	0	1540
8	CHANDRAPUR	0	3227	0	2635	0	1116
9	DHULE	0	306	0	2527	0	939
10	GADCHIROLI	0	538	0	1661	0	1317
11	GONDIA	0	733	0	1129	0	526
12	HINGOLI	0	2024	0	3331	0	980
13	JALGAON	0	776	0	2105	0	1269
14	JALNA	0	1137	0	3273	0	2429
15	KOLHAPUR	0	338	0	966	0	352
16	LATUR	0	1435	0	3757	0	1879
17	NAGPUR	0	426	0	1009	0	286
18	NANDED	0	3826	0	4291	0	1331
19	NANDURBAR	0	82	0	1028	0	1030
20	NASHIK	0	358	0	1574	0	838
21	OSMANABAD	0	1649	0	3337	0	1293
22	PALGHAR	0	410	0	1766	0	679
23	PARBHANI	0	870	0	2456	0	883
24	PUNE	0	261	0	956	0	613
25	RAIGAD	0	354	0	522	0	532
26	RATNAGIRI	0	58	0	165	0	140
27	SANGLI	0	177	0	820	0	380
28	SATARA	0	106	0	424	0	269
29	SINDHUDURG	0	13	0	65	0	47
30	SOLAPUR	0	724	0	1446	0	680
31	THANE	0	139	0	436	0	204
32	WARDHA	0	326	0	1163	0	431
33	WASHIM	0	544	0	1369	0	798
34	YAVATMAL	0	785	0	3795	0	1969
	Total	0	29462	0	67813	0	32677

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2535	1797	3151	1440	53
AKOLA	4232	3525	3558	865	586
AMRAVATI	7552	5644	7147	1490	1039
AURANGABAD	2411	2255	4876	1066	408
BEED	2188	1867	6631	1573	470
BHANDARA	7058	5303	4756	740	2184
BULDHANA	2641	2159	3934	839	703
CHANDRAPUR	3049	1958	3480	692	289
DHULE	5714	4108	5885	2163	1575
GADCHIROLI	4026	2475	2246	1182	895
GONDIA	1978	1904	3212	1025	147
HINGOLI	1035	670	2598	468	100
JALGAON	7902	6657	11095	1984	684
JALNA	1371	1084	3073	751	287
KOLHAPUR	1966	747	2384	278	91
LATUR	798	729	2627	428	47
NAGPUR	3383	2351	2570	445	581
NANDED	9670	9180	14754	2002	369
NANDURBAR	11619	10021	7032	4636	5140
NASHIK	7082	3586	4771	2048	1542
OSMANABAD	1044	585	1241	446	7
PALGHAR	917	654	1320	624	438
PARBHANI	860	738	4425	564	98
PUNE	2264	1739	1950	498	452
RAIGAD	741	240	489	238	165
RATNAGIRI	181	44	335	123	58
SANGLI	3034	2327	3434	523	143
SATARA	702	385	852	213	140
SINDHUDURG	143	89	201	64	26
SOLAPUR	4962	4596	5012	1206	501
THANE	209	188	566	157	150
WARDHA	1173	811	950	208	237
WASHIM	1228	869	2520	421	94
YAVATMAL	6543	4390	6869	1811	1668
