



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ०९.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९८७२	०	१०४१८४८	७००	०	०	०
राज्य योजना	५६१३२३	९२८	४०४८१८	२२४	०	०	०
एकूण	१९७११९५	९२८	१४४६६६६	९२४	०	०	०

PMAY-G Completion Progress Bar

73.9%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

72.1%


State Schemes: Incomplete Houses bifurcation

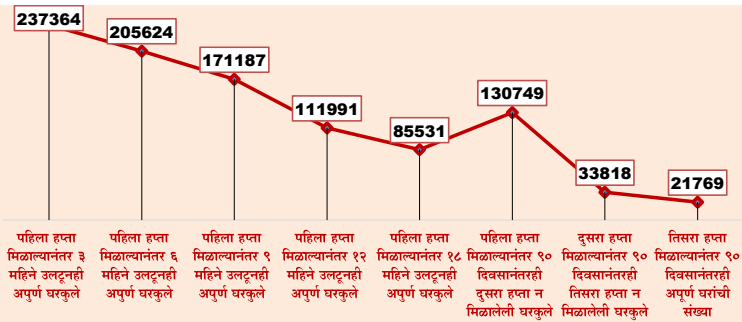


Abhiyan Achievement Day 170

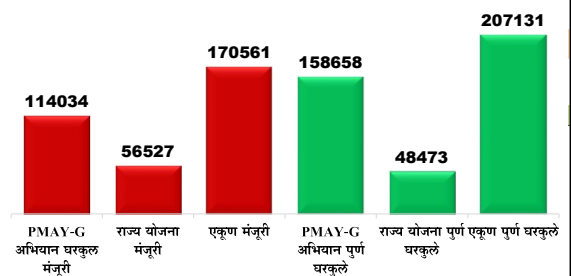

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	08.05.2023	09.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414863	413718	413697	0	1166
2	AMRAVATI DIV.	274802	274354	274354	0	448
3	AURANGABAD DIV.	238003	237302	237302	0	701
4	NAGPUR DIV.	291929	291278	291271	0	658
5	KONKAN DIV.	69835	69626	69626	0	209
6	PUNE DIV.	124520	123623	123622	0	898
Total		1413952	1409901	1409872	0	4080

Sr. No.	District	Target (PWL+Awaas Plus)	08.05.2023	09.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60791	60756	60756	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95514	95271	95271	0	243
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BHANDARA	64987	64930	64930	0	57
7	BULDHANA	44752	44713	44713	0	39
8	CHANDRAPUR	43097	42975	42975	0	122
9	DHULE	64999	64917	64917	0	82
10	GONDIA	96493	96144	96144	0	349
11	HINGOLI	18109	18083	18083	0	26
12	JALNA	24038	24023	24023	0	15
13	KOLHAPUR	17660	17652	17652	0	8
14	LATUR	20679	20493	20493	0	186
15	NANDED	69533	69463	69463	0	70
16	NANDURBAR	119607	118959	118959	0	648
17	NASHIK	89735	89683	89683	0	52
18	OSMANABAD	14506	14411	14411	0	95
19	PALGHAR	35376	35188	35188	0	188
20	PARBHANI	19088	19062	19062	0	26
21	PUNE	20543	20529	20529	0	14
22	RAIGAD	9830	9820	9820	0	10
23	RATNAGIRI	9891	9885	9885	0	6
24	SANGLI	21813	21641	21641	0	172
25	SINDHUDURG	5133	5133	5133	0	0
26	SOLAPUR	49159	48462	48462	0	697
27	THANE	9605	9600	9600	0	5
28	WARDHA	18633	18607	18607	0	26
29	WASHIM	20390	20363	20363	0	27
30	YAVATMAL	65354	65229	65229	0	125
31	NAGPUR	37016	37001	37000	-1	16
32	SATARA	15345	15339	15338	-1	7
33	GADCHIROLI	31703	31621	31615	-6	88
34	JALGAON	79731	79403	79382	-21	349
Total		1413952	1409901	1409872	0	4080

Remaining Sanction RANK


SINDHUDURG	0
THANE	5
RATNAGIRI	6
SATARA	7
KOLHAPUR	8
RAIGAD	10
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	16
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	27
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
BEED	57
BHANDARA	57
NANDED	70
DHULE	82
GADCHIROLI	88
OSMANABAD	95
CHANDRAPUR	122
YAVATMAL	125
SANGLI	172
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	243
GONDIA	349
JALGAON	349
NANDURBAR	648
SOLAPUR	697

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	418	144	274	-1
14	PARBHANI	332	15	317	331	54	277	-39
15	SATARA	1309	598	711	1304	630	674	-32
16	NASHIK	1824	1475	349	1803	1001	802	474
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2748	1459	1289	4
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2828	1298	1530	-14
21	NAGPUR	5134	3397	1737	5025	3425	1600	-28
22	JALGAON	22872	21026	1846	22932	20997	1935	29
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2044	255	1789	2310	258	2052	-3
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	BHANDARA	5825	3230	2595	5674	3231	2443	-1
27	YAVATMAL	3437	1119	2318	3642	1181	2461	-62
28	WASHIM	3477	883	2594	3443	865	2578	18
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7365	3901	3464	-59
31	AHMEDNAGAR	7762	4828	2934	7759	4161	3598	667
32	SOLAPUR	7960	2595	5365	7248	1412	5836	1183
33	BULDHANA	15085	8586	6499	15213	7276	7937	1310
34	AMRAVATI	21721	11392	10329	21561	11389	10172	3
	Total	127640	73603	54037	127269	67876	59393	5966

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	08.05.2023	09.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NASHIK DIV.	413697	329523	329737	214	83960	272	3110
2	NAGPUR DIV.	291271	239020	239234	214	52037	183	1927
3	AURANGABAD DIV.	237302	140266	140348	82	96954	193	3591
4	AMRAVATI DIV.	274354	186670	186751	81	87603	174	3245
5	PUNE DIV.	123622	87872	87927	55	35695	62	1322
6	KONKAN DIV.	69626	57797	57851	54	11775	50	436
Total		1409872	1041148	1041848	700	368024	933	13631

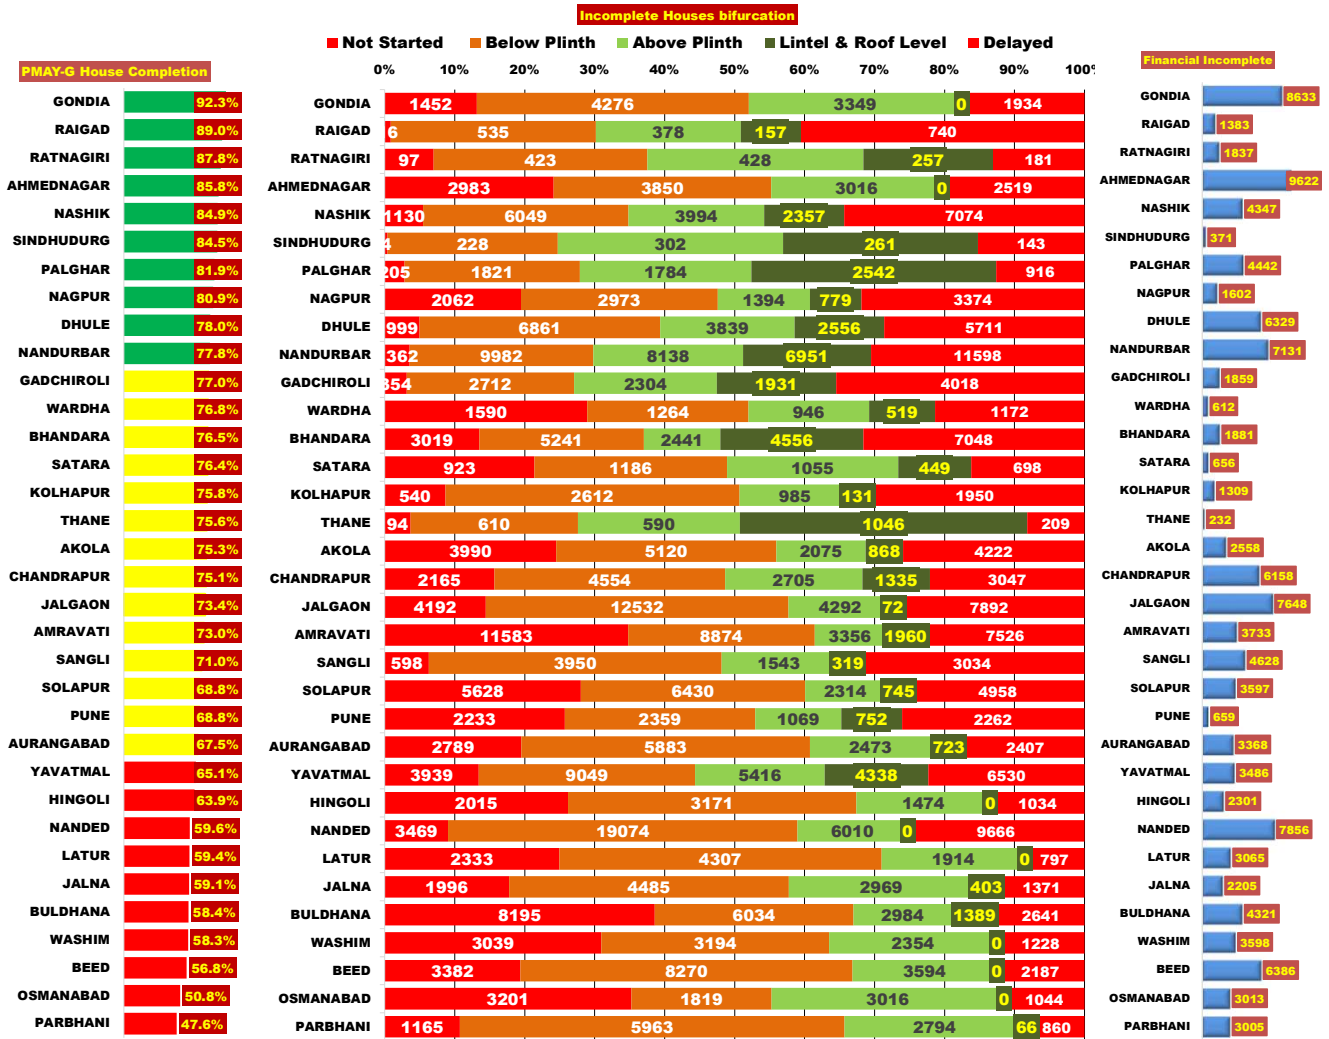

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	08.05.2023	09.05.2023	Daily_Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	96144	88646	88738	92	7406	66	274
2	JALGAON	79382	58213	58294	81	21088	49	781
3	NANDURBAR	118959	92462	92526	64	26433	40	979
4	GADCHIROLI	31615	24292	24339	47	7276	27	269
5	AHMEDNAGAR	60756	52056	52102	46	8654	82	321
6	AMRAVATI	95271	69498	69544	46	25727	47	953
7	AURANGABAD	36514	24609	24647	38	11867	32	440
8	BHANDARA	64930	49639	49673	34	15257	33	565
9	THANE	9600	7239	7260	21	2340	5	87
10	YAVATMAL	65229	42473	42494	21	22735	53	842
11	NANDED	69463	41349	41367	18	28096	47	1041
12	KOLHAPUR	17652	13367	13384	17	4268	8	158
13	NASHIK	89683	76136	76153	17	13530	55	501
14	PALGHAR	35188	28820	28836	16	6352	23	235
15	SOLAPUR	48462	33329	33345	16	15117	20	560
16	NAGPUR	37000	29912	29927	15	7073	12	262
17	WARDHA	18607	14273	14288	15	4319	10	160
18	AKOLA	48778	36711	36725	14	12053	21	446
19	RATNAGIRI	9885	8668	8680	12	1205	15	45
20	CHANDRAPUR	42975	32258	32269	11	10706	35	397
21	BEED	35253	20000	20010	10	15243	22	565
22	SATARA	15338	11715	11725	10	3613	14	134
23	PUNE	20529	14107	14116	9	6413	9	238
24	DHULE	64917	50656	50662	6	14255	45	528
25	PARBHANI	19062	9068	9074	6	9988	17	370
26	JALNA	24023	14196	14200	4	9823	22	364
27	SINDHUDURG	5133	4334	4338	4	795	4	29
28	HINGOLI	18083	11560	11563	3	6520	15	241
29	LATUR	20493	12168	12171	3	8322	22	308
30	SANGLI	21641	15354	15357	3	6284	11	233
31	RAIGAD	9820	8736	8737	1	1083	4	40
32	BULDHANA	44713	26122	26122	0	18591	30	689
33	OSMANABAD	14411	7316	7316	0	7095	15	263
34	WASHIM	20363	11866	11866	0	8497	23	315
Total		1409872	1041148	1041848	700	368024	933	13631

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	08.05.2023	09.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	93361	93861	500	24569
2	NASHIK DIV.	141552	110794	111029	235	30523
3	AURANGABAD DIV.	200327	167388	167494	106	32833
4	AMRAVATI DIV.	110069	94363	94450	87	15619
5	KONKAN DIV.	34744	31461	31461	0	3283
6	PUNE DIV.	65859	63028	63028	0	2831
Total		670981	560395	561323	928	109658


Sr. No.	District	Target	08.05.2023	09.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	27191	27648	457	12637
2	AHMEDNAGAR	35298	32994	33220	226	2078
3	YAVATMAL	30045	26314	26381	67	3664
4	BEED	26878	25803	25860	57	1018
5	GONDIA	14261	12872	12896	24	1365
6	NANDED	26760	21375	21396	21	5364
7	WASHIM	11503	10335	10352	17	1151
8	LATUR	28004	26298	26312	14	1692
9	OSMANABAD	24853	17039	17053	14	7800
10	BHANDARA	17612	15568	15576	8	2036
11	GADCHIROLI	16834	15292	15298	6	1536
12	DHULE	21790	18081	18086	5	3704
13	NAGPUR	16291	11216	11221	5	5070
14	NASHIK	32035	22858	22862	4	9173
15	AMRAVATI	23224	19870	19873	3	3351
16	AKOLA	23681	17823	17823	0	5858
17	AURANGABAD	26141	23833	23833	0	2308
18	BULDHANA	21616	20021	20021	0	1595
19	HINGOLI	27298	16132	16132	0	11166
20	JALGAON	25851	22723	22723	0	3128
21	JALNA	20609	19260	19260	0	1349
22	KOLHAPUR	13090	12529	12529	0	561
23	NANDURBAR	26578	14138	14138	0	12440
24	PALGHAR	11792	11208	11208	0	584
25	PARBHANI	19784	17648	17648	0	2136
26	PUNE	14672	12773	12773	0	1899
27	RAIGAD	7418	6475	6475	0	943
28	RATNAGIRI	7129	6691	6691	0	438
29	SANGLI	8732	8604	8604	0	128
30	SATARA	10647	10647	10647	0	0
31	SINDHUDURG	2141	2108	2108	0	33
32	SOLAPUR	18718	18475	18475	0	243
33	THANE	6264	4979	4979	0	1285
34	WARDHA	13147	11222	11222	0	1925
Total		670981	560395	561323	928	109658

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	561
PALGHAR	584
RAIGAD	943
BEED	1018
WASHIM	1151
THANE	1285
JALNA	1349
GONDIA	1365
GADCHIROLI	1536
BULDHANA	1595
LATUR	1692
PUNE	1899
WARDHA	1925
BHANDARA	2036
AHMEDNAGAR	2078
PARBHANI	2136
AURANGABAD	2308
JALGAON	3128
AMRAVATI	3351
YAVATMAL	3664
DHULE	3704
NAGPUR	5070
NANDED	5364
AKOLA	5858
OSMANABAD	7800
NASHIK	9173
HINGOLI	11166
NANDURBAR	12440
CHANDRAPUR	12637

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	08.05.2023	09.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	93861	69713	69778	65	24083	43	892
2	AURANGABAD DIV.	167494	104599	104644	45	62850	86	2328
3	NASHIK DIV.	111029	89197	89236	39	21793	66	807
4	AMRAVATI DIV.	94450	65165	65203	38	29247	53	1083
5	KONKAN DIV.	31461	23824	23851	27	7610	15	282
6	PUNE DIV.	63028	52096	52106	10	10922	24	405
Total		561323	404594	404818	224	156505	285	5796

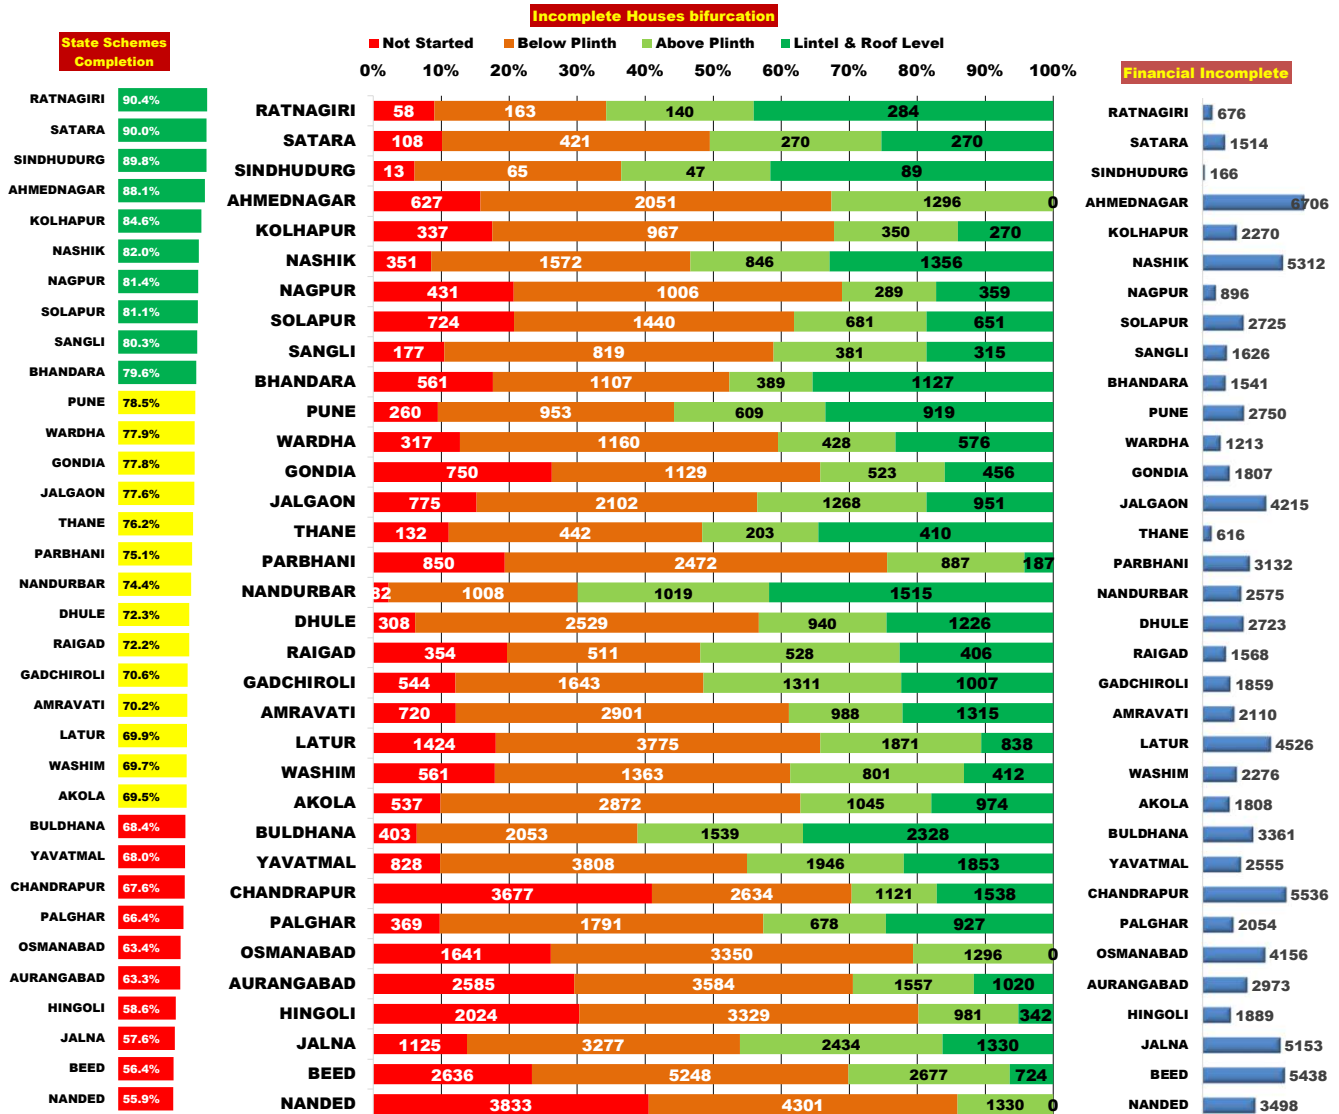

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	08.05.2023	09.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	CHANDRAPUR	27648	18657	18678	21	8970	12	332
2	AHMEDNAGAR	33220	29257	29275	18	3945	27	146
3	GADCHIROLI	15298	10776	10793	17	4505	9	167
4	AMRAVATI	19873	13934	13949	15	5924	9	219
5	YAVATMAL	26381	17931	17946	15	8435	13	312
6	WARDHA	11222	8730	8741	11	2481	6	92
7	BEED	25860	14565	14575	10	11285	13	418
8	GONDIA	12896	10028	10038	10	2858	8	106
9	JALNA	19260	11084	11094	10	8166	23	302
10	LATUR	26312	18394	18404	10	7908	13	293
11	AURANGABAD	23833	15078	15087	9	8746	9	324
12	NANDURBAR	14138	10506	10514	8	3624	6	134
13	PALGHAR	11208	7435	7443	8	3765	6	139
14	DHULE	18086	13076	13083	7	5003	9	185
15	SOLAPUR	18475	14972	14979	7	3496	7	129
16	AKOLA	17823	12389	12395	6	5428	9	201
17	RAIGAD	6475	4670	4676	6	1799	3	67
18	JALGAON	22723	17622	17627	5	5096	11	189
19	NAGPUR	11221	9131	9136	5	2085	3	77
20	THANE	4979	3787	3792	5	1187	2	44
21	RATNAGIRI	6691	6042	6046	4	645	3	24
22	SINDHUDURG	2108	1890	1894	4	214	1	8
23	KOLHAPUR	12529	10602	10605	3	1924	3	71
24	NANDED	21396	11956	11959	3	9437	8	350
25	BULDHANA	20021	13696	13698	2	6323	16	234
26	OSMANABAD	17053	10815	10817	2	6236	10	231
27	BHANDARA	15576	12391	12392	1	3184	4	118
28	HINGOLI	16132	9455	9456	1	6676	6	247
29	NASHIK	22862	18736	18737	1	4125	12	153
30	PARBHANI	17648	13252	13252	0	4396	4	163
31	PUNE	12773	10032	10032	0	2741	5	102
32	SANGLI	8604	6912	6912	0	1692	3	63
33	SATARA	10647	9578	9578	0	1069	5	40
34	WASHIM	10352	7215	7215	0	3137	7	116
Total		561323	404594	404818	224	156505	285	5796

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10666	0	39274	0	23279
2	AMRAVATI DIV.	0	30679	0	32271	0	16185
3	AURANGABAD DIV.	0	20319	0	52972	0	24244
4	NAGPUR DIV.	0	10429	0	21020	0	13139
5	KONKAN DIV.	0	413	0	3617	0	3482
6	PUNE DIV.	0	9796	0	16537	0	6966
	Total	0	82302	0	165691	0	87295

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	13
THANE	94
RATNAGIRI	97
PALGHAR	205
GADCHIROLI	329
SANGLI	472
KOLHAPUR	540
SATARA	923
DHULE	999
NASHIK	1130
PARBHANI	1165
NANDURBAR	1362
GONDIA	1452
WARDHA	1590
NAGPUR	1927
JALNA	1966
HINGOLI	2015
CHANDRAPUR	2112
PUNE	2233
LATUR	2333
AURANGABAD	2788
AHMEDNAGAR	2983
BHANDARA	3019
WASHIM	3036
OSMANABAD	3201
BEED	3382
NANDED	3469
YAVATMAL	3932
AKOLA	3990
JALGAON	4192
SOLAPUR	5628
BULDHANA	8184
AMRAVATI	11537

PMAY-G 2nd Ins Pending

SINDHUDURG	228
RATNAGIRI	423
RAIGAD	535
THANE	610
SATARA	1186
WARDHA	1264
OSMANABAD	1819
PALGHAR	1821
PUNE	2359
KOLHAPUR	2612
GADCHIROLI	2712
NAGPUR	2973
HINGOLI	3171
WASHIM	3194
AHMEDNAGAR	3850
SANGLI	3950
GONDIA	4276
LATUR	4307
JALNA	4485
CHANDRAPUR	4554
AKOLA	5120
BHANDARA	5241
AURANGABAD	5883
PARBHANI	5963
BULDHANA	6034
NASHIK	6049
SOLAPUR	6430
DHULE	6861
BEED	8270
AMRAVATI	8874
YAVATMAL	9049
NANDURBAR	9982
JALGAON	12532
NANDED	19074

PMAY-G 3rd Ins Pending

SINDHUDURG	302
RAIGAD	378
RATNAGIRI	428
THANE	590
WARDHA	946
KOLHAPUR	985
SATARA	1055
PUNE	1069
NAGPUR	1394
HINGOLI	1474
SANGLI	1543
PALGHAR	1784
LATUR	1914
AKOLA	2075
GADCHIROLI	2304
SOLAPUR	2314
WASHIM	2354
BHANDARA	2441
AURANGABAD	2473
CHANDRAPUR	2705
PARBHANI	2794
JALNA	2969
BULDHANA	2984
OSMANABAD	3016
AHMEDNAGAR	3016
GONDIA	3349
AMRAVATI	3356
BEED	3594
DHULE	3839
NASHIK	3994
JALGAON	4292
YAVATMAL	5416
NANDED	6010
NANDURBAR	8138

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	2983	0	3850	0	3016
2	AKOLA	0	3990	0	5120	0	2075
3	AMRAVATI	0	11537	0	8874	0	3356
4	AURANGABAD	0	2788	0	5883	0	2473
5	BEED	0	3382	0	8270	0	3594
6	BHANDARA	0	3019	0	5241	0	2441
7	BULDHANA	0	8184	0	6034	0	2984
8	CHANDRAPUR	0	2112	0	4554	0	2705
9	DHULE	0	999	0	6861	0	3839
10	GADCHIROLI	0	329	0	2712	0	2304
11	GONDIA	0	1452	0	4276	0	3349
12	HINGOLI	0	2015	0	3171	0	1474
13	JALGAON	0	4192	0	12532	0	4292
14	JALNA	0	1966	0	4485	0	2969
15	KOLHAPUR	0	540	0	2612	0	985
16	LATUR	0	2333	0	4307	0	1914
17	NAGPUR	0	1927	0	2973	0	1394
18	NANDED	0	3469	0	19074	0	6010
19	NANDURBAR	0	1362	0	9982	0	8138
20	NASHIK	0	1130	0	6049	0	3994
21	OSMANABAD	0	3201	0	1819	0	3016
22	PALGHAR	0	205	0	1821	0	1784
23	PARBHANI	0	1165	0	5963	0	2794
24	PUNE	0	2233	0	2359	0	1069
25	RAIGAD	0	13	0	535	0	378
26	RATNAGIRI	0	97	0	423	0	428
27	SANGLI	0	472	0	3950	0	1543
28	SINDHUDURG	0	4	0	228	0	302
29	SOLAPUR	0	5628	0	6430	0	2314
30	THANE	0	94	0	610	0	590
31	WARDHA	0	1590	0	1264	0	946
32	WASHIM	0	3036	0	3194	0	2354
33	YAVATMAL	0	3932	0	9049	0	5416
34	SATARA	-29	923	-1	1186	0	1055
	Total	0	82302	0	165691	0	87295

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2143	0	9262	0	5369
2	AMRAVATI DIV.	0	3049	0	12997	0	6319
3	AURANGABAD DIV.	0	16118	0	29336	0	13033
4	NAGPUR DIV.	0	6280	0	8679	0	4061
5	KONKAN DIV.	0	926	0	2972	0	1596
6	PUNE DIV.	0	1606	0	4600	0	2291
Total		0	30122	0	67846	0	32669

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
NANDURBAR	82
SATARA	108
THANE	132
SANGLI	177
PUNE	260
DHULE	308
WARDHA	317
KOLHAPUR	337
NASHIK	351
RAIGAD	354
PALGHAR	369
BULDHANA	403
NAGPUR	431
AKOLA	537
GADCHIROLI	544
BHANDARA	561
WASHIM	561
AHMEDNAGAR	627
AMRAVATI	720
SOLAPUR	724
GONDIA	750
JALGAON	775
YAVATMAL	828
PARBHANI	850
JALNA	1125
LATUR	1424
OSMANABAD	1641
HINGOLI	2024
AURANGABAD	2585
BEED	2636
CHANDRAPUR	3677
NANDED	3833

State Schemes 2nd Ins Pending

SINDHUDURG	65
RATNAGIRI	163
SATARA	421
THANE	442
RAIGAD	511
SANGLI	819
PUNE	953
KOLHAPUR	967
NAGPUR	1006
NANDURBAR	1008
BHANDARA	1107
GONDIA	1129
WARDHA	1160
WASHIM	1363
SOLAPUR	1440
NASHIK	1572
GADCHIROLI	1643
PALGHAR	1791
AHMEDNAGAR	2051
BULDHANA	2053
JALGAON	2102
PARBHANI	2472
DHULE	2529
CHANDRAPUR	2634
AKOLA	2872
AMRAVATI	2901
JALNA	3277
HINGOLI	3329
OSMANABAD	3350
AURANGABAD	3584
LATUR	3775
YAVATMAL	3808
NANDED	4301
BEED	5248

State Schemes 3rd Ins Pending

SINDHUDURG	47
RATNAGIRI	140
THANE	203
SATARA	270
NAGPUR	289
KOLHAPUR	350
SANGLI	381
BHANDARA	389
WARDHA	428
GONDIA	523
RAIGAD	528
PUNE	609
PALGHAR	678
SOLAPUR	681
WASHIM	801
NASHIK	846
PARBHANI	887
DHULE	940
HINGOLI	981
AMRAVATI	988
NANDURBAR	1019
AKOLA	1045
CHANDRAPUR	1121
JALGAON	1268
AHMEDNAGAR	1296
OSMANABAD	1296
GADCHIROLI	1311
NANDED	1330
BULDHANA	1539
AURANGABAD	1557
LATUR	1871
YAVATMAL	1946
JALNA	2434
BEED	2677

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	627	0	2051	0	1296
2	AKOLA	0	537	0	2872	0	1045
3	AMRAVATI	0	720	0	2901	0	988
4	AURANGABAD	0	2585	0	3584	0	1557
5	BEED	0	2636	0	5248	0	2677
6	BHANDARA	0	561	0	1107	0	389
7	BULDHANA	0	403	0	2053	0	1539
8	CHANDRAPUR	0	3677	0	2634	0	1121
9	DHULE	0	308	0	2529	0	940
10	GADCHIROLI	0	544	0	1643	0	1311
11	GONDIA	0	750	0	1129	0	523
12	HINGOLI	0	2024	0	3329	0	981
13	JALGAON	0	775	0	2102	0	1268
14	JALNA	0	1125	0	3277	0	2434
15	KOLHAPUR	0	337	0	967	0	350
16	LATUR	0	1424	0	3775	0	1871
17	NAGPUR	0	431	0	1006	0	289
18	NANDED	0	3833	0	4301	0	1330
19	NANDURBAR	0	82	0	1008	0	1019
20	NASHIK	0	351	0	1572	0	846
21	OSMANABAD	0	1641	0	3350	0	1296
22	PALGHAR	0	369	0	1791	0	678
23	PARBHANI	0	850	0	2472	0	887
24	PUNE	0	260	0	953	0	609
25	RAIGAD	0	354	0	511	0	528
26	RATNAGIRI	0	58	0	163	0	140
27	SANGLI	0	177	0	819	0	381
28	SINDHUDURG	0	13	0	65	0	47
29	SOLAPUR	0	724	0	1440	0	681
30	THANE	0	132	0	442	0	203
31	WARDHA	0	317	0	1160	0	428
32	WASHIM	0	561	0	1363	0	801
33	YAVATMAL	0	828	0	3808	0	1946
34	SATARA	-2	108	0	421	0	270
	Total	0	30122	0	67846	0	32669

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2519	1788	3174	1543	54
AKOLA	4222	3517	3593	869	582
AMRAVATI	7526	5627	7248	1513	1059
AURANGABAD	2407	2252	4998	1106	425
BEED	2187	1866	6629	1597	474
BHANDARA	7048	5296	4754	754	2245
BULDHANA	2641	2159	4037	859	712
CHANDRAPUR	3047	1958	3521	713	292
DHULE	5711	4106	5873	2204	1622
GADCHIROLI	4018	2470	2260	1221	916
GONDIA	1934	1860	3262	1042	145
HINGOLI	1034	670	2607	476	102
JALGAON	7892	6652	11114	1992	698
JALNA	1371	1084	3130	770	293
KOLHAPUR	1950	740	2400	290	105
LATUR	797	728	2680	462	54
NAGPUR	3374	2346	2573	447	594
NANDED	9666	9176	14696	2001	368
NANDURBAR	11598	10008	7100	4686	5139
NASHIK	7074	3585	4770	2034	1558
OSMANABAD	1044	585	1245	450	7
PALGHAR	916	653	1347	676	497
PARBHANI	860	738	4512	564	102
PUNE	2262	1738	1959	514	459
RAIGAD	740	240	483	234	168
RATNAGIRI	181	44	336	133	60
SANGLI	3034	2327	3438	542	146
SATARA	698	385	863	222	147
SINDDHURG	143	89	201	66	28
SOLAPUR	4958	4592	5023	1216	509
THANE	209	188	567	169	184
WARDHA	1172	811	949	213	244
WASHIM	1228	869	2521	424	94
YAVATMAL	6530	4384	6886	1816	1687
