



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ११.०५.२०२३

प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९६४३	०	१०४२९५२	४९४	०	०	०
राज्य योजना	५६२८३३	९९९	४०५२१६	१९०	०	०	०
एकूण	१९७२४७६	९९९	१४४८१६८	६८४	०	०	०


PMAY-G Completion Progress Bar

74.0%



State Schemes Progress Bar

72.0%


PMAY-G: Incomplete Houses bifurcation




State Schemes: Incomplete Houses bifurcation

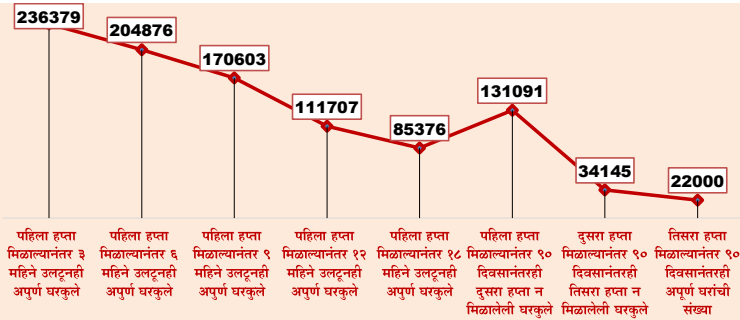


Abhiyan Achievement Day 172

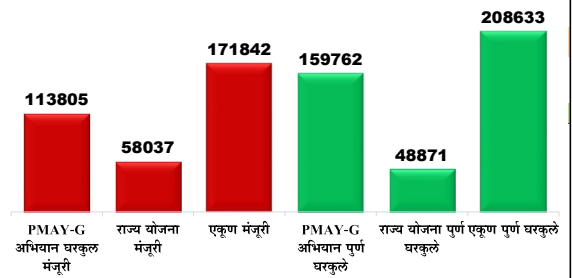

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	10.05.2023	11.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414860	413694	413655	0	1205
2	AMRAVATI DIV.	274792	274348	274317	0	475
3	AURANGABAD DIV.	238003	237302	237302	0	701
4	NAGPUR DIV.	291914	291257	291250	0	664
5	KONKAN DIV.	69834	69625	69625	0	209
6	PUNE DIV.	124458	123595	123494	0	964
Total		1413861	1409821	1409643	0	4218

Sr. No.	District	Target (PWL+Awaas Plus)	10.05.2023	11.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60791	60756	60756	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95514	95266	95266	0	248
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BULDHANA	44752	44713	44713	0	39
7	DHULE	64999	64917	64917	0	82
8	GADCHIROLI	31703	31615	31615	0	88
9	HINGOLI	18109	18083	18083	0	26
10	JALNA	24038	24023	24023	0	15
11	KOLHAPUR	17660	17652	17652	0	8
12	LATUR	20679	20493	20493	0	186
13	NAGPUR	37007	36991	36991	0	16
14	NANDED	69533	69463	69463	0	70
15	NANDURBAR	119607	118959	118959	0	648
16	NASHIK	89735	89683	89683	0	52
17	OSMANABAD	14506	14411	14411	0	95
18	PALGHAR	35376	35188	35188	0	188
19	PARBHANI	19088	19062	19062	0	26
20	RAIGAD	9830	9820	9820	0	10
21	RATNAGIRI	9890	9884	9884	0	6
22	SANGLI	21813	21641	21641	0	172
23	SINDHUDURG	5133	5133	5133	0	0
24	THANE	9605	9600	9600	0	5
25	WARDHA	18633	18607	18607	0	26
26	CHANDRAPUR	43097	42975	42974	-1	123
27	PUNE	20541	20528	20527	-1	14
28	WASHIM	20390	20363	20362	-1	28
29	BHANDARA	64981	64925	64922	-3	59
30	GONDIA	96493	96144	96141	-3	352
31	YAVATMAL	65344	65228	65198	-30	146
32	JALGAON	79728	79379	79340	-39	388
33	SATARA	15342	15312	15273	-39	69
34	SOLAPUR	49102	48462	48401	-61	701
Total		1413861	1409821	1409643	0	4218

Remaining Sanction RANK


SINDHUDURG	0
THANE	5
RATNAGIRI	6
KOLHAPUR	8
RAIGAD	10
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	16
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	28
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
BEED	57
BHANDARA	59
SATARA	69
NANDED	70
DHULE	82
GADCHIROLI	88
OSMANABAD	95
CHANDRAPUR	123
YAVATMAL	146
SANGLI	172
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	248
GONDIA	352
JALGAON	388
NANDURBAR	648
SOLAPUR	701

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	418	145	273	-2
14	PARBHANI	332	15	317	331	54	277	-39
15	SATARA	1309	598	711	1301	630	671	-32
16	NASHIK	1824	1475	349	1803	1023	780	452
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2747	1486	1261	-23
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2828	1298	1530	-14
21	NAGPUR	5134	3397	1737	5022	3422	1600	-25
22	JALGAON	22872	21026	1846	22908	20974	1934	52
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2044	255	1789	2310	258	2052	-3
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	YAVATMAL	3437	1119	2318	3675	1253	2422	-134
27	BHANDARA	5825	3230	2595	5666	3231	2435	-1
28	WASHIM	3477	883	2594	3443	865	2578	18
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AKOLA	7074	3842	3232	7367	3903	3464	-61
31	AHMEDNAGAR	7762	4828	2934	7759	4294	3465	534
32	SOLAPUR	7960	2595	5365	7232	1410	5822	1185
33	BULDHANA	15085	8586	6499	15213	7582	7631	1004
34	AMRAVATI	21721	11392	10329	21559	11392	10167	0
	Total	127640	73603	54037	127247	68414	58833	5523

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	10.05.2023	11.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	291250	239433	239577	144	51673	183	2067
2	NASHIK DIV.	413655	329869	329975	106	83680	270	3347
3	AMRAVATI DIV.	274317	186861	186965	104	87352	173	3494
4	AURANGABAD DIV.	237302	140420	140484	64	96818	191	3873
5	PUNE DIV.	123494	87966	88020	54	35474	62	1419
6	KONKAN DIV.	69625	57909	57931	22	11694	50	468
Total		1409643	1042458	1042952	494	366691	929	14668

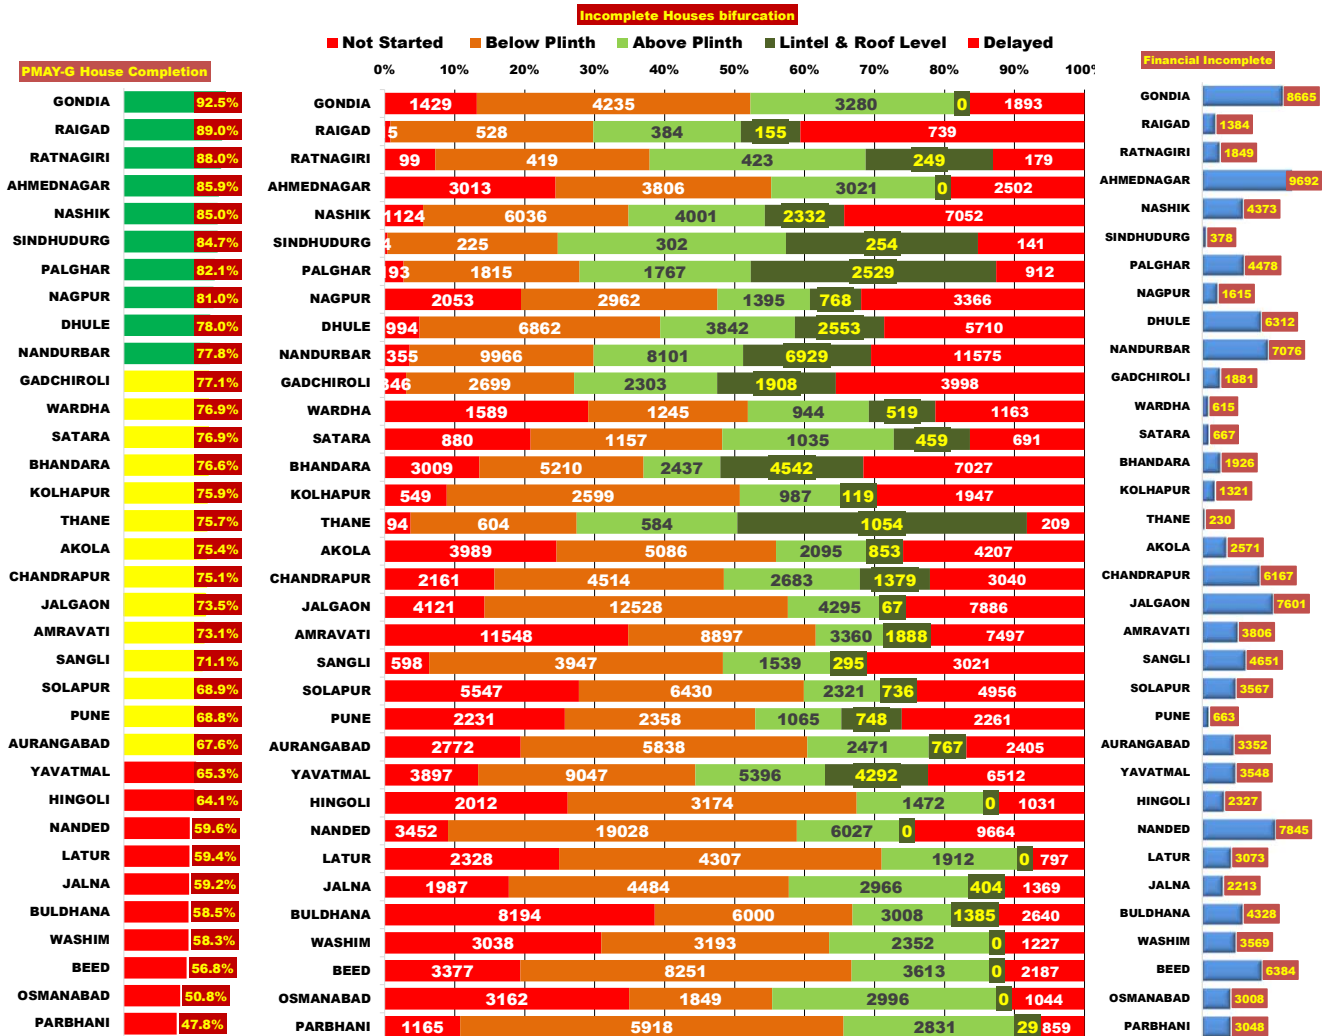

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	10.05.2023	11.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	GONDIA	96141	88862	88921	59	7220	66	289
2	AMRAVATI	95266	69573	69619	46	25647	46	1026
3	AHMEDNAGAR	60756	52147	52182	35	8574	82	343
4	NANDURBAR	118959	92576	92608	32	26351	40	1054
5	PARBHANI	19062	9095	9119	24	9943	17	398
6	YAVATMAL	65198	42549	42573	24	22625	53	905
7	BHANDARA	64922	49701	49724	23	15198	33	608
8	GADCHIROLI	31615	24362	24384	22	7231	27	289
9	HINGOLI	18083	11568	11590	22	6493	15	260
10	JALGAON	79340	58308	58329	21	21011	49	840
11	AKOLA	48778	36735	36755	20	12023	21	481
12	NAGPUR	36991	29929	29948	19	7043	12	282
13	NASHIK	89683	76174	76190	16	13493	55	540
14	WARDHA	18607	14294	14310	16	4297	10	172
15	SOLAPUR	48401	33352	33367	15	15034	20	601
16	PALGHAR	35188	28871	28884	13	6304	23	252
17	SANGLI	21641	15377	15388	11	6253	11	250
18	SATARA	15273	11731	11742	11	3531	14	141
19	KOLHAPUR	17652	13388	13398	10	4254	8	170
20	WASHIM	20362	11871	11881	10	8481	23	339
21	PUNE	20527	14118	14125	7	6402	9	256
22	AURANGABAD	36514	24661	24667	6	11847	32	474
23	CHANDRAPUR	42974	32285	32290	5	10684	35	427
24	JALNA	24023	14207	14212	5	9811	22	392
25	NANDED	69463	41377	41382	5	28081	47	1123
26	BULDHANA	44713	26133	26137	4	18576	30	743
27	RATNAGIRI	9884	8691	8694	3	1190	14	48
28	SINDHUDURG	5133	4345	4348	3	785	4	31
29	THANE	9600	7261	7264	3	2336	5	93
30	BEED	35253	20019	20021	2	15232	22	609
31	DHULE	64917	50664	50666	2	14251	45	570
32	LATUR	20493	12177	12177	0	8316	22	333
33	OSMANABAD	14411	7316	7316	0	7095	15	284
34	RAIGAD	9820	8741	8741	0	1079	4	43
Total		1409643	1042458	1042952	494	366691	929	14668

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	10.05.2023	11.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	94163	94783	620	23647
2	NASHIK DIV.	141552	111174	111360	186	30192
3	AURANGABAD DIV.	200327	167545	167652	107	32675
4	AMRAVATI DIV.	110069	94543	94549	6	15520
5	KONKAN DIV.	34744	31461	31461	0	3283
6	PUNE DIV.	65859	63028	63028	0	2831
Total		670981	561914	562833	919	108148


Sr. No.	District	Target	10.05.2023	11.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	27766	28272	506	12013
2	AHMEDNAGAR	35298	33365	33551	186	1747
3	GONDIA	14261	13050	13122	72	1139
4	BEED	26878	25884	25943	59	935
5	HINGOLI	27298	16132	16160	28	11138
6	WARDHA	13147	11222	11250	28	1897
7	OSMANABAD	24853	17053	17066	13	7787
8	GADCHIROLI	16834	15308	15317	9	1517
9	NANDED	26760	21396	21403	7	5357
10	YAVATMAL	30045	26392	26398	6	3647
11	BHANDARA	17612	15594	15599	5	2013
12	AKOLA	23681	17823	17823	0	5858
13	AMRAVATI	23224	19878	19878	0	3346
14	AURANGABAD	26141	23833	23833	0	2308
15	BULDHANA	21616	20021	20021	0	1595
16	DHULE	21790	18086	18086	0	3704
17	JALGAON	25851	22723	22723	0	3128
18	JALNA	20609	19287	19287	0	1322
19	KOLHAPUR	13090	12529	12529	0	561
20	LATUR	28004	26312	26312	0	1692
21	NAGPUR	16291	11223	11223	0	5068
22	NANDURBAR	26578	14138	14138	0	12440
23	NASHIK	32035	22862	22862	0	9173
24	PALGHAR	11792	11208	11208	0	584
25	PARBHANI	19784	17648	17648	0	2136
26	PUNE	14672	12773	12773	0	1899
27	RAIGAD	7418	6475	6475	0	943
28	RATNAGIRI	7129	6691	6691	0	438
29	SANGLI	8732	8604	8604	0	128
30	SATARA	10647	10647	10647	0	0
31	SINDHUDURG	2141	2108	2108	0	33
32	SOLAPUR	18718	18475	18475	0	243
33	THANE	6264	4979	4979	0	1285
34	WASHIM	11503	10429	10429	0	1074
Total		670981	561914	562833	919	108148

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
SOLAPUR	243
RATNAGIRI	438
KOLHAPUR	561
PALGHAR	584
BEED	935
RAIGAD	943
WASHIM	1074
GONDIA	1139
THANE	1285
JALNA	1322
GADCHIROLI	1517
BULDHANA	1595
LATUR	1692
AHMEDNAGAR	1747
WARDHA	1897
PUNE	1899
BHANDARA	2013
PARBHANI	2136
AURANGABAD	2308
JALGAON	3128
AMRAVATI	3346
YAVATMAL	3647
DHULE	3704
NAGPUR	5068
NANDED	5357
AKOLA	5858
OSMANABAD	7787
NASHIK	9173
HINGOLI	11138
CHANDRAPUR	12013
NANDURBAR	12440

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	10.05.2023	11.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NAGPUR DIV.	94783	69816	69866	50	24917	43	997
2	AMRAVATI DIV.	94549	65246	65291	45	29258	53	1170
3	NASHIK DIV.	111360	89259	89294	35	22066	65	883
4	AURANGABAD DIV.	167652	104718	104750	32	62902	85	2516
5	KONKAN DIV.	31461	23876	23891	15	7570	15	303
6	PUNE DIV.	63028	52111	52124	13	10904	24	436
Total		562833	405026	405216	190	157617	284	6305

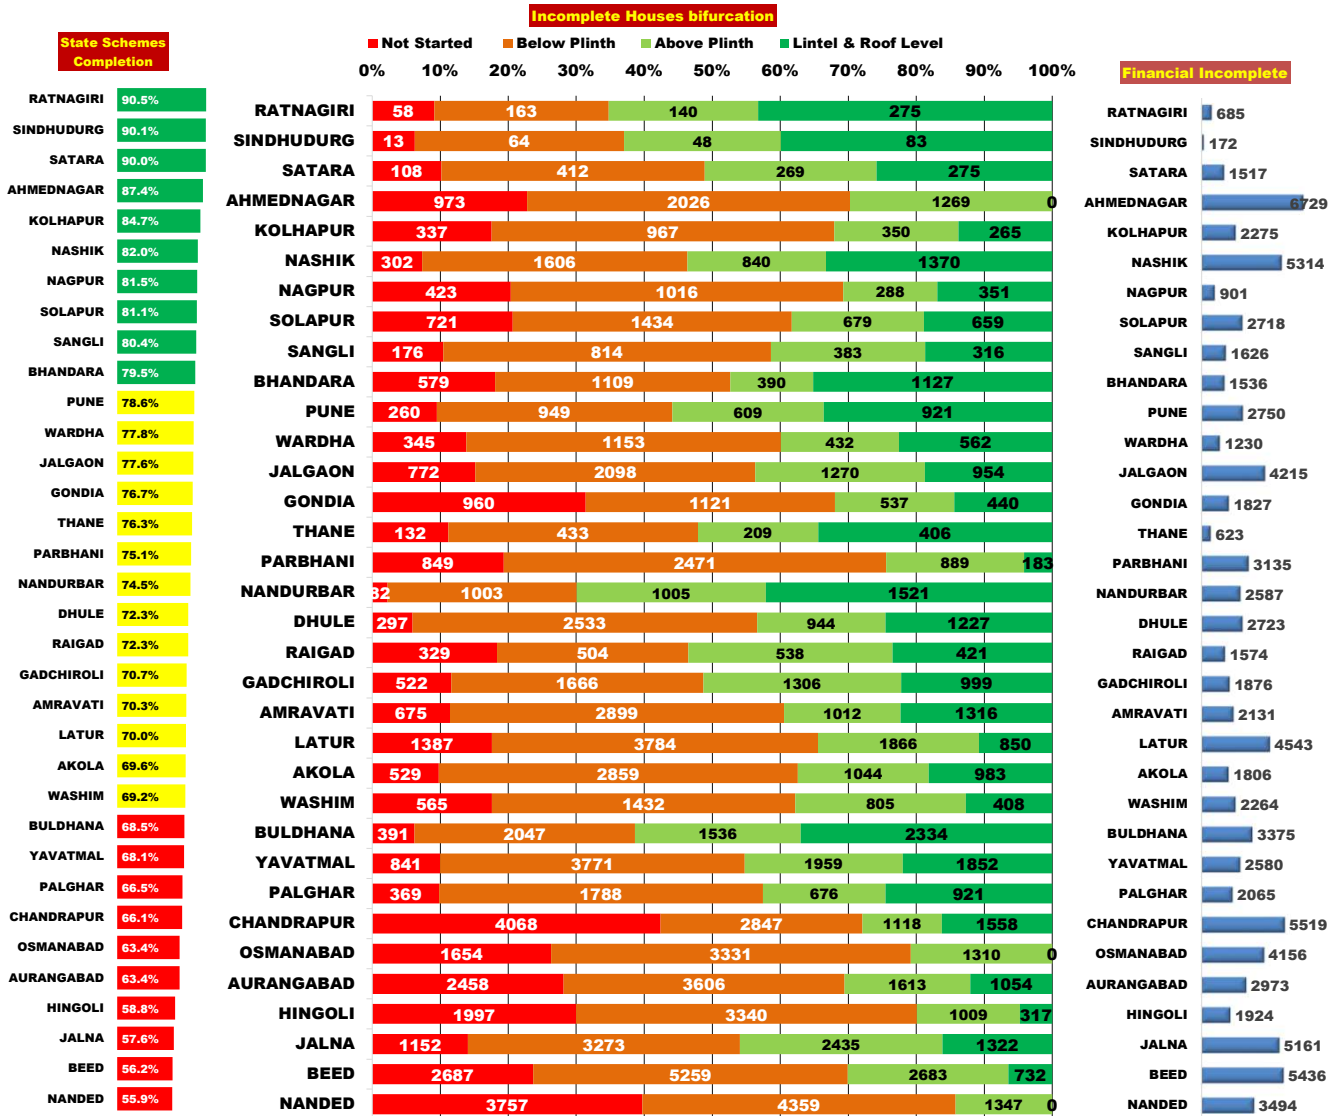

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	10.05.2023	11.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AHMEDNAGAR	33551	29286	29309	23	4242	27	170
2	GADCHIROLI	15317	10805	10824	19	4493	9	180
3	AMRAVATI	19878	13959	13976	17	5902	9	236
4	WARDHA	11250	8744	8758	14	2492	6	100
5	BULDHANA	20021	13701	13713	12	6308	16	252
6	GONDIA	13122	10053	10064	11	3058	8	122
7	LATUR	26312	18415	18425	10	7887	13	315
8	AURANGABAD	23833	15093	15102	9	8731	9	349
9	YAVATMAL	26398	17966	17975	9	8423	13	337
10	AKOLA	17823	12402	12408	6	5415	9	217
11	NANDURBAR	14138	10521	10527	6	3611	6	144
12	PALGHAR	11208	7448	7454	6	3754	6	150
13	HINGOLI	16160	9492	9497	5	6663	6	267
14	SATARA	10647	9578	9583	5	1064	5	43
15	JALNA	19287	11101	11105	4	8182	23	327
16	NAGPUR	11223	9141	9145	4	2078	3	83
17	NASHIK	22862	18740	18744	4	4118	12	165
18	RATNAGIRI	6691	6051	6055	4	636	3	25
19	KOLHAPUR	12529	10607	10610	3	1919	3	77
20	BEED	25943	14580	14582	2	11361	13	454
21	CHANDRAPUR	28272	18679	18681	2	9591	12	384
22	OSMANABAD	17066	10817	10819	2	6247	9	250
23	SANGLI	8604	6913	6915	2	1689	3	68
24	SINDHUDURG	2108	1898	1900	2	208	1	8
25	SOLAPUR	18475	14980	14982	2	3493	7	140
26	THANE	4979	3797	3799	2	1180	2	47
27	DHULE	18086	13084	13085	1	5001	9	200
28	JALGAON	22723	17628	17629	1	5094	11	204
29	PUNE	12773	10033	10034	1	2739	5	110
30	RAIGAD	6475	4682	4683	1	1792	3	72
31	WASHIM	10429	7218	7219	1	3210	7	128
32	BHANDARA	15599	12394	12394	0	3205	4	128
33	NANDED	21403	11964	11964	0	9439	8	378
34	PARBHANI	17648	13256	13256	0	4392	4	176
Total		562833	405026	405216	190	157617	284	6305

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10607	0	39198	0	23260
2	AMRAVATI DIV.	0	30599	0	32223	0	16211
3	AURANGABAD DIV.	0	20224	0	52849	0	24288
4	NAGPUR DIV.	0	10374	0	20865	0	13042
5	KONKAN DIV.	0	402	0	3591	0	3460
6	PUNE DIV.	0	9679	0	16491	0	6947
	Total	0	81885	0	165217	0	87208

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	12
THANE	94
RATNAGIRI	99
PALGHAR	193
GADCHIROLI	321
SANGLI	472
KOLHAPUR	549
SATARA	880
DHULE	994
NASHIK	1124
PARBHANI	1165
NANDURBAR	1355
GONDIA	1429
WARDHA	1589
NAGPUR	1918
JALNA	1957
HINGOLI	2012
CHANDRAPUR	2108
PUNE	2231
LATUR	2328
AURANGABAD	2771
BHANDARA	3009
AHMEDNAGAR	3013
WASHIM	3035
OSMANABAD	3162
BEED	3377
NANDED	3452
YAVATMAL	3890
AKOLA	3989
JALGAON	4121
SOLAPUR	5547
BULDHANA	8183
AMRAVATI	11502

PMAY-G 2nd Ins Pending

SINDHUDURG	225
RATNAGIRI	419
RAIGAD	528
THANE	604
SATARA	1157
WARDHA	1245
PALGHAR	1815
OSMANABAD	1849
PUNE	2358
KOLHAPUR	2599
GADCHIROLI	2699
NAGPUR	2962
HINGOLI	3174
WASHIM	3193
AHMEDNAGAR	3806
SANGLI	3947
GONDIA	4235
LATUR	4307
JALNA	4484
CHANDRAPUR	4514
AKOLA	5086
BHANDARA	5210
AURANGABAD	5838
PARBHANI	5918
BULDHANA	6000
NASHIK	6036
SOLAPUR	6430
DHULE	6862
BEED	8251
AMRAVATI	8897
YAVATMAL	9047
NANDURBAR	9966
JALGAON	12528
NANDED	19028

PMAY-G 3rd Ins Pending

SINDHUDURG	302
RAIGAD	384
RATNAGIRI	423
THANE	584
WARDHA	944
KOLHAPUR	987
SATARA	1035
PUNE	1065
NAGPUR	1395
HINGOLI	1472
SANGLI	1539
PALGHAR	1767
LATUR	1912
AKOLA	2095
GADCHIROLI	2303
SOLAPUR	2321
WASHIM	2352
BHANDARA	2437
AURANGABAD	2471
CHANDRAPUR	2683
PARBHANI	2831
JALNA	2966
OSMANABAD	2996
BULDHANA	3008
AHMEDNAGAR	3021
GONDIA	3280
AMRAVATI	3360
BEED	3613
DHULE	3842
NASHIK	4001
JALGAON	4295
YAVATMAL	5396
NANDED	6027
NANDURBAR	8101

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	3989	0	5086	0	2095
2	AMRAVATI	0	11502	0	8897	0	3360
3	AURANGABAD	0	2771	0	5838	0	2471
4	BEEED	0	3377	0	8251	0	3613
5	BHANDARA	0	3009	0	5210	0	2437
6	BULDHANA	0	8183	0	6000	0	3008
7	CHANDRAPUR	0	2108	0	4514	0	2683
8	DHULE	0	994	0	6862	0	3842
9	GADCHIROLI	0	321	0	2699	0	2303
10	GONDIA	0	1429	0	4235	0	3280
11	HINGOLI	0	2012	0	3174	0	1472
12	JALGAON	0	4121	0	12528	0	4295
13	JALNA	0	1957	0	4484	0	2966
14	LATUR	0	2328	0	4307	0	1912
15	NAGPUR	0	1918	0	2962	0	1395
16	NANDED	0	3452	0	19028	0	6027
17	NANDURBAR	0	1355	0	9966	0	8101
18	NASHIK	0	1124	0	6036	0	4001
19	OSMANABAD	0	3162	0	1849	0	2996
20	PALGHAR	0	193	0	1815	0	1767
21	PARBHANI	0	1165	0	5918	0	2831
22	PUNE	0	2231	0	2358	0	1065
23	RAIGAD	0	12	0	528	0	384
24	RATNAGIRI	0	99	0	419	0	423
25	SANGLI	0	472	0	3947	0	1539
26	SATARA	0	880	0	1157	0	1035
27	SINDHUDURG	0	4	0	225	0	302
28	THANE	0	94	0	604	0	584
29	WARDHA	0	1589	0	1245	0	944
30	WASHIM	0	3035	0	3193	0	2352
31	YAVATMAL	0	3890	0	9047	0	5396
32	SOLAPUR	-3	5547	0	6430	0	2321
33	KOLHAPUR	-9	549	0	2599	0	987
34	AHMEDNAGAR	-32	3013	-1	3806	0	3021
	Total	0	81885	0	165217	0	87208

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	2426	0	9266	0	5328
2	AMRAVATI DIV.	0	3001	0	13008	0	6356
3	AURANGABAD DIV.	0	15941	0	29423	0	13152
4	NAGPUR DIV.	0	6897	0	8912	0	4071
5	KONKAN DIV.	0	901	0	2952	0	1611
6	PUNE DIV.	0	1602	0	4576	0	2290
Total		0	30768	0	68137	0	32808

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
NANDURBAR	82
SATARA	108
THANE	132
SANGLI	176
PUNE	260
DHULE	297
NASHIK	302
RAIGAD	329
KOLHAPUR	337
WARDHA	345
PALGHAR	369
BULDHANA	391
NAGPUR	423
GADCHIROLI	522
AKOLA	529
WASHIM	565
BHANDARA	579
AMRAVATI	675
SOLAPUR	721
JALGAON	772
YAVATMAL	841
PARBHANI	849
GONDIA	960
AHMEDNAGAR	973
JALNA	1152
LATUR	1387
OSMANABAD	1654
HINGOLI	1997
AURANGABAD	2458
BEED	2687
NANDED	3757
CHANDRAPUR	4068

State Schemes 2nd Ins Pending

SINDHUDURG	64
RATNAGIRI	163
SATARA	412
THANE	433
RAIGAD	504
SANGLI	814
PUNE	949
KOLHAPUR	967
NANDURBAR	1003
NAGPUR	1016
BHANDARA	1109
GONDIA	1121
WARDHA	1153
WASHIM	1432
SOLAPUR	1434
NASHIK	1606
GADCHIROLI	1666
PALGHAR	1788
AHMEDNAGAR	2026
BULDHANA	2047
JALGAON	2098
PARBHANI	2471
DHULE	2533
CHANDRAPUR	2847
AKOLA	2859
AMRAVATI	2899
JALNA	3273
OSMANABAD	3331
HINGOLI	3340
AURANGABAD	3606
YAVATMAL	3771
LATUR	3784
NANDED	4359
BEED	5259

State Schemes 3rd Ins Pending

SINDHUDURG	48
RATNAGIRI	140
THANE	209
SATARA	269
NAGPUR	288
KOLHAPUR	350
SANGLI	383
BHANDARA	390
WARDHA	432
GONDIA	537
RAIGAD	538
PUNE	609
PALGHAR	676
SOLAPUR	679
WASHIM	805
NASHIK	840
PARBHANI	889
DHULE	944
NANDURBAR	1005
HINGOLI	1009
AMRAVATI	1012
AKOLA	1044
CHANDRAPUR	1118
AHMEDNAGAR	1269
JALGAON	1270
GADCHIROLI	1306
OSMANABAD	1310
NANDED	1347
BULDHANA	1536
AURANGABAD	1613
LATUR	1866
YAVATMAL	1959
JALNA	2435
BEED	2683

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	0	529	0	2859	0	1044
2	AMRAVATI	0	675	0	2899	0	1012
3	AURANGABAD	0	2458	0	3606	0	1613
4	BEED	0	2687	0	5259	0	2683
5	BHANDARA	0	579	0	1109	0	390
6	BULDHANA	0	391	0	2047	0	1536
7	CHANDRAPUR	0	4068	0	2847	0	1118
8	DHULE	0	297	0	2533	0	944
9	GADCHIROLI	0	522	0	1666	0	1306
10	GONDIA	0	960	0	1121	0	537
11	HINGOLI	0	1997	0	3340	0	1009
12	JALGAON	0	772	0	2098	0	1270
13	JALNA	0	1152	0	3273	0	2435
14	KOLHAPUR	0	337	0	967	0	350
15	LATUR	0	1387	0	3784	0	1866
16	NAGPUR	0	423	0	1016	0	288
17	NANDED	0	3757	0	4359	0	1347
18	NANDURBAR	0	82	0	1003	0	1005
19	NASHIK	0	302	0	1606	0	840
20	OSMANABAD	0	1654	0	3331	0	1310
21	PALGHAR	0	369	0	1788	0	676
22	PARBHANI	0	849	0	2471	0	889
23	PUNE	0	260	0	949	0	609
24	RAIGAD	0	329	0	504	0	538
25	RATNAGIRI	0	58	0	163	0	140
26	SANGLI	0	176	0	814	0	383
27	SATARA	0	108	0	412	0	269
28	SINDHUDURG	0	13	0	64	0	48
29	SOLAPUR	0	721	0	1434	0	679
30	THANE	0	132	0	433	0	209
31	WARDHA	0	345	0	1153	0	432
32	WASHIM	0	565	0	1432	0	805
33	YAVATMAL	-1	841	0	3771	0	1959
34	AHMEDNAGAR	-18	973	0	2026	0	1269
	Total	0	30768	0	68137	0	32808

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2502	1783	3182	1590	52
AKOLA	4207	3511	3567	864	579
AMRAVATI	7497	5607	7312	1521	1062
AURANGABAD	2405	2250	4994	1100	444
BEED	2187	1866	6783	1612	477
BHANDARA	7027	5286	4737	779	2301
BULDHANA	2640	2159	4039	868	719
CHANDRAPUR	3040	1956	3492	713	292
DHULE	5710	4106	5871	2261	1653
GADCHIROLI	3998	2462	2266	1238	910
GONDIA	1893	1824	3227	1037	142
HINGOLI	1031	668	2607	476	100
JALGAON	7886	6650	11119	2007	701
JALNA	1369	1083	3208	784	309
KOLHAPUR	1947	738	2395	292	106
LATUR	797	728	2695	465	54
NAGPUR	3366	2342	2567	446	589
NANDED	9664	9174	14703	2010	370
NANDURBAR	11575	9990	7152	4687	5143
NASHIK	7052	3582	4763	2038	1564
OSMANABAD	1044	585	1242	440	7
PALGHAR	912	650	1341	732	541
PARBHANI	859	737	4526	581	109
PUNE	2261	1738	1963	518	467
RAIGAD	739	240	483	233	166
RATNAGIRI	179	44	334	133	60
SANGLI	3021	2319	3476	561	152
SATARA	691	383	841	222	149
SINDHUDURG	141	87	199	66	28
SOLAPUR	4956	4590	5032	1228	514
THANE	209	188	563	168	187
WARDHA	1163	807	944	210	242
WASHIM	1227	869	2531	429	95
YAVATMAL	6512	4374	6937	1836	1716
