



# अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : १३.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण  
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९५८८	०	१०४३९२९	४६५	०	०	०
राज्य योजना	५६४९६५	१२२७	४०५६४३	२२६	६	१२	२३
एकूण	१९७४५५३	१२२७	१४४९५७२	६९१	६	१२	२३

PMAY-G Completion Progress Bar

74.1%



PMAY-G: Incomplete Houses bifurcation



State Schemes Progress Bar

71.8%



State Schemes: Incomplete Houses bifurcation

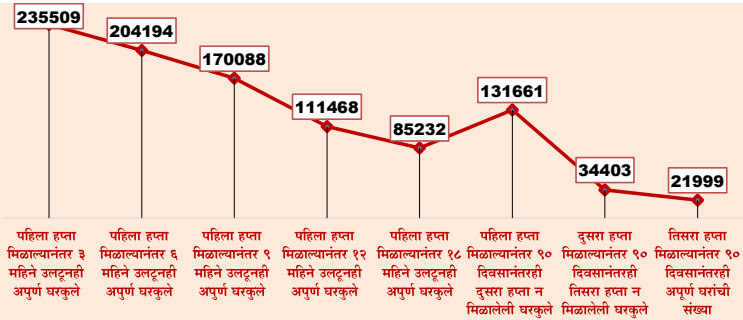


Abhiyan Achievement

Day

174

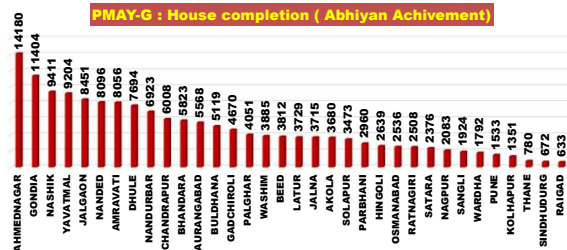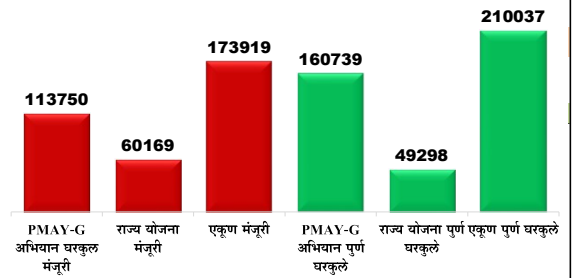

State Schemes : House completion (Abhiyan Achievement)



राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

# Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	12.05.2023	13.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414860	413654	413654	0	1206
2	AMRAVATI DIV.	274791	274308	274304	0	487
3	AURANGABAD DIV.	238003	237302	237302	0	701
4	NAGPUR DIV.	291913	291234	291234	0	679
5	KONKAN DIV.	69834	69625	69613	0	221
6	PUNE DIV.	124455	123486	123481	0	974
<b>Total</b>		<b>1413856</b>	<b>1409609</b>	<b>1409588</b>	<b>0</b>	<b>4268</b>

Sr. No.	District	Target (PWL+Awaas Plus)	12.05.2023	13.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60791	60756	60756	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95514	95266	95266	0	248
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BHANDARA	64981	64922	64922	0	59
7	BULDHANA	44752	44713	44713	0	39
8	CHANDRAPUR	43096	42958	42958	0	138
9	DHULE	64999	64917	64917	0	82
10	GADCHIROLI	31703	31615	31615	0	88
11	GONDIA	96493	96141	96141	0	352
12	HINGOLI	18109	18083	18083	0	26
13	JALGAON	79728	79339	79339	0	389
14	JALNA	24038	24023	24023	0	15
15	KOLHAPUR	17659	17646	17646	0	13
16	LATUR	20679	20493	20493	0	186
17	NAGPUR	37007	36991	36991	0	16
18	NANDED	69533	69463	69463	0	70
19	NANDURBAR	119607	118959	118959	0	648
20	NASHIK	89735	89683	89683	0	52
21	OSMANABAD	14506	14411	14411	0	95
22	PALGHAR	35376	35188	35188	0	188
23	PARBHANI	19088	19062	19062	0	26
24	PUNE	20541	20527	20527	0	14
25	RAIGAD	9830	9820	9820	0	10
26	SANGLI	21813	21641	21641	0	172
27	SINDHUDURG	5133	5133	5133	0	0
28	SOLAPUR	49100	48399	48399	0	701
29	THANE	9605	9600	9600	0	5
30	WARDHA	18633	18607	18607	0	26
31	WASHIM	20390	20362	20362	0	28
32	YAVATMAL	65343	65189	65185	-4	158
33	SATARA	15342	15273	15268	-5	74
34	RATNAGIRI	9890	9884	9872	-12	18
<b>Total</b>		<b>1413856</b>	<b>1409609</b>	<b>1409588</b>	<b>0</b>	<b>4268</b>

Remaining Sanction RANK


SINDHUDURG	0
THANE	5
RAIGAD	10
KOLHAPUR	13
AKOLA	14
PUNE	14
JALNA	15
NAGPUR	16
RATNAGIRI	18
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	28
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
BEED	57
BHANDARA	59
NANDED	70
SATARA	74
DHULE	82
GADCHIROLI	88
OSMANABAD	95
CHANDRAPUR	138
YAVATMAL	158
SANGLI	172
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	248
GONDIA	352
JALGAON	389
NANDURBAR	648
SOLAPUR	701

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	11	0	11	11	0	0
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	257	0	257	227	30	30
9	THANE	127	74	53	127	60	67	14
10	NANDED	362	277	85	362	242	120	35
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	101	111	212	72	140	29
13	SANGLI	431	143	288	418	145	273	-2
14	PARBHANI	332	15	317	331	54	277	-39
15	SATARA	1309	598	711	1301	630	671	-32
16	NASHIK	1824	1475	349	1803	1023	780	452
17	HINGOLI	1713	787	926	1713	466	1247	321
18	CHANDRAPUR	2791	1463	1328	2745	1486	1259	-23
19	JALNA	1413	165	1248	1374	85	1289	80
20	WARDHA	2819	1284	1535	2828	1334	1494	-50
21	NAGPUR	5134	3397	1737	5023	3422	1601	-25
22	JALGAON	22872	21026	1846	22906	20973	1933	53
23	PUNE	2925	992	1933	2924	885	2039	107
24	LATUR	2044	255	1789	2310	258	2052	-3
25	OSMANABAD	2470	104	2366	2470	56	2414	48
26	YAVATMAL	3437	1119	2318	3674	1253	2421	-134
27	BHANDARA	5825	3230	2595	5666	3231	2435	-1
28	WASHIM	3477	883	2594	3443	865	2578	18
29	AURANGABAD	3328	1779	1549	3290	288	3002	1491
30	AHMEDNAGAR	7762	4828	2934	7759	4451	3308	377
31	AKOLA	7074	3842	3232	7367	3903	3464	-61
32	SOLAPUR	7960	2595	5365	7230	1410	5820	1185
33	BULDHANA	15085	8586	6499	15213	7582	7631	1004
34	AMRAVATI	21721	11392	10329	21559	11392	10167	0
	<b>Total</b>	<b>127640</b>	<b>73603</b>	<b>54037</b>	<b>127241</b>	<b>68606</b>	<b>58635</b>	<b>5367</b>

## प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	12.05.2023	13.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	<b>NAGPUR DIV.</b>	<b>291234</b>	<b>239741</b>	<b>239908</b>	<b>167</b>	<b>51326</b>	<b>183</b>	<b>2232</b>
2	<b>NASHIK DIV.</b>	<b>413654</b>	<b>330087</b>	<b>330173</b>	<b>86</b>	<b>83481</b>	<b>268</b>	<b>3630</b>
3	<b>AURANGABAD DIV.</b>	<b>237302</b>	<b>140551</b>	<b>140616</b>	<b>65</b>	<b>96686</b>	<b>190</b>	<b>4204</b>
4	<b>AMRAVATI DIV.</b>	<b>274304</b>	<b>187042</b>	<b>187101</b>	<b>59</b>	<b>87203</b>	<b>172</b>	<b>3791</b>
5	<b>KONKAN DIV.</b>	<b>69613</b>	<b>57997</b>	<b>58052</b>	<b>55</b>	<b>11561</b>	<b>50</b>	<b>503</b>
6	<b>PUNE DIV.</b>	<b>123481</b>	<b>88046</b>	<b>88079</b>	<b>33</b>	<b>35402</b>	<b>61</b>	<b>1539</b>
<b>Total</b>		<b>1409588</b>	<b>1043464</b>	<b>1043929</b>	<b>465</b>	<b>365659</b>	<b>924</b>	<b>15898</b>

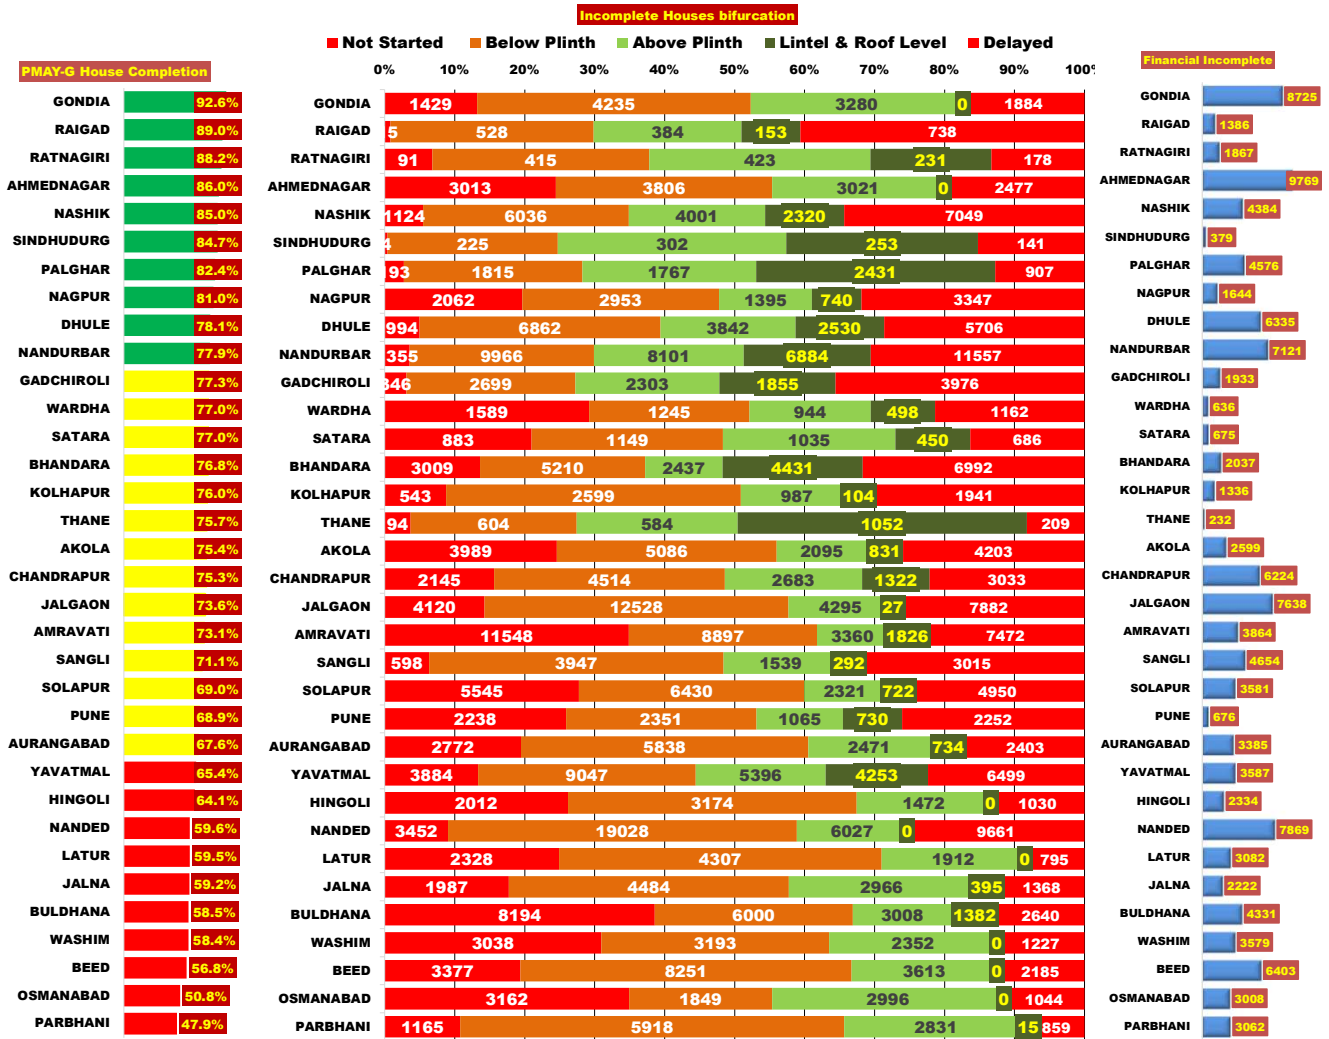

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	12.05.2023	13.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	BHANDARA	64922	49783	49835	52	15087	33	656
2	PALGHAR	35188	28940	28982	42	6206	23	270
3	GONDIA	96141	88941	88982	41	7159	66	311
4	AHMEDNAGAR	60756	52225	52260	35	8496	81	369
5	JALGAON	79339	58341	58369	28	20970	49	912
6	GADCHIROLI	31615	24410	24437	27	7178	27	312
7	NAGPUR	36991	29953	29976	23	7015	12	305
8	YAVATMAL	65185	42589	42612	23	22573	53	981
9	AKOLA	48778	36758	36777	19	12001	21	522
10	BEED	35253	20021	20040	19	15213	22	661
11	CHANDRAPUR	42958	32332	32347	15	10611	35	461
12	KOLHAPUR	17646	13398	13413	15	4233	8	184
13	NANDED	69463	41391	41406	15	28057	47	1220
14	NANDURBAR	118959	92638	92653	15	26306	40	1144
15	RATNAGIRI	9872	8700	8712	12	1160	14	50
16	PARBHANI	19062	9122	9133	11	9929	17	432
17	AMRAVATI	95266	69671	69681	10	25585	46	1112
18	WARDHA	18607	14322	14331	9	4276	10	186
19	AURANGABAD	36514	24692	24700	8	11814	32	514
20	SATARA	15268	11743	11751	8	3517	14	153
21	LATUR	20493	12196	12203	7	8290	21	360
22	PUNE	20527	14136	14143	7	6384	9	278
23	DHULE	64917	50684	50689	5	14228	44	619
24	WASHIM	20362	11886	11891	5	8471	22	368
25	JALNA	24023	14218	14221	3	9802	21	426
26	NASHIK	89683	76199	76202	3	13481	54	586
27	BULDHANA	44713	26138	26140	2	18573	29	808
28	HINGOLI	18083	11595	11597	2	6486	15	282
29	SOLAPUR	48399	33379	33381	2	15018	20	653
30	RAIGAD	9820	8742	8743	1	1077	4	47
31	SANGLI	21641	15390	15391	1	6250	11	272
32	OSMANABAD	14411	7316	7316	0	7095	15	308
33	SINDHUDURG	5133	4349	4349	0	784	4	34
34	THANE	9600	7266	7266	0	2334	4	101
<b>Total</b>		<b>1409588</b>	<b>1043464</b>	<b>1043929</b>	<b>465</b>	<b>365659</b>	<b>924</b>	<b>15898</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	12.05.2023	13.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	95159	95609	450	22821
2	PUNE DIV.	65859	63030	63380	350	2479
3	AURANGABAD DIV.	200327	168022	168224	204	32103
4	NASHIK DIV.	141552	111445	111546	101	30006
5	AMRAVATI DIV.	110069	94622	94710	88	15359
6	KONKAN DIV.	34744	31462	31496	34	3248
<b>Total</b>		<b>670981</b>	<b>563740</b>	<b>564965</b>	<b>1227</b>	<b>106016</b>


Sr. No.	District	Target	12.05.2023	13.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	28641	29012	371	11273
2	KOLHAPUR	13090	12529	12879	350	211
3	HINGOLI	27298	16261	16399	138	10899
4	AHMEDNAGAR	35298	33636	33737	101	1561
5	GONDIA	14261	13127	13196	69	1065
6	BULDHANA	21616	20021	20073	52	1543
7	NANDED	26760	21487	21529	42	5231
8	YAVATMAL	30045	26409	26445	36	3600
9	RAIGAD	7418	6475	6509	34	909
10	JALNA	20609	19287	19311	24	1298
11	GADCHIROLI	16834	15319	15329	10	1505
12	AKOLA	23681	17823	17823	0	5858
13	AMRAVATI	23224	19878	19878	0	3346
14	AURANGABAD	26141	23953	23953	0	2188
15	BEED	26878	26007	26007	0	871
16	BHANDARA	17612	15599	15599	0	2013
17	DHULE	21790	18086	18086	0	3704
18	JALGAON	25851	22723	22723	0	3128
19	LATUR	28004	26312	26312	0	1692
20	NAGPUR	16291	11223	11223	0	5068
21	NANDURBAR	26578	14138	14138	0	12440
22	NASHIK	32035	22862	22862	0	9173
23	PALGHAR	11792	11208	11208	0	584
24	PARBHANI	19784	17648	17648	0	2136
25	PUNE	14672	12773	12773	0	1899
26	RATNAGIRI	7129	6691	6691	0	438
27	SANGLI	8732	8604	8604	0	128
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2108	2108	0	33
30	SOLAPUR	18718	18477	18477	0	241
31	THANE	6264	4980	4980	0	1284
32	WARDHA	13147	11250	11250	0	1897
33	WASHIM	11503	10491	10491	0	1012
34	OSMANABAD	24853	17067	17065	-2	7788
<b>Total</b>		<b>670981</b>	<b>563740</b>	<b>564965</b>	<b>1227</b>	<b>106016</b>

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	211
SOLAPUR	241
RATNAGIRI	438
PALGHAR	584
BEED	871
RAIGAD	909
WASHIM	1012
GONDIA	1065
THANE	1284
JALNA	1298
GADCHIROLI	1505
BULDHANA	1543
AHMEDNAGAR	1561
LATUR	1692
WARDHA	1897
PUNE	1899
BHANDARA	2013
PARBHANI	2136
AURANGABAD	2188
JALGAON	3128
AMRAVATI	3346
YAVATMAL	3600
DHULE	3704
NAGPUR	5068
NANDED	5231
AKOLA	5858
OSMANABAD	7788
NASHIK	9173
HINGOLI	10899
CHANDRAPUR	11273
NANDURBAR	12440

## राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	12.05.2023	13.05.2023	Daily_Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	168224	104810	104885	75	63339	85	2754
2	AMRAVATI DIV.	94710	65330	65386	56	29324	53	1275
3	NAGPUR DIV.	95609	69914	69962	48	25647	43	1115
4	NASHIK DIV.	111546	89317	89341	24	22205	65	965
5	KONKAN DIV.	31496	23909	23922	13	7574	15	329
6	PUNE DIV.	63380	52137	52147	10	11233	23	488
<b>Total</b>		<b>564965</b>	<b>405417</b>	<b>405643</b>	<b>226</b>	<b>159322</b>	<b>283</b>	<b>6927</b>

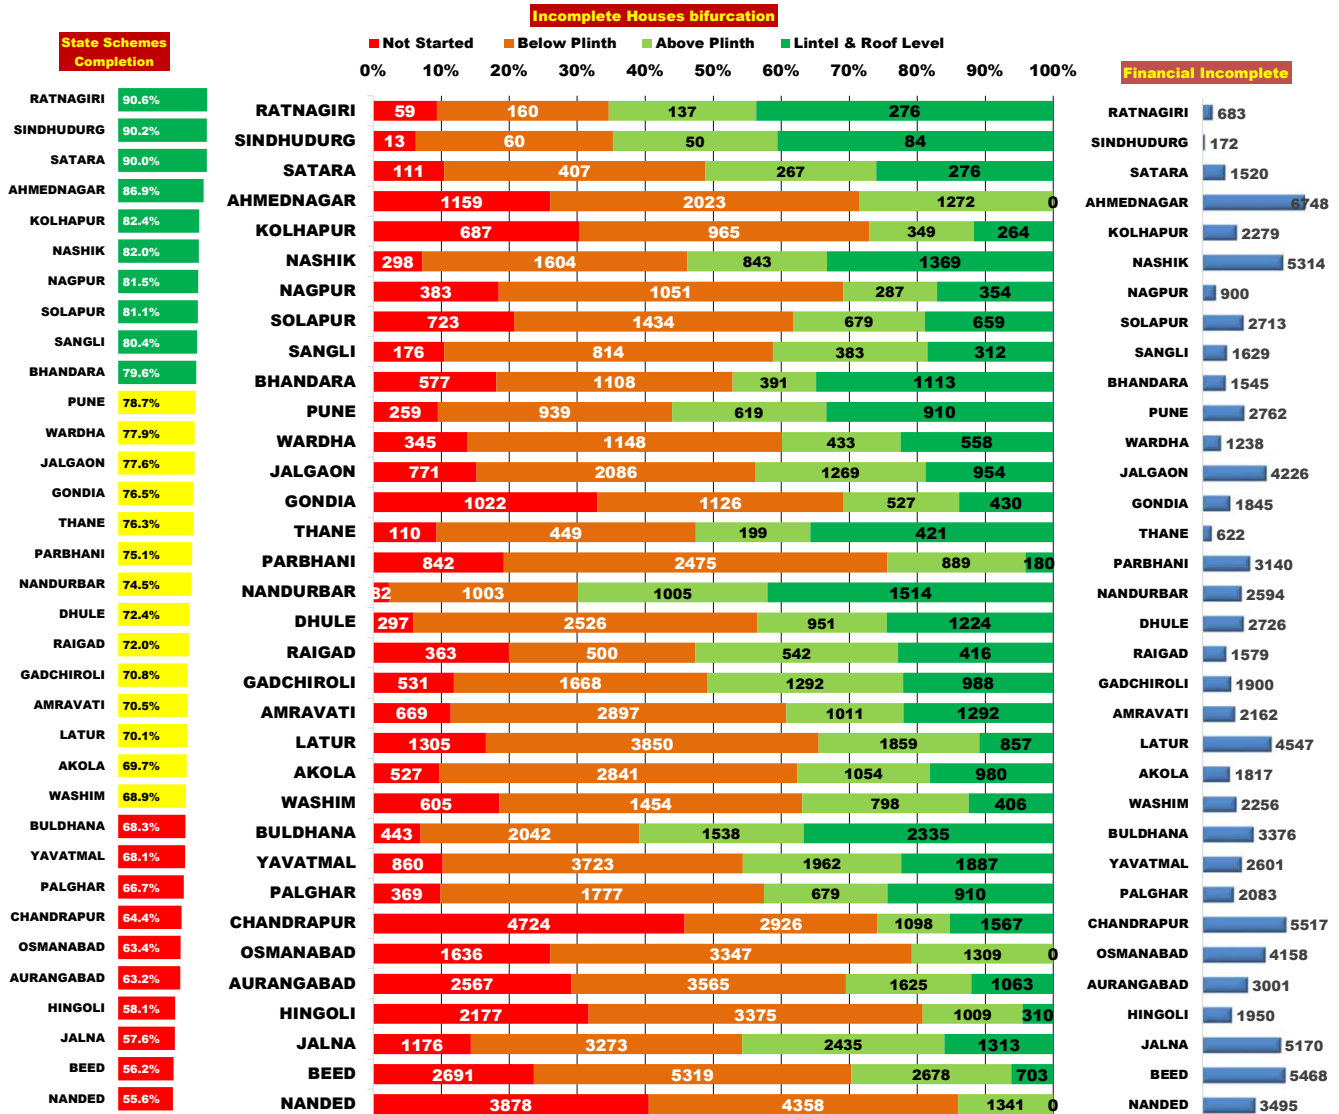



राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	12.05.2023	13.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	BEED	26007	14582	14616	34	11391	13	495
2	YAVATMAL	26445	17986	18013	27	8432	13	367
3	GONDIA	13196	10074	10091	17	3105	8	135
4	AMRAVATI	19878	13994	14009	15	5869	9	255
5	AURANGABAD	23953	15121	15133	12	8820	9	383
6	GADCHIROLI	15329	10839	10850	11	4479	9	195
7	HINGOLI	16399	9518	9528	10	6871	6	299
8	JALGAON	22723	17633	17643	10	5080	11	221
9	AHMEDNAGAR	33737	29320	29328	8	4409	27	192
10	PALGHAR	11208	7465	7473	8	3735	6	162
11	BHANDARA	15599	12403	12410	7	3189	4	139
12	CHANDRAPUR	29012	18690	18697	7	10315	12	448
13	LATUR	26312	18434	18441	7	7871	13	342
14	AKOLA	17823	12415	12421	6	5402	9	235
15	JALNA	19311	11108	11114	6	8197	23	356
16	WASHIM	10491	7222	7228	6	3263	7	142
17	NASHIK	22862	18744	18748	4	4114	12	179
18	PARBHANI	17648	13258	13262	4	4386	4	191
19	SANGLI	8604	6915	6919	4	1685	3	73
20	WARDHA	11250	8762	8766	4	2484	6	108
21	KOLHAPUR	12879	10611	10614	3	2265	3	98
22	RATNAGIRI	6691	6056	6059	3	632	3	27
23	BULDHANA	20073	13713	13715	2	6358	15	276
24	NAGPUR	11223	9146	9148	2	2075	3	90
25	NANDED	21529	11967	11969	2	9560	8	416
26	NANDURBAR	14138	10532	10534	2	3604	6	157
27	RAIGAD	6509	4686	4688	2	1821	3	79
28	SATARA	10647	9584	9586	2	1061	5	46
29	PUNE	12773	10045	10046	1	2727	5	119
30	DHULE	18086	13088	13088	0	4998	9	217
31	OSMANABAD	17065	10822	10822	0	6243	9	271
32	SINDHUDURG	2108	1901	1901	0	207	1	9
33	SOLAPUR	18477	14982	14982	0	3495	7	152
34	THANE	4980	3801	3801	0	1179	2	51
	<b>Total</b>	<b>564965</b>	<b>405417</b>	<b>405643</b>	<b>226</b>	<b>159322</b>	<b>283</b>	<b>6927</b>

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10606	0	39198	0	23260
2	AMRAVATI DIV.	0	30586	0	32223	0	16211
3	AURANGABAD DIV.	0	20224	0	52849	0	24288
4	NAGPUR DIV.	0	10367	0	20856	0	13042
5	KONKAN DIV.	0	394	0	3587	0	3460
6	PUNE DIV.	0	9681	0	16476	0	6947
	<b>Total</b>	<b>0</b>	<b>81858</b>	<b>0</b>	<b>165189</b>	<b>0</b>	<b>87208</b>

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	12
RATNAGIRI	91
THANE	94
PALGHAR	193
GADCHIROLI	321
SANGLI	472
KOLHAPUR	543
SATARA	883
DHULE	994
NASHIK	1124
PARBHANI	1165
NANDURBAR	1355
GONDIA	1429
WARDHA	1589
NAGPUR	1927
JALNA	1957
HINGOLI	2012
CHANDRAPUR	2092
PUNE	2238
LATUR	2328
AURANGABAD	2771
BHANDARA	3009
AHMEDNAGAR	3013
WASHIM	3035
OSMANABAD	3162
BEED	3377
NANDED	3452
YAVATMAL	3877
AKOLA	3989
JALGAON	4120
SOLAPUR	5545
BULDHANA	8183
AMRAVATI	11502

PMAY-G 2nd Ins Pending

SINDHUDURG	225
RATNAGIRI	415
RAIGAD	528
THANE	604
SATARA	1149
WARDHA	1245
PALGHAR	1815
OSMANABAD	1849
PUNE	2351
KOLHAPUR	2599
GADCHIROLI	2699
NAGPUR	2953
HINGOLI	3174
WASHIM	3193
AHMEDNAGAR	3806
SANGLI	3947
GONDIA	4235
LATUR	4307
JALNA	4484
CHANDRAPUR	4514
AKOLA	5086
BHANDARA	5210
AURANGABAD	5838
PARBHANI	5918
BULDHANA	6000
NASHIK	6036
SOLAPUR	6430
DHULE	6862
BEED	8251
AMRAVATI	8897
YAVATMAL	9047
NANDURBAR	9966
JALGAON	12528
NANDED	19028

PMAY-G 3rd Ins Pending

SINDHUDURG	302
RAIGAD	384
RATNAGIRI	423
THANE	584
WARDHA	944
KOLHAPUR	987
SATARA	1035
PUNE	1065
NAGPUR	1395
HINGOLI	1472
SANGLI	1539
PALGHAR	1767
LATUR	1912
AKOLA	2095
GADCHIROLI	2303
SOLAPUR	2321
WASHIM	2352
BHANDARA	2437
AURANGABAD	2471
CHANDRAPUR	2683
PARBHANI	2831
JALNA	2966
OSMANABAD	2996
BULDHANA	3008
AHMEDNAGAR	3021
GONDIA	3280
AMRAVATI	3360
BEED	3613
DHULE	3842
NASHIK	4001
JALGAON	4295
YAVATMAL	5396
NANDED	6027
NANDURBAR	8101

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	3013	0	3806	0	3021
2	AKOLA	0	3989	0	5086	0	2095
3	AMRAVATI	0	11502	0	8897	0	3360
4	AURANGABAD	0	2771	0	5838	0	2471
5	BEED	0	3377	0	8251	0	3613
6	BHANDARA	0	3009	0	5210	0	2437
7	BULDHANA	0	8183	0	6000	0	3008
8	CHANDRAPUR	0	2092	0	4514	0	2683
9	DHULE	0	994	0	6862	0	3842
10	GADCHIROLI	0	321	0	2699	0	2303
11	GONDIA	0	1429	0	4235	0	3280
12	HINGOLI	0	2012	0	3174	0	1472
13	JALGAON	0	4120	0	12528	0	4295
14	JALNA	0	1957	0	4484	0	2966
15	KOLHAPUR	0	543	0	2599	0	987
16	LATUR	0	2328	0	4307	0	1912
17	NANDED	0	3452	0	19028	0	6027
18	NANDURBAR	0	1355	0	9966	0	8101
19	NASHIK	0	1124	0	6036	0	4001
20	OSMANABAD	0	3162	0	1849	0	2996
21	PALGHAR	0	193	0	1815	0	1767
22	PARBHANI	0	1165	0	5918	0	2831
23	PUNE	0	2238	0	2351	0	1065
24	RAIGAD	0	12	0	528	0	384
25	RATNAGIRI	0	91	0	415	0	423
26	SANGLI	0	472	0	3947	0	1539
27	SINDHUDURG	0	4	0	225	0	302
28	SOLAPUR	0	5545	0	6430	0	2321
29	THANE	0	94	0	604	0	584
30	WARDHA	0	1589	0	1245	0	944
31	WASHIM	0	3035	0	3193	0	2352
32	YAVATMAL	0	3877	0	9047	0	5396
33	SATARA	-8	883	0	1149	0	1035
34	NAGPUR	-9	1927	0	2953	0	1395
	<b>Total</b>	<b>0</b>	<b>81858</b>	<b>0</b>	<b>165189</b>	<b>0</b>	<b>87208</b>

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	KONKAN DIV.	5	914	5	2946	10	1607
2	AMRAVATI DIV.	1	3104	6	12957	11	6363
3	NAGPUR DIV.	0	7582	0	9027	2	4028
4	NASHIK DIV.	0	2607	1	9242	0	5340
5	AURANGABAD DIV.	0	16272	0	29562	0	13145
6	PUNE DIV.	0	1956	0	4559	0	2297
<b>Total</b>		<b>6</b>	<b>32435</b>	<b>12</b>	<b>68293</b>	<b>23</b>	<b>32780</b>

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	59
NANDURBAR	82
THANE	110
SATARA	111
SANGLI	176
PUNE	259
DHULE	297
NASHIK	298
WARDHA	345
RAIGAD	363
PALGHAR	369
NAGPUR	383
BULDHANA	443
AKOLA	527
GADCHIROLI	531
BHANDARA	577
WASHIM	605
AMRAVATI	669
KOLHAPUR	687
SOLAPUR	723
JALGAON	771
PARBHANI	842
YAVATMAL	860
GONDIA	1022
AHMEDNAGAR	1159
JALNA	1176
LATUR	1305
OSMANABAD	1636
HINGOLI	2177
AURANGABAD	2567
BEED	2691
NANDED	3878
CHANDRAPUR	4724

State Schemes 2nd Ins Pending

SINDHUDURG	60
RATNAGIRI	160
SATARA	407
THANE	449
RAIGAD	500
SANGLI	814
PUNE	939
KOLHAPUR	965
NANDURBAR	1003
NAGPUR	1051
BHANDARA	1108
GONDIA	1126
WARDHA	1148
SOLAPUR	1434
WASHIM	1454
NASHIK	1604
GADCHIROLI	1668
PALGHAR	1777
AHMEDNAGAR	2023
BULDHANA	2042
JALGAON	2086
PARBHANI	2475
DHULE	2526
AKOLA	2841
AMRAVATI	2897
CHANDRAPUR	2926
JALNA	3273
OSMANABAD	3347
HINGOLI	3375
AURANGABAD	3565
YAVATMAL	3723
LATUR	3850
NANDED	4358
BEED	5319

State Schemes 3rd Ins Pending

SINDHUDURG	50
RATNAGIRI	137
THANE	199
SATARA	267
NAGPUR	287
KOLHAPUR	349
SANGLI	383
BHANDARA	391
WARDHA	433
GONDIA	527
RAIGAD	542
PUNE	619
PALGHAR	679
SOLAPUR	679
WASHIM	798
NASHIK	843
PARBHANI	889
DHULE	951
NANDURBAR	1005
HINGOLI	1009
AMRAVATI	1011
AKOLA	1054
CHANDRAPUR	1098
JALGAON	1269
AHMEDNAGAR	1272
GADCHIROLI	1292
OSMANABAD	1309
NANDED	1341
BULDHANA	1538
AURANGABAD	1625
LATUR	1859
YAVATMAL	1962
JALNA	2435
BEED	2678

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	YAVATMAL	1	860	6	3723	11	1962
2	THANE	4	110	5	449	8	199
3	GADCHIROLI	0	531	0	1668	2	1292
4	PALGHAR	0	369	0	1777	2	679
5	JALGAON	0	771	1	2086	0	1269
6	RATNAGIRI	1	59	0	160	0	137
7	AHMEDNAGAR	0	1159	0	2023	0	1272
8	AKOLA	0	527	0	2841	0	1054
9	AMRAVATI	0	669	0	2897	0	1011
10	AURANGABAD	0	2567	0	3565	0	1625
11	BEED	0	2691	0	5319	0	2678
12	BHANDARA	0	577	0	1108	0	391
13	BULDHANA	0	443	0	2042	0	1538
14	CHANDRAPUR	0	4724	0	2926	0	1098
15	DHULE	0	297	0	2526	0	951
16	GONDIA	0	1022	0	1126	0	527
17	HINGOLI	0	2177	0	3375	0	1009
18	JALNA	0	1176	0	3273	0	2435
19	KOLHAPUR	0	687	0	965	0	349
20	LATUR	0	1305	0	3850	0	1859
21	NANDED	0	3878	0	4358	0	1341
22	NANDURBAR	0	82	0	1003	0	1005
23	NASHIK	0	298	0	1604	0	843
24	OSMANABAD	0	1636	0	3347	0	1309
25	PARBHANI	0	842	0	2475	0	889
26	PUNE	0	259	0	939	0	619
27	RAIGAD	0	363	0	500	0	542
28	SANGLI	0	176	0	814	0	383
29	SINDHUDURG	0	13	0	60	0	50
30	SOLAPUR	0	723	0	1434	0	679
31	WARDHA	0	345	0	1148	0	433
32	WASHIM	0	605	0	1454	0	798
33	NAGPUR	-2	383	0	1051	0	287
34	SATARA	-8	111	0	407	0	267
	<b>Total</b>	<b>6</b>	<b>32435</b>	<b>12</b>	<b>68293</b>	<b>23</b>	<b>32780</b>

## प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले     
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले     
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले  
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले     
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

जिल्हा	पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले	दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले	तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या
AHMEDNAGAR	2477	1772	3193	1607	47
AKOLA	4203	3508	3571	869	580
AMRAVATI	7472	5595	7322	1528	1067
AURANGABAD	2403	2248	4995	1109	444
BEED	2185	1864	6834	1635	481
BHANDARA	6992	5258	4754	780	2278
BULDHANA	2640	2159	4039	868	717
CHANDRAPUR	3033	1954	3496	715	291
DHULE	5706	4103	5872	2268	1649
GADCHIROLI	3976	2457	2270	1238	902
GONDIA	1884	1815	3241	1044	143
HINGOLI	1030	668	2612	482	99
JALGAON	7882	6648	11122	2007	699
JALNA	1368	1082	3230	793	308
KOLHAPUR	1941	737	2397	294	111
LATUR	795	726	2702	467	54
NAGPUR	3347	2327	2558	447	587
NANDED	9661	9171	14703	2032	371
NANDURBAR	11557	9975	7194	4750	5158
NASHIK	7049	3582	4802	2063	1572
OSMANABAD	1044	585	1242	440	7
PALGHAR	907	648	1341	733	533
PARBHANI	859	737	4545	581	110
PUNE	2252	1731	1962	518	463
RAIGAD	738	239	483	233	166
RATNAGIRI	178	44	333	136	66
SANGLI	3015	2316	3468	561	153
SATARA	686	378	844	238	154
SINDHUDURG	141	87	199	67	29
SOLAPUR	4950	4585	5033	1234	516
THANE	209	188	564	168	188
WARDHA	1162	807	944	210	241
WASHIM	1227	869	2547	437	95
YAVATMAL	6499	4369	7249	1851	1720
