



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २१.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९२७५	०	१०४६९२६	६०	१३३	४१२	५८५
राज्य योजना	५६७९०७	५१	४०६६८३	२७	२३९	२५७	२८०
एकूण	१९७७१८२	५१	१४५३६०९	८७	३७२	६६९	८६५

PMAY-G Completion Progress Bar

74.3%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

71.6%


State Schemes: Incomplete Houses bifurcation

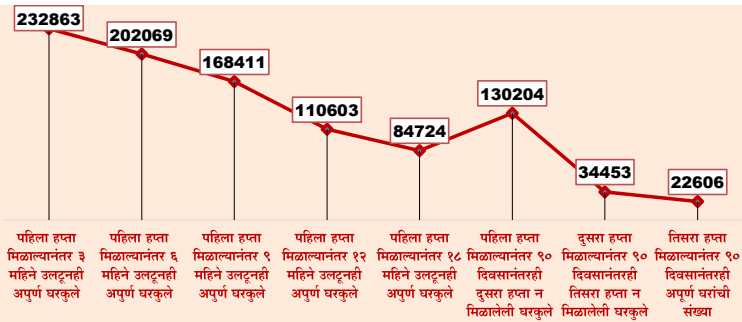


Abhiyan Achievement Day 182

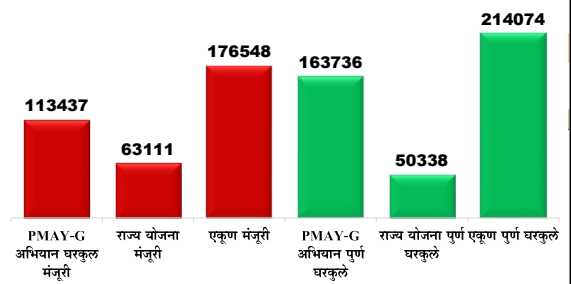

PMAY-G : House completion (Abhiyan Achievement)



State Schemes : House completion (Abhiyan Achievement)



राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.



State Schemes Remaining 1st Installments Bottom 10 Dist.



PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	20.05.2023	21.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414813	413556	413556	0	1257
2	AMRAVATI DIV.	274769	274281	274281	0	488
3	AURANGABAD DIV.	238003	237299	237299	0	704
4	NAGPUR DIV.	291895	291215	291215	0	680
5	KONKAN DIV.	69832	69611	69611	0	221
6	PUNE DIV.	124373	123313	123313	0	1060
Total		1413685	1409275	1409275	0	4410

Sr. No.	District	Target (PWL+Awaas Plus)	20.05.2023	21.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60787	60752	60752	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95496	95248	95248	0	248
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BHANDARA	64981	64920	64920	0	61
7	BULDHANA	44752	44713	44713	0	39
8	CHANDRAPUR	43093	42958	42958	0	135
9	DHULE	64999	64917	64917	0	82
10	GADCHIROLI	31703	31615	31615	0	88
11	GONDIA	96493	96138	96138	0	355
12	HINGOLI	18109	18083	18083	0	26
13	JALGAON	79686	79246	79246	0	440
14	JALNA	24038	24023	24023	0	15
15	KOLHAPUR	17658	17637	17637	0	21
16	LATUR	20679	20493	20493	0	186
17	NAGPUR	36992	36977	36977	0	15
18	NANDED	69533	69463	69463	0	70
19	NANDURBAR	119606	118958	118958	0	648
20	NASHIK	89735	89683	89683	0	52
21	OSMANABAD	14506	14408	14408	0	98
22	PALGHAR	35376	35188	35188	0	188
23	PARBHANI	19088	19062	19062	0	26
24	PUNE	20513	20433	20433	0	80
25	RAIGAD	9830	9820	9820	0	10
26	RATNAGIRI	9888	9871	9871	0	17
27	SANGLI	21778	21606	21606	0	172
28	SATARA	15329	15243	15243	0	86
29	SINDHUDURG	5133	5133	5133	0	0
30	SOLAPUR	49095	48394	48394	0	701
31	THANE	9605	9599	9599	0	6
32	WARDHA	18633	18607	18607	0	26
33	WASHIM	20390	20362	20362	0	28
34	YAVATMAL	65339	65180	65180	0	159
Total		1413685	1409275	1409275	0	4410

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
KOLHAPUR	21
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	28
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
BEED	57
BHANDARA	61
NANDED	70
PUNE	80
DHULE	82
SATARA	86
GADCHIROLI	88
OSMANABAD	98
CHANDRAPUR	135
YAVATMAL	159
SANGLI	172
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	248
GONDIA	355
JALGAON	440
NANDURBAR	648
SOLAPUR	701

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1294	630	664	29
16	NASHIK	1802	1324	478	1803	1072	731	252
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1666	1137	2829	1347	1482	319
21	NAGPUR	5054	3588	1466	5018	3443	1575	145
22	LATUR	2299	1121	1178	2310	477	1833	644
23	JALGAON	22928	20121	2807	22878	20945	1933	-824
24	PUNE	2924	1602	1322	2889	885	2004	717
25	BHANDARA	5782	3543	2239	5669	3266	2403	277
26	YAVATMAL	3612	1450	2162	3673	1269	2404	181
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3443	865	2578	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7755	4453	3302	-270
31	AKOLA	7072	3935	3137	7367	3903	3464	32
32	SOLAPUR	7297	3684	3613	7228	1410	5818	2274
33	BULDHANA	15191	10571	4620	15214	7967	7247	2604
34	AMRAVATI	21529	12817	8712	21543	11392	10151	1425
	Total	127095	80050	47045	127144	69317	57827	12094

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	20.05.2023	21.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI DIV.	274281	187866	187886	20	86395	169	5760
2	AURANGABAD DIV.	237299	140976	140993	17	96306	184	6420
3	NASHIK DIV.	413556	330707	330722	15	82834	259	5522
4	NAGPUR DIV.	291215	240612	240617	5	50598	179	3373
5	PUNE DIV.	123313	88347	88349	2	34964	60	2331
6	KONKAN DIV.	69611	58358	58359	1	11252	49	750
Total		1409275	1046866	1046926	60	362349	900	24157

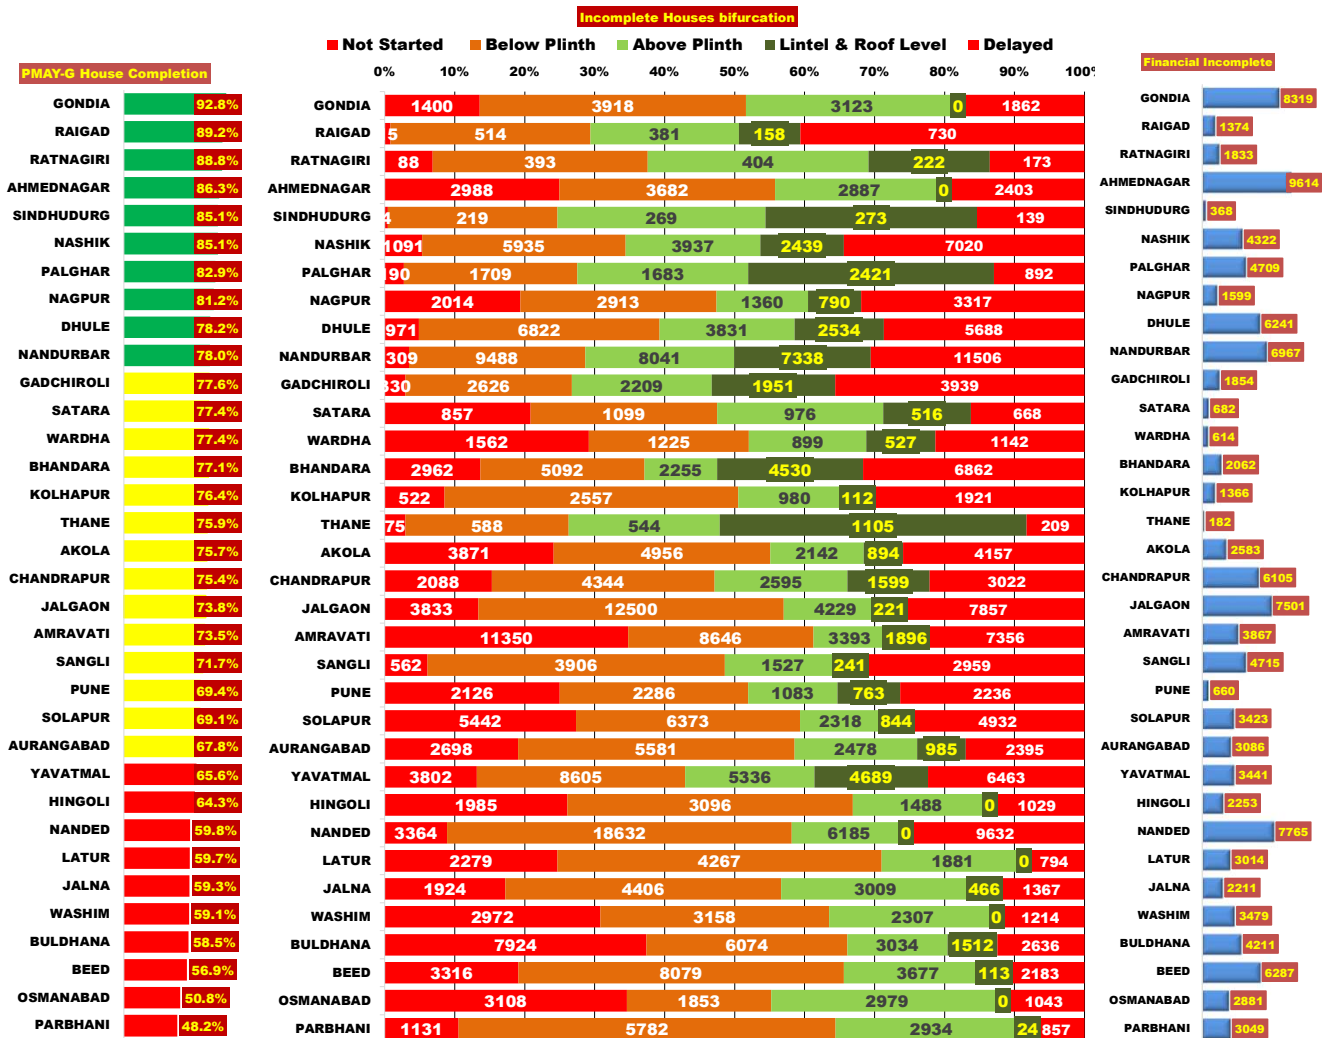

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	20.05.2023	21.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI	95248	69996	70009	13	25239	46	1683
2	AHMEDNAGAR	60752	52427	52437	10	8315	79	554
3	NANDED	69463	41527	41537	10	27926	45	1862
4	YAVATMAL	65180	42748	42755	7	22425	51	1495
5	NASHIK	89683	76276	76281	5	13402	52	893
6	WARDHA	18607	14389	14394	5	4213	10	281
7	PARBHANI	19062	9188	9191	3	9871	17	658
8	JALNA	24023	14246	14248	2	9775	21	652
9	KOLHAPUR	17637	13464	13466	2	4171	8	278
10	AURANGABAD	36514	24772	24773	1	11741	31	783
11	BEED	35253	20067	20068	1	15185	21	1012
12	PALGHAR	35188	29184	29185	1	6003	23	400
13	AKOLA	48778	36915	36915	0	11863	21	791
14	BHANDARA	64920	50081	50081	0	14839	33	989
15	BULDHANA	44713	26179	26179	0	18534	28	1236
16	CHANDRAPUR	42958	32385	32385	0	10573	33	705
17	DHULE	64917	50759	50759	0	14158	43	944
18	GADCHIROLI	31615	24524	24524	0	7091	26	473
19	GONDIA	96138	89198	89198	0	6940	64	463
20	HINGOLI	18083	11627	11627	0	6456	15	430
21	JALGAON	79246	58463	58463	0	20783	47	1386
22	LATUR	20493	12231	12231	0	8262	21	551
23	NAGPUR	36977	30035	30035	0	6942	12	463
24	NANDURBAR	118958	92782	92782	0	26176	39	1745
25	OSMANABAD	14408	7318	7318	0	7090	14	473
26	PUNE	20433	14175	14175	0	6258	9	417
27	RAIGAD	9820	8755	8755	0	1065	4	71
28	RATNAGIRI	9871	8764	8764	0	1107	14	74
29	SANGLI	21606	15496	15496	0	6110	11	407
30	SATARA	15243	11795	11795	0	3448	13	230
31	SINDHUDURG	5133	4368	4368	0	765	4	51
32	SOLAPUR	48394	33417	33417	0	14977	19	998
33	THANE	9599	7287	7287	0	2312	4	154
34	WASHIM	20362	12028	12028	0	8334	22	556
Total		1409275	1046866	1046926	60	362349	900	24157

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	20.05.2023	21.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	96568	96618	50	21812
2	AURANGABAD DIV.	200327	168926	168927	1	31400
3	KONKAN DIV.	34744	31861	31861	0	2883
4	PUNE DIV.	65859	63381	63381	0	2478
5	NASHIK DIV.	141552	112270	112270	0	29282
6	AMRAVATI DIV.	110155	94850	94850	0	15305
Total		671067	567856	567907	51	103160


Sr. No.	District	Target	20.05.2023	21.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	29596	29646	50	10639
2	BEED	26878	26045	26046	1	832
3	AHMEDNAGAR	35298	34423	34423	0	875
4	AKOLA	23681	17832	17832	0	5849
5	AMRAVATI	23224	19890	19890	0	3334
6	AURANGABAD	26141	24255	24255	0	1886
7	BHANDARA	17612	15606	15606	0	2006
8	BULDHANA	21702	20094	20094	0	1608
9	DHULE	21790	18088	18088	0	3702
10	GADCHIROLI	16834	15332	15332	0	1502
11	GONDIA	14261	13336	13336	0	925
12	HINGOLI	27298	16589	16589	0	10709
13	JALGAON	25851	22723	22723	0	3128
14	JALNA	20609	19324	19324	0	1285
15	KOLHAPUR	13090	12889	12889	0	201
16	LATUR	28004	26314	26314	0	1690
17	NAGPUR	16291	11448	11448	0	4843
18	NANDED	26760	21679	21679	0	5081
19	NANDURBAR	26578	14141	14141	0	12437
20	NASHIK	32035	22895	22895	0	9140
21	OSMANABAD	24853	17070	17070	0	7783
22	PALGHAR	11792	11479	11479	0	313
23	PARBHANI	19784	17650	17650	0	2134
24	PUNE	14672	12763	12763	0	1909
25	RAIGAD	7418	6600	6600	0	818
26	RATNAGIRI	7129	6691	6691	0	438
27	SANGLI	8732	8604	8604	0	128
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2108	2108	0	33
30	SOLAPUR	18718	18478	18478	0	240
31	THANE	6264	4983	4983	0	1281
32	WARDHA	13147	11250	11250	0	1897
33	WASHIM	11503	10510	10510	0	993
34	YAVATMAL	30045	26524	26524	0	3521
Total		671067	567856	567907	51	103160

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	240
PALGHAR	313
RATNAGIRI	438
RAIGAD	818
BEED	832
AHMEDNAGAR	875
GONDIA	925
WASHIM	993
THANE	1281
JALNA	1285
GADCHIROLI	1502
BULDHANA	1608
LATUR	1690
AURANGABAD	1886
WARDHA	1897
PUNE	1909
BHANDARA	2006
PARBHANI	2134
JALGAON	3128
AMRAVATI	3334
YAVATMAL	3521
DHULE	3702
NAGPUR	4843
NANDED	5081
AKOLA	5849
OSMANABAD	7783
NASHIK	9140
CHANDRAPUR	10639
HINGOLI	10709
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	20.05.2023	21.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI DIV.	94850	65709	65717	8	29133	52	1942
2	AURANGABAD DIV.	168927	105108	105115	7	63812	82	4254
3	PUNE DIV.	63381	52199	52203	4	11178	23	745
4	NASHIK DIV.	112270	89508	89512	4	22758	63	1517
5	NAGPUR DIV.	96618	70154	70158	4	26460	42	1764
6	KONKAN DIV.	31861	23978	23978	0	7883	14	526
Total		567907	406656	406683	27	161224	277	10748

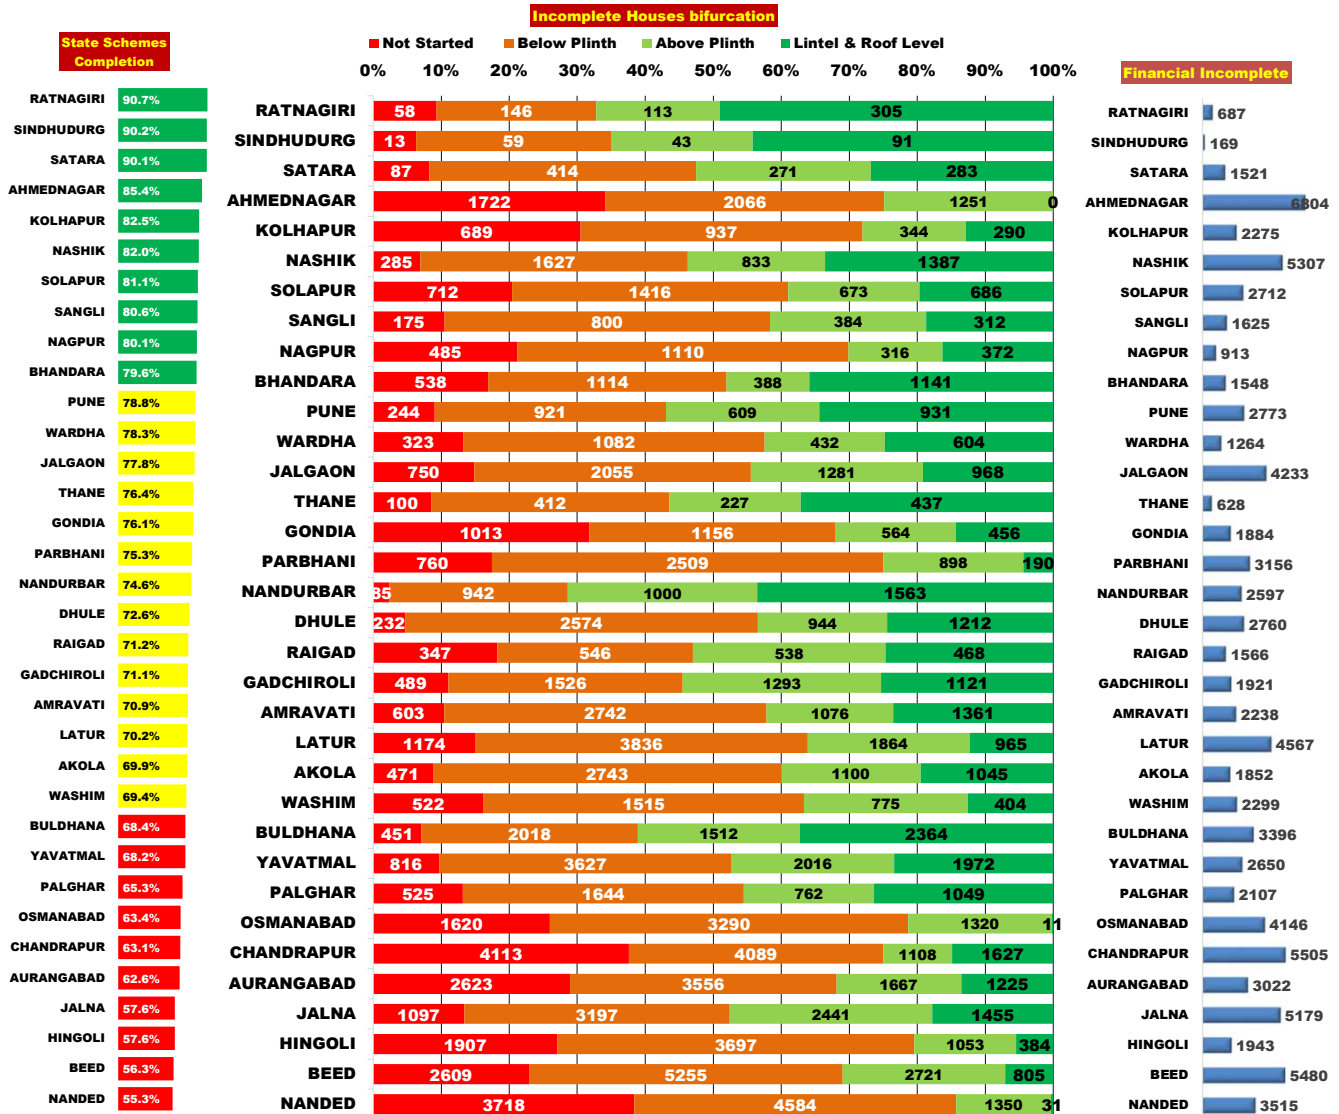

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	20.05.2023	21.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AHMEDNAGAR	34423	29399	29403	4	5020	26	335
2	KOLHAPUR	12889	10625	10629	4	2260	3	151
3	YAVATMAL	26524	18089	18093	4	8431	13	562
4	AMRAVATI	19890	14105	14108	3	5782	9	385
5	BEED	26046	14653	14656	3	11390	13	759
6	AURANGABAD	24255	15182	15184	2	9071	9	605
7	NAGPUR	11448	9163	9165	2	2283	3	152
8	WARDHA	11250	8807	8809	2	2441	6	163
9	BULDHANA	20094	13748	13749	1	6345	15	423
10	NANDED	21679	11995	11996	1	9683	8	646
11	PARBHANI	17650	13292	13293	1	4357	4	290
12	AKOLA	17832	12473	12473	0	5359	8	357
13	BHANDARA	15606	12425	12425	0	3181	4	212
14	CHANDRAPUR	29646	18709	18709	0	10937	12	729
15	DHULE	18088	13126	13126	0	4962	9	331
16	GADCHIROLI	15332	10903	10903	0	4429	9	295
17	GONDIA	13336	10147	10147	0	3189	8	213
18	HINGOLI	16589	9548	9548	0	7041	6	469
19	JALGAON	22723	17669	17669	0	5054	10	337
20	JALNA	19324	11134	11134	0	8190	22	546
21	LATUR	26314	18475	18475	0	7839	12	523
22	NANDURBAR	14141	10551	10551	0	3590	6	239
23	NASHIK	22895	18763	18763	0	4132	11	275
24	OSMANABAD	17070	10829	10829	0	6241	9	416
25	PALGHAR	11479	7499	7499	0	3980	6	265
26	PUNE	12763	10058	10058	0	2705	5	180
27	RAIGAD	6600	4701	4701	0	1899	3	127
28	RATNAGIRI	6691	6069	6069	0	622	3	41
29	SANGLI	8604	6933	6933	0	1671	3	111
30	SATARA	10647	9592	9592	0	1055	5	70
31	SINDHUDURG	2108	1902	1902	0	206	1	14
32	SOLAPUR	18478	14991	14991	0	3487	6	232
33	THANE	4983	3807	3807	0	1176	2	78
34	WASHIM	10510	7294	7294	0	3216	7	214
Total		567907	406656	406683	27	161224	277	10748

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	47	10192	101	38427	110	22925
2	AMRAVATI DIV.	29	29853	85	31439	120	16212
3	AURANGABAD DIV.	21	19774	122	51696	84	24631
4	NAGPUR DIV.	13	10143	50	20118	126	12441
5	KONKAN DIV.	12	369	32	3423	107	3281
6	PUNE DIV.	11	9383	22	16221	38	6884
Total		133	79714	412	161324	585	86374

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	12
THANE	75
RATNAGIRI	88
PALGHAR	190
GADCHIROLI	305
SANGLI	436
KOLHAPUR	522
SATARA	857
DHULE	971
NASHIK	1091
PARBHANI	1131
NANDURBAR	1309
GONDIA	1400
WARDHA	1562
NAGPUR	1879
JALNA	1894
HINGOLI	1985
CHANDRAPUR	2035
PUNE	2126
LATUR	2279
AURANGABAD	2697
BHANDARA	2962
WASHIM	2969
AHMEDNAGAR	2988
OSMANABAD	3108
BEED	3316
NANDED	3364
YAVATMAL	3795
JALGAON	3833
AKOLA	3871
SOLAPUR	5442
BULDHANA	7914
AMRAVATI	11304

PMAY-G 2nd Ins Pending

SINDHUDURG	219
RATNAGIRI	393
RAIGAD	514
THANE	588
SATARA	1099
WARDHA	1225
PALGHAR	1709
OSMANABAD	1853
PUNE	2286
KOLHAPUR	2557
GADCHIROLI	2626
NAGPUR	2913
HINGOLI	3096
WASHIM	3158
AHMEDNAGAR	3682
SANGLI	3906
GONDIA	3918
LATUR	4267
CHANDRAPUR	4344
JALNA	4406
AKOLA	4956
BHANDARA	5092
AURANGABAD	5581
PARBHANI	5782
NASHIK	5935
BULDHANA	6074
SOLAPUR	6373
DHULE	6822
BEED	8079
YAVATMAL	8605
AMRAVATI	8646
NANDURBAR	9488
JALGAON	12500
NANDED	18632

PMAY-G 3rd Ins Pending

SINDHUDURG	269
RAIGAD	381
RATNAGIRI	404
THANE	544
WARDHA	899
SATARA	976
KOLHAPUR	980
PUNE	1083
NAGPUR	1360
HINGOLI	1488
SANGLI	1527
PALGHAR	1683
LATUR	1881
AKOLA	2142
GADCHIROLI	2209
BHANDARA	2255
WASHIM	2307
SOLAPUR	2318
AURANGABAD	2478
CHANDRAPUR	2595
AHMEDNAGAR	2887
PARBHANI	2934
OSMANABAD	2979
JALNA	3009
BULDHANA	3034
GONDIA	3123
AMRAVATI	3393
BEED	3677
DHULE	3831
NASHIK	3937
JALGAON	4229
YAVATMAL	5336
NANDED	6185
NANDURBAR	8041

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	JALGAON	46	3833	54	12500	41	4229
2	PALGHAR	0	190	28	1709	72	1683
3	AKOLA	18	3871	36	4956	35	2142
4	AMRAVATI	9	11304	30	8646	49	3393
5	BHANDARA	3	2962	15	5092	53	2255
6	JALNA	3	1894	26	4406	28	3009
7	NANDURBAR	0	1309	24	9488	31	8041
8	GONDIA	4	1400	12	3918	37	3123
9	AURANGABAD	2	2697	17	5581	26	2478
10	PARBHANI	2	1131	31	5782	11	2934
11	BEED	6	3316	25	8079	9	3677
12	SOLAPUR	5	5442	14	6373	19	2318
13	WASHIM	0	2969	7	3158	25	2307
14	WARDHA	3	1562	11	1225	17	899
15	AHMEDNAGAR	0	2988	11	3682	15	2887
16	THANE	12	75	0	588	13	544
17	CHANDRAPUR	1	2035	11	4344	9	2595
18	OSMANABAD	8	3108	4	1853	8	2979
19	YAVATMAL	2	3795	12	8605	6	5336
20	NASHIK	0	1091	5	5935	14	3937
21	NANDED	0	3364	17	18632	1	6185
22	DHULE	1	971	7	6822	9	3831
23	SINDHUDURG	0	4	0	219	13	269
24	SATARA	2	857	5	1099	5	976
25	PUNE	0	2126	1	2286	10	1083
26	RATNAGIRI	0	88	3	393	8	404
27	NAGPUR	2	1879	1	2913	5	1360
28	KOLHAPUR	4	522	2	2557	1	980
29	BULDHANA	0	7914	0	6074	5	3034
30	GADCHIROLI	0	305	0	2626	5	2209
31	LATUR	0	2279	2	4267	1	1881
32	SANGLI	0	436	0	3906	3	1527
33	RAIGAD	0	12	1	514	1	381
34	HINGOLI	0	1985	0	3096	0	1488
	Total	133	79714	412	161324	585	86374

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AURANGABAD DIV.	109	15508	77	29924	65	13314
2	NAGPUR DIV.	88	6961	70	10077	69	4101
3	AMRAVATI DIV.	31	2863	40	12645	70	6479
4	NASHIK DIV.	8	3074	47	9264	48	5309
5	KONKAN DIV.	1	1043	20	2807	19	1683
6	PUNE DIV.	2	1907	3	4488	9	2281
Total		239	31356	257	69205	280	33167

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
NANDURBAR	85
SATARA	87
THANE	100
SANGLI	175
DHULE	232
PUNE	244
NASHIK	285
WARDHA	323
RAIGAD	347
BULDHANA	451
AKOLA	471
NAGPUR	485
GADCHIROLI	489
WASHIM	522
PALGHAR	525
BHANDARA	538
AMRAVATI	603
KOLHAPUR	689
SOLAPUR	712
JALGAON	750
PARBHANI	760
YAVATMAL	816
GONDIA	1013
JALNA	1097
LATUR	1174
OSMANABAD	1620
AHMEDNAGAR	1722
HINGOLI	1907
BEED	2609
AURANGABAD	2623
NANDED	3718
CHANDRAPUR	4113

State Schemes 2nd Ins Pending

SINDHUDURG	59
RATNAGIRI	146
THANE	412
SATARA	414
RAIGAD	546
SANGLI	800
PUNE	921
KOLHAPUR	937
NANDURBAR	942
WARDHA	1082
NAGPUR	1110
BHANDARA	1114
GONDIA	1156
SOLAPUR	1416
WASHIM	1515
GADCHIROLI	1526
NASHIK	1627
PALGHAR	1644
BULDHANA	2018
JALGAON	2055
AHMEDNAGAR	2066
PARBHANI	2509
DHULE	2574
AMRAVATI	2742
AKOLA	2743
JALNA	3197
OSMANABAD	3290
AURANGABAD	3556
YAVATMAL	3627
HINGOLI	3697
LATUR	3836
CHANDRAPUR	4089
NANDED	4584
BEED	5255

State Schemes 3rd Ins Pending

SINDHUDURG	43
RATNAGIRI	113
THANE	227
SATARA	271
NAGPUR	316
KOLHAPUR	344
SANGLI	384
BHANDARA	388
WARDHA	432
RAIGAD	538
GONDIA	564
PUNE	609
SOLAPUR	673
PALGHAR	762
WASHIM	775
NASHIK	833
PARBHANI	898
DHULE	944
NANDURBAR	1000
HINGOLI	1053
AMRAVATI	1076
AKOLA	1100
CHANDRAPUR	1108
AHMEDNAGAR	1251
JALGAON	1281
GADCHIROLI	1293
OSMANABAD	1320
NANDED	1350
BULDHANA	1512
AURANGABAD	1667
LATUR	1864
YAVATMAL	2016
JALNA	2441
BEED	2721

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AKOLA	12	471	14	2743	37	1100
2	CHANDRAPUR	46	4113	5	4089	6	1108
3	GADCHIROLI	0	489	32	1526	23	1293
4	GONDIA	37	1013	9	1156	9	564
5	JALNA	6	1097	27	3197	22	2441
6	NANDURBAR	0	85	28	942	27	1000
7	YAVATMAL	14	816	19	3627	21	2016
8	PARBHANI	39	760	6	2509	4	898
9	AURANGABAD	32	2623	4	3556	7	1667
10	LATUR	21	1174	6	3836	12	1864
11	NANDED	10	3718	16	4584	10	1350
12	WARDHA	2	323	12	1082	17	432
13	BHANDARA	3	538	10	1114	12	388
14	THANE	1	100	10	412	12	227
15	AHMEDNAGAR	0	1722	10	2066	12	1251
16	AMRAVATI	4	603	6	2742	10	1076
17	HINGOLI	1	1907	10	3697	4	1053
18	BEED	0	2609	8	5255	6	2721
19	JALGAON	8	750	4	2055	0	1281
20	DHULE	0	232	4	2574	7	944
21	PALGHAR	0	525	5	1644	4	762
22	RAIGAD	0	347	5	546	0	538
23	SATARA	1	87	2	414	2	271
24	BULDHANA	1	451	1	2018	2	1512
25	NAGPUR	0	485	2	1110	2	316
26	PUNE	0	244	0	921	4	609
27	SANGLI	1	175	1	800	2	384
28	NASHIK	0	285	1	1627	2	833
29	SINDHUDURG	0	13	0	59	3	43
30	SOLAPUR	0	712	0	1416	1	673
31	KOLHAPUR	0	689	0	937	0	344
32	OSMANABAD	0	1620	0	3290	0	1320
33	RATNAGIRI	0	58	0	146	0	113
34	WASHIM	0	522	0	1515	0	775
	Total	239	31356	257	69205	280	33167

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2403	1732	3122	1632	44
AKOLA	4157	3475	3487	871	579
AMRAVATI	7356	5525	7136	1506	1061
AURANGABAD	2395	2240	4811	1077	465
BEED	2183	1862	6751	1630	491
BHANDARA	6862	5167	4642	783	2291
BULDHANA	2636	2157	4114	855	740
CHANDRAPUR	3022	1948	3410	702	298
DHULE	5688	4094	5865	2350	1710
GADCHIROLI	3939	2446	2283	1230	936
GONDIA	1862	1793	3100	1011	143
HINGOLI	1029	667	2575	482	108
JALGAON	7857	6632	11006	2027	744
JALNA	1367	1081	3295	824	328
KOLHAPUR	1921	733	2348	294	111
LATUR	794	725	2765	472	55
NAGPUR	3317	2312	2532	440	588
NANDED	9632	9144	14660	2051	375
NANDURBAR	11506	9946	7158	4679	5242
NASHIK	7020	3574	4771	2053	1605
OSMANABAD	1043	584	1221	433	8
PALGHAR	892	640	1331	735	568
PARBHANI	857	736	4696	609	128
PUNE	2236	1724	1939	539	480
RAIGAD	730	239	477	240	166
RATNAGIRI	173	42	328	137	75
SANGLI	2959	2274	3485	585	153
SATARA	668	371	817	233	151
SINDDHURG	139	87	193	70	32
SOLAPUR	4932	4569	4969	1240	534
THANE	209	188	536	167	252
WARDHA	1142	798	928	211	242
WASHIM	1214	864	2486	440	100
YAVATMAL	6463	4355	6967	1845	1803
