



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २३.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९२३४	०	१०४८८३०	१८५२	०	०	०
राज्य योजना	५६८०९४	१३४	४०७०११	३१०	०	०	०
एकूण	१९७७३२८	१३४	१४५५९४१	२१६२	०	०	०

PMAY-G Completion Progress Bar

74.4%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

71.6%


State Schemes: Incomplete Houses bifurcation

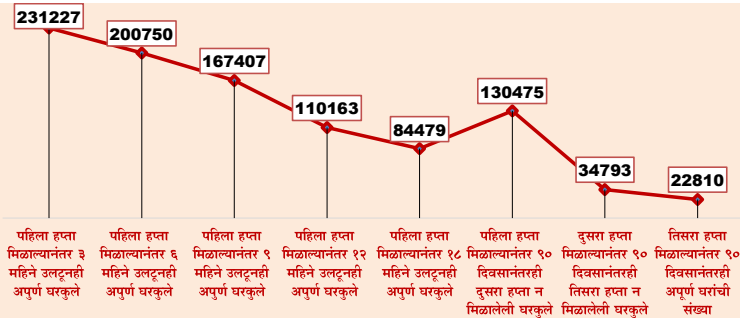


Abhiyan Achievement Day 184

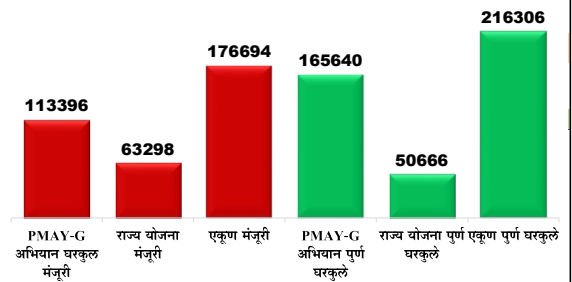

PMAY-G : House completion (Abhiyan Achievement)

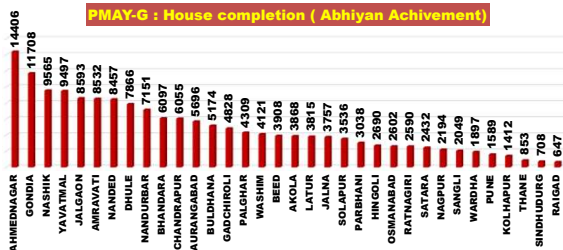

State Schemes : House completion (Abhiyan Achievement)

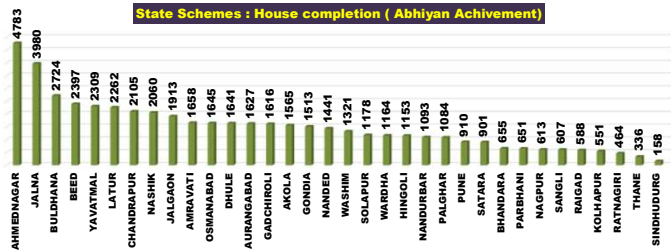


राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	22.05.2023	23.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414813	413556	413544	0	1269
2	AMRAVATI DIV.	274769	274281	274279	0	490
3	AURANGABAD DIV.	238003	237299	237299	0	704
4	NAGPUR DIV.	291895	291215	291214	0	681
5	KONKAN DIV.	69832	69611	69611	0	221
6	PUNE DIV.	124373	123313	123287	0	1086
Total		1413685	1409275	1409234	0	4451

Sr. No.	District	Target (PWL+Awaas Plus)	22.05.2023	23.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60787	60752	60752	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95496	95248	95248	0	248
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	CHANDRAPUR	43093	42958	42958	0	135
7	DHULE	64999	64917	64917	0	82
8	GADCHIROLI	31703	31615	31615	0	88
9	GONDIA	96493	96138	96138	0	355
10	HINGOLI	18109	18083	18083	0	26
11	JALNA	24038	24023	24023	0	15
12	KOLHAPUR	17658	17637	17637	0	21
13	LATUR	20679	20493	20493	0	186
14	NAGPUR	36992	36977	36977	0	15
15	NANDED	69533	69463	69463	0	70
16	NANDURBAR	119606	118958	118958	0	648
17	NASHIK	89735	89683	89683	0	52
18	OSMANABAD	14506	14408	14408	0	98
19	PALGHAR	35376	35188	35188	0	188
20	PARBHANI	19088	19062	19062	0	26
21	PUNE	20513	20433	20433	0	80
22	RAIGAD	9830	9820	9820	0	10
23	RATNAGIRI	9888	9871	9871	0	17
24	SANGLI	21778	21606	21606	0	172
25	SINDHUDURG	5133	5133	5133	0	0
26	SOLAPUR	49095	48394	48394	0	701
27	THANE	9605	9599	9599	0	6
28	WARDHA	18633	18607	18607	0	26
29	WASHIM	20390	20362	20362	0	28
30	YAVATMAL	65339	65180	65180	0	159
31	BHANDARA	64981	64920	64919	-1	62
32	BULDHANA	44752	44713	44711	-2	41
33	JALGAON	79686	79246	79234	-12	452
34	SATARA	15329	15243	15217	-26	112
Total		1413685	1409275	1409234	0	4451

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
KOLHAPUR	21
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	28
AHMEDNAGAR	35
BULDHANA	41
NASHIK	52
BEED	57
BHANDARA	62
NANDED	70
PUNE	80
DHULE	82
GADCHIROLI	88
OSMANABAD	98
SATARA	112
CHANDRAPUR	135
YAVATMAL	159
SANGLI	172
LATUR	186
PALGHAR	188
AURANGABAD	226
AMRAVATI	248
GONDIA	355
JALGAON	452
NANDURBAR	648
SOLAPUR	701

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1294	630	664	29
16	NASHIK	1802	1324	478	1803	1072	731	252
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1666	1137	2829	1347	1482	319
21	NAGPUR	5054	3588	1466	5018	3443	1575	145
22	LATUR	2299	1121	1178	2310	477	1833	644
23	JALGAON	22928	20121	2807	22877	20944	1933	-823
24	PUNE	2924	1602	1322	2889	885	2004	717
25	BHANDARA	5782	3543	2239	5669	3266	2403	277
26	YAVATMAL	3612	1450	2162	3673	1269	2404	181
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3443	865	2578	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7755	4453	3302	-270
31	AKOLA	7072	3935	3137	7367	3903	3464	32
32	SOLAPUR	7297	3684	3613	7228	1410	5818	2274
33	BULDHANA	15191	10571	4620	15210	7977	7233	2594
34	AMRAVATI	21529	12817	8712	21543	11392	10151	1425
	Total	127095	80050	47045	127139	69326	57813	12084

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	22.05.2023	23.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237299	141002	141524	522	95775	185	7367
2	AMRAVATI DIV.	274279	187902	188349	447	85930	170	6610
3	NASHIK DIV.	413544	330738	331095	357	82449	259	6342
4	NAGPUR DIV.	291214	240628	240907	279	50307	178	3870
5	KONKAN DIV.	69611	58359	58515	156	11096	49	854
6	PUNE DIV.	123287	88349	88440	91	34847	60	2681
Total		1409234	1046978	1048830	1852	360404	900	27723

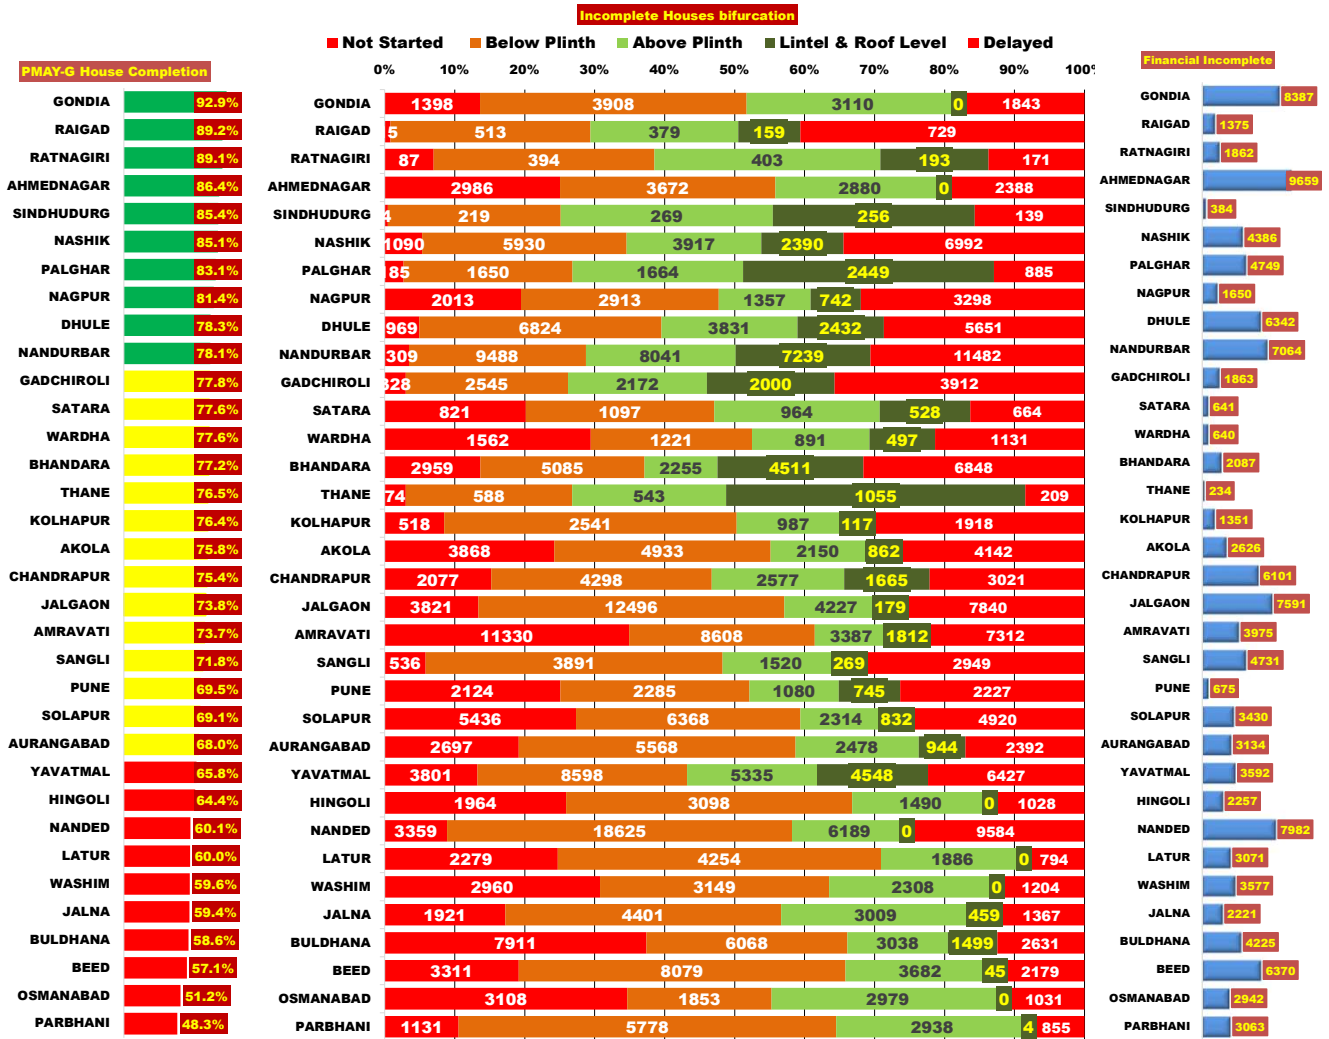

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	22.05.2023	23.05.2023	Daily Achievement	Remaining	Aug. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	69463	41537	41767	230	27696	46	2130
2	YAVATMAL	65180	42761	42905	144	22275	52	1713
3	AMRAVATI	95248	70016	70157	141	25091	46	1930
4	DHULE	64917	50759	50861	102	14056	43	1081
5	NANDURBAR	118958	92784	92881	97	26077	39	2006
6	WASHIM	20362	12031	12127	96	8235	22	633
7	GONDIA	96138	89202	89286	84	6852	64	527
8	NASHIK	89683	76281	76356	75	13327	52	1025
9	GADCHIROLI	31615	24527	24595	68	7020	26	540
10	BEED	35253	20069	20136	67	15117	21	1163
11	OSMANABAD	14408	7318	7382	64	7026	14	540
12	LATUR	20493	12231	12289	58	8204	21	631
13	PALGHAR	35188	29185	29240	55	5948	23	458
14	THANE	9599	7287	7339	52	2260	5	174
15	AURANGABAD	36514	24777	24828	51	11686	31	899
16	AKOLA	48778	36915	36965	50	11813	21	909
17	NAGPUR	36977	30037	30087	50	6890	12	530
18	AHMEDNAGAR	60752	52437	52486	49	8266	78	636
19	WARDHA	18607	14396	14436	40	4171	10	321
20	JALGAON	79234	58477	58511	34	20723	47	1594
21	RATNAGIRI	9871	8764	8794	30	1077	14	83
22	BHANDARA	64919	50081	50109	28	14810	33	1139
23	SOLAPUR	48394	33417	33444	27	14950	19	1150
24	PUNE	20433	14175	14199	24	6234	9	480
25	HINGOLI	18083	11627	11648	21	6435	15	495
26	PARBHANI	19062	9191	9211	20	9851	17	758
27	SANGLI	21606	15496	15516	20	6090	11	468
28	SINDHUDURG	5133	4368	4385	17	748	4	58
29	BULDHANA	44711	26179	26195	16	18516	28	1424
30	SATARA	15217	11795	11807	12	3410	13	262
31	JALNA	24023	14252	14263	11	9760	20	751
32	CHANDRAPUR	42958	32385	32394	9	10564	33	813
33	KOLHAPUR	17637	13466	13474	8	4163	8	320
34	RAIGAD	9820	8755	8757	2	1063	4	82
Total		1409234	1046978	1048830	1852	360404	900	27723

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	22.05.2023	23.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	96618	96704	86	21726
2	KONKAN DIV.	34744	31861	31891	30	2853
3	AURANGABAD DIV.	200327	168980	168998	18	31329
4	PUNE DIV.	65859	63381	63381	0	2478
5	NASHIK DIV.	141552	112270	112270	0	29282
6	AMRAVATI DIV.	110155	94850	94850	0	15305
Total		671067	567960	568094	134	102973


Sr. No.	District	Target	22.05.2023	23.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	29646	29728	82	10557
2	PALGHAR	11792	11479	11509	30	283
3	NANDED	26760	21732	21750	18	5010
4	GADCHIROLI	16834	15332	15335	3	1499
5	GONDIA	14261	13336	13337	1	924
6	AHMEDNAGAR	35298	34423	34423	0	875
7	AKOLA	23681	17832	17832	0	5849
8	AMRAVATI	23224	19890	19890	0	3334
9	AURANGABAD	26141	24255	24255	0	1886
10	BEED	26878	26046	26046	0	832
11	BHANDARA	17612	15606	15606	0	2006
12	BULDHANA	21702	20094	20094	0	1608
13	DHULE	21790	18088	18088	0	3702
14	HINGOLI	27298	16589	16589	0	10709
15	JALGAON	25851	22723	22723	0	3128
16	JALNA	20609	19324	19324	0	1285
17	KOLHAPUR	13090	12889	12889	0	201
18	LATUR	28004	26314	26314	0	1690
19	NAGPUR	16291	11448	11448	0	4843
20	NANDURBAR	26578	14141	14141	0	12437
21	NASHIK	32035	22895	22895	0	9140
22	OSMANABAD	24853	17070	17070	0	7783
23	PARBHANI	19784	17650	17650	0	2134
24	PUNE	14672	12763	12763	0	1909
25	RAIGAD	7418	6600	6600	0	818
26	RATNAGIRI	7129	6691	6691	0	438
27	SANGLI	8732	8604	8604	0	128
28	SATARA	10647	10647	10647	0	0
29	SINDHUDURG	2141	2108	2108	0	33
30	SOLAPUR	18718	18478	18478	0	240
31	THANE	6264	4983	4983	0	1281
32	WARDHA	13147	11250	11250	0	1897
33	WASHIM	11503	10510	10510	0	993
34	YAVATMAL	30045	26524	26524	0	3521
Total		671067	567960	568094	134	102973

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	240
PALGHAR	283
RATNAGIRI	438
RAIGAD	818
BEED	832
AHMEDNAGAR	875
GONDIA	924
WASHIM	993
THANE	1281
JALNA	1285
GADCHIROLI	1499
BULDHANA	1608
LATUR	1690
AURANGABAD	1886
WARDHA	1897
PUNE	1909
BHANDARA	2006
PARBHANI	2134
JALGAON	3128
AMRAVATI	3334
YAVATMAL	3521
DHULE	3702
NAGPUR	4843
NANDED	5010
AKOLA	5849
OSMANABAD	7783
NASHIK	9140
CHANDRAPUR	10557
HINGOLI	10709
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	22.05.2023	23.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	168998	105121	105262	141	63736	82	4903
2	AMRAVATI DIV.	94850	65725	65775	50	29075	52	2237
3	NAGPUR DIV.	96704	70162	70211	49	26493	42	2038
4	NASHIK DIV.	112270	89512	89547	35	22723	62	1748
5	KONKAN DIV.	31891	23978	24004	26	7887	14	607
6	PUNE DIV.	63381	52203	52212	9	11169	23	859
Total		568094	406701	407011	310	161083	275	12391

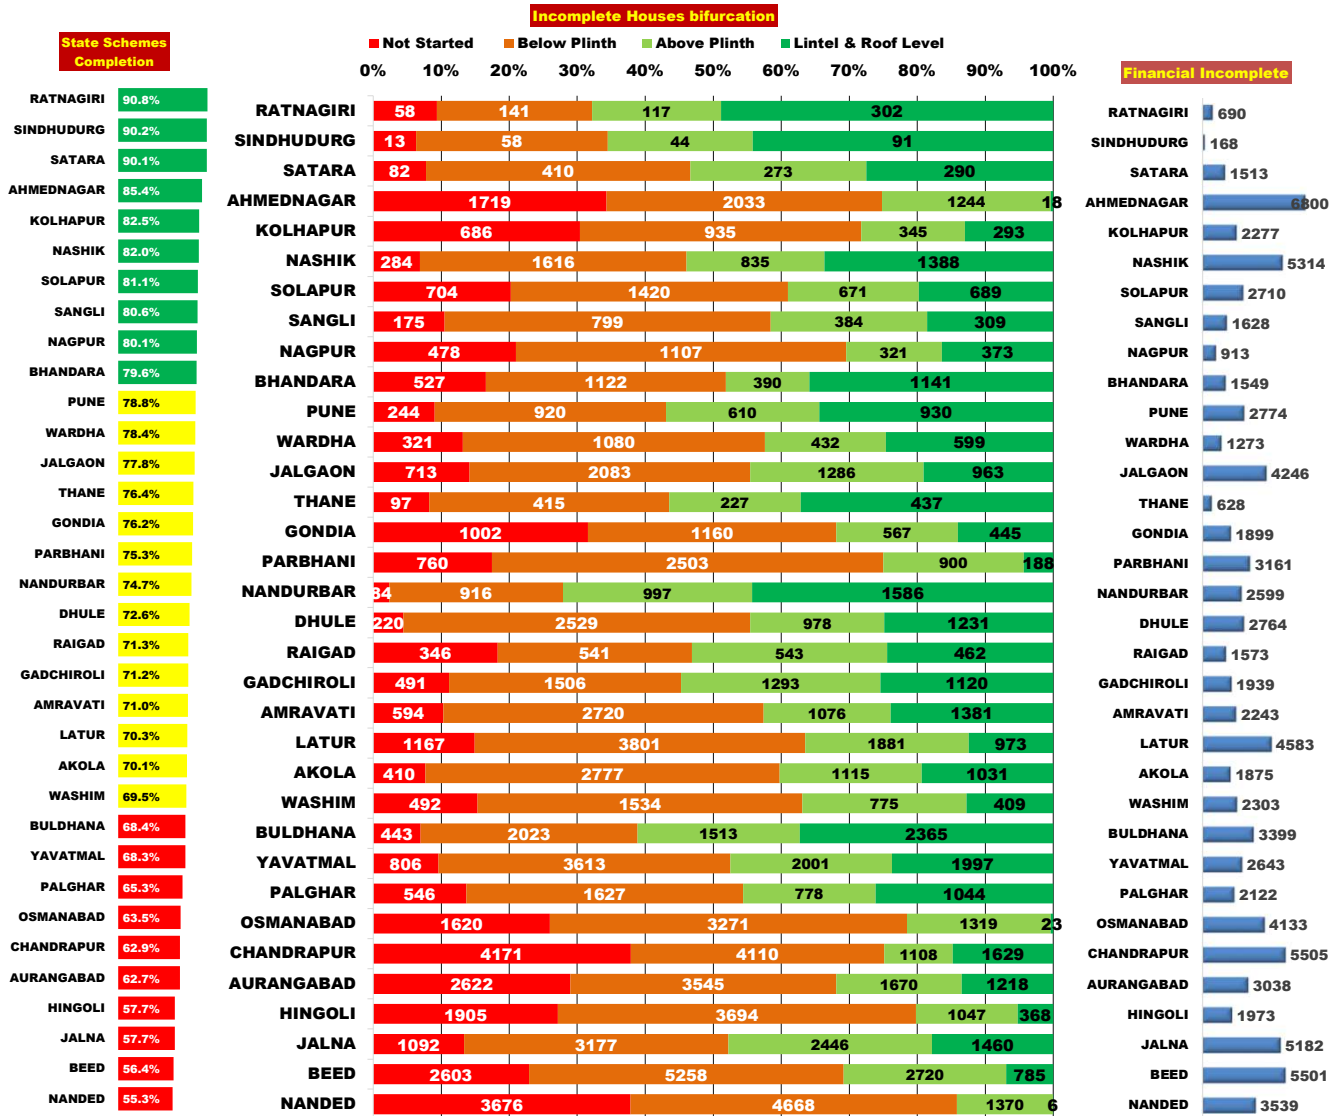

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	22.05.2023	23.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	21750	11996	12030	34	9720	8	748
2	HINGOLI	16589	9548	9575	27	7014	6	540
3	AKOLA	17832	12474	12499	25	5333	9	410
4	BEED	26046	14656	14680	24	11366	13	874
5	GADCHIROLI	15335	10905	10925	20	4410	9	339
6	LATUR	26314	18475	18492	17	7822	12	602
7	AURANGABAD	24255	15184	15200	16	9055	9	697
8	GONDIA	13337	10147	10163	16	3174	8	244
9	PALGHAR	11509	7499	7514	15	3995	6	307
10	AMRAVATI	19890	14108	14119	11	5771	9	444
11	JALGAON	22723	17669	17678	9	5045	10	388
12	JALNA	19324	11140	11149	9	8175	22	629
13	NASHIK	22895	18763	18772	9	4123	11	317
14	WARDHA	11250	8809	8818	9	2432	6	187
15	YAVATMAL	26524	18098	18107	9	8417	13	647
16	OSMANABAD	17070	10829	10837	8	6233	9	479
17	NANDURBAR	14141	10551	10558	7	3583	6	276
18	RAIGAD	6600	4701	4708	7	1892	3	146
19	AHMEDNAGAR	34423	29403	29409	6	5014	26	386
20	PARBHANI	17650	13293	13299	6	4351	4	335
21	WASHIM	10510	7295	7300	5	3210	7	247
22	DHULE	18088	13126	13130	4	4958	9	381
23	RATNAGIRI	6691	6069	6073	4	618	3	48
24	SANGLI	8604	6933	6937	4	1667	3	128
25	SOLAPUR	18478	14991	14994	3	3484	6	268
26	NAGPUR	11448	9167	9169	2	2279	3	175
27	BHANDARA	15606	12425	12426	1	3180	4	245
28	CHANDRAPUR	29728	18709	18710	1	11018	11	848
29	KOLHAPUR	12889	10629	10630	1	2259	3	174
30	PUNE	12763	10058	10059	1	2704	5	208
31	BULDHANA	20094	13750	13750	0	6344	15	488
32	SATARA	10647	9592	9592	0	1055	5	81
33	SINDHUDURG	2108	1902	1902	0	206	1	16
34	THANE	4983	3807	3807	0	1176	2	90
	Total	568094	406701	407011	310	161083	275	12391

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10175	0	38410	0	22896
2	AMRAVATI DIV.	0	29814	0	31356	0	16218
3	AURANGABAD DIV.	0	19739	0	51656	0	24651
4	NAGPUR DIV.	0	10124	0	19970	0	12362
5	KONKAN DIV.	0	362	0	3364	0	3258
6	PUNE DIV.	0	9309	0	16182	0	6865
	Total	0	79523	0	160938	0	86250

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	12
THANE	74
RATNAGIRI	87
PALGHAR	185
GADCHIROLI	303
SANGLI	410
KOLHAPUR	518
SATARA	821
DHULE	969
NASHIK	1090
PARBHANI	1131
NANDURBAR	1309
GONDIA	1398
WARDHA	1562
NAGPUR	1878
JALNA	1891
HINGOLI	1964
CHANDRAPUR	2024
PUNE	2124
LATUR	2279
AURANGABAD	2696
WASHIM	2957
BHANDARA	2959
AHMEDNAGAR	2986
OSMANABAD	3108
BEED	3311
NANDED	3359
YAVATMAL	3794
JALGAON	3821
AKOLA	3868
SOLAPUR	5436
BULDHANA	7911
AMRAVATI	11284

PMAY-G 2nd Ins Pending

SINDHUDURG	219
RATNAGIRI	394
RAIGAD	513
THANE	588
SATARA	1097
WARDHA	1221
PALGHAR	1650
OSMANABAD	1853
PUNE	2285
KOLHAPUR	2541
GADCHIROLI	2545
NAGPUR	2913
HINGOLI	3098
WASHIM	3149
AHMEDNAGAR	3672
SANGLI	3891
GONDIA	3908
LATUR	4254
CHANDRAPUR	4298
JALNA	4401
AKOLA	4933
BHANDARA	5085
AURANGABAD	5568
PARBHANI	5778
NASHIK	5930
BULDHANA	6068
SOLAPUR	6368
DHULE	6824
BEED	8079
YAVATMAL	8598
AMRAVATI	8608
NANDURBAR	9488
JALGAON	12496
NANDED	18625

PMAY-G 3rd Ins Pending

SINDHUDURG	269
RAIGAD	379
RATNAGIRI	403
THANE	543
WARDHA	891
SATARA	964
KOLHAPUR	987
PUNE	1080
NAGPUR	1357
HINGOLI	1490
SANGLI	1520
PALGHAR	1664
LATUR	1886
AKOLA	2150
GADCHIROLI	2172
BHANDARA	2255
WASHIM	2308
SOLAPUR	2314
AURANGABAD	2478
CHANDRAPUR	2577
AHMEDNAGAR	2880
PARBHANI	2938
OSMANABAD	2979
JALNA	3009
BULDHANA	3038
GONDIA	3110
AMRAVATI	3387
BEED	3682
DHULE	3831
NASHIK	3917
JALGAON	4227
YAVATMAL	5335
NANDED	6189
NANDURBAR	8041

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	2986	0	3672	0	2880
2	AKOLA	0	3868	0	4933	0	2150
3	AMRAVATI	0	11284	0	8608	0	3387
4	AURANGABAD	0	2696	0	5568	0	2478
5	BEED	0	3311	0	8079	0	3682
6	BHANDARA	0	2959	0	5085	0	2255
7	BULDHANA	0	7911	0	6068	0	3038
8	CHANDRAPUR	0	2024	0	4298	0	2577
9	DHULE	0	969	0	6824	0	3831
10	GADCHIROLI	0	303	0	2545	0	2172
11	GONDIA	0	1398	0	3908	0	3110
12	HINGOLI	0	1964	0	3098	0	1490
13	JALGAON	0	3821	0	12496	0	4227
14	JALNA	0	1891	0	4401	0	3009
15	KOLHAPUR	0	518	0	2541	0	987
16	LATUR	0	2279	0	4254	0	1886
17	NAGPUR	0	1878	0	2913	0	1357
18	NANDED	0	3359	0	18625	0	6189
19	NANDURBAR	0	1309	0	9488	0	8041
20	NASHIK	0	1090	0	5930	0	3917
21	OSMANABAD	0	3108	0	1853	0	2979
22	PALGHAR	0	185	0	1650	0	1664
23	PARBHANI	0	1131	0	5778	0	2938
24	PUNE	0	2124	0	2285	0	1080
25	RAIGAD	0	12	0	513	0	379
26	RATNAGIRI	0	87	0	394	0	403
27	SANGLI	0	410	0	3891	0	1520
28	SATARA	0	821	0	1097	0	964
29	SINDHUDURG	0	4	0	219	0	269
30	SOLAPUR	0	5436	0	6368	0	2314
31	THANE	0	74	0	588	0	543
32	WARDHA	0	1562	0	1221	0	891
33	WASHIM	0	2957	0	3149	0	2308
34	YAVATMAL	0	3794	0	8598	0	5335
	Total	0	79523	0	160938	0	86250

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	3020	0	9177	0	5340
2	AMRAVATI DIV.	0	2745	0	12667	0	6480
3	AURANGABAD DIV.	0	15445	0	29917	0	13353
4	NAGPUR DIV.	0	6990	0	10085	0	4111
5	KONKAN DIV.	0	1060	0	2782	0	1709
6	PUNE DIV.	0	1891	0	4484	0	2283
Total		0	31151	0	69112	0	33276

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
SATARA	82
NANDURBAR	84
THANE	97
SANGLI	175
DHULE	220
PUNE	244
NASHIK	284
WARDHA	321
RAIGAD	346
AKOLA	410
BULDHANA	443
NAGPUR	478
GADCHIROLI	491
WASHIM	492
BHANDARA	527
PALGHAR	546
AMRAVATI	594
KOLHAPUR	686
SOLAPUR	704
JALGAON	713
PARBHANI	760
YAVATMAL	806
GONDIA	1002
JALNA	1092
LATUR	1167
OSMANABAD	1620
AHMEDNAGAR	1719
HINGOLI	1905
BEED	2603
AURANGABAD	2622
NANDED	3676
CHANDRAPUR	4171

State Schemes 2nd Ins Pending

SINDHUDURG	58
RATNAGIRI	141
SATARA	410
THANE	415
RAIGAD	541
SANGLI	799
NANDURBAR	916
PUNE	920
KOLHAPUR	935
WARDHA	1080
NAGPUR	1107
BHANDARA	1122
GONDIA	1160
SOLAPUR	1420
GADCHIROLI	1506
WASHIM	1534
NASHIK	1616
PALGHAR	1627
BULDHANA	2023
AHMEDNAGAR	2033
JALGAON	2083
PARBHANI	2503
DHULE	2529
AMRAVATI	2720
AKOLA	2777
JALNA	3177
OSMANABAD	3271
AURANGABAD	3545
YAVATMAL	3613
HINGOLI	3694
LATUR	3801
CHANDRAPUR	4110
NANDED	4668
BEED	5258

State Schemes 3rd Ins Pending

SINDHUDURG	44
RATNAGIRI	117
THANE	227
SATARA	273
NAGPUR	321
KOLHAPUR	345
SANGLI	384
BHANDARA	390
WARDHA	432
RAIGAD	543
GONDIA	567
PUNE	610
SOLAPUR	671
WASHIM	775
PALGHAR	778
NASHIK	835
PARBHANI	900
DHULE	978
NANDURBAR	997
HINGOLI	1047
AMRAVATI	1076
CHANDRAPUR	1108
AKOLA	1115
AHMEDNAGAR	1244
JALGAON	1286
GADCHIROLI	1293
OSMANABAD	1319
NANDED	1370
BULDHANA	1513
AURANGABAD	1670
LATUR	1881
YAVATMAL	2001
JALNA	2446
BEED	2720

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	1719	0	2033	0	1244
2	AKOLA	0	410	0	2777	0	1115
3	AMRAVATI	0	594	0	2720	0	1076
4	AURANGABAD	0	2622	0	3545	0	1670
5	BEED	0	2603	0	5258	0	2720
6	BHANDARA	0	527	0	1122	0	390
7	BULDHANA	0	443	0	2023	0	1513
8	CHANDRAPUR	0	4171	0	4110	0	1108
9	DHULE	0	220	0	2529	0	978
10	GADCHIROLI	0	491	0	1506	0	1293
11	GONDIA	0	1002	0	1160	0	567
12	HINGOLI	0	1905	0	3694	0	1047
13	JALGAON	0	713	0	2083	0	1286
14	JALNA	0	1092	0	3177	0	2446
15	KOLHAPUR	0	686	0	935	0	345
16	LATUR	0	1167	0	3801	0	1881
17	NAGPUR	0	478	0	1107	0	321
18	NANDED	0	3676	0	4668	0	1370
19	NANDURBAR	0	84	0	916	0	997
20	NASHIK	0	284	0	1616	0	835
21	OSMANABAD	0	1620	0	3271	0	1319
22	PALGHAR	0	546	0	1627	0	778
23	PARBHANI	0	760	0	2503	0	900
24	PUNE	0	244	0	920	0	610
25	RAIGAD	0	346	0	541	0	543
26	RATNAGIRI	0	58	0	141	0	117
27	SANGLI	0	175	0	799	0	384
28	SATARA	0	82	0	410	0	273
29	SINDHUDURG	0	13	0	58	0	44
30	SOLAPUR	0	704	0	1420	0	671
31	THANE	0	97	0	415	0	227
32	WARDHA	0	321	0	1080	0	432
33	WASHIM	0	492	0	1534	0	775
34	YAVATMAL	0	806	0	3613	0	2001
	Total	0	31151	0	69112	0	33276

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
 ■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

जिल्हा	पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले	पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले	दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले	तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या
AHMEDNAGAR	2388	1725	3147	1672	44
AKOLA	4142	3465	3462	870	575
AMRAVATI	7312	5503	7119	1516	1061
AURANGABAD	2392	2238	4859	1096	469
BEED	2179	1858	6764	1636	495
BHANDARA	6848	5158	4643	797	2334
BULDHANA	2631	2153	4176	891	757
CHANDRAPUR	3021	1947	3385	719	308
DHULE	5651	4082	5861	2378	1695
GADCHIROLI	3912	2441	2214	1177	961
GONDIA	1843	1777	3098	1015	143
HINGOLI	1028	666	2578	481	110
JALGAON	7840	6620	11029	2063	751
JALNA	1367	1081	3315	839	339
KOLHAPUR	1918	732	2329	289	111
LATUR	794	725	2816	485	54
NAGPUR	3298	2302	2533	437	577
NANDED	9584	9099	14729	2066	386
NANDURBAR	11482	9931	7193	4689	5217
NASHIK	6992	3570	4775	2055	1601
OSMANABAD	1031	582	1221	436	8
PALGHAR	885	635	1290	738	590
PARBHANI	855	734	4697	636	132
PUNE	2227	1718	1951	542	487
RAIGAD	729	239	476	241	166
RATNAGIRI	171	41	331	144	81
SANGLI	2949	2267	3455	591	164
SATARA	664	370	819	237	160
SINDHUDURG	139	87	193	72	35
SOLAPUR	4920	4558	5072	1254	542
THANE	209	188	538	196	306
WARDHA	1131	793	925	213	235
WASHIM	1204	857	2482	447	97
YAVATMAL	6427	4337	7000	1875	1819
