



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : २४.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०९११८	०	१०५१५६८	२७३८	२४३	७५५	९१७
राज्य योजना	५६८४०४	३१०	४०८२२२	१२११	६३९	५५६	३९४
एकूण	१९७७५२२	३१०	१४५९७९०	३९४९	८८२	१३११	१३११

PMAY-G Completion Progress Bar

74.6%



PMAY-G: Incomplete Houses bifurcation




State Schemes Progress Bar

71.8%


State Schemes: Incomplete Houses bifurcation

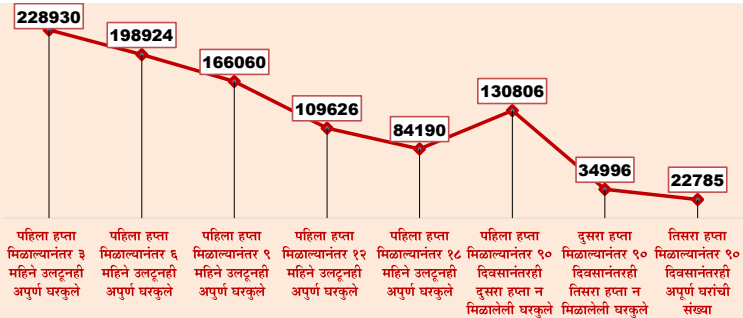


Abhiyan Achievement Day 185

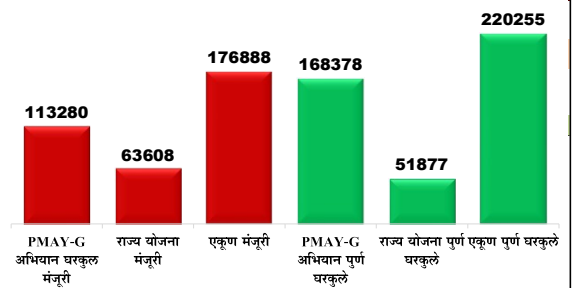

PMAY-G : House completion (Abhiyan Achievement)

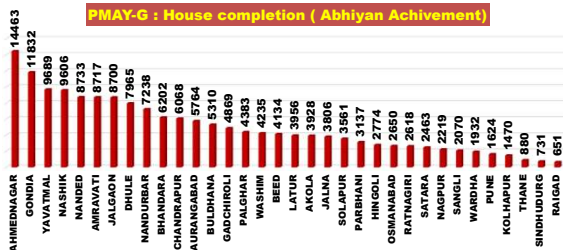

State Schemes : House completion (Abhiyan Achievement)

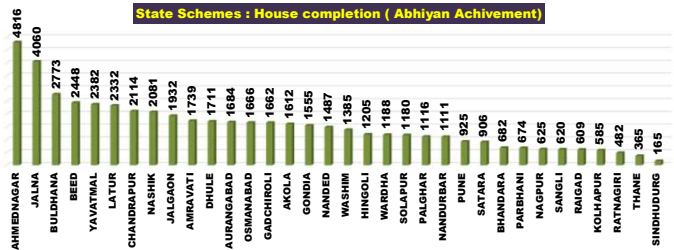

राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.



PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.




PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	23.05.2023	24.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414813	413544	413544	0	1269
2	AMRAVATI DIV.	274751	274279	274229	0	522
3	AURANGABAD DIV.	238003	237299	237299	0	704
4	NAGPUR DIV.	291887	291214	291207	0	680
5	KONKAN DIV.	69832	69611	69611	0	221
6	PUNE DIV.	124345	123287	123228	0	1117
Total		1413631	1409234	1409118	0	4513

Sr. No.	District	Target (PWL+Awaas Plus)	23.05.2023	24.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60787	60752	60752	0	35
2	AKOLA	48792	48778	48778	0	14
3	AURANGABAD	36740	36514	36514	0	226
4	BEED	35310	35253	35253	0	57
5	BHANDARA	64980	64919	64919	0	61
6	CHANDRAPUR	43093	42958	42958	0	135
7	DHULE	64999	64917	64917	0	82
8	GADCHIROLI	31703	31615	31615	0	88
9	GONDIA	96493	96138	96138	0	355
10	HINGOLI	18109	18083	18083	0	26
11	JALGAON	79686	79234	79234	0	452
12	JALNA	24038	24023	24023	0	15
13	LATUR	20679	20493	20493	0	186
14	NANDED	69533	69463	69463	0	70
15	NANDURBAR	119606	118958	118958	0	648
16	NASHIK	89735	89683	89683	0	52
17	OSMANABAD	14506	14408	14408	0	98
18	PALGHAR	35376	35188	35188	0	188
19	PARBHANI	19088	19062	19062	0	26
20	RAIGAD	9830	9820	9820	0	10
21	RATNAGIRI	9888	9871	9871	0	17
22	SANGLI	21778	21606	21606	0	172
23	SINDHUDURG	5133	5133	5133	0	0
24	SOLAPUR	49095	48394	48394	0	701
25	THANE	9605	9599	9599	0	6
26	WARDHA	18633	18607	18607	0	26
27	WASHIM	20390	20362	20362	0	28
28	SATARA	15324	15217	15216	-1	108
29	AMRAVATI	95490	95248	95242	-6	248
30	NAGPUR	36985	36977	36970	-7	15
31	PUNE	20506	20433	20426	-7	80
32	BULDHANA	44740	44711	44701	-10	39
33	YAVATMAL	65339	65180	65146	-34	193
34	KOLHAPUR	17642	17637	17586	-51	56
Total		1413631	1409234	1409118	0	4513

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	28
AHMEDNAGAR	35
BULDHANA	39
NASHIK	52
KOLHAPUR	56
BEED	57
BHANDARA	61
NANDED	70
PUNE	80
DHULE	82
GADCHIROLI	88
OSMANABAD	98
SATARA	108
CHANDRAPUR	135
SANGLI	172
LATUR	186
PALGHAR	188
YAVATMAL	193
AURANGABAD	226
AMRAVATI	248
GONDIA	355
JALGAON	452
NANDURBAR	648
SOLAPUR	701

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1294	630	664	29
16	NASHIK	1802	1324	478	1803	1072	731	252
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1666	1137	2829	1347	1482	319
21	NAGPUR	5054	3588	1466	5011	3443	1568	145
22	LATUR	2299	1121	1178	2310	477	1833	644
23	JALGAON	22928	20121	2807	22877	20944	1933	-823
24	PUNE	2924	1602	1322	2882	885	1997	717
25	YAVATMAL	3612	1450	2162	3665	1291	2374	159
26	BHANDARA	5782	3543	2239	5669	3266	2403	277
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3443	865	2578	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7755	4453	3302	-270
31	AKOLA	7072	3935	3137	7367	3905	3462	30
32	SOLAPUR	7297	3684	3613	7228	1410	5818	2274
33	BULDHANA	15191	10571	4620	15600	7977	7623	2594
34	AMRAVATI	21529	12817	8712	21539	11392	10147	1425
	Total	127095	80050	47045	127503	69350	58153	12060

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	23.05.2023	24.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237299	141524	142515	991	94784	189	7899
2	AMRAVATI DIV.	274229	188349	189036	687	85193	172	7099
3	NASHIK DIV.	413544	331095	331486	391	82058	259	6838
4	NAGPUR DIV.	291207	240907	241250	343	49957	179	4163
5	PUNE DIV.	123228	88440	88610	170	34618	60	2885
6	KONKAN DIV.	69611	58515	58671	156	10940	50	912
Total		1409118	1048830	1051568	2738	357550	910	29796

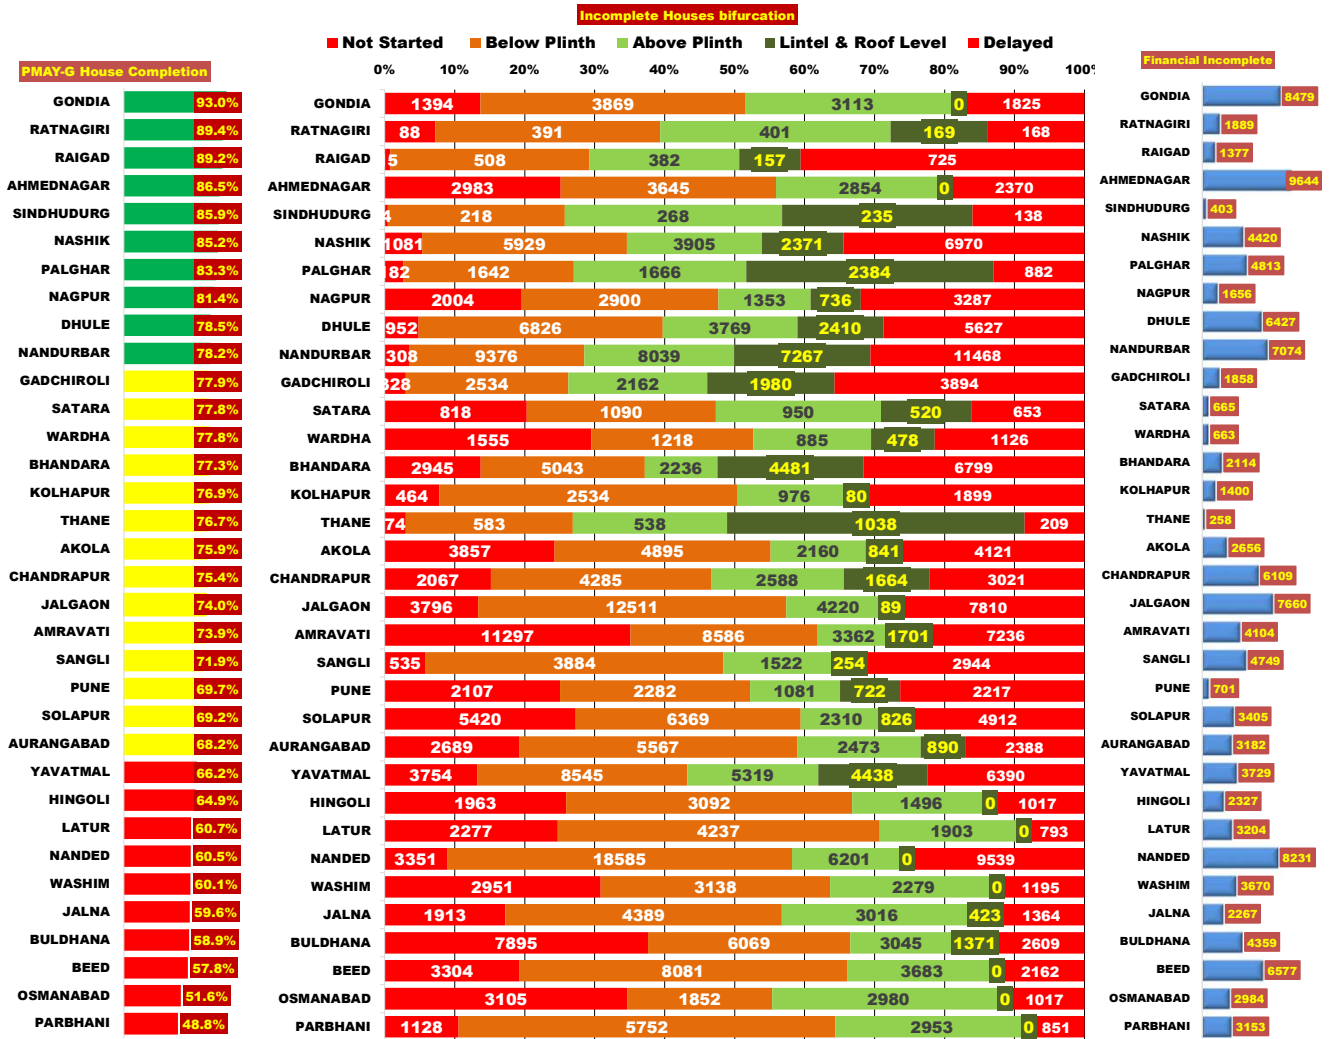

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	23.05.2023	24.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	69463	41767	42043	276	27420	47	2285
2	BEED	35253	20136	20362	226	14891	22	1241
3	YAVATMAL	65146	42905	43097	192	22049	52	1837
4	AMRAVATI	95242	70157	70342	185	24900	47	2075
5	LATUR	20493	12289	12430	141	8063	21	672
6	BULDHANA	44701	26195	26331	136	18370	29	1531
7	GONDIA	96138	89286	89410	124	6728	64	561
8	WASHIM	20362	12127	12241	114	8121	23	677
9	JALGAON	79234	58511	58618	107	20616	47	1718
10	BHANDARA	64919	50109	50214	105	14705	34	1225
11	DHULE	64917	50861	50960	99	13957	43	1163
12	PARBHANI	19062	9211	9310	99	9752	17	813
13	NANDURBAR	118958	92881	92968	87	25990	39	2166
14	HINGOLI	18083	11648	11732	84	6351	15	529
15	PALGHAR	35188	29240	29314	74	5874	24	490
16	AURANGABAD	36514	24828	24896	68	11618	31	968
17	AKOLA	48778	36965	37025	60	11753	21	979
18	KOLHAPUR	17586	13474	13532	58	4054	8	338
19	AHMEDNAGAR	60752	52486	52543	57	8209	78	684
20	JALNA	24023	14263	14312	49	9711	21	809
21	OSMANABAD	14408	7382	7430	48	6978	14	582
22	GADCHIROLI	31615	24595	24636	41	6979	26	582
23	NASHIK	89683	76356	76397	41	13286	52	1107
24	PUNE	20426	14199	14234	35	6192	9	516
25	WARDHA	18607	14436	14471	35	4136	10	345
26	SATARA	15216	11807	11838	31	3378	13	282
27	RATNAGIRI	9871	8794	8822	28	1049	14	87
28	THANE	9599	7339	7366	27	2233	5	186
29	NAGPUR	36970	30087	30112	25	6858	12	572
30	SOLAPUR	48394	33444	33469	25	14925	19	1244
31	SINDHUDURG	5133	4385	4408	23	725	4	60
32	SANGLI	21606	15516	15537	21	6069	11	506
33	CHANDRAPUR	42958	32394	32407	13	10551	33	879
34	RAIGAD	9820	8757	8761	4	1059	4	88
Total		1409118	1048830	1051568	2738	357550	910	29796

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	23.05.2023	24.05.2023	Daily_Achievement	Remaining
1	NAGPUR DIV.	118430	96704	96848	144	21582
2	AMRAVATI DIV.	110155	94850	94914	64	15241
3	AURANGABAD DIV.	200327	168998	169034	36	31293
4	KONKAN DIV.	34744	31891	31926	35	2818
5	NASHIK DIV.	141552	112270	112297	27	29255
6	PUNE DIV.	65859	63381	63385	4	2474
Total		671067	568094	568404	310	102663


Sr. No.	District	Target	23.05.2023	24.05.2023	Daily_Achievement	Remaining
1	CHANDRAPUR	40285	29728	29846	118	10439
2	NANDED	26760	21750	21785	35	4975
3	RAIGAD	7418	6600	6635	35	783
4	WASHIM	11503	10510	10542	32	961
5	YAVATMAL	30045	26524	26552	28	3493
6	GONDIA	14261	13337	13362	25	899
7	AHMEDNAGAR	35298	34423	34446	23	852
8	NASHIK	32035	22895	22899	4	9136
9	SOLAPUR	18718	18478	18482	4	236
10	BULDHANA	21702	20094	20097	3	1605
11	AMRAVATI	23224	19890	19891	1	3333
12	GADCHIROLI	16834	15335	15336	1	1498
13	PARBHANI	19784	17650	17651	1	2133
14	AKOLA	23681	17832	17832	0	5849
15	AURANGABAD	26141	24255	24255	0	1886
16	BEED	26878	26046	26046	0	832
17	BHANDARA	17612	15606	15606	0	2006
18	DHULE	21790	18088	18088	0	3702
19	HINGOLI	27298	16589	16589	0	10709
20	JALGAON	25851	22723	22723	0	3128
21	JALNA	20609	19324	19324	0	1285
22	KOLHAPUR	13090	12889	12889	0	201
23	LATUR	28004	26314	26314	0	1690
24	NAGPUR	16291	11448	11448	0	4843
25	NANDURBAR	26578	14141	14141	0	12437
26	OSMANABAD	24853	17070	17070	0	7783
27	PALGHAR	11792	11509	11509	0	283
28	PUNE	14672	12763	12763	0	1909
29	RATNAGIRI	7129	6691	6691	0	438
30	SANGLI	8732	8604	8604	0	128
31	SATARA	10647	10647	10647	0	0
32	SINDHUDURG	2141	2108	2108	0	33
33	THANE	6264	4983	4983	0	1281
34	WARDHA	13147	11250	11250	0	1897
Total		671067	568094	568404	310	102663

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	236
PALGHAR	283
RATNAGIRI	438
RAIGAD	783
BEED	832
AHMEDNAGAR	852
GONDIA	899
WASHIM	961
THANE	1281
JALNA	1285
GADCHIROLI	1498
BULDHANA	1605
LATUR	1690
AURANGABAD	1886
WARDHA	1897
PUNE	1909
BHANDARA	2006
PARBHANI	2133
JALGAON	3128
AMRAVATI	3333
YAVATMAL	3493
DHULE	3702
NAGPUR	4843
NANDED	4975
AKOLA	5849
OSMANABAD	7783
NASHIK	9136
CHANDRAPUR	10439
HINGOLI	10709
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	23.05.2023	24.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	169034	105262	105662	400	63372	84	5281
2	AMRAVATI DIV.	94914	65775	66089	314	28825	53	2402
3	NASHIK DIV.	112297	89547	89708	161	22589	63	1882
4	NAGPUR DIV.	96848	70211	70371	160	26477	42	2206
5	KONKAN DIV.	31926	24004	24111	107	7815	15	651
6	PUNE DIV.	63385	52212	52281	69	11104	23	925
Total		568404	407011	408222	1211	160182	280	13349

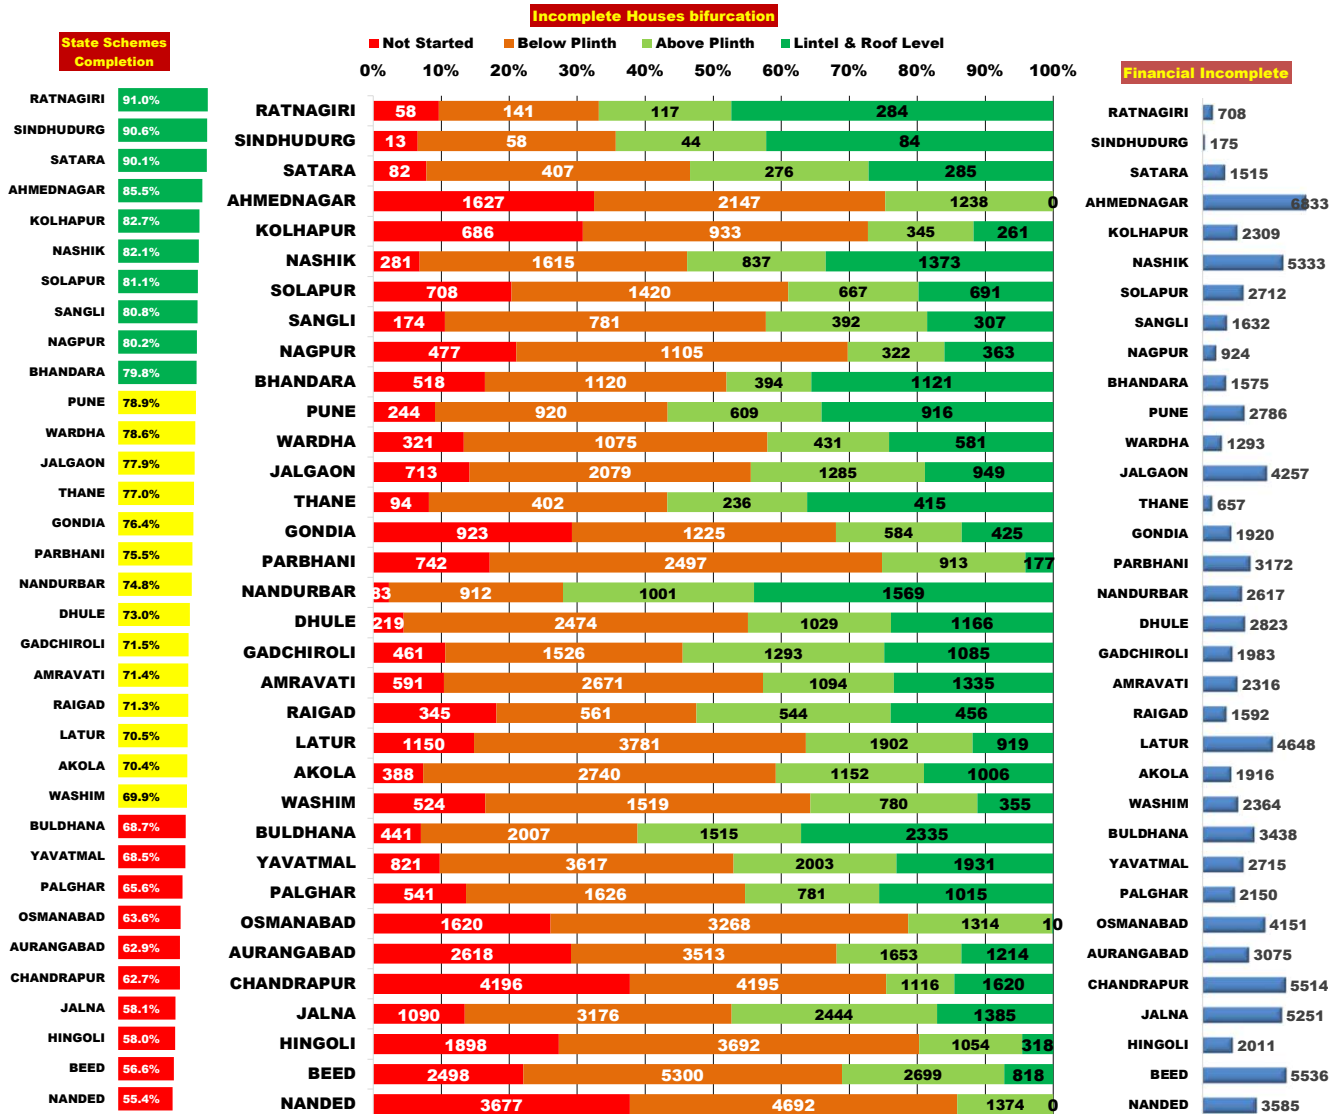

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	23.05.2023	24.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI	19891	14119	14200	81	5691	9	474
2	JALNA	19324	11149	11229	80	8095	22	675
3	YAVATMAL	26552	18107	18180	73	8372	13	698
4	DHULE	18088	13130	13200	70	4888	9	407
5	LATUR	26314	18492	18562	70	7752	13	646
6	WASHIM	10542	7300	7364	64	3178	7	265
7	AURANGABAD	24255	15200	15257	57	8998	9	750
8	HINGOLI	16589	9575	9627	52	6962	7	580
9	BEED	26046	14680	14731	51	11315	13	943
10	BULDHANA	20097	13750	13799	49	6298	15	525
11	AKOLA	17832	12499	12546	47	5286	9	441
12	GADCHIROLI	15336	10925	10971	46	4365	9	364
13	NANDED	21785	12030	12076	46	9709	8	809
14	GONDIA	13362	10163	10205	42	3157	8	263
15	KOLHAPUR	12889	10630	10664	34	2225	3	185
16	AHMEDNAGAR	34446	29409	29442	33	5004	26	417
17	PALGHAR	11509	7514	7546	32	3963	6	330
18	THANE	4983	3807	3836	29	1147	2	96
19	BHANDARA	15606	12426	12453	27	3153	4	263
20	WARDHA	11250	8818	8842	24	2408	6	201
21	PARBHANI	17651	13299	13322	23	4329	4	361
22	NASHIK	22899	18772	18793	21	4106	11	342
23	OSMANABAD	17070	10837	10858	21	6212	9	518
24	RAIGAD	6635	4708	4729	21	1906	3	159
25	JALGAON	22723	17678	17697	19	5026	10	419
26	NANDURBAR	14141	10558	10576	18	3565	6	297
27	RATNAGIRI	6691	6073	6091	18	600	3	50
28	PUNE	12763	10059	10074	15	2689	5	224
29	SANGLI	8604	6937	6950	13	1654	3	138
30	NAGPUR	11448	9169	9181	12	2267	3	189
31	CHANDRAPUR	29846	18710	18719	9	11127	11	927
32	SINDHUDURG	2108	1902	1909	7	199	1	17
33	SATARA	10647	9592	9597	5	1050	5	88
34	SOLAPUR	18482	14994	14996	2	3486	6	291
Total		568404	407011	408222	1211	160182	280	13349

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AMRAVATI DIV.	76	29688	199	31233	252	16165
2	NASHIK DIV.	55	10120	178	38287	287	22787
3	NAGPUR DIV.	37	10080	158	19849	183	12337
4	AURANGABAD DIV.	40	19699	141	51555	87	24705
5	PUNE DIV.	32	9218	55	16159	81	6839
6	KONKAN DIV.	3	360	24	3342	27	3255
Total		243	79165	755	160425	917	86088

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	12
THANE	74
RATNAGIRI	88
PALGHAR	182
GADCHIROLI	303
SANGLI	409
KOLHAPUR	464
SATARA	818
DHULE	952
NASHIK	1081
PARBHANI	1128
NANDURBAR	1308
GONDIA	1394
WARDHA	1555
NAGPUR	1869
JALNA	1883
HINGOLI	1963
CHANDRAPUR	2014
PUNE	2107
LATUR	2277
AURANGABAD	2688
BHANDARA	2945
WASHIM	2948
AHMEDNAGAR	2983
OSMANABAD	3105
BEED	3304
NANDED	3351
YAVATMAL	3747
JALGAON	3796
AKOLA	3857
SOLAPUR	5420
BULDHANA	7885
AMRAVATI	11251

PMAY-G 2nd Ins Pending

SINDHUDURG	218
RATNAGIRI	391
RAIGAD	508
THANE	583
SATARA	1090
WARDHA	1218
PALGHAR	1642
OSMANABAD	1852
PUNE	2282
KOLHAPUR	2534
GADCHIROLI	2534
NAGPUR	2900
HINGOLI	3092
WASHIM	3138
AHMEDNAGAR	3645
GONDIA	3869
SANGLI	3884
LATUR	4237
CHANDRAPUR	4285
JALNA	4389
AKOLA	4895
BHANDARA	5043
AURANGABAD	5567
PARBHANI	5752
NASHIK	5929
BULDHANA	6069
SOLAPUR	6369
DHULE	6826
BEED	8081
YAVATMAL	8545
AMRAVATI	8586
NANDURBAR	9376
JALGAON	12511
NANDED	18585

PMAY-G 3rd Ins Pending

SINDHUDURG	268
RAIGAD	382
RATNAGIRI	401
THANE	538
WARDHA	885
SATARA	950
KOLHAPUR	976
PUNE	1081
NAGPUR	1353
HINGOLI	1496
SANGLI	1522
PALGHAR	1666
LATUR	1903
AKOLA	2160
GADCHIROLI	2162
BHANDARA	2236
WASHIM	2279
SOLAPUR	2310
AURANGABAD	2473
CHANDRAPUR	2588
AHMEDNAGAR	2854
PARBHANI	2953
OSMANABAD	2980
JALNA	3016
BULDHANA	3045
GONDIA	3113
AMRAVATI	3362
BEED	3683
DHULE	3769
NASHIK	3905
JALGAON	4220
YAVATMAL	5319
NANDED	6201
NANDURBAR	8039

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NANDURBAR	1	1308	113	9376	115	8039
2	YAVATMAL	13	3747	66	8545	82	5319
3	AMRAVATI	27	11251	49	8586	74	3362
4	BHANDARA	14	2945	56	5043	75	2236
5	DHULE	17	952	15	6826	77	3769
6	AKOLA	11	3857	49	4895	39	2160
7	NANDED	8	3351	48	18585	36	6201
8	AHMEDNAGAR	3	2983	30	3645	56	2854
9	GONDIA	4	1394	43	3869	40	3113
10	WASHIM	9	2948	20	3138	49	2279
11	JALGAON	25	3796	10	12511	17	4220
12	SOLAPUR	16	5420	15	6369	19	2310
13	PARBHANI	3	1128	29	5752	14	2953
14	CHANDRAPUR	10	2014	23	4285	12	2588
15	JALNA	8	1883	20	4389	13	3016
16	NASHIK	9	1081	10	5929	22	3905
17	BULDHANA	16	7885	15	6069	8	3045
18	NAGPUR	2	1869	15	2900	19	1353
19	PUNE	10	2107	13	2282	12	1081
20	KOLHAPUR	3	464	10	2534	21	976
21	SATARA	2	818	9	1090	23	950
22	WARDHA	7	1555	10	1218	16	885
23	GADCHIROLI	0	303	11	2534	21	2162
24	AURANGABAD	8	2688	9	5567	14	2473
25	LATUR	2	2277	19	4237	2	1903
26	PALGHAR	3	182	11	1642	9	1666
27	BEED	7	3304	5	8081	4	3683
28	SANGLI	1	409	8	3884	6	1522
29	THANE	0	74	5	583	10	538
30	OSMANABAD	3	3105	4	1852	3	2980
31	HINGOLI	1	1963	7	3092	1	1496
32	RAIGAD	0	12	5	508	2	382
33	RATNAGIRI	-1	88	2	391	4	401
34	SINDHUDURG	0	4	1	218	2	268
	Total	243	79165	755	160425	917	86088

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	AURANGABAD DIV.	188	15293	186	29919	186	13353
2	NAGPUR DIV.	238	6896	77	10246	48	4140
3	AMRAVATI DIV.	44	2765	157	12554	93	6544
4	NASHIK DIV.	124	2923	74	9227	24	5390
5	KONKAN DIV.	44	1051	38	2788	25	1722
6	PUNE DIV.	1	1894	24	4461	18	2289
Total		639	30822	556	69195	394	33438

State Schemes 1st Ins Pending

State Schemes 2nd Ins Pending

State Schemes 3rd Ins Pending

SINDHUDURG	13
RATNAGIRI	58
SATARA	82
NANDURBAR	83
THANE	94
SANGLI	174
DHULE	219
PUNE	244
NASHIK	281
WARDHA	321
RAIGAD	345
AKOLA	388
BULDHANA	441
GADCHIROLI	461
NAGPUR	477
BHANDARA	518
WASHIM	524
PALGHAR	541
AMRAVATI	591
KOLHAPUR	686
SOLAPUR	708
JALGAON	713
PARBHANI	742
YAVATMAL	821
GONDIA	923
JALNA	1090
LATUR	1150
OSMANABAD	1620
AHMEDNAGAR	1627
HINGOLI	1898
BEED	2498
AURANGABAD	2618
NANDED	3677
CHANDRAPUR	4196

SINDHUDURG	58
RATNAGIRI	141
THANE	402
SATARA	407
RAIGAD	561
SANGLI	781
NANDURBAR	912
PUNE	920
KOLHAPUR	933
WARDHA	1075
NAGPUR	1105
BHANDARA	1120
GONDIA	1225
SOLAPUR	1420
WASHIM	1519
GADCHIROLI	1526
NASHIK	1615
PALGHAR	1626
BULDHANA	2007
JALGAON	2079
AHMEDNAGAR	2147
DHULE	2474
PARBHANI	2497
AMRAVATI	2671
AKOLA	2740
JALNA	3176
OSMANABAD	3268
AURANGABAD	3513
YAVATMAL	3617
HINGOLI	3692
LATUR	3781
CHANDRAPUR	4195
NANDED	4692
BEED	5300

SINDHUDURG	44
RATNAGIRI	117
THANE	236
SATARA	276
NAGPUR	322
KOLHAPUR	345
SANGLI	392
BHANDARA	394
WARDHA	431
RAIGAD	544
GONDIA	584
PUNE	609
SOLAPUR	667
WASHIM	780
PALGHAR	781
NASHIK	837
PARBHANI	913
NANDURBAR	1001
DHULE	1029
HINGOLI	1054
AMRAVATI	1094
CHANDRAPUR	1116
AKOLA	1152
AHMEDNAGAR	1238
JALGAON	1285
GADCHIROLI	1293
OSMANABAD	1314
NANDED	1374
BULDHANA	1515
AURANGABAD	1653
LATUR	1902
YAVATMAL	2003
JALNA	2444
BEED	2699

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achievement)	1st Installment Remaining	2nd Installment (Daily Achievement)	2nd Installment Remaining	3rd Installment (Daily Achievement)	3rd Installment Remaining
1	BEED	105	2498	63	5300	84	2699
2	GONDIA	104	923	39	1225	22	584
3	AHMEDNAGAR	115	1627	1	2147	7	1238
4	AKOLA	22	388	59	2740	22	1152
5	CHANDRAPUR	93	4196	8	4195	0	1116
6	AURANGABAD	4	2618	36	3513	53	1653
7	AMRAVATI	4	591	53	2671	35	1094
8	LATUR	17	1150	37	3781	16	1902
9	RAIGAD	36	345	16	561	15	544
10	DHULE	1	219	56	2474	5	1029
11	PARBHANI	19	742	25	2497	12	913
12	GADCHIROLI	31	461	11	1526	11	1293
13	NANDED	34	3677	10	4692	6	1374
14	BULDHANA	5	441	21	2007	19	1515
15	SANGLI	1	174	19	781	11	392
16	YAVATMAL	13	821	9	3617	7	2003
17	BHANDARA	9	518	11	1120	7	394
18	THANE	3	94	16	402	7	236
19	WASHIM	0	524	15	1519	10	780
20	NASHIK	7	281	8	1615	6	837
21	HINGOLI	7	1898	9	3692	2	1054
22	PALGHAR	5	541	6	1626	3	781
23	OSMANABAD	0	1620	3	3268	8	1314
24	WARDHA	0	321	5	1075	6	431
25	JALNA	2	1090	3	3176	5	2444
26	JALGAON	0	713	4	2079	5	1285
27	NANDURBAR	1	83	5	912	1	1001
28	NAGPUR	1	477	3	1105	2	322
29	KOLHAPUR	0	686	2	933	2	345
30	SOLAPUR	0	708	0	1420	4	667
31	SATARA	0	82	3	407	0	276
32	PUNE	0	244	0	920	1	609
33	RATNAGIRI	0	58	0	141	0	117
34	SINDHUDURG	0	13	0	58	0	44
	Total	639	30822	556	69195	394	33438

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2370	1719	3158	1664	43
AKOLA	4121	3452	3443	869	570
AMRAVATI	7236	5465	7094	1519	1048
AURANGABAD	2388	2234	4870	1110	479
BEED	2162	1844	6807	1673	481
BHANDARA	6799	5133	4595	802	2323
BULDHANA	2609	2142	4245	910	764
CHANDRAPUR	3021	1947	3419	743	318
DHULE	5627	4073	5848	2352	1672
GADCHIROLI	3894	2435	2226	1176	965
GONDIA	1825	1762	3086	1015	144
HINGOLI	1017	661	2614	484	106
JALGAON	7810	6598	11083	2103	749
JALNA	1364	1078	3343	872	360
KOLHAPUR	1899	729	2324	287	108
LATUR	793	724	2847	491	51
NAGPUR	3287	2291	2546	437	591
NANDED	9539	9057	14717	2070	388
NANDURBAR	11468	9923	7148	4629	5200
NASHIK	6970	3566	4910	2099	1608
OSMANABAD	1017	579	1210	447	6
PALGHAR	882	635	1299	743	599
PARBHANI	851	730	4718	657	136
PUNE	2217	1711	1957	545	479
RAIGAD	725	239	469	252	168
RATNAGIRI	168	41	331	145	80
SANGLI	2944	2265	3451	601	158
SATARA	653	366	821	251	162
SINDHUDURG	138	86	194	74	41
SOLAPUR	4912	4551	5093	1252	545
THANE	209	188	536	196	318
WARDHA	1126	793	936	217	241
WASHIM	1195	851	2486	448	94
YAVATMAL	6390	4322	6982	1863	1790
