



अमृत महा आवास अभियान २०२२-२३

दैनिक प्रगती अहवाल : ३१.०५.२०२३


प्रधानमंत्री आवास योजना ग्रामीण – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, भूमिहीन, आर्थिकदृष्ट्या अपुर्ण
राज्य पुरस्कृत ग्रामीण आवास योजना – मंजूरी, पूर्ण घरकुले, हप्ते वितरण, आर्थिकदृष्ट्या अपुर्ण

योजना	एकूण मंजूरी	दैनिक मंजूरी	एकूण पूर्ण	दैनिक पूर्ण घरकुले	दैनिक पहिला हप्ता वितरित	दैनिक दुसरा हप्ता वितरित	दैनिक तिसरा हप्ता वितरित
प्रधानमंत्री आवास योजना ग्रामीण	१४०८८२४	०	१०६५५००	६०९	०	०	०
राज्य योजना	५७१७९०	१५३६	४११७१०	३४७	०	०	०
एकूण	१९८०६१४	१५३६	१४७७२१०	९५६	०	०	०

PMAY-G Completion Progress Bar

75.6%



PMAY-G: Incomplete Houses bifurcation





State Schemes Progress Bar

72.0%


State Schemes: Incomplete Houses bifurcation

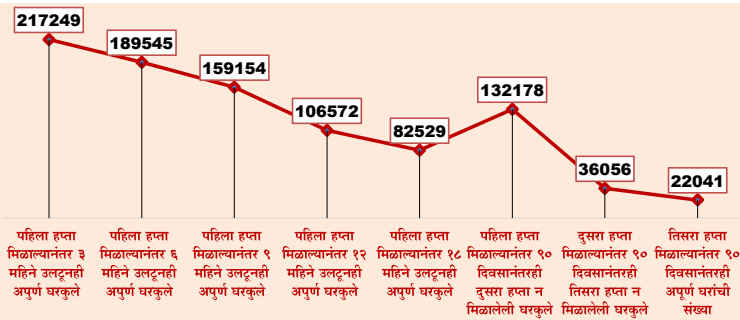

Abhiyan Achievement Day 192

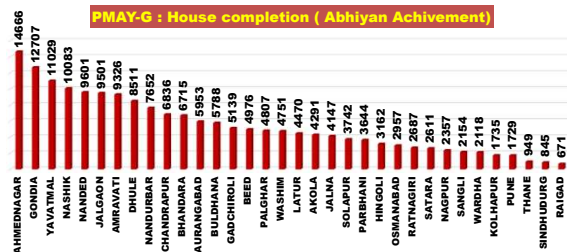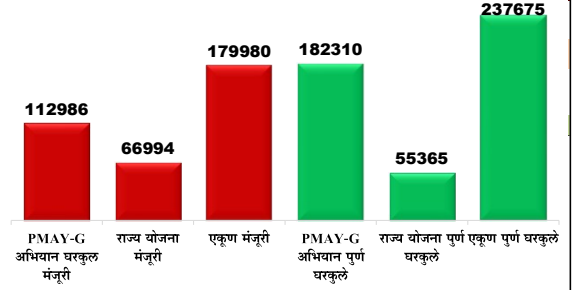

State Schemes: House completion (Abhiyan Achievement)




राज्य व्यवस्थापन कक्ष- ग्रामीण गृहनिर्माण


४ था मजला, दक्षिण कक्ष, सिडको भवन, सीबीडी बेलापूर, नवी मुंबई - ४०० ६१४.

Top and Bottom Ten Districts


PMAY-G Delayed Houses TOP 10 Dist.




State Schemes Sanction TOP 10 Dist.




PMAY-G Remaining 1st Installments Bottom 10 Dist.




PMAY-G Delayed Houses Bottom 10 Dist.




State Schemes Sanction Bottom 10 Dist.




PMAY-G Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Completion TOP 10 Dist.




State Schemes Completion TOP 10 Dist.




PMAY-G Remaining 3rd Installments Bottom 10 Dist.




PMAY-G Completion Bottom 10 Dist.




State Schemes Completion Bottom 10 Dist.




State Schemes Remaining 1st Installments Bottom 10 Dist.



PMAY-G Daily Completion Top 10 Dist.




State Schemes Daily Completion Top 10 Dist.




State Schemes Remaining 2nd Installments Bottom 10 Dist.




PMAY-G Daily Completion Bottom 10 Dist.




State Schemes Daily Completion Bottom 10 Dist.




State Schemes Remaining 3rd Installments Bottom 10 Dist.




PMAY-G : Current Pace of Completion Per Day (Abhiyan)




State Schemes : Current Pace of Completion Per Day (Abhiyan)



PMAY-G Required Pace of Completion Per Day



State Schemes Required Pace of Completion Per Day



प्रधानमंत्री आवास योजना ग्रामीण - मंजूरी (PWL+Awaas Plus)

Sr. No.	Division	Target (PWL+Awaas Plus)	30.05.2023	31.05.2023	Daily_Achievement	Remaining
1	NASHIK DIV.	414870	413492	413490	0	1380
2	AMRAVATI DIV.	274735	274217	274210	0	525
3	AURANGABAD DIV.	237996	237299	237285	0	711
4	NAGPUR DIV.	291888	291202	291202	0	686
5	KONKAN DIV.	69871	69611	69611	0	260
6	PUNE DIV.	124141	123045	123026	0	1115
Total		1413501	1408866	1408824	0	4677

Sr. No.	District	Target (PWL+Awaas Plus)	30.05.2023	31.05.2023	Daily_Achievement	Remaining
1	AHMEDNAGAR	60787	60752	60752	0	35
2	AKOLA	48792	48778	48778	0	14
3	AMRAVATI	95496	95242	95242	0	254
4	AURANGABAD	36740	36514	36514	0	226
5	BEED	35310	35253	35253	0	57
6	BHANDARA	64976	64914	64914	0	62
7	BULDHANA	44741	44696	44696	0	45
8	CHANDRAPUR	43094	42958	42958	0	136
9	DHULE	65009	64917	64917	0	92
10	GADCHIROLI	31707	31615	31615	0	92
11	GONDIA	96493	96138	96138	0	355
12	HINGOLI	18109	18083	18083	0	26
13	JALNA	24038	24023	24023	0	15
14	KOLHAPUR	17636	17585	17585	0	51
15	LATUR	20679	20493	20493	0	186
16	NAGPUR	36985	36970	36970	0	15
17	NANDED	69533	69463	69463	0	70
18	NANDURBAR	119664	118958	118958	0	706
19	NASHIK	89748	89683	89683	0	65
20	PALGHAR	35415	35188	35188	0	227
21	PARBHANI	19088	19062	19062	0	26
22	PUNE	20367	20292	20292	0	75
23	RAIGAD	9830	9820	9820	0	10
24	RATNAGIRI	9888	9871	9871	0	17
25	SANGLI	21778	21606	21606	0	172
26	SINDHUDURG	5133	5133	5133	0	0
27	THANE	9605	9599	9599	0	6
28	WARDHA	18633	18607	18607	0	26
29	WASHIM	20384	20355	20355	0	29
30	JALGAON	79662	79182	79180	-2	482
31	SATARA	15279	15168	15163	-5	116
32	YAVATMAL	65322	65146	65139	-7	183
33	OSMANABAD	14499	14408	14394	-14	105
34	SOLAPUR	49081	48394	48380	-14	701
Total		1413501	1408866	1408824	0	4677

Remaining Sanction RANK


SINDHUDURG	0
THANE	6
RAIGAD	10
AKOLA	14
JALNA	15
NAGPUR	15
RATNAGIRI	17
HINGOLI	26
PARBHANI	26
WARDHA	26
WASHIM	29
AHMEDNAGAR	35
BULDHANA	45
KOLHAPUR	51
BEED	57
BHANDARA	62
NASHIK	65
NANDED	70
PUNE	75
DHULE	92
GADCHIROLI	92
OSMANABAD	105
SATARA	116
CHANDRAPUR	136
SANGLI	172
YAVATMAL	183
LATUR	186
AURANGABAD	226
PALGHAR	227
AMRAVATI	254
GONDIA	355
JALGAON	482
SOLAPUR	701
NANDURBAR	706

प्रधानमंत्री आवास योजना - ग्रामीण : भूमिहीन लाभार्थी अहवाल

Sr. No.	District	Google Sheet Report			AwaasSoft Report			
		Total Landless	Provided land	Remaining	Landless beneficiaries tagged in AwaasSoft	Landless beneficiaries provided land	Remaining Landless	Remaining Tag (provided land)
1	DHULE	18	18	0	18	18	0	0
2	GADCHIROLI	8	8	0	8	8	0	0
3	NANDURBAR	0	0	0	0	0	0	0
4	PALGHAR	11	9	2	11	11	0	-2
5	RAIGAD	6	6	0	6	6	0	0
6	RATNAGIRI	23	23	0	23	23	0	0
7	SINDHUDURG	420	420	0	420	420	0	0
8	KOLHAPUR	257	238	19	257	227	30	11
9	THANE	127	69	58	127	60	67	9
10	NANDED	362	319	43	362	242	120	77
11	GONDIA	2450	2450	0	2450	2327	123	123
12	BEED	212	125	87	212	72	140	53
13	SANGLI	430	198	232	410	144	266	54
14	PARBHANI	331	63	268	331	54	277	9
15	SATARA	1304	659	645	1247	630	617	29
16	NASHIK	1802	1324	478	1803	1072	731	252
17	HINGOLI	1713	795	918	1713	466	1247	329
18	CHANDRAPUR	2769	1221	1548	2750	1486	1264	-265
19	JALNA	1381	406	975	1374	85	1289	321
20	WARDHA	2803	1669	1134	2829	1347	1482	322
21	NAGPUR	5088	3612	1476	5020	3456	1564	156
22	LATUR	2299	1121	1178	2310	477	1833	644
23	PUNE	2924	1602	1322	2781	880	1901	722
24	JALGAON	22928	20121	2807	22868	20935	1933	-814
25	YAVATMAL	3612	1450	2162	3664	1291	2373	159
26	BHANDARA	5675	3543	2132	5666	3266	2400	277
27	OSMANABAD	2470	287	2183	2469	56	2413	231
28	WASHIM	3457	1398	2059	3436	865	2571	533
29	AURANGABAD	3297	1733	1564	3290	288	3002	1445
30	AHMEDNAGAR	7756	4183	3573	7755	4453	3302	-270
31	AKOLA	7072	3935	3137	7367	3920	3447	15
32	SOLAPUR	7297	3684	3613	7223	1408	5815	2276
33	BULDHANA	15191	8938	6253	15601	7978	7623	960
34	AMRAVATI	21529	12817	8712	21539	11392	10147	1425
	Total	127022	78444	48578	127340	69363	57977	10432

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	30.05.2023	31.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	237285	146296	146471	175	90814	203	18163
2	NASHIK DIV.	413490	333808	333927	119	79563	263	15913
3	NAGPUR DIV.	291202	243887	244000	113	47202	187	9440
4	AMRAVATI DIV.	274210	192264	192342	78	81868	183	16374
5	KONKAN DIV.	69611	59297	59367	70	10244	52	2049
6	PUNE DIV.	123026	89339	89393	54	33633	62	6727
Total		1408824	1064891	1065500	609	343324	950	68665

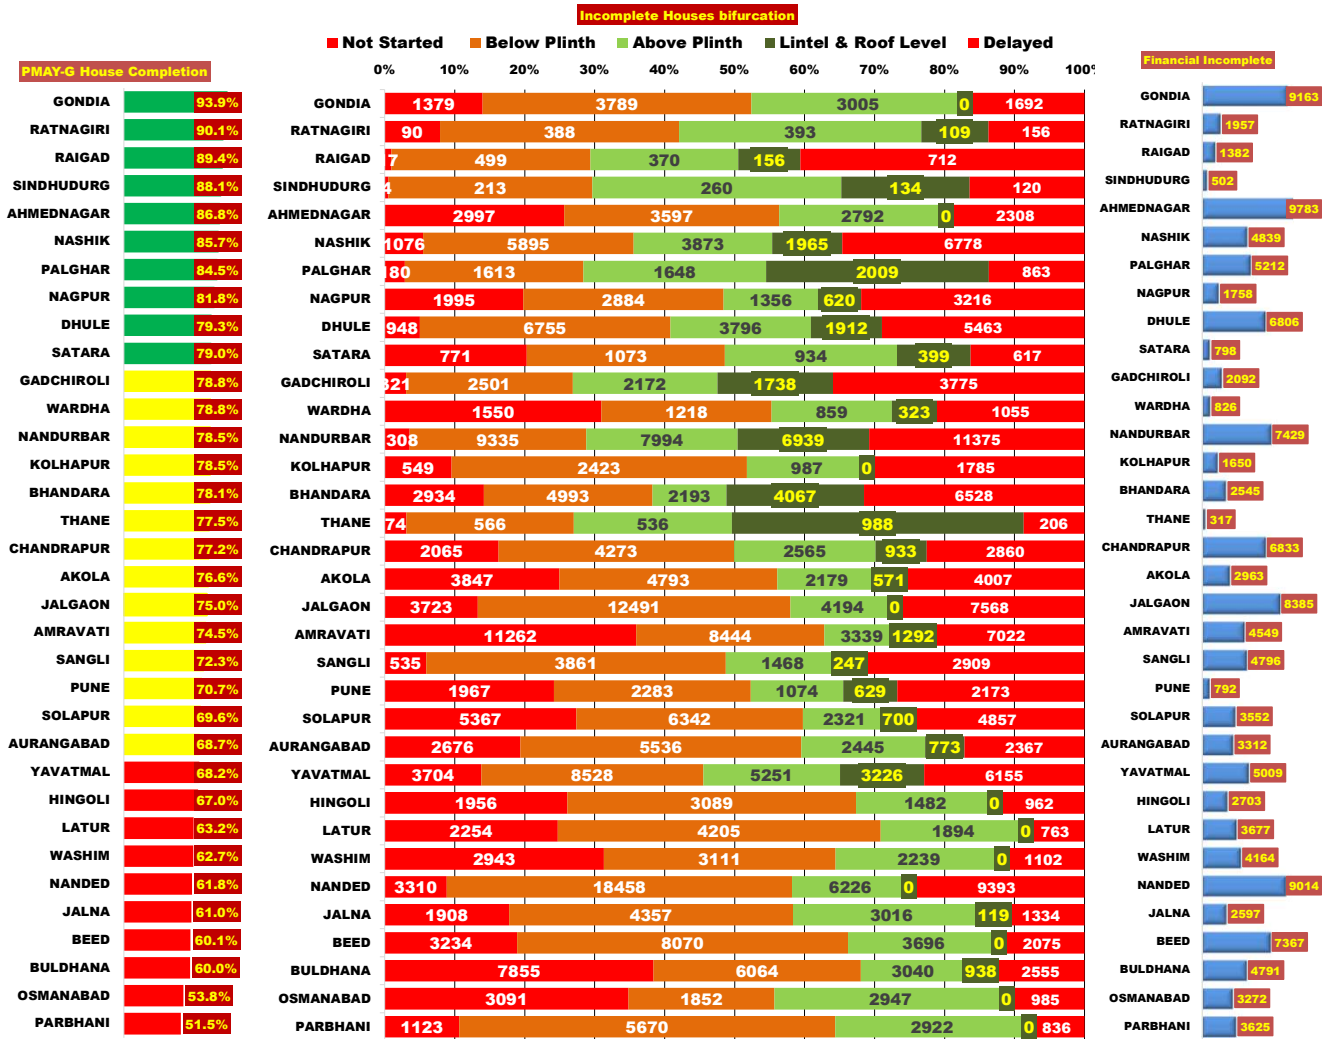

प्रधानमंत्री आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	30.05.2023	31.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	NANDED	69463	42814	42911	97	26552	50	5310
2	BHANDARA	64914	50673	50727	54	14187	35	2837
3	NASHIK	89683	76826	76874	48	12809	53	2562
4	PALGHAR	35188	29691	29738	47	5450	25	1090
5	PARBHANI	19062	9788	9817	29	9245	19	1849
6	AHMEDNAGAR	60752	52720	52746	26	8006	76	1601
7	GADCHIROLI	31615	24880	24906	26	6709	27	1342
8	AMRAVATI	95242	70926	70951	25	24291	49	4858
9	AURANGABAD	36514	25060	25085	25	11429	31	2286
10	YAVATMAL	65139	44413	44437	24	20702	57	4140
11	NANDURBAR	118958	93359	93382	23	25576	40	5115
12	JALGAON	79180	59400	59419	19	19761	49	3952
13	SANGLI	21606	15602	15621	19	5985	11	1197
14	CHANDRAPUR	42958	33158	33175	17	9783	36	1957
15	SOLAPUR	48380	33635	33650	15	14730	19	2946
16	WASHIM	20355	12743	12757	14	7598	25	1520
17	JALNA	24023	14641	14653	12	9370	22	1874
18	KOLHAPUR	17585	13786	13797	11	3788	9	758
19	THANE	9599	7424	7435	11	2164	5	433
20	BULDHANA	44696	26799	26809	10	17887	30	3577
21	GONDIA	96138	90276	90285	9	5853	66	1171
22	RATNAGIRI	9871	8883	8891	8	980	14	196
23	WARDHA	18607	14650	14657	7	3950	11	790
24	AKOLA	48778	37383	37388	5	11390	22	2278
25	SATARA	15163	11981	11986	5	3177	14	635
26	BEED	35253	21200	21204	4	14049	26	2810
27	PUNE	20292	14335	14339	4	5953	9	1191
28	DHULE	64917	51503	51506	3	13411	44	2682
29	HINGOLI	18083	12117	12120	3	5963	16	1193
30	LATUR	20493	12941	12944	3	7549	23	1510
31	RAIGAD	9820	8778	8781	3	1039	3	208
32	OSMANABAD	14394	7735	7737	2	6657	15	1331
33	SINDHUDURG	5133	4521	4522	1	611	4	122
34	NAGPUR	36970	30250	30250	0	6720	12	1344
Total		1408824	1064891	1065500	609	343324	950	68665

राज्यपुरस्कृत आवास योजना ग्रामीण - मंजूरी

Sr. No.	Division	Target	30.05.2023	31.05.2023	Daily_Achievement	Remaining
1	AURANGABAD DIV.	200327	169947	170685	738	29642
2	AMRAVATI DIV.	110155	94956	95406	450	14749
3	NASHIK DIV.	141552	112792	113029	237	28523
4	NAGPUR DIV.	118430	97228	97298	70	21132
5	KONKAN DIV.	34744	31950	31985	35	2759
6	PUNE DIV.	65859	63381	63387	6	2472
Total		671067	570254	571790	1536	99277


Sr. No.	District	Target	30.05.2023	31.05.2023	Daily_Achievement	Remaining
1	AURANGABAD	26141	24401	24847	446	1294
2	YAVATMAL	30045	26568	26953	385	3092
3	HINGOLI	27298	17125	17416	291	9882
4	JALGAON	25851	23190	23399	209	2452
5	BULDHANA	21702	20098	20163	65	1539
6	CHANDRAPUR	40285	30100	30156	56	10129
7	RAIGAD	7418	6659	6694	35	724
8	AHMEDNAGAR	35298	34467	34495	28	803
9	NAGPUR	16291	11448	11456	8	4835
10	PUNE	14672	12759	12765	6	1907
11	GADCHIROLI	16834	15340	15344	4	1490
12	GONDIA	14261	13484	13486	2	775
13	NANDED	26760	21896	21897	1	4863
14	AKOLA	23681	17832	17832	0	5849
15	AMRAVATI	23224	19907	19907	0	3317
16	BEED	26878	26082	26082	0	796
17	BHANDARA	17612	15606	15606	0	2006
18	DHULE	21790	18088	18088	0	3702
19	JALNA	20609	19339	19339	0	1270
20	KOLHAPUR	13090	12889	12889	0	201
21	LATUR	28004	26330	26330	0	1674
22	NANDURBAR	26578	14141	14141	0	12437
23	NASHIK	32035	22906	22906	0	9129
24	OSMANABAD	24853	17115	17115	0	7738
25	PALGHAR	11792	11509	11509	0	283
26	PARBHANI	19784	17659	17659	0	2125
27	RATNAGIRI	7129	6691	6691	0	438
28	SANGLI	8732	8604	8604	0	128
29	SATARA	10647	10647	10647	0	0
30	SINDHUDURG	2141	2108	2108	0	33
31	SOLAPUR	18718	18482	18482	0	236
32	THANE	6264	4983	4983	0	1281
33	WARDHA	13147	11250	11250	0	1897
34	WASHIM	11503	10551	10551	0	952
Total		671067	570254	571790	1536	99277

Remaining Sanction RANK

SATARA	0
SINDHUDURG	33
SANGLI	128
KOLHAPUR	201
SOLAPUR	236
PALGHAR	283
RATNAGIRI	438
RAIGAD	724
GONDIA	775
BEED	796
AHMEDNAGAR	803
WASHIM	952
JALNA	1270
THANE	1281
AURANGABAD	1294
GADCHIROLI	1490
BULDHANA	1539
LATUR	1674
WARDHA	1897
PUNE	1907
BHANDARA	2006
PARBHANI	2125
JALGAON	2452
YAVATMAL	3092
AMRAVATI	3317
DHULE	3702
NAGPUR	4835
NANDED	4863
AKOLA	5849
OSMANABAD	7738
NASHIK	9129
HINGOLI	9882
CHANDRAPUR	10129
NANDURBAR	12437

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	Division	Sanction	30.05.2023	31.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AURANGABAD DIV.	170685	106730	106842	112	63843	87	12769
2	AMRAVATI DIV.	95406	66775	66862	87	28544	56	5709
3	NAGPUR DIV.	97298	70966	71029	63	26269	44	5254
4	NASHIK DIV.	113029	90149	90194	45	22835	63	4567
5	PUNE DIV.	63387	52496	52519	23	10868	23	2174
6	KONKAN DIV.	31985	24247	24264	17	7721	15	1544
Total		571790	411363	411710	347	160080	288	32016

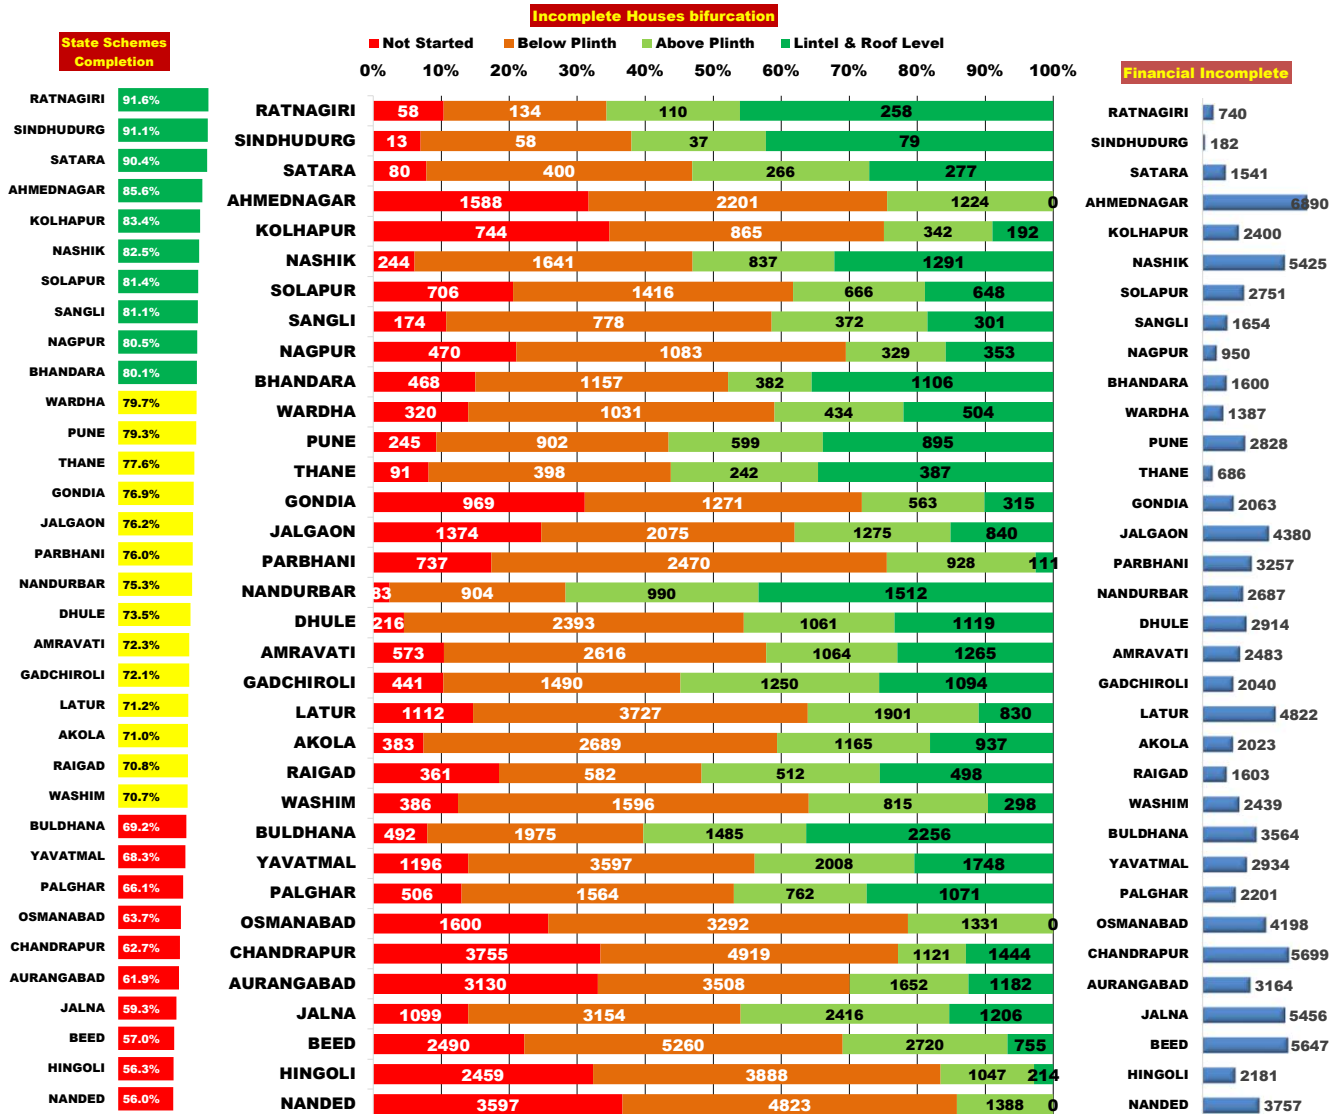

राज्यपुरस्कृत आवास योजना ग्रामीण - पूर्ण घरकूले

Sr. No.	District	Sanction	30.05.2023	31.05.2023	Daily Achievement	Remaining	Avg. Completed Per Day From 20.11.22 to Today	To be Completed in Per Day till 05.06.23
1	AMRAVATI	19907	14348	14389	41	5518	10	1104
2	NANDED	21897	12218	12257	39	9640	9	1928
3	AURANGABAD	24847	15353	15375	22	9472	9	1894
4	AKOLA	17832	12640	12658	18	5174	9	1035
5	GADCHIROLI	15344	11053	11069	16	4275	9	855
6	JALNA	19339	11448	11464	16	7875	22	1575
7	NASHIK	22906	18877	18893	16	4013	11	803
8	OSMANABAD	17115	10892	10908	16	6207	9	1241
9	YAVATMAL	26953	18388	18404	16	8549	14	1710
10	BHANDARA	15606	12480	12493	13	3113	4	623
11	NANDURBAR	14141	10639	10652	13	3489	6	698
12	CHANDRAPUR	30156	18906	18917	11	11239	12	2248
13	GONDIA	13486	10358	10368	10	3118	9	624
14	PALGHAR	11509	7596	7606	10	3903	6	781
15	WARDHA	11250	8951	8961	10	2289	7	458
16	LATUR	26330	18751	18760	9	7570	13	1514
17	SANGLI	8604	6970	6979	9	1625	3	325
18	AHMEDNAGAR	34495	29507	29515	8	4980	25	996
19	KOLHAPUR	12889	10738	10746	8	2143	3	429
20	BULDHANA	20163	13948	13955	7	6208	15	1242
21	JALGAON	23399	17829	17835	6	5564	11	1113
22	BEED	26082	14852	14857	5	11225	13	2245
23	RATNAGIRI	6691	6126	6131	5	560	3	112
24	WASHIM	10551	7451	7456	5	3095	8	619
25	PARBHANI	17659	13409	13413	4	4246	4	849
26	NAGPUR	11456	9218	9221	3	2235	3	447
27	PUNE	12765	10121	10124	3	2641	5	528
28	DHULE	18088	13297	13299	2	4789	9	958
29	SATARA	10647	9622	9624	2	1023	5	205
30	HINGOLI	17416	9807	9808	1	7608	7	1522
31	RAIGAD	6694	4740	4741	1	1953	3	391
32	SOLAPUR	18482	15045	15046	1	3436	6	687
33	THANE	4983	3864	3865	1	1118	2	224
34	SINDHUDURG	2108	1921	1921	0	187	1	37
Total		571790	411363	411710	347	160080	288	32016

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	10052	0	38073	0	22649
2	AMRAVATI DIV.	0	29545	0	30940	0	16048
3	AURANGABAD DIV.	0	19521	0	51237	0	24628
4	NAGPUR DIV.	0	10033	0	19658	0	12150
5	KONKAN DIV.	0	362	0	3279	0	3207
6	PUNE DIV.	0	9063	0	15982	0	6784
	Total	0	78576	0	159169	0	85466

PMAY-G 1st Ins Pending

SINDHUDURG	4
RAIGAD	14
THANE	74
RATNAGIRI	90
PALGHAR	180
GADCHIROLI	298
SANGLI	409
KOLHAPUR	549
SATARA	771
DHULE	948
NASHIK	1076
PARBHANI	1123
NANDURBAR	1308
GONDIA	1379
WARDHA	1550
NAGPUR	1860
JALNA	1878
HINGOLI	1956
PUNE	1967
CHANDRAPUR	2012
LATUR	2254
AURANGABAD	2675
BHANDARA	2934
WASHIM	2940
AHMEDNAGAR	2997
OSMANABAD	3091
BEED	3234
NANDED	3310
YAVATMAL	3697
JALGAON	3723
AKOLA	3847
SOLAPUR	5367
BULDHANA	7845
AMRAVATI	11216

PMAY-G 2nd Ins Pending

SINDHUDURG	213
RATNAGIRI	388
RAIGAD	499
THANE	566
SATARA	1073
WARDHA	1218
PALGHAR	1613
OSMANABAD	1852
PUNE	2283
KOLHAPUR	2423
GADCHIROLI	2501
NAGPUR	2884
HINGOLI	3089
WASHIM	3111
AHMEDNAGAR	3597
GONDIA	3789
SANGLI	3861
LATUR	4205
CHANDRAPUR	4273
JALNA	4357
AKOLA	4793
BHANDARA	4993
AURANGABAD	5536
PARBHANI	5670
NASHIK	5895
BULDHANA	6064
SOLAPUR	6342
DHULE	6755
BEED	8070
AMRAVATI	8444
YAVATMAL	8528
NANDURBAR	9335
JALGAON	12491
NANDED	18458

PMAY-G 3rd Ins Pending

SINDHUDURG	260
RAIGAD	370
RATNAGIRI	393
THANE	536
WARDHA	859
SATARA	934
KOLHAPUR	987
PUNE	1074
NAGPUR	1356
SANGLI	1468
HINGOLI	1482
PALGHAR	1648
LATUR	1894
GADCHIROLI	2172
AKOLA	2179
BHANDARA	2193
WASHIM	2239
SOLAPUR	2321
AURANGABAD	2445
CHANDRAPUR	2565
AHMEDNAGAR	2792
PARBHANI	2922
OSMANABAD	2947
GONDIA	3005
JALNA	3016
BULDHANA	3040
AMRAVATI	3339
BEED	3696
DHULE	3796
NASHIK	3873
JALGAON	4194
YAVATMAL	5251
NANDED	6226
NANDURBAR	7994

प्रधानमंत्री आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	2997	0	3597	0	2792
2	AKOLA	0	3847	0	4793	0	2179
3	AMRAVATI	0	11216	0	8444	0	3339
4	AURANGABAD	0	2675	0	5536	0	2445
5	BEED	0	3234	0	8070	0	3696
6	BHANDARA	0	2934	0	4993	0	2193
7	BULDHANA	0	7845	0	6064	0	3040
8	CHANDRAPUR	0	2012	0	4273	0	2565
9	DHULE	0	948	0	6755	0	3796
10	GADCHIROLI	0	298	0	2501	0	2172
11	GONDIA	0	1379	0	3789	0	3005
12	HINGOLI	0	1956	0	3089	0	1482
13	JALGAON	0	3723	0	12491	0	4194
14	JALNA	0	1878	0	4357	0	3016
15	KOLHAPUR	0	549	0	2423	0	987
16	LATUR	0	2254	0	4205	0	1894
17	NAGPUR	0	1860	0	2884	0	1356
18	NANDED	0	3310	0	18458	0	6226
19	NANDURBAR	0	1308	0	9335	0	7994
20	NASHIK	0	1076	0	5895	0	3873
21	OSMANABAD	0	3091	0	1852	0	2947
22	PALGHAR	0	180	0	1613	0	1648
23	PARBHANI	0	1123	0	5670	0	2922
24	PUNE	0	1967	0	2283	0	1074
25	RAIGAD	0	14	0	499	0	370
26	RATNAGIRI	0	90	0	388	0	393
27	SANGLI	0	409	0	3861	0	1468
28	SINDHUDURG	0	4	0	213	0	260
29	SOLAPUR	0	5367	0	6342	0	2321
30	THANE	0	74	0	566	0	536
31	WARDHA	0	1550	0	1218	0	859
32	WASHIM	0	2940	0	3111	0	2239
33	YAVATMAL	0	3697	0	8528	0	5251
34	SATARA	-1	771	0	1073	0	934
	Total	0	78576	0	159169	0	85466

राज्यपुरस्कृत आवास योजना ग्रामीण - हप्ते वितरण

Sr. No.	Division	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	NASHIK DIV.	0	3505	0	9214	0	5387
2	AMRAVATI DIV.	0	3030	0	12473	0	6537
3	AURANGABAD DIV.	0	16224	0	30122	0	13383
4	NAGPUR DIV.	0	6423	0	10951	0	4079
5	KONKAN DIV.	0	1029	0	2736	0	1663
6	PUNE DIV.	0	1949	0	4361	0	2245
Total		0	32160	0	69857	0	33294

State Schemes 1st Ins Pending

SINDHUDURG	13
RATNAGIRI	58
SATARA	80
NANDURBAR	83
THANE	91
SANGLI	174
DHULE	216
NASHIK	244
PUNE	245
WARDHA	320
RAIGAD	361
AKOLA	383
WASHIM	386
GADCHIROLI	441
BHANDARA	468
NAGPUR	470
BULDHANA	492
PALGHAR	506
AMRAVATI	573
SOLAPUR	706
PARBHANI	737
KOLHAPUR	744
GONDIA	969
JALNA	1099
LATUR	1112
YAVATMAL	1196
JALGAON	1374
AHMEDNAGAR	1588
OSMANABAD	1600
HINGOLI	2459
BEED	2490
AURANGABAD	3130
NANDED	3597
CHANDRAPUR	3755

State Schemes 2nd Ins Pending

SINDHUDURG	58
RATNAGIRI	134
THANE	398
SATARA	400
RAIGAD	582
SANGLI	778
KOLHAPUR	865
PUNE	902
NANDURBAR	904
WARDHA	1031
NAGPUR	1083
BHANDARA	1157
GONDIA	1271
SOLAPUR	1416
GADCHIROLI	1490
PALGHAR	1564
WASHIM	1596
NASHIK	1641
BULDHANA	1975
JALGAON	2075
AHMEDNAGAR	2201
DHULE	2393
PARBHANI	2470
AMRAVATI	2616
AKOLA	2689
JALNA	3154
OSMANABAD	3292
AURANGABAD	3508
YAVATMAL	3597
LATUR	3727
HINGOLI	3888
NANDED	4823
CHANDRAPUR	4919
BEED	5260

State Schemes 3rd Ins Pending

SINDHUDURG	37
RATNAGIRI	110
THANE	242
SATARA	266
NAGPUR	329
KOLHAPUR	342
SANGLI	372
BHANDARA	382
WARDHA	434
RAIGAD	512
GONDIA	563
PUNE	599
SOLAPUR	666
PALGHAR	762
WASHIM	815
NASHIK	837
PARBHANI	928
NANDURBAR	990
HINGOLI	1047
DHULE	1061
AMRAVATI	1064
CHANDRAPUR	1121
AKOLA	1165
AHMEDNAGAR	1224
GADCHIROLI	1250
JALGAON	1275
OSMANABAD	1331
NANDED	1388
BULDHANA	1485
AURANGABAD	1652
LATUR	1901
YAVATMAL	2008
JALNA	2416
BEED	2720

राज्यपुरस्कृत आवास योजना ग्रामीण -हप्ते वितरण

Sr. No.	District	1st Installment (Daily Achivement)	1st Installment Remaining	2nd Installment (Daily Achivement)	2nd Installment Remaining	3rd Installment (Daily Achivement)	3rd Installment Remaining
1	AHMEDNAGAR	0	1588	0	2201	0	1224
2	AKOLA	0	383	0	2689	0	1165
3	AMRAVATI	0	573	0	2616	0	1064
4	AURANGABAD	0	3130	0	3508	0	1652
5	BEED	0	2490	0	5260	0	2720
6	BHANDARA	0	468	0	1157	0	382
7	BULDHANA	0	492	0	1975	0	1485
8	CHANDRAPUR	0	3755	0	4919	0	1121
9	DHULE	0	216	0	2393	0	1061
10	GADCHIROLI	0	441	0	1490	0	1250
11	GONDIA	0	969	0	1271	0	563
12	HINGOLI	0	2459	0	3888	0	1047
13	JALGAON	0	1374	0	2075	0	1275
14	JALNA	0	1099	0	3154	0	2416
15	KOLHAPUR	0	744	0	865	0	342
16	LATUR	0	1112	0	3727	0	1901
17	NAGPUR	0	470	0	1083	0	329
18	NANDED	0	3597	0	4823	0	1388
19	NANDURBAR	0	83	0	904	0	990
20	NASHIK	0	244	0	1641	0	837
21	OSMANABAD	0	1600	0	3292	0	1331
22	PALGHAR	0	506	0	1564	0	762
23	PARBHANI	0	737	0	2470	0	928
24	PUNE	0	245	0	902	0	599
25	RAIGAD	0	361	0	582	0	512
26	RATNAGIRI	0	58	0	134	0	110
27	SANGLI	0	174	0	778	0	372
28	SATARA	0	80	0	400	0	266
29	SINDHUDURG	0	13	0	58	0	37
30	SOLAPUR	0	706	0	1416	0	666
31	THANE	0	91	0	398	0	242
32	WARDHA	0	320	0	1031	0	434
33	WASHIM	0	386	0	1596	0	815
34	YAVATMAL	0	1196	0	3597	0	2008
	Total	0	32160	0	69857	0	33294

प्रधानमंत्री आवास योजना ग्रामीण - Delayed Houses

■ पहिला हप्ता मिळाल्यानंतर १२ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १८ महिने उलटूनही अपूर्ण घरकुले
 ■ पहिला हप्ता मिळाल्यानंतर १० दिवसानंतरही दुसरा हप्ता न मिळालेले घरकुले
■ दुसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही तिसरा हप्ता न मिळालेले घरकुले
 ■ तिसरा हप्ता मिळाल्यानंतर १० दिवसानंतरही अपूर्ण घरांची संख्या

AHMEDNAGAR	2308	1681	3175	1695	41
AKOLA	4007	3363	3493	886	555
AMRAVATI	7022	5347	7031	1531	1021
AURANGABAD	2367	2214	4890	1136	485
BEED	2075	1778	6852	1720	427
BHANDARA	6528	4964	4598	841	2271
BULDHANA	2555	2108	4330	920	734
CHANDRAPUR	2860	1913	3462	791	310
DHULE	5463	4016	5816	2366	1568
GADCHIROLI	3775	2374	2237	1210	938
GONDIA	1692	1636	3090	1039	128
HINGOLI	962	644	2639	511	98
JALGAON	7568	6435	11154	2185	649
JALNA	1334	1060	3389	927	333
KOLHAPUR	1785	708	2296	298	82
LATUR	763	697	2912	504	41
NAGPUR	3216	2251	2548	439	580
NANDED	9393	8919	14897	2146	383
NANDURBAR	11375	9864	7521	4809	5213
NASHIK	6778	3536	4923	2127	1551
OSMANABAD	985	576	1231	451	5
PALGHAR	863	628	1300	782	604
PARBHANI	836	719	4810	704	125
PUNE	2173	1688	1981	551	471
RAIGAD	712	236	469	251	166
RATNAGIRI	156	39	336	153	77
SANGLI	2909	2239	3439	614	159
SATARA	617	352	852	286	174
SINDHUDURG	120	76	196	76	31
SOLAPUR	4857	4504	5116	1264	541
THANE	206	187	520	195	314
WARDHA	1055	765	943	221	214
WASHIM	1102	796	2524	475	49
YAVATMAL	6155	4216	7208	1952	1703
